




OIL WELL CEMENTING INC.

Date 1/28/70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6598

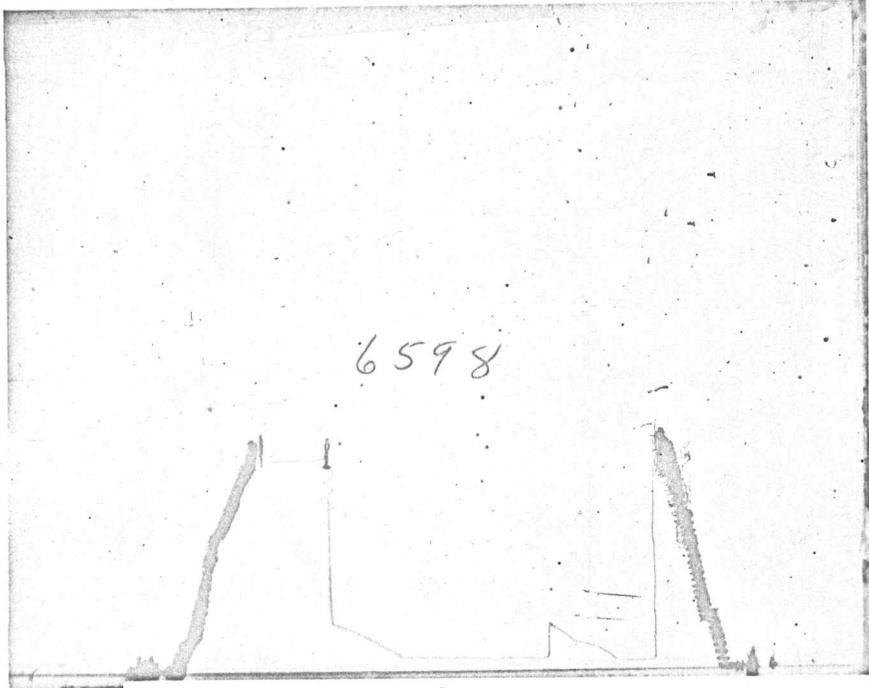

Company Gorski Contractor American Drlg.  
 Well No. B-1 Lease Vopat County Ellsworth Sec. 22 Twp 14 Rng 10  
 Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 F.H.  
 Interval Tested From 2428 To 2464 Depth of Well 2464 Size Choke 5/8  
 Fluid Recovered In \_\_\_\_\_ Temp. 86 Elev. \_\_\_\_\_  
 Initial Hyd. 1519 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.  
 First Initial Flow Pressure 55 P.S.I. Opened Tool 7:05 A.M. ~~###~~  
 First Final Flow Pressure \_\_\_\_\_ P.S.I. First Flow Pres. 30 Min.  
 Initial Closed-in Pressure 308 P.S.I. Initial Closed-in Pres. 60 Min.  
 Second Initial Flow Pressure 99 P.S.I. Second Flow Pres. 120 Min.  
 Second Final Flow Pressure \_\_\_\_\_ P.S.I. Final Closed-in Pres. 60 Min.  
 Final Closed-in Pressure 319 P.S.I.

Blow Good Blow Thru-Out Test

Recovery 1320' Gas In Pipe 90' Oil Gas Cut Mud

Remarks 10% Oil 80% Mud

Approved By Elster Tester Bowman




OIL WELL CEMENTING INC.

Date 1/30/70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6599

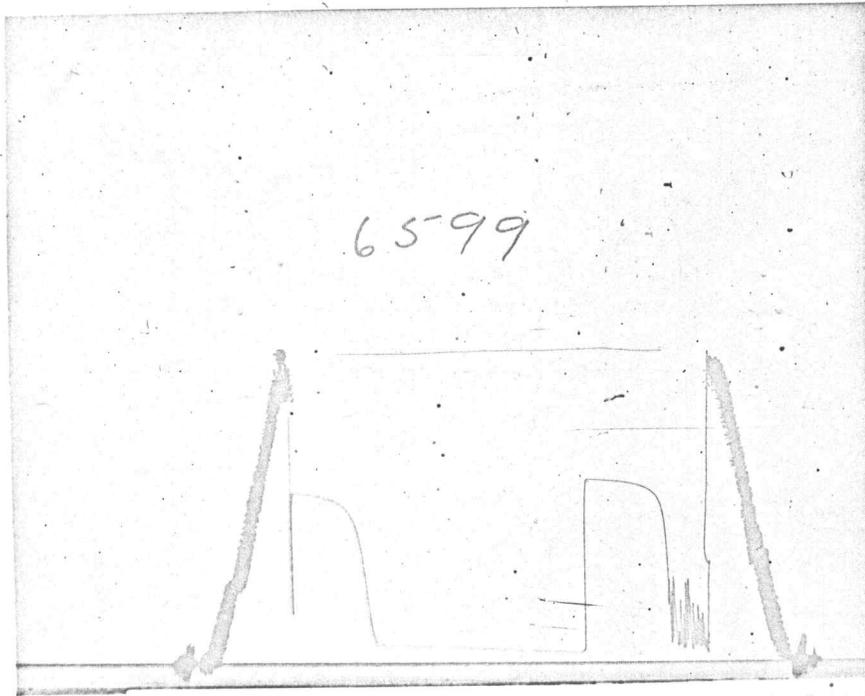

Company Gorski Contractor American Drlg.  
 Well No. B-1 Lease Vopat County Ellsworth Sec. 22 Twp 14 Rng 10  
 Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 F.H.  
 Interval Tested From 2899 To 2915 Depth of Well 2915 Size Choke 5/8  
 Fluid Recovered In \_\_\_\_\_ Temp. 101 Elev. \_\_\_\_\_  
 Initial Hyd. 1625 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.  
 First Initial Flow Pressure 44 P.S.I. Opened Tool 1:10 ~~###~~ P.M.  
 First Final Flow Pressure \_\_\_\_\_ P.S.I. First Flow Pres. 30 Min.  
 Initial Closed-in Pressure 1002 P.S.I. Initial Closed-in Pres. 60 Min.  
 Second Initial Flow Pressure 66 P.S.I. Second Flow Pres. 150 Min.  
 Second Final Flow Pressure 110 P.S.I. Final Closed-in Pres. 60 Min.  
 Final Closed-in Pressure 926 P.S.I.

Blow Weak For 30 Min. Open Tool On F.F. no Blow for 10 Min. Then Blow Weak Thru-Out

Recovery 150' Sli. Oil Cut Muddy Water

Remarks 10% oil 5% Mud 85% Water

Approved By Flster Tester Bowman
