

Company **Vess Oil Corporation**
 Address **1700 Waterfront Pkwy Bldg 500**
 CSZ **Wichita, KS 67206**
 Attn. **Roger Martin**

Lease Name **Barnhill A**
 Lease # **31**
 Legal Desc **N/2 S/2 N/2 SE**
 Section **6**
 Township **26S**
 County **Butler**
 Drilling Cont **C & G Drilling #1**

Job Ticket **3423**
 Range **5E**
 State **KS**

Comments **Field: El Dorado**

GENERAL INFORMATION

Test # **1** Test Date **4/8/2011**
 Tester **Jimmy Ricketts**
 Test Type **Conventional Bottom Hole**

Chokes **3/4** Hole Size **7 7/8**
 Top Recorder # **11027**
 Mid Recorder #
 Bott Recorder # **w1023**

Successful Test
 # of Packers **2.0** Packer Size **6 3/4**

Mileage **110** Approved By

Mud Type **Gel Chem**
 Mud Weight **9.4** Viscosity **48.0**
 Filtrate **10.4** Chlorides **800**

Standby Time **0**
 Extra Equipmnt **Jars & Safety Joint**
 Time on Site **8:40 PM**
 Tool Picked Up **10:00 PM**
 Tool Layed Dwn **6:30 AM**

Drill Collar Len **151.0**
 Wght Pipe Len **0**

Elevation **1399.00** Kelley Bushings **1405.00**

Formation **Arbuckle**
 Interval Top **2426.0** Bottom **2487.0**
 Anchor Len Below **61.0** Between **0**
 Total Depth **2487.0**


Start Date/Time **4/7/2011 9:53 PM**
 End Date/Time **4/8/2011 7:36 AM**

Blow Type **Weak blow building to strong blow 10 minutes into initial flow period.**
Weak blow building to strong blow 11 minutes into final flow period.
Times: 30, 45, 45, 60. API gravity was 36.

RECOVERY

Feet	Description	Gas	Oil	Water	Mud
270	Clean oil	0% 0ft	100% 270ft	0% 0ft	0% 0ft
95	Oil cut mud	0% 0ft	11% 10.5ft	0% 0ft	89% 84.6ft
90	Clean oil	0% 0ft	100% 90ft	0% 0ft	0% 0ft
30	Oil cut mud	0% 0ft	11% 3.3ft	0% 0ft	89% 26.7ft
1	Oil cut mud in tool sample	0% 0ft	14% 0.1ft	0% 0ft	86% 0.9ft

DST Fluids **0**

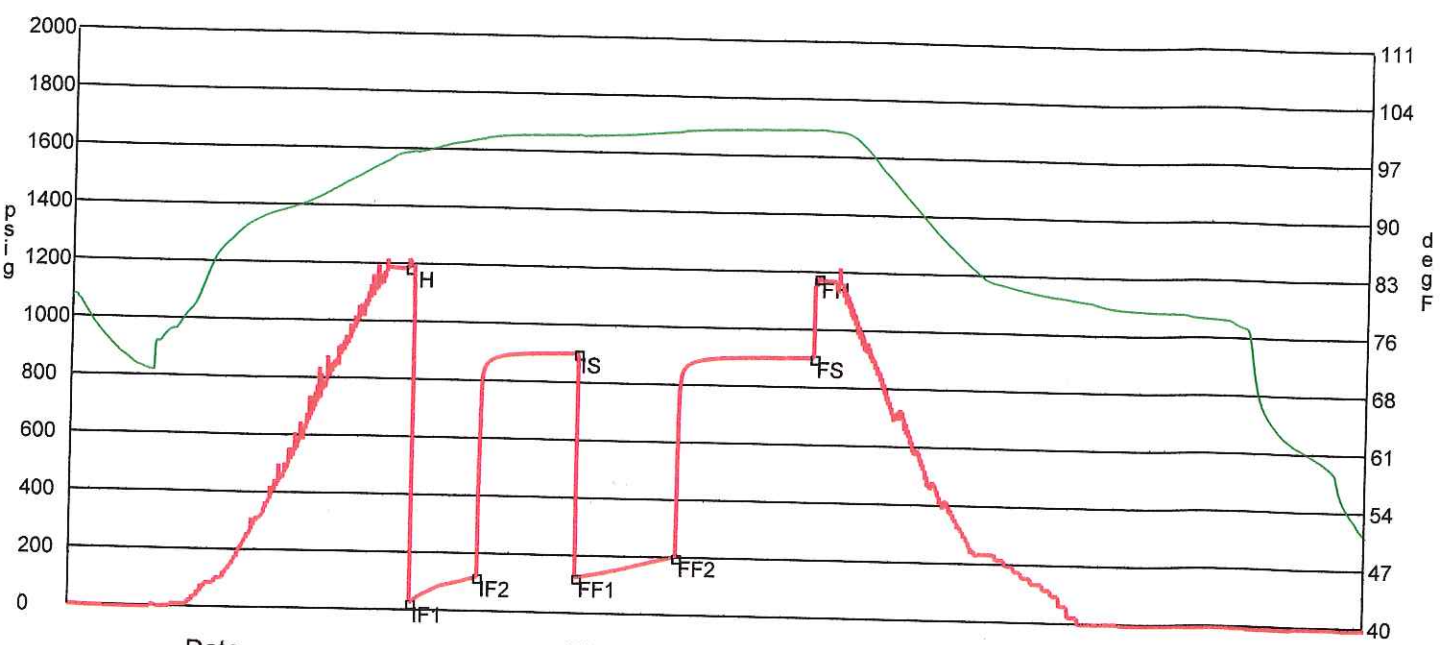

	Date	Time	Pressure	Temp	
IH	4/8/2011 12:23:10 AM	2.502778	1184.174	96.38	Initial Hydro-static
IF1	4/8/2011 12:26:00 AM	2.55	23.321	96.396	Initial Flow (1)
IF2	4/8/2011 12:56:00 AM	3.05	116.711	98.176	Initial Flow (2)
IS	4/8/2011 1:40:00 AM	3.783333	900.111	98.863	Initial Shut-In
FF1	4/8/2011 1:40:50 AM	3.797222	123.839	98.77	Final Flow (1)
FF2	4/8/2011 2:25:40 AM	4.544444	200.952	99.519	Final Flow (2)
FS	4/8/2011 3:26:10 AM	5.552778	900.628	100.056	Final Shut-In
FH	4/8/2011 3:27:30 AM	5.575	1177.849	100.093	Final Hydro-static

GAS FLOWS

Min Into IFP Min Into FFP Gas Flows Pressure Choke

COMPANY VESS OIL CORPORATION
 LEASE AND WELL NO. BARNHILL A #31
 SEC 6
 TWP 26S
 RGE 5E
 TEST NO. 1
 DATE 4-8-
