



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Pauley Oil

15-17s-8w Ellsworth, KS

314 5th. St.
Clafin, KS 67525

S. Rolfs #4

Job Ticket: 50868

DST#: 2

ATTN: Wyatt Urban


Test Start: 2013.03.25 @ 09:27:56

GENERAL INFORMATION:

Formation: **Arbuckle**
 Deviated: **No Whipstock:** ft (KB)
 Time Tool Opened: 11:00:11
 Time Test Ended: 12:55:26
 Interval: **3187.00 ft (KB) To 3277.00 ft (KB) (TVD)**
 Total Depth: **3277.00 ft (KB) (TVD)**
 Hole Diameter: **7.88 inches** Hole Condition: **Fair**
 Test Type: **Conventional Bottom Hole (Reset)**
 Tester: **Ryan Reynolds**
 Unit No: **48**
 Reference Elevations: **1770.00 ft (KB)**
1757.00 ft (CF)
KB to GR/CF: 13.00 ft

Serial #: **8790** Inside
 Press@RunDepth: kPag @ **3188.00 ft (KB)**
 Start Date: **2013.03.25** End Date: **2013.03.25** Capacity: **55000.00 kPag**
 Start Time: **09:28:01** End Time: **12:55:26** Last Calib.: **2013.03.25**
 Time On Blrm: **2013.03.25 @ 10:57:11**
 Time Off Blrm: **2013.03.25 @ 11:07:41**

TEST COMMENT: **Packer Failure, No Test.**

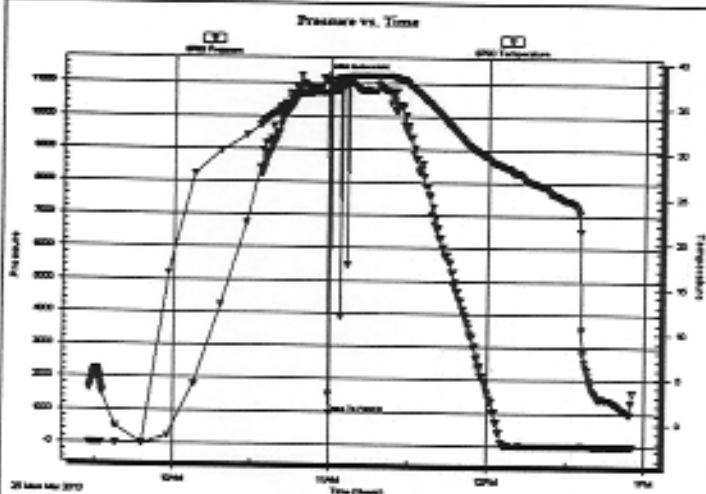

PRESSURE SUMMARY

Time (Min.)	Pressure (kPag)	Temp (deg C)	Annotation
0	11176.9	36.57	Initial Hydro-static
3	951.73	36.39	Open To Flow (1)
11	11066.5	38.39	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
200.00	Drig mud 100% mud	2.81

* Recovery from multiple tests

Gas Rates

Choke (inches)	Pressure (kPag)	Gas Rate (Mcf/D)
