



DRILL STEM TEST REPORT

Prepared For: **TDI LLC**

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

Paulette #1

22-15s-19w Ellis,KS

Start Date: 2014.06.24 @ 18:25:00

End Date: 2014.06.25 @ 00:35:00

Job Ticket #: 55296 DST #: 1

Trilobite Testing, Inc
PO Box 362 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620

Printed: 2014.06.27 @ 10:23:52



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TDI LLC

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

22-15s-19w Ellis,KS

Paulette #1

Job Ticket: 55296

DST#: 1

Test Start: 2014.06.24 @ 18:25:00

GENERAL INFORMATION:

Formation: **L.K.C. "B - D"**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 20:02:00

Time Test Ended: 00:35:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Bob Hamel

Unit No: 67

Interval: 3252.00 ft (KB) To 3290.00 ft (KB) (TVD)

Total Depth: 3290.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1957.00 ft (KB)

1947.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 6625 Outside

Press@RunDepth: 73.90 psig @ 3256.00 ft (KB)

Start Date: 2014.06.24

End Date:

2014.06.25

Start Time: 18:25:01

End Time:

00:35:00

Capacity: 8000.00 psig


Last Calib.: 2014.06.24

Time On Btm: 2014.06.24 @ 20:01:00

Time Off Btm: 2014.06.24 @ 23:08:00

TEST COMMENT: I.F. - 45 - Weak blow built to 9"
I.S.I. - 45 - No blow back
F.F. - 45 - Weak blow built to 4"
F.S.I. - 45 - No blow back

Pressure vs. Time

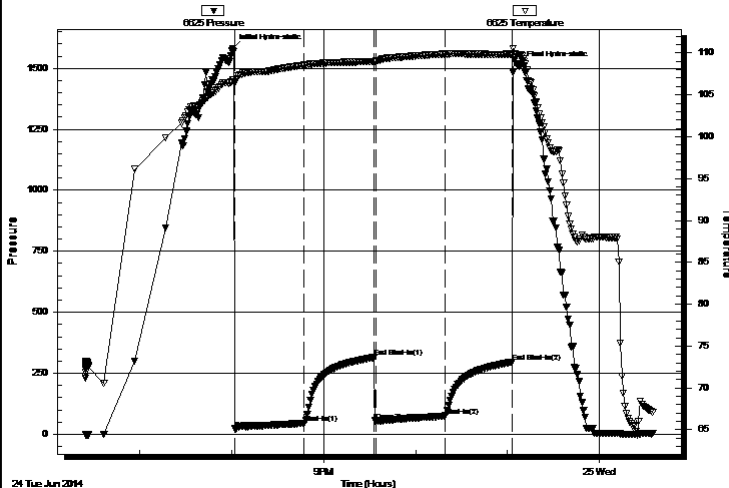

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1581.78	106.75	Initial Hydro-static
1	21.41	106.60	Open To Flow (1)
47	45.29	108.57	Shut-In(1)
92	314.29	108.96	End Shut-In(1)
93	51.97	109.01	Open To Flow (2)
138	73.90	109.87	Shut-In(2)
182	295.45	109.86	End Shut-In(2)
187	1511.02	109.77	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
83.00	S,O,S,M,W, 2%O 48%M 50%W	1.16

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TDI LLC

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

22-15s-19w Ellis, KS

Paulette #1

Job Ticket: 55296

DST#: 1

Test Start: 2014.06.24 @ 18:25:00

GENERAL INFORMATION:

Formation: **L.K.C. "B - D"**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 20:02:00

Time Test Ended: 00:35:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Bob Hamel

Unit No: 67

Interval: 3252.00 ft (KB) To 3290.00 ft (KB) (TVD)

Total Depth: 3290.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1957.00 ft (KB)

1947.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 8319 Inside

Press@RunDepth: psig @ 3256.00 ft (KB)

Start Date: 2014.06.24

End Date:

2014.06.25

Start Time: 18:25:01

End Time:

00:35:00

Capacity: 8000.00 psig


Last Calib.: 2014.06.25

Time On Btm:

Time Off Btm:

TEST COMMENT: I.F. - 45 - Weak blow built to 9"
I.S.I. - 45 - No blow back
F.F. - 45 - Weak blow built to 4"
F.S.I. - 45 - No blow back

Pressure vs. Time

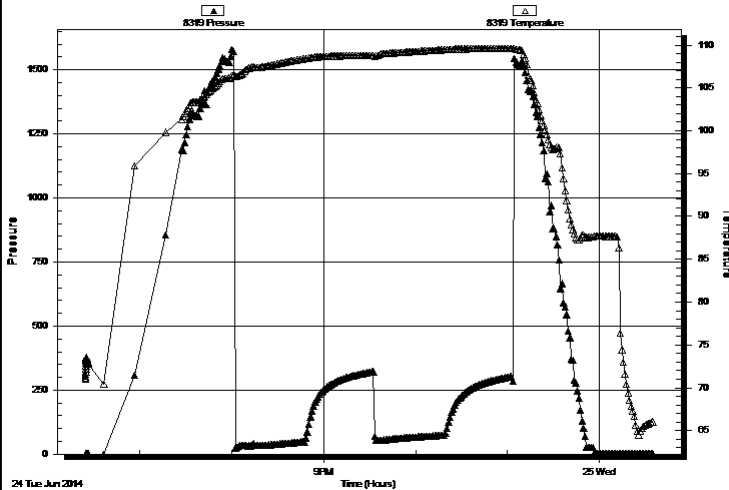

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
-------------	-----------------	--------------	------------

Recovery

Length (ft)	Description	Volume (bbl)
83.00	S,O,S,M,W, 2%O 48%M 50%W	1.16

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

TDI LLC

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

22-15s-19w Ellis,KS

Paulette #1

Job Ticket: 55296

DST#: 1

Test Start: 2014.06.24 @ 18:25:00

Tool Information

Drill Pipe:	Length:	3248.00 ft	Diameter:	3.80 inches	Volume:	45.56 bbl	Tool Weight:	2000.00 lb
Heavy Wt. Pipe:	Length:	0.00 ft	Diameter:	2.70 inches	Volume:	0.00 bbl	Weight set on Packer:	30000.00 lb
Drill Collar:	Length:	0.00 ft	Diameter:	2.25 inches	Volume:	0.00 bbl	Weight to Pull Loose:	50000.00 lb
					Total Volume:	45.56 bbl	Tool Chased	7.00 ft
Drill Pipe Above KB:		16.00 ft					String Weight: Initial	43000.00 lb
Depth to Top Packer:		3252.00 ft					Final	43000.00 lb
Depth to Bottom Packer:		ft						
Interval between Packers:		38.00 ft						
Tool Length:		58.00 ft						
Number of Packers:		2	Diameter:	6.75 inches				
Tool Comments:								

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Change Over Sub	1.00			3233.00	
Shut In Tool	5.00			3238.00	
Hydraulic tool	5.00			3243.00	
Packer	4.00			3247.00	20.00 Bottom Of Top Packer
Packer	5.00			3252.00	
Stubb	1.00			3253.00	
Perforations	3.00			3256.00	
Recorder	0.00	6625	Outside	3256.00	
Recorder	0.00	8319	Inside	3256.00	
Perforations	30.00			3286.00	
Bullnose	4.00			3290.00	38.00 Bottom Packers & Anchor

Total Tool Length: 58.00



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

TDI LLC

22-15s-19w Ellis,KS

1310 Bison Rd
Hays KS 67601

Paulette #1

Job Ticket: 55296

DST#: 1

ATTN: Herb Deines

Test Start: 2014.06.24 @ 18:25:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 63.00 sec/qt

Water Loss: 7.98 in³

Resistivity: 0.00 ohm.m

Salinity: 4500.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psig

Oil API:

Water Salinity:

deg API

5500 ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
83.00	S,O,S,M,W, 2%O 48%M 50%W	1.164

Total Length: 83.00 ft Total Volume: 1.164 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments: R.W. = 1.29 OHMS @ 61.3 DEG.


Serial #: 6625

Outside TDI LLC

Paulette #1

DST Test Number: 1

Pressure vs. Time

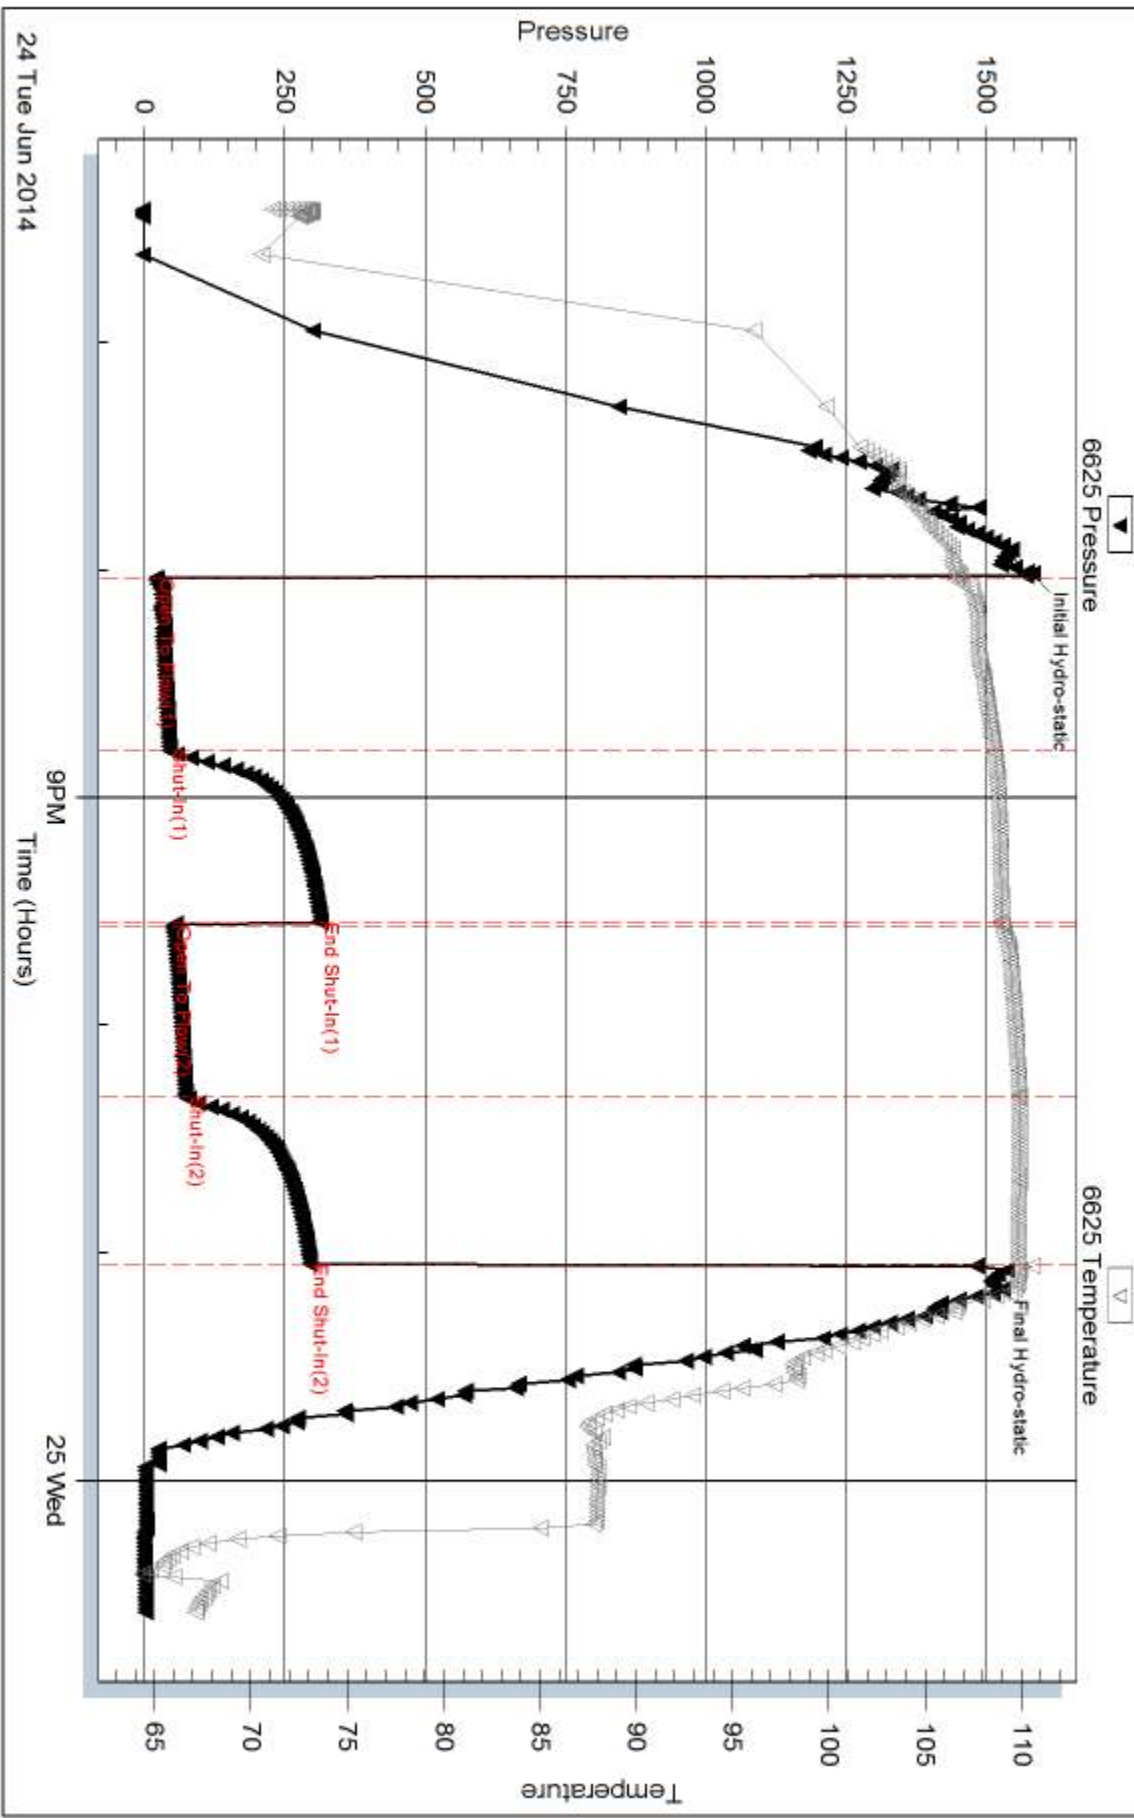


Serial #: 8319

inside TDILLC

Paulette #1

DST Test Number: 1

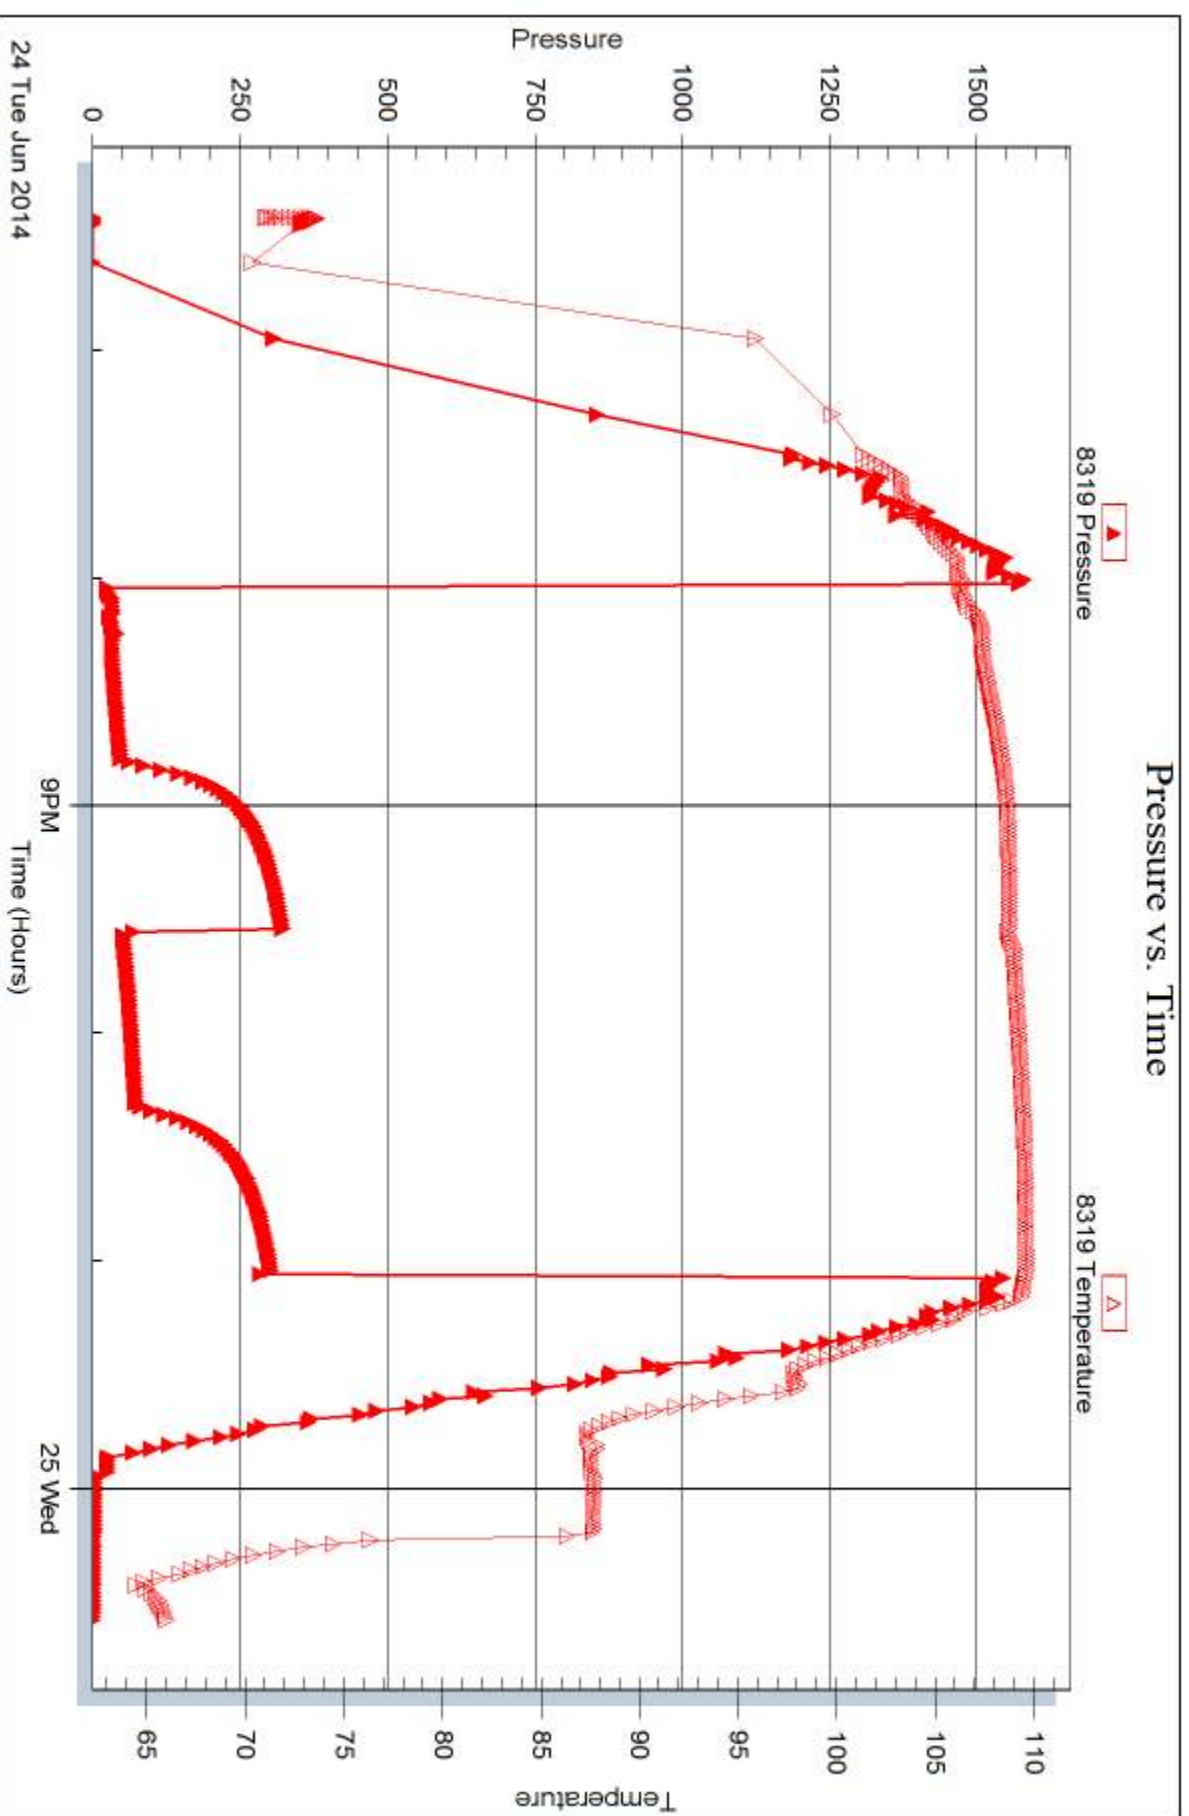



DRILL STEM TEST REPORT

Prepared For: **TDI LLC**

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

Paulette #1

22-15s-19w Ellis,KS

Start Date: 2014.06.26 @ 04:09:00

End Date: 2014.06.26 @ 10:37:30

Job Ticket #: 59384 DST #: 2

Trilobite Testing, Inc
PO Box 362 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620

Printed: 2014.06.27 @ 10:22:44



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

TDI LLC

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

22-15s-19w Ellis,KS

Paulette #1

Job Ticket: 59384

DST#: 2

Test Start: 2014.06.26 @ 04:09:00

GENERAL INFORMATION:

Formation: **LKC "F"**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 06:27:30

Time Test Ended: 10:37:30

Test Type: Conventional Bottom Hole (Reset)

Tester: Phillip Gage

Unit No: 67

Interval: 3295.00 ft (KB) To 3338.00 ft (KB) (TVD)

Total Depth: 3664.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1957.00 ft (KB)

1947.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 6625 Inside

Press@RunDepth: 217.32 psig @ 3362.00 ft (KB)

Start Date: 2014.06.26

End Date:

2014.06.26

Start Time: 04:09:01

End Time:

10:37:30

Capacity: 8000.00 psig


Last Calib.: 2014.06.26

Time On Btm: 2014.06.26 @ 06:27:00

Time Off Btm: 2014.06.26 @ 09:03:00

TEST COMMENT: 30-IF-Built to 6 1/2"
30-ISI-No Return
45-FF-Built to 2 1/4"
45-FSI-No Return

Pressure vs. Time

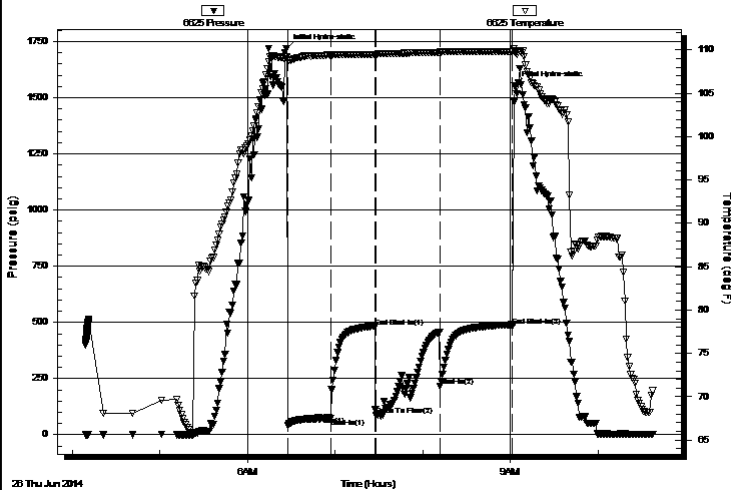

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1719.00	109.15	Initial Hydro-static
1	42.03	108.86	Open To Flow (1)
30	74.46	109.39	Shut-In(1)
60	480.75	109.43	End Shut-In(1)
61	85.88	109.49	Open To Flow (2)
105	217.32	109.75	Shut-In(2)
155	484.49	109.84	End Shut-In(2)
156	1552.27	109.93	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
83.00	VSWCM, 3%w, 97%m	1.16
15.00	M, 100%m	0.21

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------

* Recovery from multiple tests



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TDI LLC

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

22-15s-19w Ellis, KS

Paulette #1

Job Ticket: 59384

DST#: 2

Test Start: 2014.06.26 @ 04:09:00

GENERAL INFORMATION:

Formation: **LKC "F"**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 06:27:30

Time Test Ended: 10:37:30

Test Type: Conventional Bottom Hole (Reset)

Tester: Phillip Gage

Unit No: 67

Interval: 3295.00 ft (KB) To 3338.00 ft (KB) (TVD)

Total Depth: 3664.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1957.00 ft (KB)

1947.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 8652 Below (Straddle)

Press@RunDepth: psig @ 3373.00 ft (KB)

Start Date: 2014.06.26

End Date:

2014.06.26

Start Time: 04:09:05

End Time:

10:37:44

Capacity: 8000.00 psig

Last Calib.:


2014.06.26

Time On Btm:

Time Off Btm:

TEST COMMENT: 30-IF-Built to 6 1/2"
30-ISI-No Return
45-FF-Built to 2 1/4"
45-FSI-No Return

Pressure vs. Time

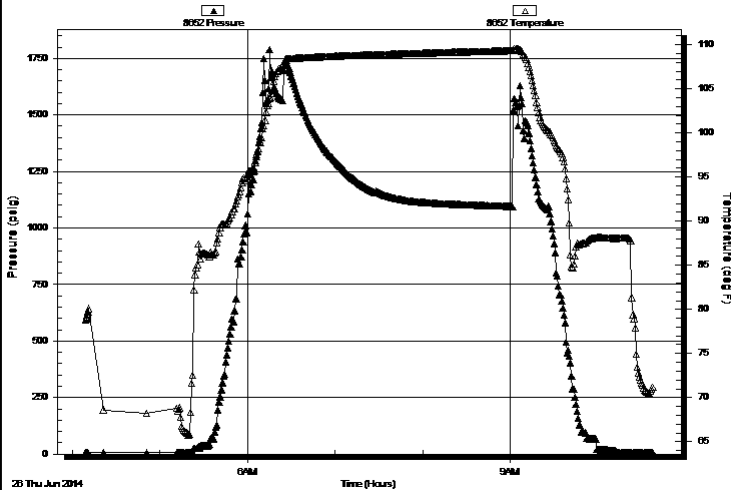

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
-------------	-----------------	--------------	------------

Recovery

Length (ft)	Description	Volume (bbl)
83.00	VSWCM, 3%w, 97%m	1.16
15.00	M, 100%m	0.21

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------

* Recovery from multiple tests



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

TDI LLC

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

22-15s-19w Ellis, KS

Paulette #1

Job Ticket: 59384

DST#: 2

Test Start: 2014.06.26 @ 04:09:00

GENERAL INFORMATION:

Formation: **LKC "F"**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 06:27:30

Time Test Ended: 10:37:30

Test Type: Conventional Bottom Hole (Reset)

Tester: Phillip Gage

Unit No: 67

Interval: 3295.00 ft (KB) To 3338.00 ft (KB) (TVD)

Total Depth: 3664.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1957.00 ft (KB)

1947.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 8319 Outside

Press@RunDepth: psig @ 3362.00 ft (KB)

Start Date: 2014.06.26

End Date:

2014.06.26

Start Time: 04:09:01

End Time:

10:37:30

Capacity: 8000.00 psig


Last Calib.: 2014.06.26

Time On Btm:

Time Off Btm:

TEST COMMENT: 30-IF-Built to 6 1/2"
30-ISI-No Return
45-FF-Built to 2 1/4"
45-FSI-No Return

Pressure vs. Time

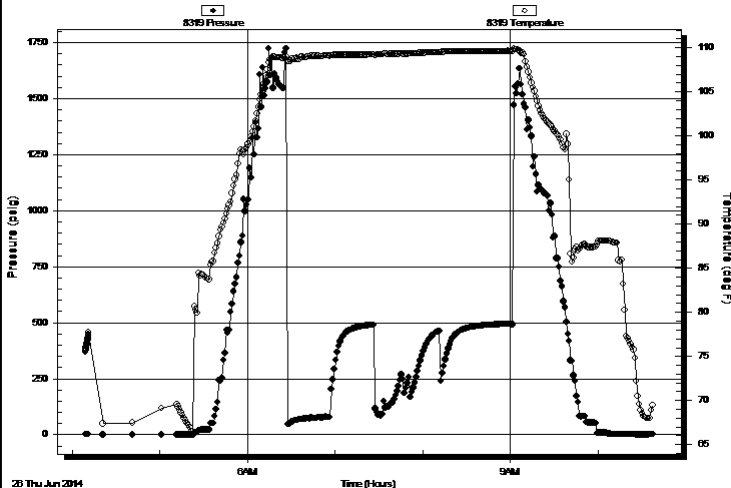

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
-------------	-----------------	--------------	------------

Recovery

Length (ft)	Description	Volume (bbl)
83.00	VSWCM, 3%w, 97%m	1.16
15.00	M, 100%m	0.21

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------

* Recovery from multiple tests



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

TDI LLC

1310 Bison Rd
Hays KS 67601

ATTN: Herb Deines

22-15s-19w Ellis,KS

Paulette #1

Job Ticket: 59384

DST#: 2

Test Start: 2014.06.26 @ 04:09:00

Tool Information

Drill Pipe:	Length:	3293.00 ft	Diameter:	3.80 inches	Volume:	46.19 bbl	Tool Weight:	2200.00 lb
Heavy Wt. Pipe:	Length:	0.00 ft	Diameter:	2.70 inches	Volume:	0.00 bbl	Weight set on Packer:	25000.00 lb
Drill Collar:	Length:	0.00 ft	Diameter:	2.25 inches	Volume:	0.00 bbl	Weight to Pull Loose:	50000.00 lb
					Total Volume:	46.19 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:		18.00 ft					String Weight: Initial	46000.00 lb
Depth to Top Packer:		3295.00 ft					Final	49000.00 lb
Depth to Bottom Packer:		ft						
Interval between Packers:		406.00 ft						
Tool Length:		426.00 ft						
Number of Packers:		2	Diameter:	6.75 inches				
Tool Comments:								

Tool Description

Length (ft) Serial No. Position Depth (ft) Accum. Lengths

Change Over Sub	1.00			3276.00		
Shut In Tool	5.00			3281.00		
Hydraulic tool	5.00			3286.00		
Packer	4.00			3290.00	20.00	Bottom Of Top Packer
Packer	5.00			3295.00		
Stubb	1.00			3296.00		
Change Over Sub	1.00			3297.00		
Drill Pipe	31.00			3328.00		
Change Over Sub	1.00			3329.00		
Change Over Sub	1.00			3330.00		
Drill Pipe	31.00			3361.00		
Change Over Sub	1.00			3362.00		
Recorder	0.00	6625	Inside	3362.00		
Recorder	0.00	8319	Outside	3362.00		
Perforations	5.00			3367.00		
Blank Off Sub	1.00			3368.00		
Stubb	3.00			3371.00	406.00	Tool Interval
Packer	1.00			3372.00		
Stubb	1.00			3373.00		
Recorder	0.00	8652	Below	3373.00		
Perforations	6.00			3379.00		
Change Over Sub	1.00			3380.00		
Drill Pipe	316.00			3696.00		
Change Over Sub	1.00			3697.00		
Bullnose	4.00			3701.00	1000425.00	Bottom Packers & Anchor

Total Tool Length: 426.00



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

TDI LLC

22-15s-19w Ellis,KS

1310 Bison Rd
Hays KS 67601

Paulette #1

Job Ticket: 59384

DST#: 2

ATTN: Herb Deines

Test Start: 2014.06.26 @ 04:09:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 54.00 sec/qt

Water Loss: 9.19 in³

Resistivity: 0.00 ohm.m

Salinity: 6200.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psig

Oil API:

Water Salinity:

deg API

ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
83.00	VSWCM, 3%w , 97%m	1.164
15.00	M, 100%m	0.210

Total Length: 98.00 ft

Total Volume: 1.374 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


Serial #: 6625

Inside TDI LLC

Paulette #1

DST Test Number: 2

Pressure vs. Time

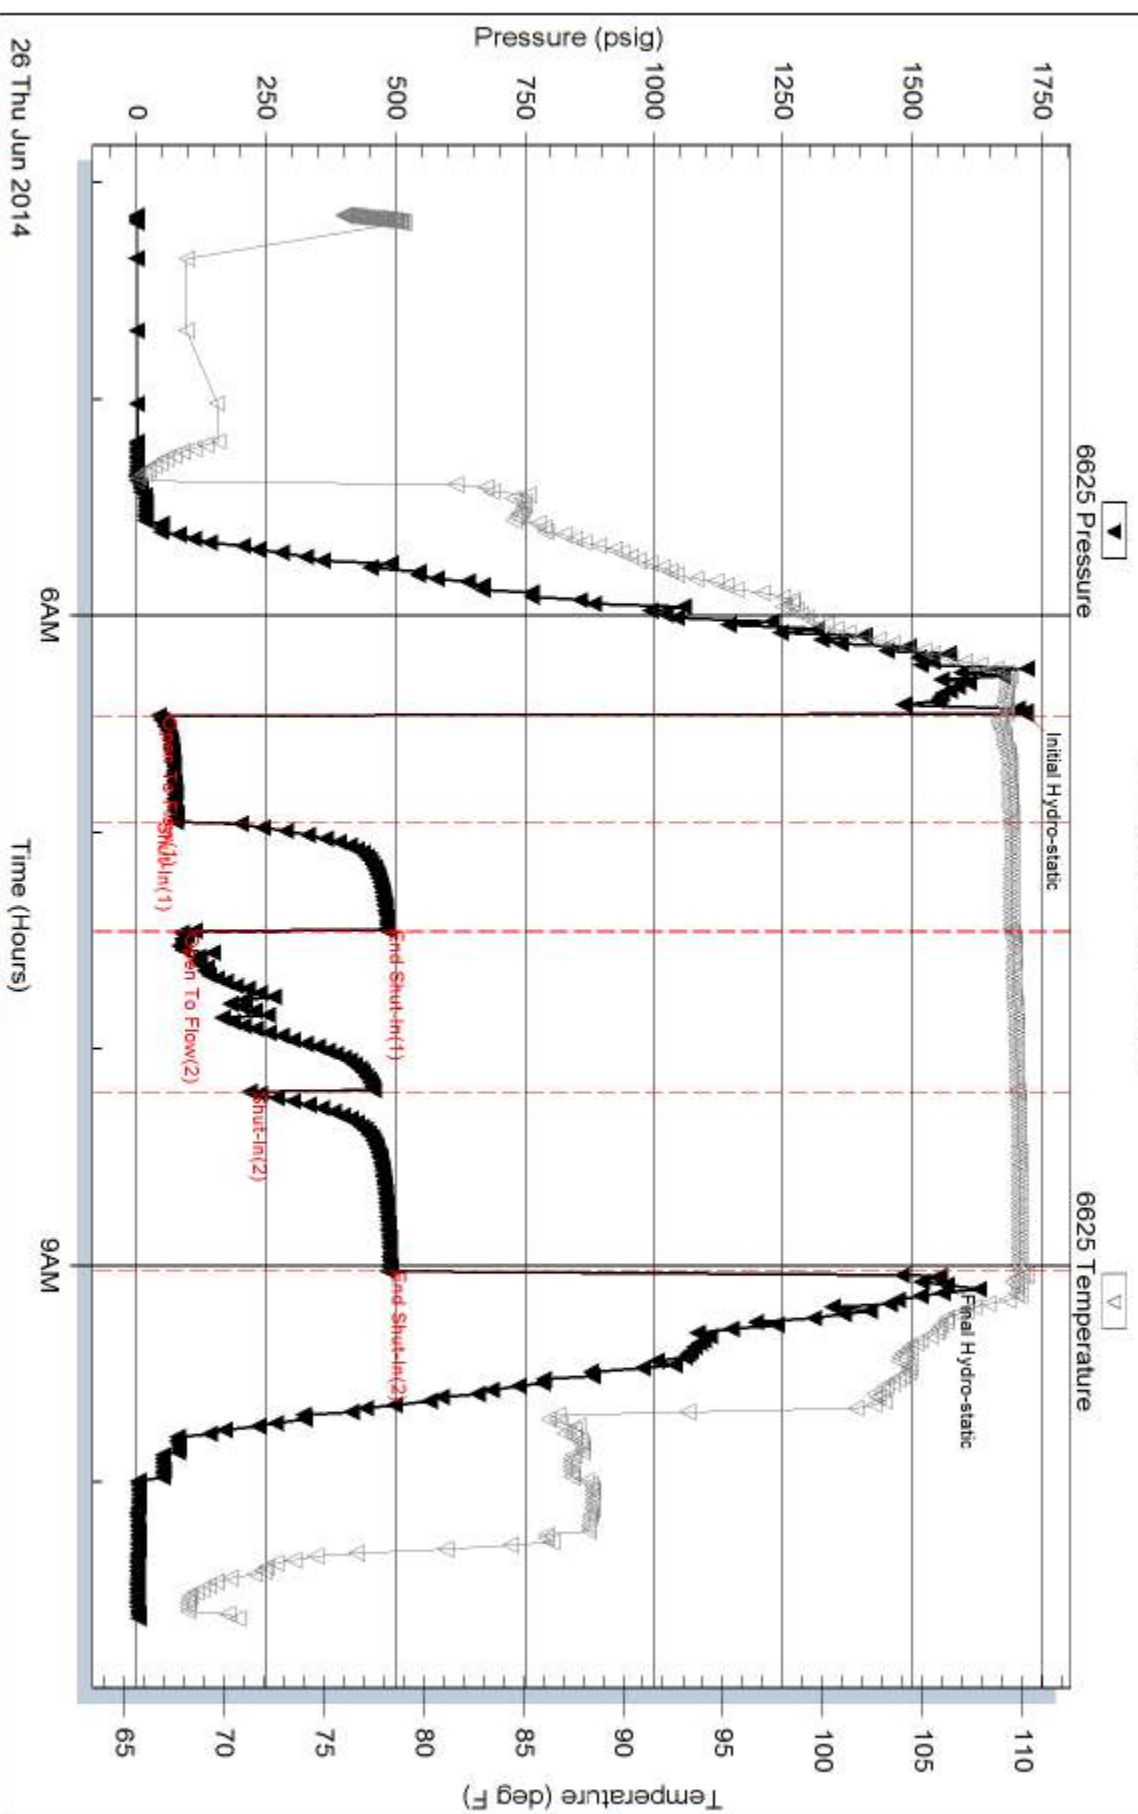


Serial #: 8652

Below (Strat) 14JC

Paulette #1

DST Test Number: 2

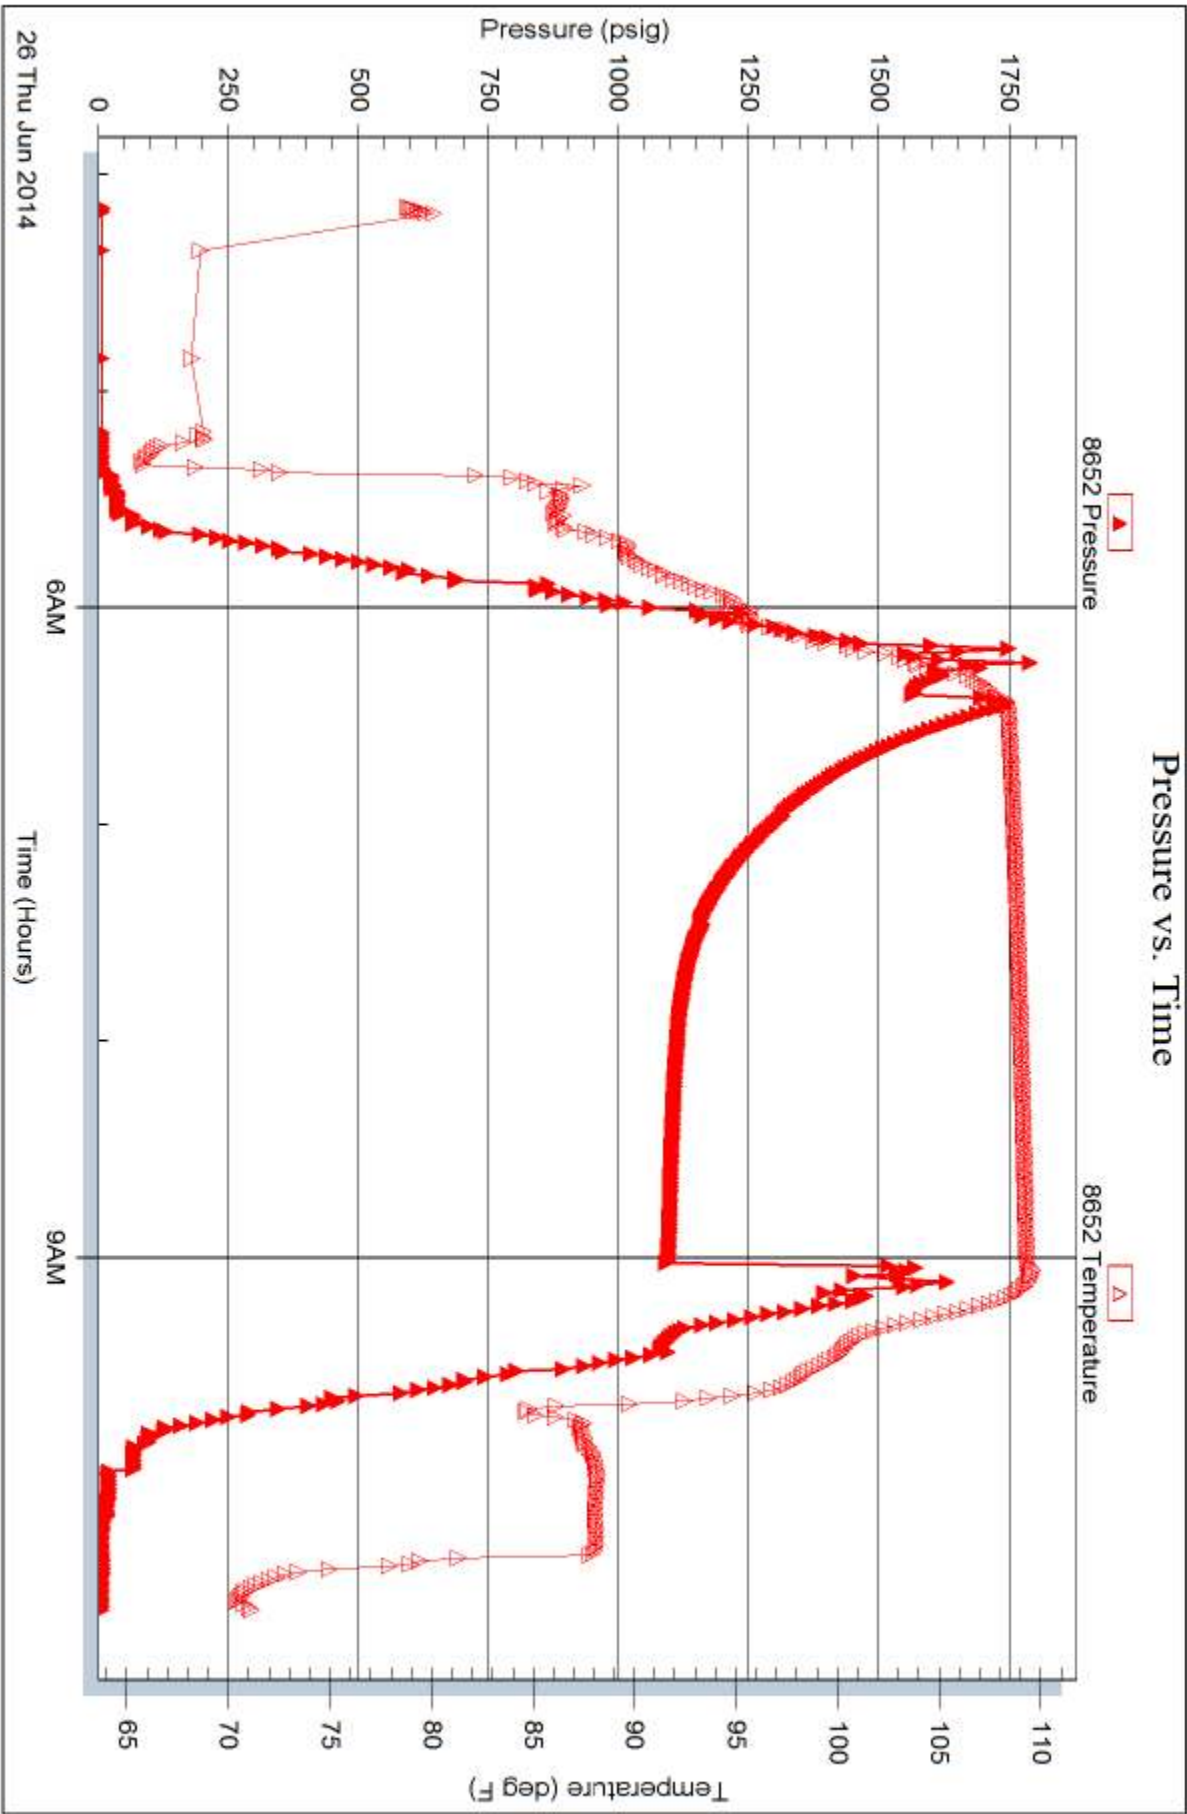


Serial #: 8319

Outside TDI LLC

Paulette #1

DST Test Number: 2

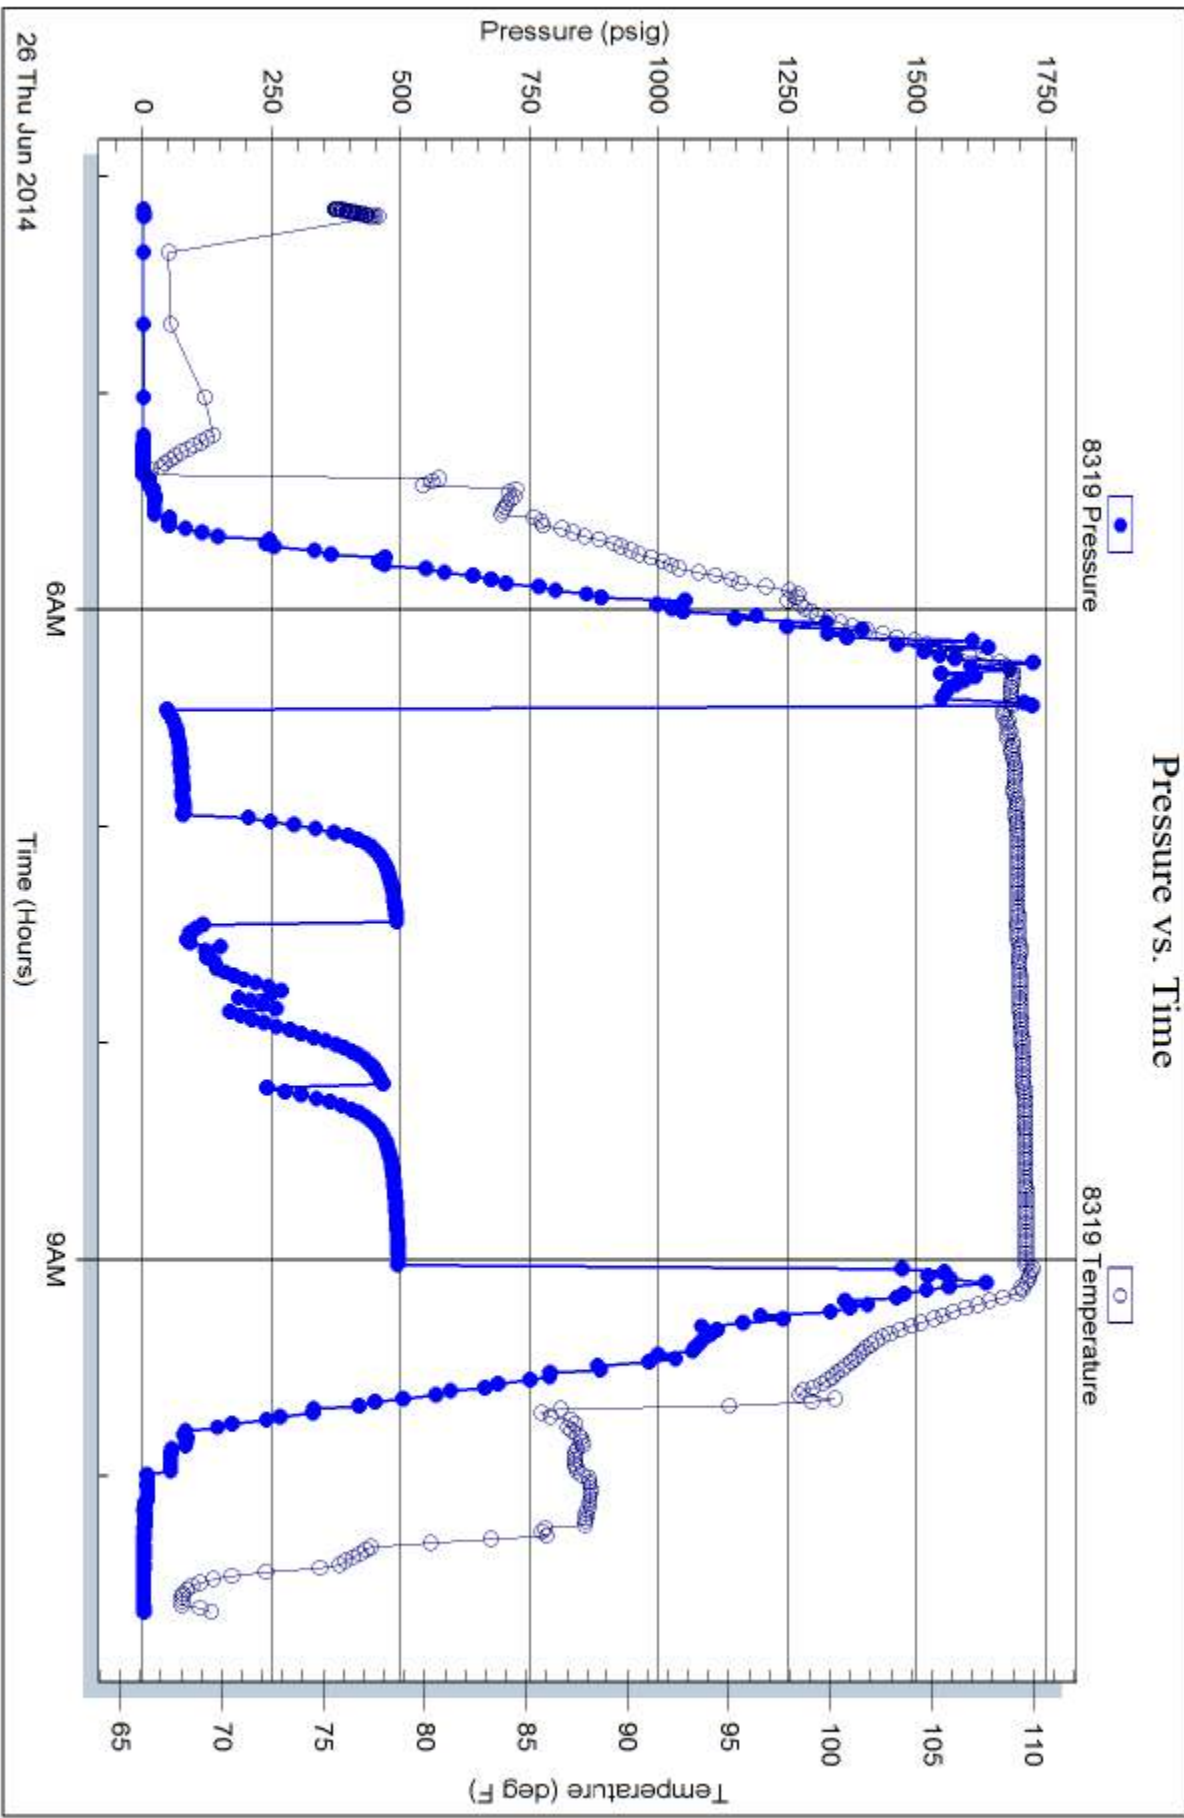



TRILOBITE TESTING INC.

1515 Commerce Parkway • Hays, Kansas 67601

Test Ticket

NO. 55296

Well Name & No. Bonlette #1 Test No. 1 Date 6-24-14
 Company I.D.I. h.c. Elevation 1,952 KB 1,947 GL
 Address 1310 Bison R.D. Hays KS. 67601
 Co. Rep / Geo. Herb Deines Rig Southwind #1
 Location: Sec. 22 Twp. 15-S Rge. 19-W Co. Ellis State KS.

Interval Tested 3252-3290 Zone Tested B.C.D
 Anchor Length 38' Drill Pipe Run 3298 Mud Wt. 8.8
 Top Packer Depth 3247 Drill Collars Run — Vis 63
 Bottom Packer Depth 3252 Wt. Pipe Run — WL 8.0
 Total Depth 3290 Chlorides 4500 ppm System LCM 1/2

Blow Description IF-45-1/2" INT. Blow Built to (9" in 45 min.)
I.S.I-45- No B.B.
E.F.-45-W.S.B. Started @ 2 min. Built to (4" in 45 min.)
E.S.I-45- No B.B.

Rec	Feet of	%gas	%oil	%water	%mud
Rec <u>83'</u>	Feet of <u>S, O, S, M, W</u>	%gas <u>2</u>	%oil <u>50</u>	%water <u>48</u>	%mud
Rec	Feet of	%gas	%oil	%water	%mud
Rec	Feet of	%gas	%oil	%water	%mud
Rec	Feet of	%gas	%oil	%water	%mud

Rec Total 83' BHT 109.8 Gravity — API RW 1.29 @ 61.3 °F Chlorides 5,500 ppm
 (A) Initial Hydrostatic 1,582 ☒ Test 1150 T-On Location 17:45:00
 (B) First Initial Flow 21 ☐ Jars — T-Started 18:25:00
 (C) First Final Flow 45 ☐ Safety Joint — T-Open 20:28:00
 (D) Initial Shut-In 314 ☐ Circ Sub — T-Pulled 23:28:00
 (E) Second Initial Flow 52 ☐ Hourly Standby — T-Out 00:57:00
 (F) Second Final Flow 79 ☒ Mileage 24 / R.T. 37.20 Comments "Thank-you"
 (G) Final Shut-In 295 ☐ Sampler —
 (H) Final Hydrostatic 1,511 ☐ Straddle —
☐ Shale Packer —
☐ Extra Packer —
☐ Extra Recorder —
☐ Day Standby —
☐ Accessibility —

Initial Open 45
 Initial Shut-In 45
 Final Flow 45
 Final Shut-In 45

☐ Ruined Shale Packer
☐ Ruined Packer
☐ Extra Copies
 Sub Total 0
 Total 1187.20
 MP/DST Disc't —

Approved By _____

Our Representative Bert Hume

Trilobite Testing Inc. shall not be liable for damaged of any kind of the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test, tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.



TRILOBITE TESTING INC.

1515 Commerce Parkway • Hays, Kansas 67601

Test Ticket

NO. 59384

Well Name & No. Panlette #1 Test No. 2 Date 6-26-14
 Company TDI LLC Elevation 1952 KB 1947 GL
 Address 1310 Bison RD Hays, KS 67601
 Co. Rep / Geo. Herb Demers Rig Southwind #1
 Location: Sec. 22 Twp. 15s Rge. 19w Co. Ellis State KS

Interval Tested 3295-3338 Zone Tested UCL "FP"
 Anchor Length 43' 330' Tail Drill Pipe Run 3293 Mud Wt. 9.2
 Top Packer Depth 3290 Drill Collars Run 60' Vis 54
 Bottom Packer Depth 3295 Wt. Pipe Run — WL 9.2
 Total Depth 3664 Chlorides 6,200 ppm System LCM 1

Blow Description IF- Buite to 6 1/2"
ISF- No Return
FF- Buite to 2 1/4"
FSI- No Return

Rec	Feet of	%gas	%oil	%water	%mud
<u>83</u>	<u>VSWM</u>			<u>3</u>	<u>97</u>
<u>15</u>	<u>M</u>			<u>100</u>	

Rec Total 138 BHT 109 Gravity — API RW — @ — ° F Chlorides — ppm

(A) Initial Hydrostatic 1719
 (B) First Initial Flow 42
 (C) First Final Flow 74
 (D) Initial Shut-In 480
 (E) Second Initial Flow 85
 (F) Second Final Flow 27
 (G) Final Shut-In 484
 (H) Final Hydrostatic 1552

☒ Test 1150
☐ Jars —
☐ Safety Joint —
☐ Circ Sub —
☐ Hourly Standby —
☒ Mileage 24 RT 37.20
☐ Sampler —
☒ Straddle 600

T-On Location 04:07
 T-Started 04:09
 T-Open 06:27
 T-Pulled 08:57
 T-Out 10:38
 Comments —

Initial Open 30
 Initial Shut-In 30
 Final Flow 45
 Final Shut-In 45

☐ Shale Packer —
☐ Extra Packer —
☐ Extra Recorder —
☐ Day Standby 1d 3h
☐ Accessibility —

☐ Ruined Shale Packer —
☐ Ruined Packer —
☐ Extra Copies —
 Sub Total 100
 Total 1887.20
 MP/DST Disc't —

Sub Total 1787.20

Approved By —

Our Representative Phil Shupe

Trilobite Testing Inc. shall not be liable for damaged of any kind of the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test, tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.
