



DRILL STEM TEST REPORT

Prepared For: **American Warrior Inc.,**

3118 Cummings RD
PO Box 399
Garden City, KS 67846

ATTN: Ted Pfau

Blaesi #5-6

6-15s-41w Wallace KS


Start Date: 2014.08.01 @ 03:40:00

End Date: 2014.08.01 @ 14:08:15

Job Ticket #: 57041 DST #: 1

Trilobite Testing, Inc
PO Box 362 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620

Printed: 2013.01.01 @ 15:18:21



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

American Warrior Inc.,
3118 Cummings RD
PO Box 399
Garden City, KS 67846
ATTN: Ted Pfau

6-15s-41w Wallace KS

Blaesi #5-6

Job Ticket: 57041

DST#: 1

Test Start: 2014.08.01 @ 03:40:00

GENERAL INFORMATION:

Formation: **Morrow Sand**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 08:59:00

Time Test Ended: 14:08:15

Test Type: Conventional Bottom Hole (Initial)

Tester: Jace McKinney

Unit No: 75

Interval: 4920.00 ft (KB) To 4987.00 ft (KB) (TVD)

Total Depth: 4987.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Poor

Reference Elevations: 3793.00 ft (KB)

3783.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 8675 Inside

Press@RunDepth: 135.27 psig @ 4936.00 ft (KB)

Start Date: 2014.08.01

End Date:

2014.08.01

Start Time: 03:40:15

End Time:

14:08:15

Capacity: 8000.00 psig


Last Calib.: 2014.08.01

Time On Btm: 2014.08.01 @ 08:58:15

Time Off Btm: 2014.08.01 @ 11:50:15

TEST COMMENT: Built to 7" blow
Bled off for 5 min. No return blow
B.O.B. in 3 min.
Bled off for 10 min. No return blow

PRESSURE SUMMARY

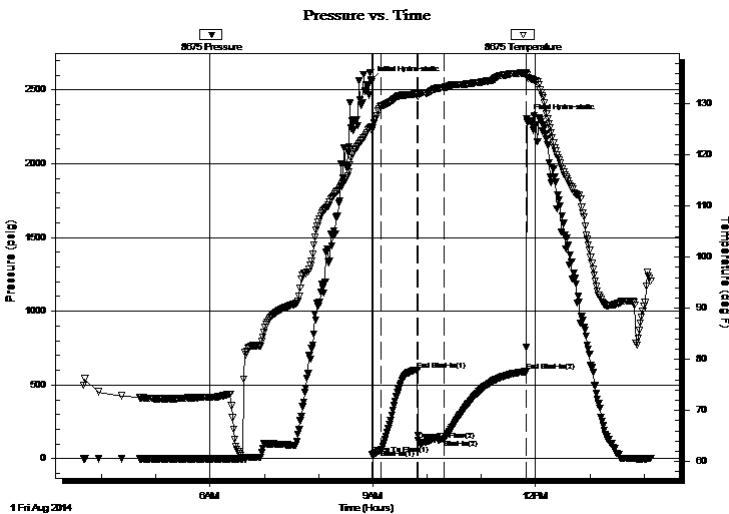


| Time (Min.) | Pressure (psig) | Temp (deg F) | Annotation |
|-------------|-----------------|--------------|----------------------|
| 0 | 2566.33 | 125.52 | Initial Hydro-static |
| 1 | 30.06 | 124.75 | Open To Flow (1) |
| 12 | 61.46 | 129.57 | Shut-In(1) |
| 51 | 602.10 | 131.93 | End Shut-In(1) |
| 52 | 127.07 | 131.54 | Open To Flow (2) |
| 81 | 135.27 | 133.26 | Shut-In(2) |
| 171 | 591.14 | 136.05 | End Shut-In(2) |
| 172 | 2304.20 | 135.68 | Final Hydro-static |

Recovery

| Length (ft) | Description | Volume (bbl) |
|-------------|-----------------------|--------------|
| 0.00 | 1685 Feet Gas In Pipe | 0.00 |
| 141.00 | gcm 5%G 95%M | 1.98 |
| 126.00 | ocmg 5%O 30%M 65%G | 1.77 |
| | | |
| | | |

Gas Rates

| | Choke (inches) | Pressure (psig) | Gas Rate (Mcf/d) |
|--|----------------|-----------------|------------------|
| | | | |



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior Inc.,

6-15s-41w Wallace KS

3118 Cummings RD
PO Box 399
Garden City, KS 67846
ATTN: Ted Pfau

Blaesi #5-6

Job Ticket: 57041

DST#: 1

Test Start: 2014.08.01 @ 03:40:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 53.00 sec/qt

Water Loss: 8.00 cm³

Resistivity: ohm.m

Salinity: 3800.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length: ft

Cushion Volume: bbl

Gas Cushion Type:

Gas Cushion Pressure: psig

Oil API:

Water Salinity: deg API

ppm

Recovery Information

Recovery Table

| Length ft | Description | Volume bbl |
|--------------|-----------------------|---------------|
| 0.00 | 1685 Feet Gas In Pipe | 0.000 |
| 141.00 | gcm 5%G 95%M | 1.978 |
| 126.00 | ocmg 5%O 30%M 65%G | 1.767 |

Total Length: 267.00 ft Total Volume: 3.745 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

Pressure vs. Time

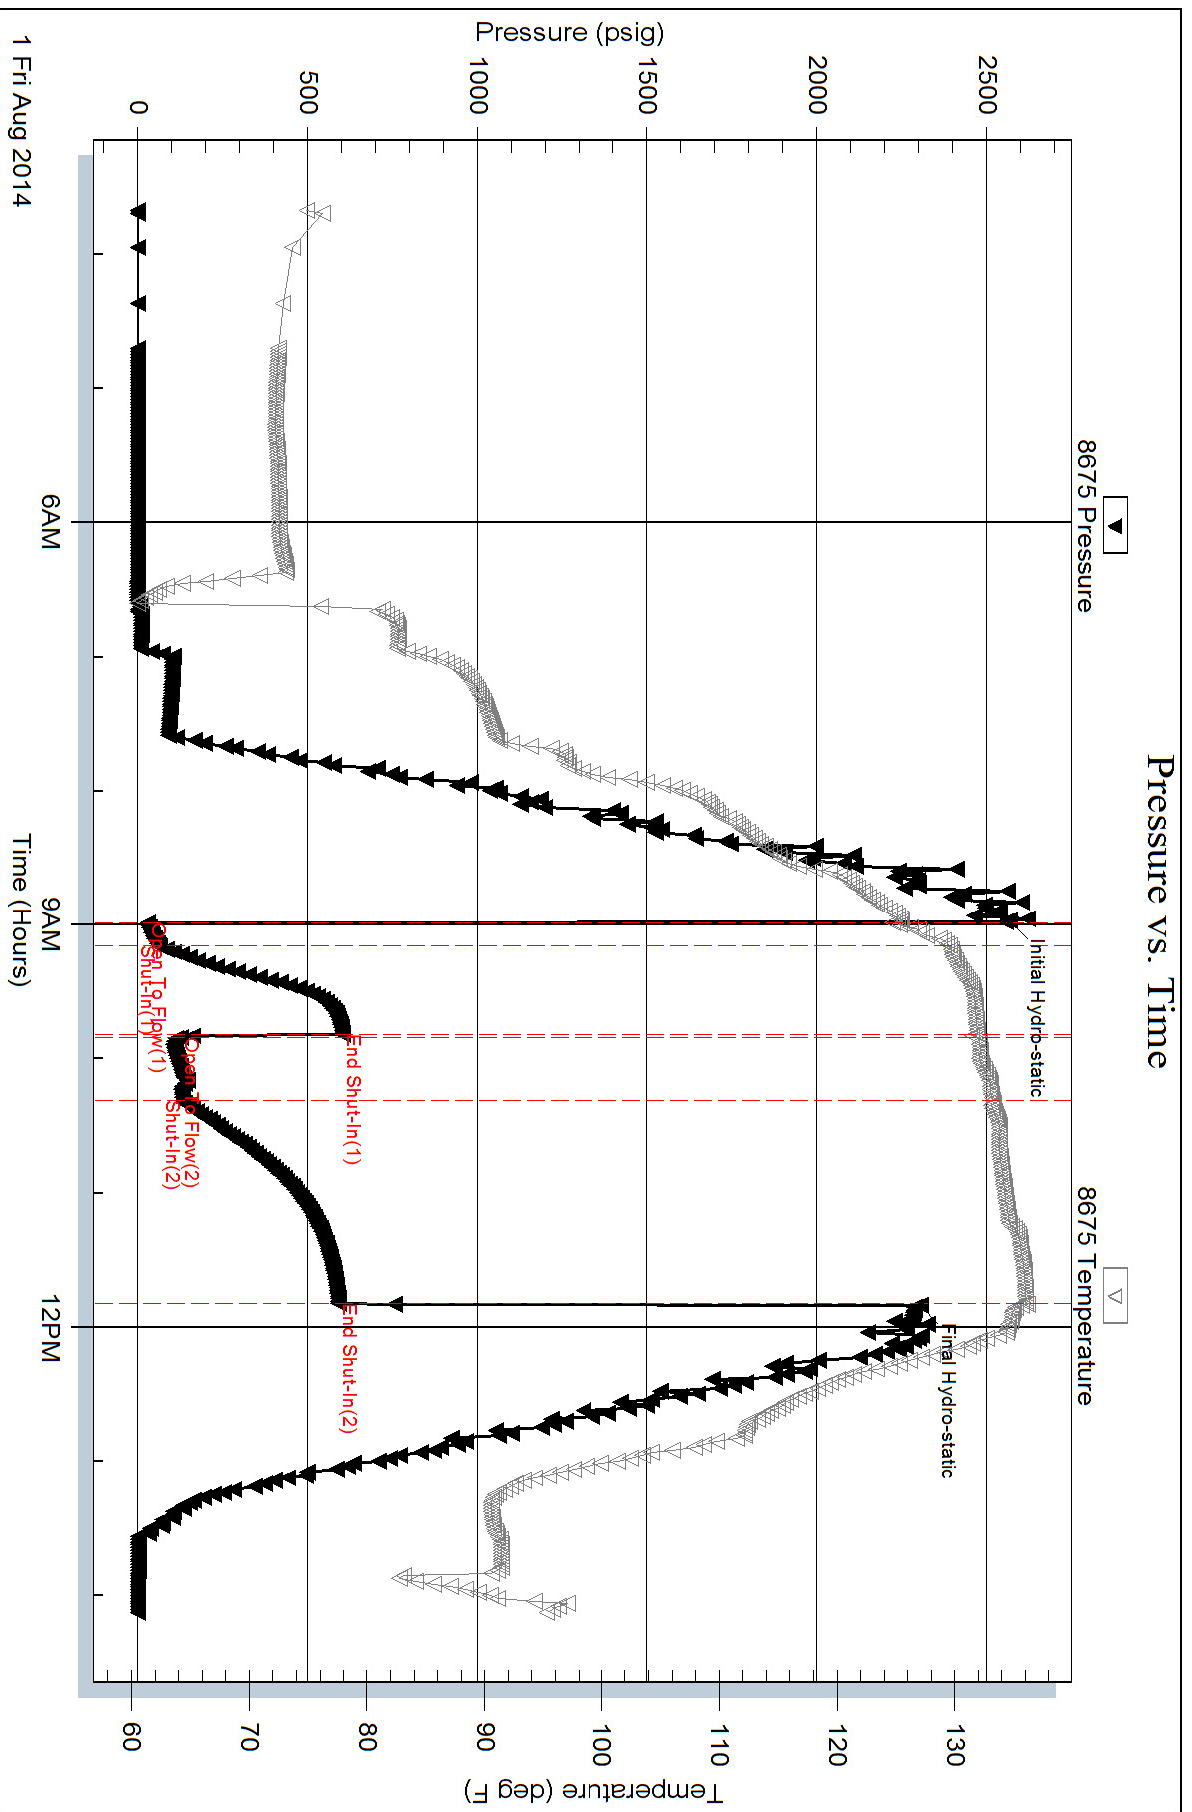

Serial #: 8650

Outside American Warrior Inc.,

Blaesi #5-6

DST Test Number: 1

