



DIAMOND TESTING
P.O. Box 157
HOISINGTON, KANSAS 67544
(800) 542-7313
DRILL-STEM TEST TICKET
FILE: FURY1DST1

TIME ON: 13:52
TIME OFF: 20:01

Company RJM Company Lease & Well No. Fury Farms #1
Contractor Southwind Drlg Rig #3 Charge to RJM Company
Elevation 1898' KB Formation KC "A&B" Effective Pay _____ Ft. Ticket No. F442
Date 10-03-16 Sec. 13 Twp. _____ 19s S Range 13w W County Barton State KANSAS
Test Approved By Wyatt Urban Diamond Representative Jake Fahrenbruch

Formation Test No. 1 Interval Tested from 3190 ft. to 3225 ft. Total Depth 3225 ft.
Packer Depth 3185 ft. Size 6 3/4 in. Packer depth _____ ft. Size 6 3/4 in.
Packer Depth 3190 ft. Size 6 3/4 in. Packer depth _____ ft. Size 6 3/4 in.
Depth of Selective Zone Set _____

Top Recorder Depth (Inside) 3192 ft. Recorder Number 5951 Cap. 5000 P.S.I.
Bottom Recorder Depth (Outside) 3193 ft. Recorder Number 5584 Cap. 5000 P.S.I.
Below Straddle Recorder Depth _____ ft. Recorder Number _____ Cap. _____ P.S.I.

Mud Type CHEMICAL Viscosity 53 (2# LCM) Drill Collar Length 0 ft. I.D. 2 1/4 in.
Weight 8.9 Water Loss 8.4 cc. Weight Pipe Length 0 ft. I.D. 2 7/8 in.
Chlorides 3,000 P.P.M. Drill Pipe Length 3,170 ft. I.D. 3 1/2 in.
Jars: Make STERLING Serial Number _____ Test Tool Length 20 ft. Tool Size 3 1/2-IF in.
Did Well Flow? NO Reversed Out NO Anchor Length 35 ft. Size 4 1/2-FH in.
Main Hole Size 7 7/8 Tool Joint Size 4 1/2 XH in. Surface Choke Size 1 in. Bottom Choke Size 5/8 in.

Blow: 1st Open: Blow inc to BOB in 17 minutes. No BB.
2nd Open: Blow at BOB in 5 seconds. No GTS. No BB.


Recovered 35 ft. of HOCM 24% oil, 76% mud
Recovered _____ ft. of 600' GIP
Recovered _____ ft. of _____
Recovered _____ ft. of _____

Recovered _____ ft. of _____	Price Job
Recovered _____ ft. of _____	Other Charges
Remarks: _____	Insurance
_____	Total

Time Set Packer(s) 15:37 A.M. P.M. Time Started Off Bottom 18:22 A.M. P.M. Maximum Temperature 103 F
Initial Hydrostatic Pressure..... (A) 1473 P.S.I.
Initial Flow Period..... Minutes 30 (B) 31 P.S.I. to (C) 65 P.S.I.
Initial Closed In Period..... Minutes 45 (D) 472 P.S.I.
Final Flow Period..... Minutes 45 (E) 64 P.S.I. to (F) 85 P.S.I.
Final Closed In Period..... Minutes 45 (G) 476 P.S.I.
Final Hydrostatic Pressure..... (H) 1468 P.S.I.

Diamond Testing shall not be liable for damages of any kind to the property or personnel of the one for whom a test is made or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statement or opinion concerning the result of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

FURY FARMS #1, DST #1, KANSAS CITY "A&B" 3190'-3225'

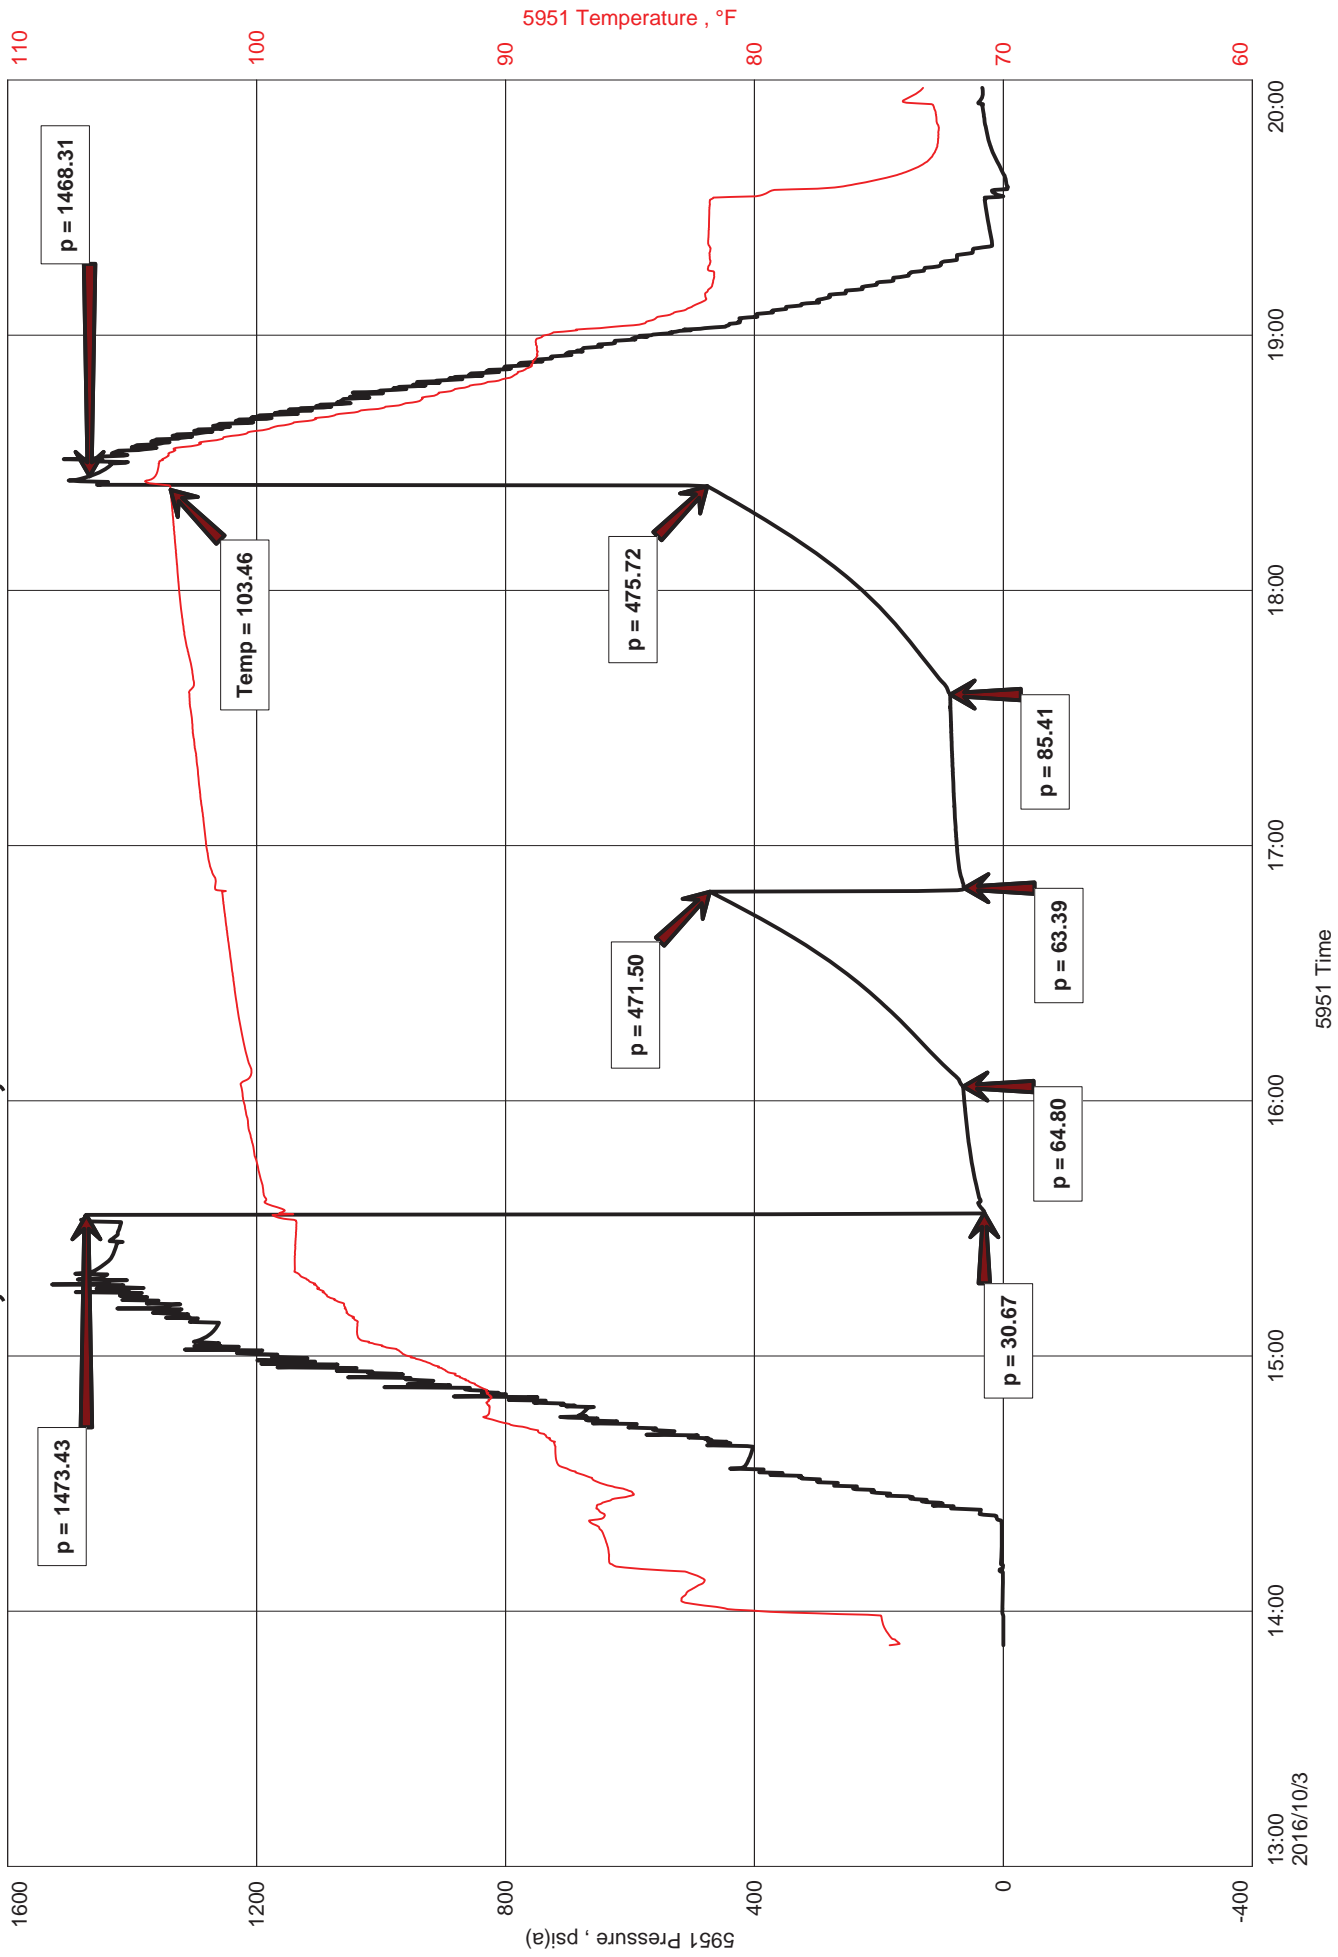

DIAMOND TESTING GENERAL REPORT

Jake Fahrenbruch, Tester

Cell: (620) 282-8977 / Office: (800) 542-7313



TEST INFORMATION

Well Name	Fury Farms #1
Company Name	RJM Company
Formation	DST #1, Kansas City "A&B", 3190'-3225'
Test Type	Bottom-Hole
Surface Location	Sec 13-19s-13w-Butler Co.-KS
KB Elevation (SL)	1898.000
Gauge Name	5951
Start Test Date	2016/10/03
Start Test Time	13:52:00
Final Test Date	2016/10/03
Final Test Time	20:01:00
Job Number	F442
Contact	Brad Miller
Site Contact	Wyatt Urban

TEST RESULTS

Initial flow, blow increased to BOB in 17 minutes. No blowback.
Final flow, blow at BOB in 5 seconds. No GTS. No blowback.

Recovered: 35' of HOCM (24% oil, 76% m) and 600' of Gas In Pipe

FURY FARMS #1, DST #1, KANSAS CITY "A&B" 3190'-3225'

