



**TRILOBITE  
TESTING, INC.**

# DRILL STEM TEST REPORT

Vincent Oil Corporation  
200 W Douglas Ave #725  
Wichita, KS 67202  
ATTN: Tom Dudgeon


**22-28S-8W Kingman**  
**Robinson 1-22**  
Job Ticket: 59926      **DST#: 1**  
Test Start: 2017.03.12 @ 10:34:05

## GENERAL INFORMATION:

Formation: **Swope**  
Deviated: No Whipstock: ft (KB)      Test Type: Conventional Bottom Hole (Initial)  
Time Tool Opened: 12:49:50      Tester: Leal Cason  
Time Test Ended: 17:50:20      Unit No: 74  
**Interval: 3702.00 ft (KB) To 3770.00 ft (KB) (TVD)**      Reference Elevations: 1630.00 ft (KB)  
Total Depth: 3770.00 ft (KB) (TVD)      1622.00 ft (CF)  
Hole Diameter: 7.88 inches Hole Condition: Good      KB to GR/CF: 8.00 ft

**Serial #: 8159      Inside**  
Press@RunDepth: 30.29 psig @ 3703.00 ft (KB)      Capacity: 8000.00 psig  
Start Date: 2017.03.12      End Date: 2017.03.12      Last Calib.: 2017.03.12  
Start Time: 10:34:06      End Time: 17:50:20      Time On Btm: 2017.03.12 @ 12:49:20  
Time Off Btm: 2017.03.12 @ 15:50:20

**TEST COMMENT:** IF: Weak 1/4 inch Blow  
IS: No Blow Back  
FF: Weak Surface Blow  
FS: No Blow Back

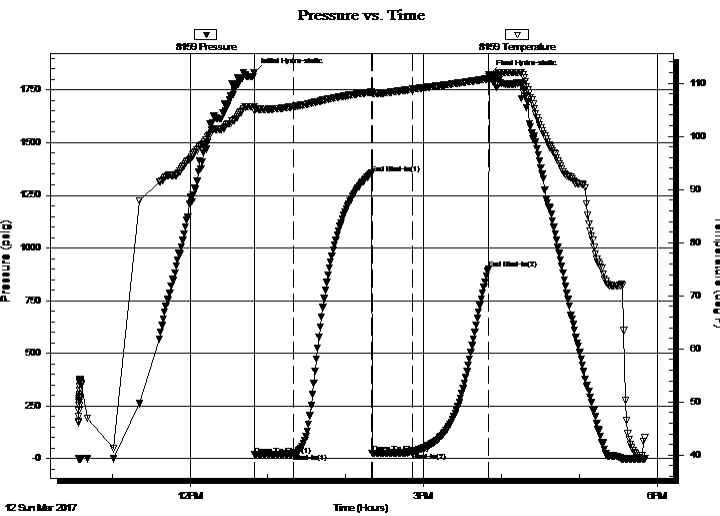

## PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1833.72	105.61	Initial Hydro-static
1	17.05	104.81	Open To Flow (1)
31	21.79	105.62	Shut-In(1)
91	1354.26	108.34	End Shut-In(1)
92	22.80	108.01	Open To Flow (2)
122	30.29	108.87	Shut-In(2)
181	897.67	110.84	End Shut-In(2)
181	1824.00	111.27	Final Hydro-static

## Recovery

Length (ft)	Description	Volume (bbl)
30.00	SGCM 2%G 98%M	0.42

## Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)



**TRILOBITE TESTING, INC.**

# DRILL STEM TEST REPORT

Vincent Oil Corporation  
 200 W Douglas Ave #725  
 Wichita, KS 67202  
 ATTN: Tom Dudgeon


**22-28S-8W Kingman**  
**Robinson 1-22**  
 Job Ticket: 59926      **DST#: 1**  
 Test Start: 2017.03.12 @ 10:34:05

## GENERAL INFORMATION:

Formation: **Swope**  
 Deviated: No Whipstock: ft (KB)  
 Time Tool Opened: 12:49:50  
 Time Test Ended: 17:50:20  
**Interval: 3702.00 ft (KB) To 3770.00 ft (KB) (TVD)**  
 Total Depth: 3770.00 ft (KB) (TVD)  
 Hole Diameter: 7.88 inches Hole Condition: Good  
 Test Type: Conventional Bottom Hole (Initial)  
 Tester: Leal Cason  
 Unit No: 74  
 Reference Elevations: 1630.00 ft (KB)  
 1622.00 ft (CF)  
 KB to GR/CF: 8.00 ft

**Serial #: 6806      Outside**  
 Press@RunDepth: psig @ 3703.00 ft (KB)      Capacity: 8000.00 psig  
 Start Date: 2017.03.12      End Date: 2017.03.12      Last Calib.: 2017.03.12  
 Start Time: 10:34:06      End Time: 17:50:35      Time On Btm:  
 Time Off Btm:

TEST COMMENT: IF: Weak 1/4 inch Blow  
 IS: No Blow Back  
 FF: Weak Surface Blow  
 FS: No Blow Back

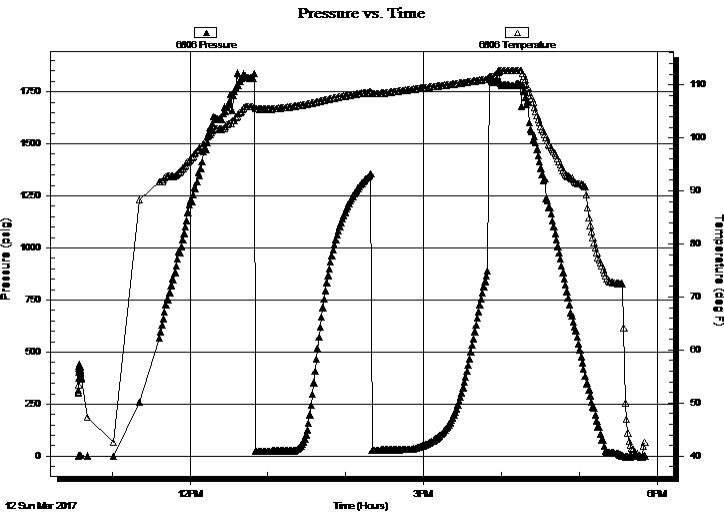

## PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation


## Recovery

Length (ft)	Description	Volume (bbl)
30.00	SGCM 2%G 98%M	0.42

## Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)

### Pressure vs. Time

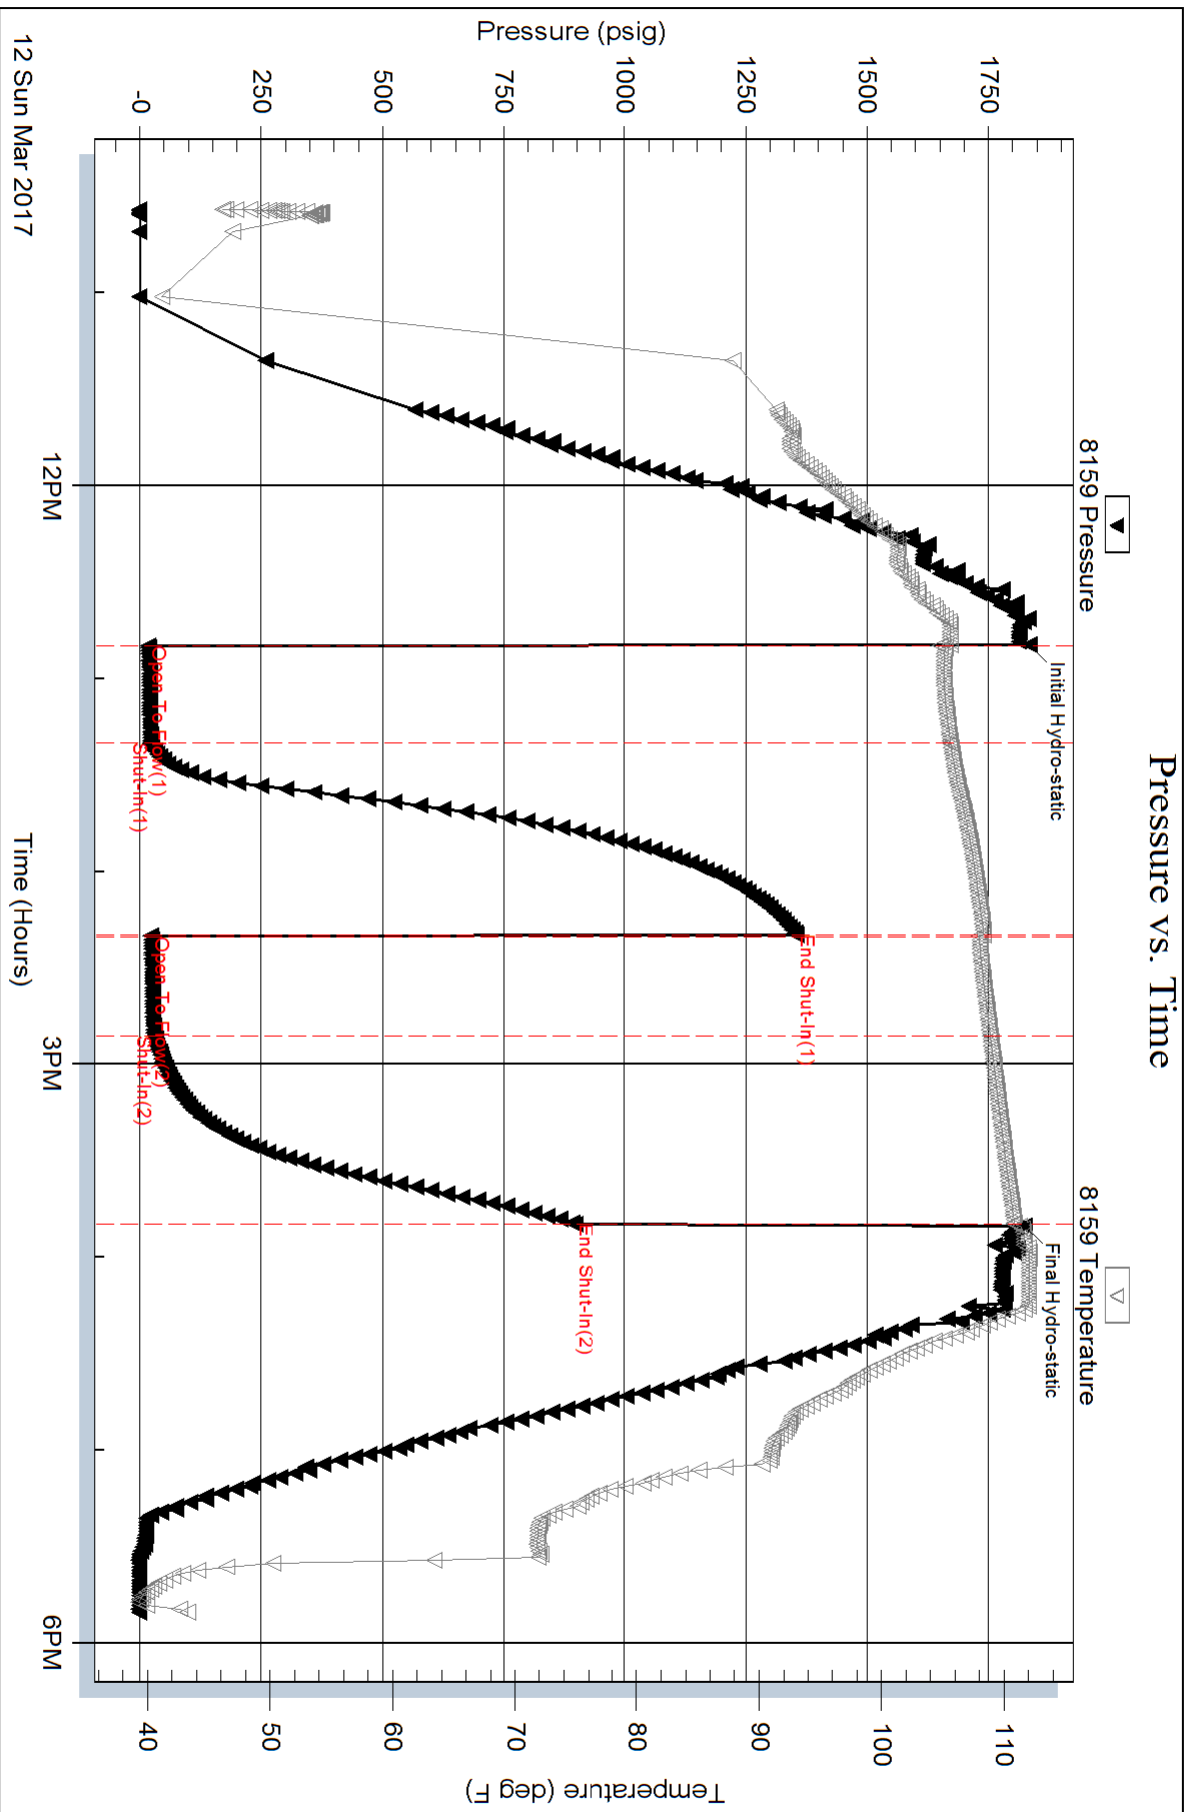

Serial #: 6806

Outside Vincent Oil Corporation

Robinson 1-22

DST Test Number: 1

