



Company: Jason Oil Company, LLC

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC - Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
23
2018

DST #1 Formation: Lans "D-G"
Test Interval: 3216 - 3266' Total Depth: 3266'

Time On: 14:30 04/23 Time Off: 20:05 04/23
Time On Bottom: 16:27 04/23 Time Off Bottom: 18:27 04/23

Electronic Volume Estimate:
2'


1st Open
Minutes: 30
Current Reading:
0" at 30 min
Max Reading: .1"

1st Close
Minutes: 30
Current Reading:
0" at 30 min
Max Reading: 0"

2nd Open
Minutes: 30
Current Reading:
0" at 30 min
Max Reading: 0"

2nd Close
Minutes: 30
Current Reading:
0" at 30 min
Max Reading: 0"

Inside Recorder

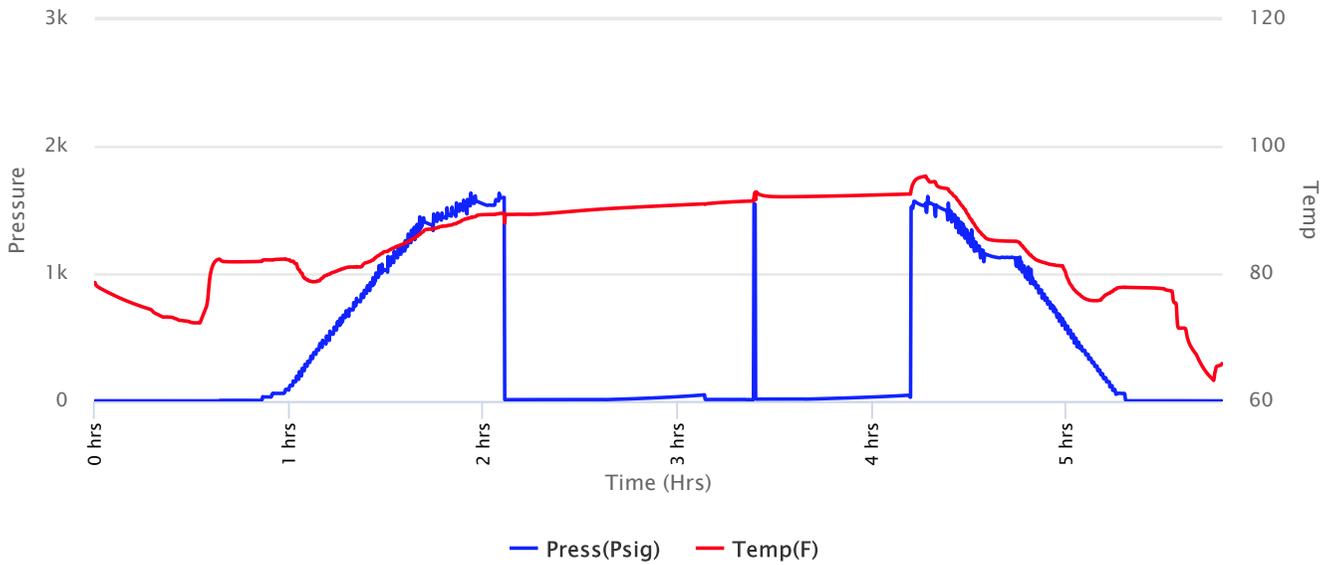



Company: Jason Oil Company, LLC

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC - Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
23
2018

DST #1 **Formation: Lans "D-G"** **Test Interval: 3216 - 3266'** **Total Depth: 3266'**
Time On: 14:30 04/23 Time Off: 20:05 04/23
Time On Bottom: 16:27 04/23 Time Off Bottom: 18:27 04/23

Recovered


Foot	BBLs	Description of Fluid	Gas %	Oil %	Water %	Mud %
2	0.00984	M	0	0	0	100

Total Recovered: 2 ft
Total Barrels Recovered: 0.00984

Reversed Out
NO

Initial Hydrostatic Pressure	1537	PSI
Initial Flow	11 to 13	PSI
Initial Closed in Pressure	50	PSI
Final Flow Pressure	13 to 17	PSI
Final Closed in Pressure	47	PSI
Final Hydrostatic Pressure	1532	PSI
Temperature	93	°F
Pressure Change Initial Close / Final Close	6.3	%

Recovery at a glance

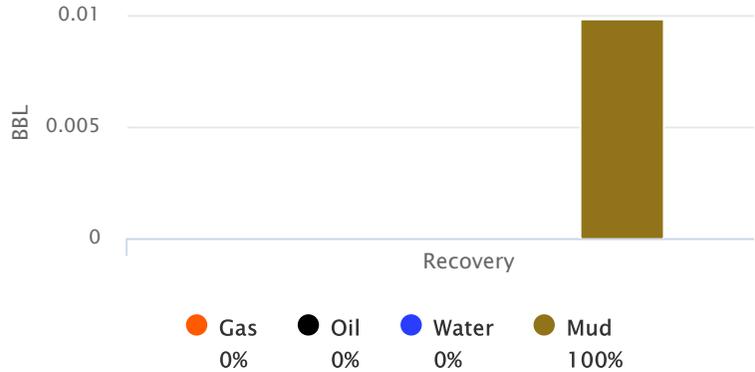



**Company: Jason Oil Company,
LLC**

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC -
Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
23
2018

DST #1	Formation: Lans "D- G"	Test Interval: 3216 - 3266'	Total Depth: 3266'
	Time On: 14:30 04/23	Time Off: 20:05 04/23	
	Time On Bottom: 16:27 04/23	Time Off Bottom: 18:27 04/23	

BUCKET MEASUREMENT:

REMARKS:

Initial Flow: Weak, surface blow. Died in 20 mins.
Initial Shut-in: No blow back.
Final Flow: No blow. No build. Flushed tool 10 mins. into Final Flow. Good surge. No blow.
Final Shut-in: No blow back.

Tool Sample: 100% mud w/several oil specks



Company: Jason Oil Company, LLC

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC - Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
23
2018

DST #1 **Formation: Lans "D-G"** **Test Interval: 3216 - 3266'** **Total Depth: 3266'**
Time On: 14:30 04/23 Time Off: 20:05 04/23
Time On Bottom: 16:27 04/23 Time Off Bottom: 18:27 04/23

Down Hole Makeup

Heads Up: 21.94 FT	Packer 1: 3211 FT
Drill Pipe: 3093.78 FT <i>ID-3 1/2</i>	Packer 2: 3216 FT
Weight Pipe: FT <i>ID-2 7/8</i>	Top Recorder: 3203 FT
Collars: 119 FT <i>ID-2 1/4</i>	Bottom Recorder: 3254 FT
Test Tool: 26.16 FT <i>ID-3 1/2-FH</i>	Well Bore Size: 7 7/8
Total Anchor: 50	Surface Choke: 1"
<u>Anchor Makeup</u>	Bottom Choke: 5/8"
Packer Sub: 1 FT	
Perforations: (top): 3 FT <i>4 1/2-FH</i>	
Change Over: .5 FT	
Drill Pipe: (in anchor): 32 FT <i>ID-3 1/2</i>	
Change Over: .5 FT	
Perforations: (below): 13 FT <i>4 1/2-FH</i>	

