



DRILL STEM TEST REPORT

Prepared For: **F.G Holl Company L.L.C**

9431 E Central St # 100 Wichita KS 67206

ATTN: Ryan Greenbaum

Zimmer #1-20

20-19s-14w Barton

Start Date: 2014.07.13 @ 03:50:00

End Date: 2014.07.13 @ 09:05:00

Job Ticket #: 19309 DST #: 8

Superior Testers Enterprises LLC
PO Box 138 Great Bend KS 67530
1-800-792-6902

Printed: 2014.07.13 @ 12:09:16



DRILL STEM TEST REPORT

F.G Holl Company L.L.C

20-19s-14w Barton

9431 E Central St # 100 Wichita KS 67206

Zimmer #1-20

Job Ticket: 19309

DST#: 8

ATTN: Ryan Greenbaum

Test Start: 2014.07.13 @ 03:50:00

GENERAL INFORMATION:

Formation: **Arbbuckle**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 05:20:00

Time Test Ended: 09:05:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Jared Scheck

Unit No: 3340-Great Bend-25

Interval: 3547.00 ft (KB) To 3553.00 ft (KB) (TVD)

Reference Elevations: 1901.00 ft (KB)

Total Depth: 3340.00 ft (KB) (TVD)

1893.00 ft (CF)

Hole Diameter: 7.88 inches Hole Condition: Fair

KB to GR/CF: 8.00 ft

Serial #: 8525

Press@RunDepth: 40.20 psig @ ft (KB)

Capacity: 5000.00 psig

Start Date: 2014.07.13

End Date: 2014.07.13

Last Calib.: 2014.07.13


Start Time: 03:50:00

End Time: 09:05:00

Time On Btm: 2014.07.13 @ 05:19:00

Time Off Btm: 2014.07.13 @ 07:38:30

TEST COMMENT: 1st Opening 15 Minutes-Weak blow built 3 inches into water in 15 minutes
 1st Shut-in 30 Minutes-No blow back
 2nd Opening 30 Minutes-Weak blow built bottom of bucket in 22 minutes
 2nd Shut-in 60 Minutes-No blow back

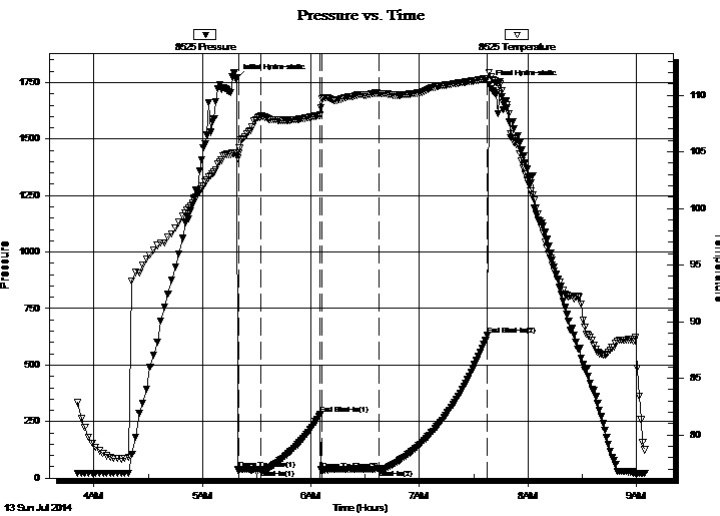

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1769.35	104.87	Initial Hydro-static
1	37.93	104.87	Open To Flow (1)
14	38.02	108.14	Shut-In(1)
46	280.88	108.23	End Shut-In(1)
47	35.27	109.68	Open To Flow (2)
79	40.20	110.16	Shut-In(2)
139	630.71	111.46	End Shut-In(2)
140	1740.90	112.01	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
20.00	oil mud 10%oil 90% mud	0.28
0.00	40 gas in pipe	0.00

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)



DRILL STEM TEST REPORT

F.G Holl Company L.L.C

20-19s-14w Barton

9431 E Central St # 100 Wichita KS 67206

Zimmer #1-20

Job Ticket: 19309

DST#: 8

ATTN: Ryan Greenbaum

Test Start: 2014.07.13 @ 03:50:00

GENERAL INFORMATION:

Formation: **Arbuckle**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 05:20:00

Time Test Ended: 09:05:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Jared Scheck

Unit No: 3340-Great Bend-25

Interval: 3547.00 ft (KB) To 3553.00 ft (KB) (TVD)

Reference Elevations: 1901.00 ft (KB)

Total Depth: 3340.00 ft (KB) (TVD)

1893.00 ft (CF)

Hole Diameter: 7.88 inches Hole Condition: Fair

KB to GR/CF: 8.00 ft

Serial #: 8400

Press@RunDepth: 612.53 psig @ ft (KB)

Capacity: 5000.00 psig

Start Date: 2014.07.13

End Date: 2014.07.13

Last Calib.: 2014.07.13


Start Time: 03:50:00

End Time: 09:05:30

Time On Btm: 2014.07.13 @ 05:19:30

Time Off Btm: 2014.07.13 @ 07:39:00

TEST COMMENT: 1st Opening 15 Minutes-Weak blow built 3 inches into water in 15 minutes
 1st Shut-in 30 Minutes-No blow back
 2nd Opening 30 Minutes-Weak blow built bottom of bucket in 22 minutes
 2nd Shut-in 60 Minutes-No blow back

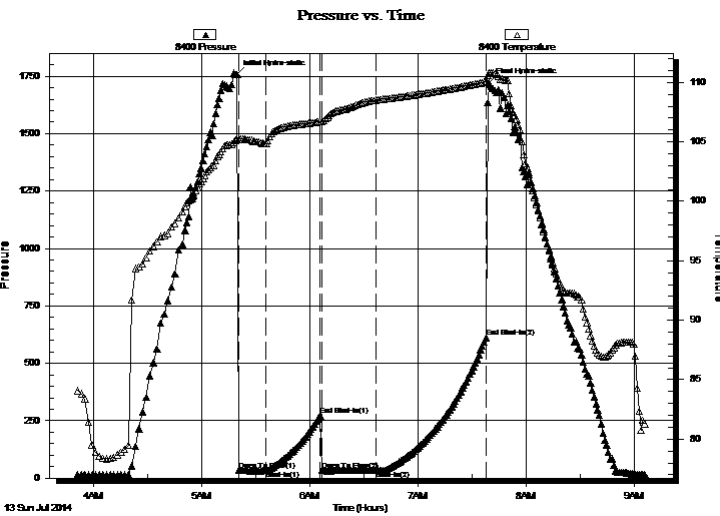

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1758.04	105.18	Initial Hydro-static
1	34.89	105.21	Open To Flow (1)
16	33.47	104.89	Shut-In(1)
46	272.25	106.69	End Shut-In(1)
47	33.13	106.67	Open To Flow (2)
77	33.45	108.51	Shut-In(2)
138	612.53	110.05	End Shut-In(2)
140	1723.25	110.77	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
20.00	oil mud 10%oil 90% mud	0.28
0.00	40 gas in pipe	0.00

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)



DRILL STEM TEST REPORT

TOOL DIAGRAM

F.G Holl Company L.L.C

20-19s-14w Barton

9431 E Central St # 100 Wichita KS 67206

Zimmer #1-20

Job Ticket: 19309

DST#: 8

ATTN: Ryan Greenbaum

Test Start: 2014.07.13 @ 03:50:00

Tool Information

Drill Pipe:	Length: 3528.00 ft	Diameter: 3.80 inches	Volume: 49.49 bbl	Tool Weight: 1000.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 20000.00 lb
Drill Collar:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight to Pull Loose: 65000.00 lb
			<u>Total Volume: 49.49 bbl</u>	Tool Chased 0.00 ft
Drill Pipe Above KB:	4.00 ft			String Weight: Initial 57000.00 lb
Depth to Top Packer:	3547.00 ft			Final 57000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	6.00 ft			
Tool Length:	29.00 ft			
Number of Packers:	1	Diameter: 6.75 inches		
Tool Comments:				

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Shut In Tool	5.00			3529.00	
Hydraulic tool	5.00			3534.00	
Jars	6.00			3540.00	
Safety Joint	2.00			3542.00	
Packer	5.00			3547.00	23.00 Bottom Of Top Packer
Recorder	1.00			3548.00	
Recorder	1.00			3549.00	
Anchor	1.00			3550.00	
Bullnose	3.00			3553.00	6.00 Anchor Tool
Total Tool Length:	29.00				



DRILL STEM TEST REPORT

FLUID SUMMARY

F.G Holl Company L.L.C

20-19s-14w Barton

9431 E Central St # 100 Wichita KS 67206

Zimmer #1-20

Job Ticket: 19309

DST#: 8

ATTN: Ryan Greenbaum

Test Start: 2014.07.13 @ 03:50:00

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 50.00 sec/qt

Cushion Volume:

bbbl

Water Loss: 10.40 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 5300.00 ppm

Filter Cake: 1.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbbl
20.00	oil mud 10%oil 90% mud	0.281
0.00	40 gas in pipe	0.000

Total Length: 20.00 ft Total Volume: 0.281 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

