

211

HILL CITY, KANSAS 67642

Company	Kansas Oil Corp.	Test No.	1
Well Name & Number	Honas B-2	Zone Tested	Lansing
Company Address	Wichita, Kansas	Date	8-9-80
Comp. Rep.	Zeb Stewart	Tester	Dan Bangle
Contractor	Spartan Drlg,	Elevation	2355 K.V.
Location: Sec.	28Twp. 11S Rge. 22W Co. Trego State Ks.	Est. Feet of Pay	

Recorder No. 10983 Type AK-1 Range 4100 PSI

Recorder Depth 3632

Tool Open Before I. S. I. 30 Mins.

Initial Shut-in _____ 60 _____ Mins.

Flow Period 30 Mins.

Final Shut-in _____ 60 _____ Mins.

Surface Choke Size 1"

Bottom Choke Size 3/4"

Main Hole Size 77/8"

Rubber Size 6 3/4"

Tool Open @ 7:20 A.M.


Blow Weak 1/2" Blow

Remarks No Blow On Second Open.

Drill Collar I. D. 2 1/4 Ft. Run 220

Price of job \$600.00

Price of 500 _____

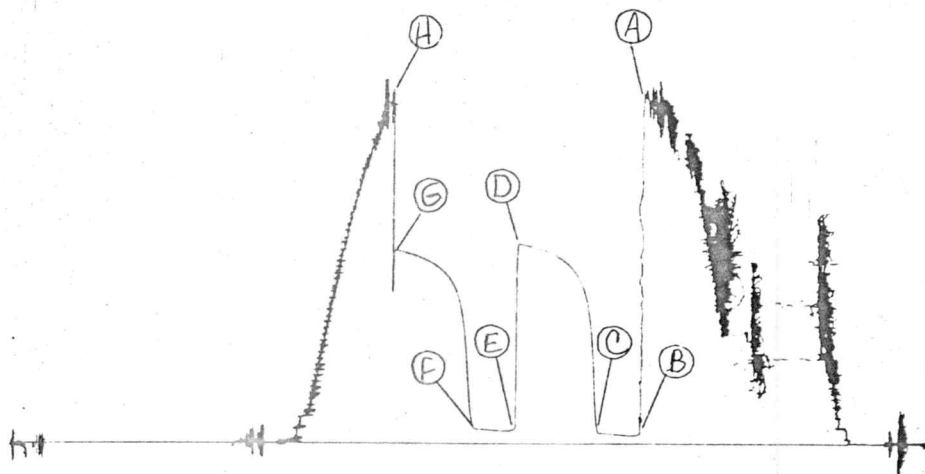

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	1814	PSI
(B) First Initial Flow Pressure	40	PSI
(C) First Final Flow Pressure	51	PSI
(D) Initial Closed-in Pressure	1063	PSI
(E) Second Initial Flow Pressure	61	PSI
(F) Second Final Flow Pressure	61	PSI
(G) Final Closed-in Pressure	1032	PSI
(H) Final Hydrostatic Mud	1804	PSI

CHENEY TESTING COMPANY

P. O. BOX 3

HILL CITY, KANSAS 67642

DRILL-STEM TEST DATA

Company <u>Kansas Oil Corp.</u>	Test No. <u>2</u>
Well Name & Number <u>Honas B-2</u>	Zone Tested <u>Lansing</u>
Company Address <u>Wichita, Kansas</u>	Date <u>8-10-80</u>
Comp. Rep. <u>Zeb Stewart</u>	Tester <u>Dan Bangle</u>
Contractor <u>Spartan Drlg.</u>	Elevation <u>2355 K.B.</u>
Location: Sec. 28 Twp. 11S Rge. 22W Co. <u>Trego</u> State <u>Ks.</u>	Est. Feet of Pay _____

Recorder No. 11090 Type AK-1 Range 4125 PSI
 Recorder Depth 3661
 (A) Initial Hydrostatic Mud 1864 PSI
 (B) First Initial Flow Pressure 102 PSI
 (C) First Final Flow Pressure 236 PSI
 (D) Initial Closed-in Pressure 565 PSI
 (E) Second Initial Flow Pressure 277 PSI
 (F) Second Final Flow Pressure 329 PSI
 (G) Final Closed-in Pressure 555 PSI
 (H) Final Hydrostatic Mud 1843 PSI
 Temperature 103
 Mud Weight 9.3 Viscosity 41
 Fluid Loss 14.0
 Interval Tested 3628-3664
 Anchor Length 36
 Top Packer Depth 3623
 Bottom Packer Depth 3628
 Total Depth 3664
 Drill Pipe Size 4 1/2 F.H.
 Wt. Pipe I. D. _____ Ft. Run -
 Recovery—Total Feet 620

Recovered 620 Feet Of Mud W/Oil (6% Oil, 13% Mud, 81% Water)

Recovered _____ Feet Of _____

Recovered _____ Feet Of _____

Recovered _____ Feet Of _____

Extra Equipment _____

Recorder No. 10983 Type AK-1 Range 4100 PSI

Recorder Depth 3658

Tool Open Before I. S. I. 30 Mins.

Initial Shut-in 60 Mins.

Flow Period 30 Mins.

Final Shut-in 60 Mins.

Surface Choke Size 1"

Bottom Choke Size 3/4"

Main Hole Size 7 7/8"

Rubber Size 6 3/4"


Tool Open @ 9:55 P.M.

Blow 1st Open Weak, 1/4" Died out

Remarks 2nd Medium 4" Blow

Drill Collar I. D. 2 1/2 Ft. Run 220

Price of Job \$600.00

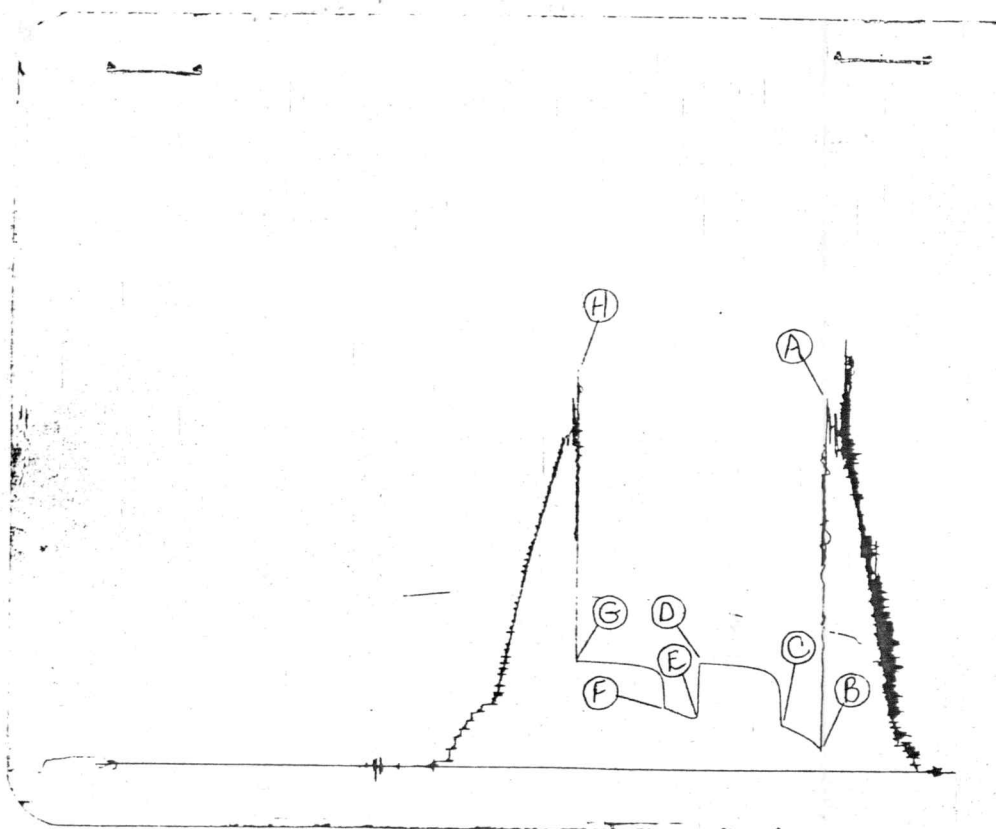

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	1864	PSI
(B) First Initial Flow Pressure	102	PSI
(C) First Final Flow Pressure	236	PSI
(D) Initial Closed-in Pressure	565	PSI
(E) Second Initial Flow Pressure	277	PSI
(F) Second Final Flow Pressure	329	PSI
(G) Final Closed-in Pressure	555	PSI
(H) Final Hydrostatic Mud	1843	PSI

CHENEY TESTING COMPANY

P. O. BOX 3 HILL CITY, KANSAS 67642

DRILL-STEM TEST DATA

Company <u>Kansas Oil Corp.</u>	Test No. <u>3</u>
Well Name & Number <u>Honas B-2</u>	Zone Tested <u>Marmaton</u>
Company Address <u>Wichita, Kansas</u>	Date <u>8-11-80</u>
Comp. Rep. <u>Zeb Stewart</u>	Tester <u>Dan Bangle</u>
Contractor <u>Spartan Drlg. Corp.</u>	Elevation <u>2355 K.B.</u>
Location: Sec. <u>28</u> Twp. <u>11S</u> Rge. <u>22W</u> Co. <u>Trego</u> State <u>Ks.</u>	Est. Feet of Pay <u> </u>

Recorder No. 11090 Type AK-1 Range 4125 PSI

Recorder Depth 3977

(A) Initial Hydrostatic Mud PSI

(B) First Initial Flow Pressure PSI

(C) First Final Flow Pressure PSI

(D) Initial Closed-in Pressure PSI

(E) Second Initial Flow Pressure PSI

(F) Second Final Flow Pressure PSI

(G) Final Closed-in Pressure PSI

(H) Final Hydrostatic Mud PSI

Temperature

Mud Weight 9.3 Viscosity 39

Fluid Loss 12.4

Interval Tested 3944-3980

Anchor Length 36

Top Packer Depth 3939

Bottom Packer Depth 3944

Total Depth 3980

Drill Pipe Size 4½ E.H.

Wt. Pipe I. D. Ft. Run 700

Recovery—Total Feet 700

Recovered 700 Feet Of Mud W/Oil Spots.

Recovered Feet Of

Recovered Feet Of

Recovered Feet Of

Extra Equipment Price of Job \$300.00

Recorder No. 10983 Type AK-1 Range 4100 PSI

Recorder Depth 3974

Tool Open Before I. S. I. 30 Mins.

Initial Shut-in 60 Mins.

Flow Period 30 Mins.

Final Shut-in 60 Mins.

Surface Choke Size 1"

Bottom Choke Size ¾"

Main Hole Size 7⅞"


Rubber Size 6¾"

Tool Open @ 10:45 A.M.

Blow 1st Open Stong 5½" Blow.

Remarks Misrun- Packer Failure - Hole
Very Tight- Damaged Bottom Packer.

Drill Collar I. D. 5¼ Ft. Run 220

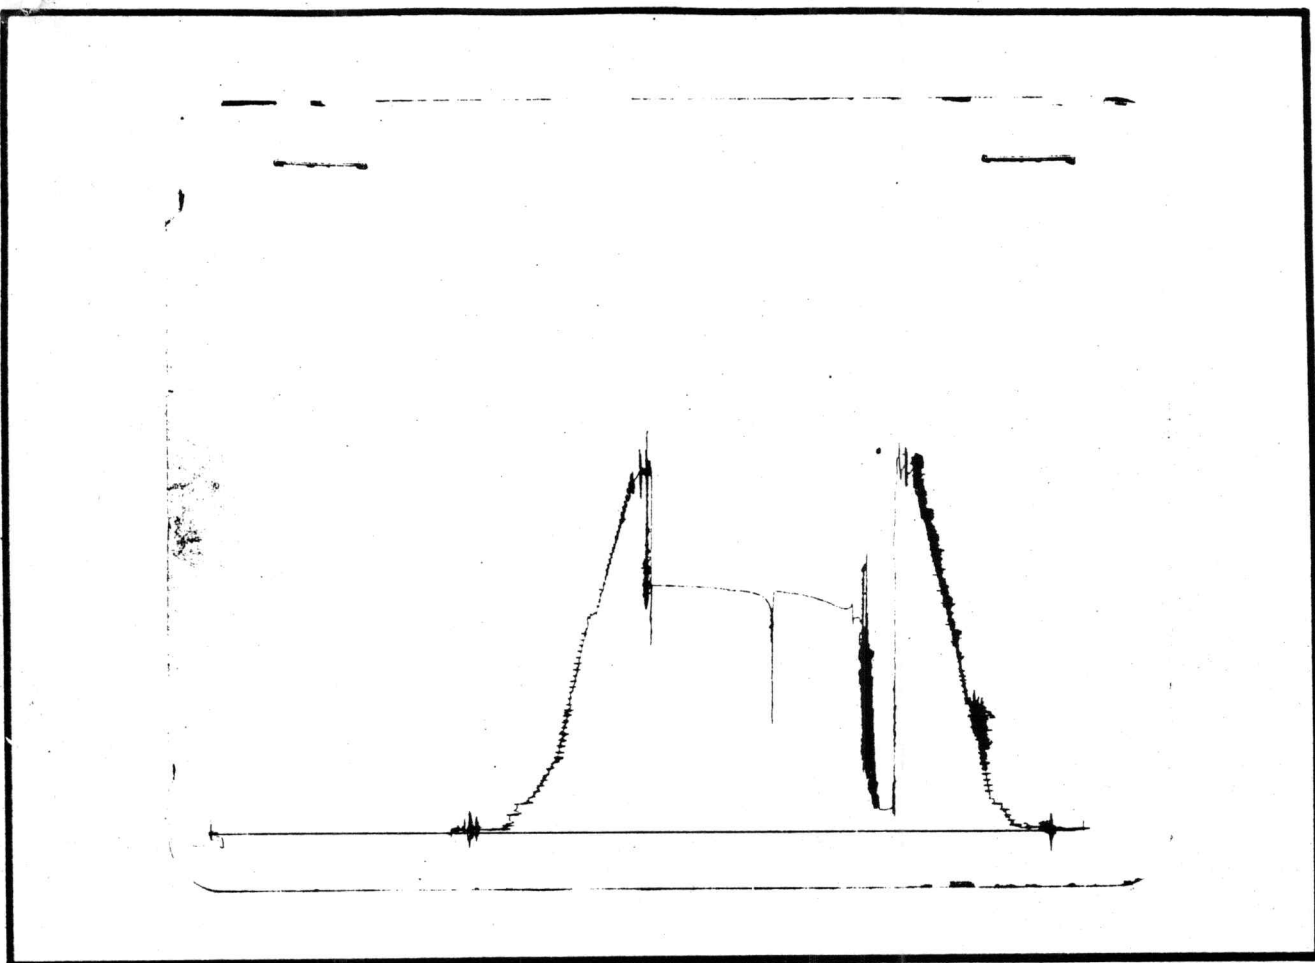

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud		PSI
(B) First Initial Flow Pressure		PSI
(C) First Final Flow Pressure		PSI
(D) Initial Closed-in Pressure		PSI
(E) Second Initial Flow Pressure		PSI
(F) Second Final Flow Pressure		PSI
(G) Final Closed-in Pressure		PSI
(H) Final Hydrostatic Mud		PSI
