

Company **Range Oil Co. Inc.**  
 Address **125 North Market Suite 1120**  
 CSZ **Wichita, KS 67202**  
 Attn. **JOHN**

Lease Name **Wasemiller**  
 Lease # **2**  
 Legal Desc **NW SE SW**  
 Section **11**  
 Township **19**  
 County **Marion**  
 Drilling Cont **Summit Rig #1**

Job Ticket **2754**  
 Range **1E**  
 State **KS**

Comments **Times- 30-30-60-60**

### GENERAL INFORMATION

Test # **1** Test Date **2/27/2007**  
 Tester **James Ricketts**  
 Test Type **Conv**  
**Successful Test**  
 # of Packers **2.0** Packer Size **6 3/4**

Mud Type **Chemical**  
 Mud Weight **9.4** Viscosity **37.0**  
 Filtrate **11.2** Chlorides **1500**

Drill Collar Len **280.0**  
 Wght Pipe Len **0**

Formation **Miss**  
 Interval Top **2701.0** Bottom **2757.0**  
 Anchor Len Below **56.0** Between **0**  
 Total Depth **2757.0**

Blow Type **Strong blow off bottom in 1 1/2 mins. initial flow period. Gas to surface in 1/2 mins. final flow period gauge 10.9M to 10.1m**

Chokes **3/4** Hole Size **7 7/8**  
 Top Recorder # **1022w**  
 Mid Recorder #  
 Bott Recorder # **11027**


Mileage **160** Approved By **JW**  
 Standby Time **0**  
 Extra Equipmnt **jars safety joint**  
 Time on Site **12:30 PM**  
 Tool Picked Up **2:30 AM**  
 Tool Layed Dwn **9:30 AM**

Elevation **1460.00** Kelley Bushings **1470.00**

Start Date/Time **2/27/2007 1:24 AM**  
 End Date/Time **2/27/2007 10:09 AM**

### RECOVERY

| Feet                | Description | Gas      | Oil    | Water  | Mud         |
|---------------------|-------------|----------|--------|--------|-------------|
| 125                 | gas cut mud | 5% 6.2ft | 0% 0ft | 0% 0ft | 95% 118.8ft |
| DST Fluids <b>0</b> |             |          |        |        |             |

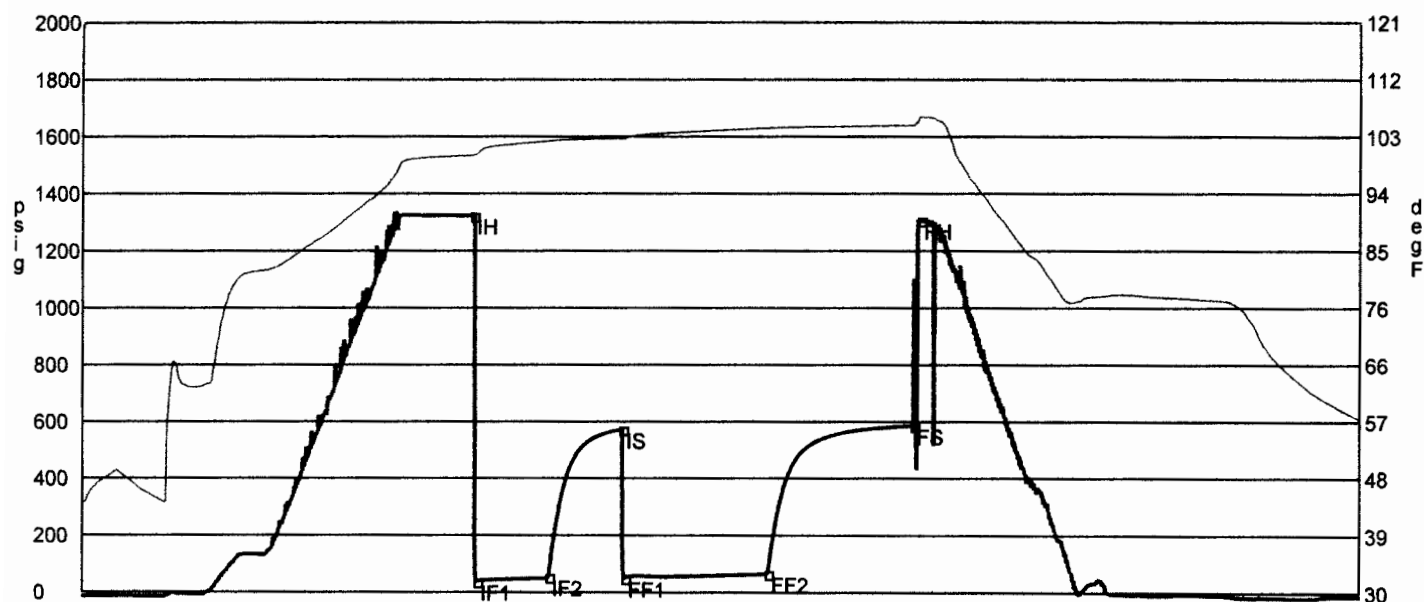

|     | Date                 | Time     | Pressure | Temp    |                      |
|-----|----------------------|----------|----------|---------|----------------------|
| IH  | 2/27/2007 4:03:30 AM | 2.658333 | 1322.916 | 99.779  | Initial Hydro-static |
| IF1 | 2/27/2007 4:05:15 AM | 2.6875   | 37.199   | 100.045 | Initial Flow (1)     |
| IF2 | 2/27/2007 4:34:45 AM | 3.179167 | 53.71    | 102.058 | Initial Flow (2)     |
| IS  | 2/27/2007 5:05:00 AM | 3.683333 | 571.415  | 102.473 | Initial Shut-In      |
| FF1 | 2/27/2007 5:06:00 AM | 3.7      | 49.313   | 102.542 | Final Flow (1)       |
| FF2 | 2/27/2007 6:05:00 AM | 4.683333 | 65.116   | 104.15  | Final Flow (2)       |
| FS  | 2/27/2007 7:04:45 AM | 5.679167 | 585.335  | 104.601 | Final Shut-In        |
| FH  | 2/27/2007 7:07:30 AM | 5.725    | 1306.958 | 105.96  | Final Hydro-static   |

## GAS FLOWS

| Min Into IFP | Min Into FFP | Gas Flows | Pressure | Choke   |
|--------------|--------------|-----------|----------|---------|
| 0            | 20           | 10.90 mcf | 3.00 h2o | 0.50 in |
| 0            | 30           | 10.10 mcf | 2.60 h2o | 0.50 in |
| 0            | 40           | 10.10 mcf | 2.60 h2o | 0.50 in |
| 0            | 40           | 10.10 mcf | 2.60 h2o | 0.50 in |
| 0            | 50           | 10.10 mcf | 2.60 h2o | 0.50 in |
| 0            | 60           | 10.10 mcf | 2.60 h2o | 0.50 in |
