

Kansas
Butler County

29 23 Rge. 4

K. H. Fernier
Pure Oil Company
Elev. T.D.
Log No. 11652


Drilling commenced Nov. 15, 1919
Drilling completed Jan. 18, 1920

Production : 1st 24 hrs. 570 bbls.
2nd 24 " 282 bbls.

Clay	100
lime	175
slate	225
lime	315
slate	355
clay	395
slate	415
lime	435
slate	455
lime	495
slate	780
sandy shale	800
slate	825
sandy slate	855
hard lime	910
lime and shale	1045
lime	1135
slate	1225
lime	1300
sandy slate	1385
lime	1400
sand and wtr.	1490
shale	1520
slate	1785
shale	1800

slate	1980
sand	2025
lime	2150
slate	2175
sand	2235
lime	2250
sandy lime	2300
lime	2310
slate	2340
lime	2355
lime and sand	2375
sand	2390
Total depth	2390

20"	20	78	Charged to well
15 1/2"	151	329	"
12 1/2"	827	1664	"
10"	1352	2721	"
8 1/4"	1800	2627	"
6 5/8"	2110		
5 3/16"	2352		

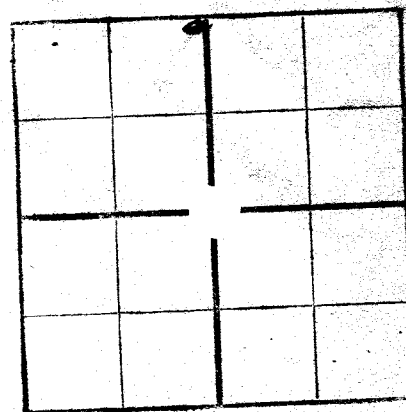

Map No. _____ Sec. 29 Twp. 23 R. 4
 Well No. 1 Farrier
Ohio Cities Gas Company
 _____ Contractor

SECTION PLAT

200 Ft. from N. Line
 _____ Ft. from S. Line
200 Ft. from E. Line
 _____ Ft. from W. Line



Location _____
 Rig up ☒
 Drilling and Remarks:

RECORD

Cased _____ in., _____ ft.
 Sand _____
 Gas _____
 Oil _____
 Total Depth _____

PRODUCTION

1st 24 hrs. Nat. _____
 1st 24 hrs. after shot _____
 Gas _____ Cu. Ft.
 Dry Hole _____
 Abandoned _____

Date

10/31

1919**Pyle**

Scout

Map No. K 14 Sec. 29 Twp. 23 R. 4
 Well No. 1 Farrier
Ohio Cities Gas Company
 _____ Contractor

SECTION PLAT

200 Ft. from N. Line
 _____ Ft. from S. Line
200 Ft. from E. Line
 _____ Ft. from W. Line



Location _____
 Rig up _____
 Drilling and Remarks:

RECORD

Cased _____ in., _____ ft.
 Sand 2378 - 2388
 Gas _____
 Oil _____
 Total Depth _____

PRODUCTION

1st 24 hrs. Nat. 600 bbls
 1st 24 hrs. after shot _____
 Gas _____ Cu. Ft.
 Dry Hole _____
 Abandoned _____

Date

1/37


191

Pyle

Scout

Map No. _____ Sec. 29 Twp. 23 R. 4
 Well No. 1 Farrier Farm
Ohio Cities Gas Company
 _____ Contractor
MW Quarter

200 Ft. from N. Line
 _____ Ft. from S. Line
200 Ft. from E. Line
 _____ Ft. from W. Line



REPORT

REPORT

10/31 Rig up
11/4 Rig up
12 Rig up
19 Spud
25 Drill 450'
12/2 Drill 800'
9 Set 10' - 1400'
16 Drill 1740'
23 Drill 2110'
1/4/20 Drill 2200'
6 2340'
14 5 3/16 at 2371' L.P.
19 Sand 2378' - 88' 2/70'
27 2378' - 88' - 600 Bbl

COMPLETED
