

Ricketts

Testing, Inc.

P.O. Box 351
WELLINGTON, KANSAS 67152
Phone (620) 326-5830

2525

DATE 3-20-2006

SEC. 29 TWN 29S RG 5e

LEGAL DESCRIPTION E/2 w/2 NE 4

TEST NO. 1

COMPANY Flowers Production Company, Inc

ADDRESS P.O. Box 249 EL Dorado, KS. 67042

LEASE Flowers Pottorff WELL NO. 129 COUNTY Butler STATE Kansas

INVOICES SENT TO: _____

DST COPIES SENT TO: _____

GENERAL INFORMATION

TOOL JT. 4 1/2 HOLE SIZE 7 7/8 PACKER O.D. 6 3/4
 ELEV. 13046L TOTAL DEPTH 2810
 TESTED FROM 2795 TO 2810
 ANCHOR LENGTH BELOW 15' BETWEEN _____
 TOOL OPEN 1:03 A.M. _____ P.M.
 TIME STARTED OFF BOTTOM 4:03 A.M. _____ P.M.
 DRLG. CONT. Gulicks Drilling RIG# 1
 TYPE OF MUD chemical
 MUD WT 9.5 VISCOSITY 40 W.L. 8.4 C.C.
 CHLORIDE 1100 GRAVITY OIL _____ B.H. TEMP 104
 LENGTH DRILL COLLAR 311' I.D. _____
 LENGTH WEIGHT PIPE _____ I.D. _____
 SUCCESSFUL TEST NO. 1 MISRUN NO. _____
 CHOKES: TOP 3/4 BOTTOM 3/4

PRESSURE DATA & TIME

	FIELD READINGS	CORRECTED READINGS
INITIAL HYDROSTATIC	_____	<u>1406</u>
INITIAL FLOW	{ _____ TO _____	<u>20</u> TO _____
INITIAL SHUT-IN	_____	<u>24</u>
INITIAL SHUT-IN	_____	<u>132</u>
FINAL FLOW	{ _____ TO _____	<u>23</u> TO _____
FINAL FLOW	_____	<u>27</u>
FINAL SHUT-IN	_____	<u>166</u>
FINAL HYDROSTATIC	_____	<u>1382</u>
TOOL OPEN: INITIAL FLOW	_____ HR.	<u>30</u> MIN.
INITIAL SHUT-IN	_____ HR.	<u>30</u> MIN.
FINAL FLOW	_____ HR.	<u>60</u> MIN.
FINAL SHUT-IN	_____ HR.	<u>60</u> MIN.
TOP RECORDER NO. <u>W1023</u>	BOTTOM RECORDER NO. <u>11027</u>	

TYPE BLOW Weak blow building to 1" I.F.P.
Surface blow throughout F.F.P

RECOVERY: 20' Drilling mud

RECEIVED

JUL 13 2006

KCC WICHITA

EXTRA EQUIPMENT Jars & Safety Joint

APPROVED BY: _____

TESTER: Jimmy Ricketts

FORMATION TESTED Cartlesville

OPERATOR TIME: Thank You

RICKETTS TESTING, INC.

SHALL NOT BE LIABLE FOR ANY DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE ONE FOR WHOM A TEST IS MADE, OR FOR ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH THE USE OF ITS EQUIPMENT, OR ITS STATEMENTS OR OPINION CONCERNING THE RESULTS OF ANY TEST. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT COST BY THE PARTY FOR WHOM THE TEST WAS MADE.

CHARGES

TEST CHARGE	\$ _____
EXTRA PACKERS	\$ _____
<u>JARS</u>	\$ _____
<u>SAFETY JOINT</u>	\$ _____
FLUID SAMPLER	\$ _____
MISRUN CHARGE	\$ _____
STAND-BY CHARGE	\$ _____
STRADDLE	\$ _____
CIRCULATING SUB.	\$ _____
MILEAGE <u>60 miles</u>	\$ <u>60.00</u>
TOTAL	\$ _____

Pressure Test Report

COMPANY INFORMATION

Company Name Flowers Production Company, Inc.
Representative Dallas Flowers
Phone
Fax
Address

E-Mail Address
Service Company

WELL INFORMATION

Well Name Flowers Pottorff 1-29 DST #1
Well Location 29-29S-5E E/2 W/2 NE4
Field and Pool Rock NE Field
Status (Oil, Gas, Water, Injection) Oil and Gas
Perforated Intervals
Mid-point of Perforated Intervals (MPP)
Drilling Rig Number Gulick Drilling #1
Elevations
 Kelly Bushing (KB) 1313 KB
 Casing Flange (CF)
 KB-CF
 Ground Level 1304 GL
Plug Back Total Depth
Total Depth 2810
Production Casing
Production Tubing

TEST INFORMATION

Type of Test DST #1 2795 to 2810
Date(s) of Test 3-20-2006
Dead-weight Gauge Tubing Pressure
Dead-weight Gauge Casing Pressure
Shut-in Date (Duration) 3-20-2006
Date / Time on Bottom 3-20-2006 1:03 am
Date / Time off Bottom 3-20-2006 4:03 am

Probe Serial Number
Probe Offset from End of Tool String
Run Depth at Probe Pressure Port 2800


PRESSURE TEST RESULTS

Maximum Recorded Probe Pressure 1435.0 psig
Maximum Recorded Probe Temperature 104.4 deg F
Final Buildup Pressure
Gradient Survey Information
 Extrapolated Pressure to MPP
 Final Gradient at Depth
Job Number

RECEIVED
JUL 13 2006
KCC WICHITA

Company Name
 Flowers Production Company, Inc.
 Well Name
 Flowers Pottorff 1-29 DST #1
 Type of Test
 DST #1 2785 to 2810
 Date(s) of Test
 3-20-2006

Flowers Pottorff 1-29 DST #1

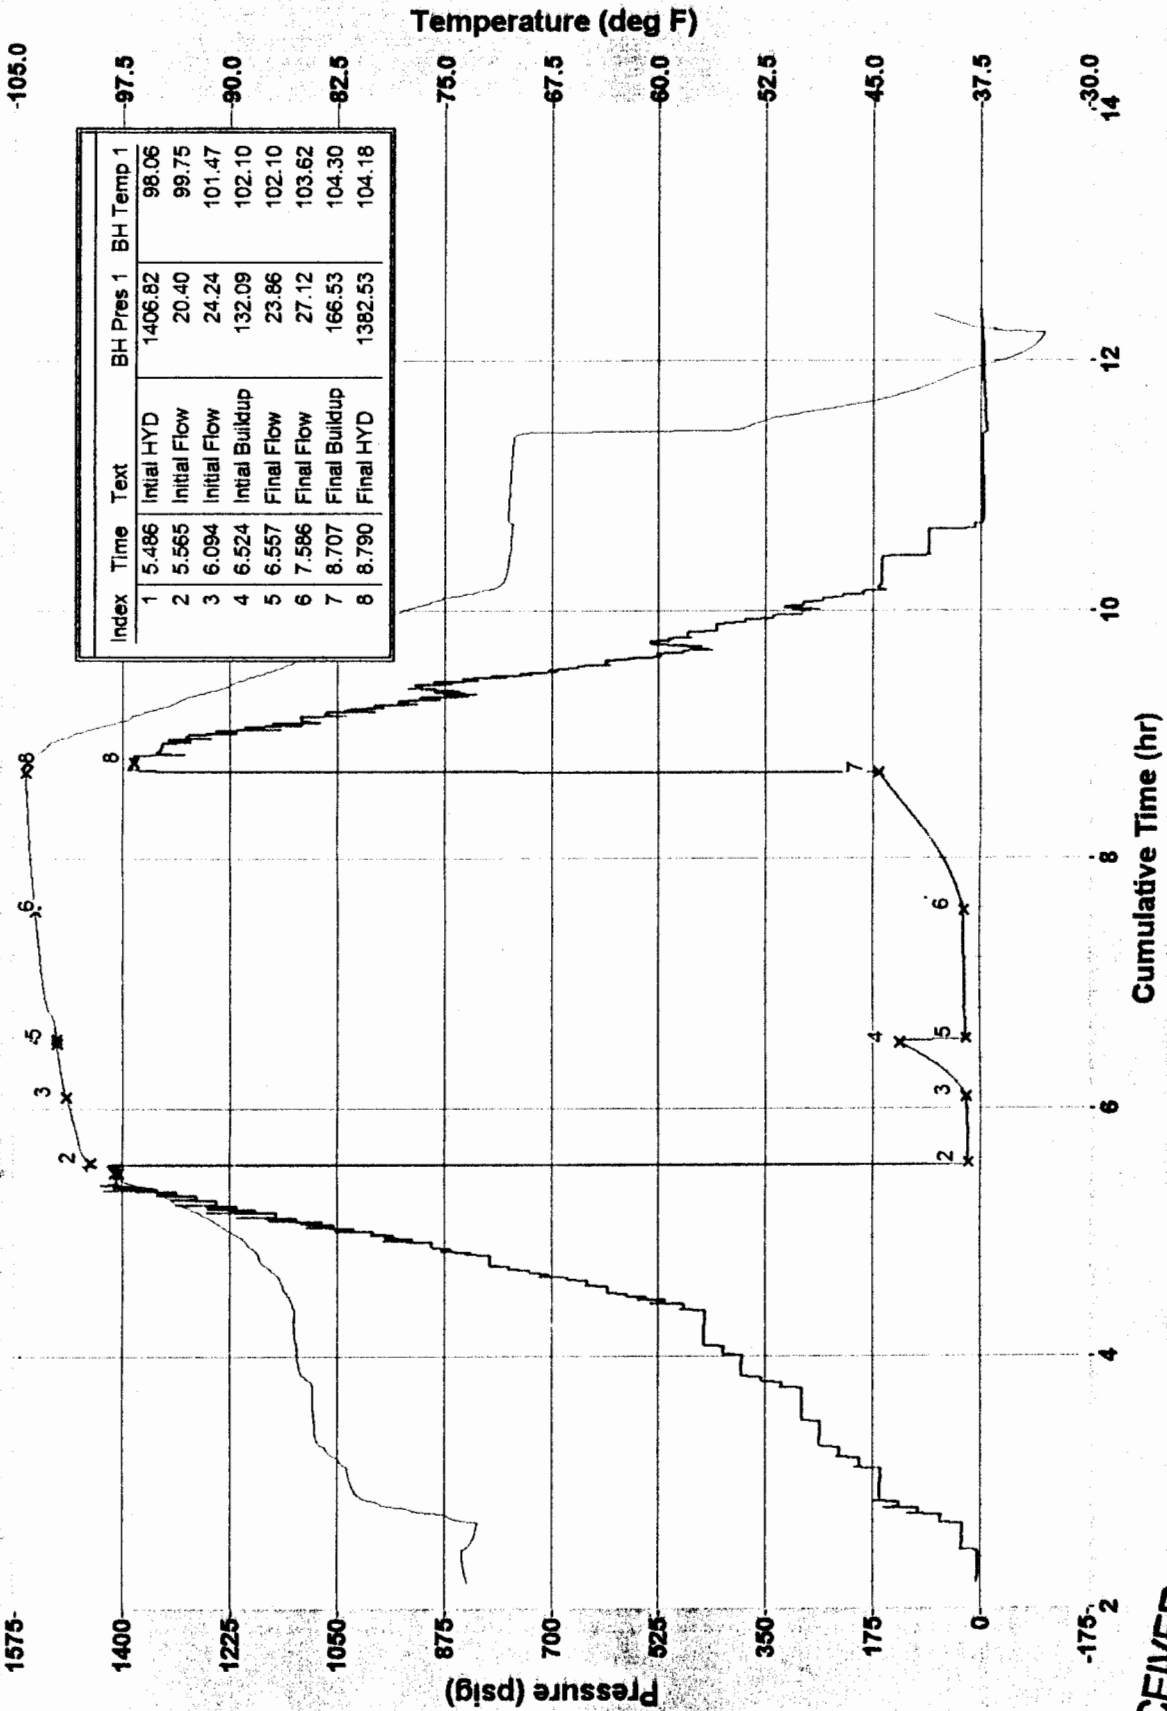


RECEIVED
 JUL 13 2006
 OCCC WICHITA

Company Name: Flowers Production Company, Inc.
 Well Name: Flowers Pottorff 1-29 DST #1
 Type of Test: DST #1 2795 to 2810
 Date(s) of Test: 3-20-2006

Flowers Pottorff 1-29 DST #1

RECEIVED
 JUL 13 2006
 KCC WICHITA

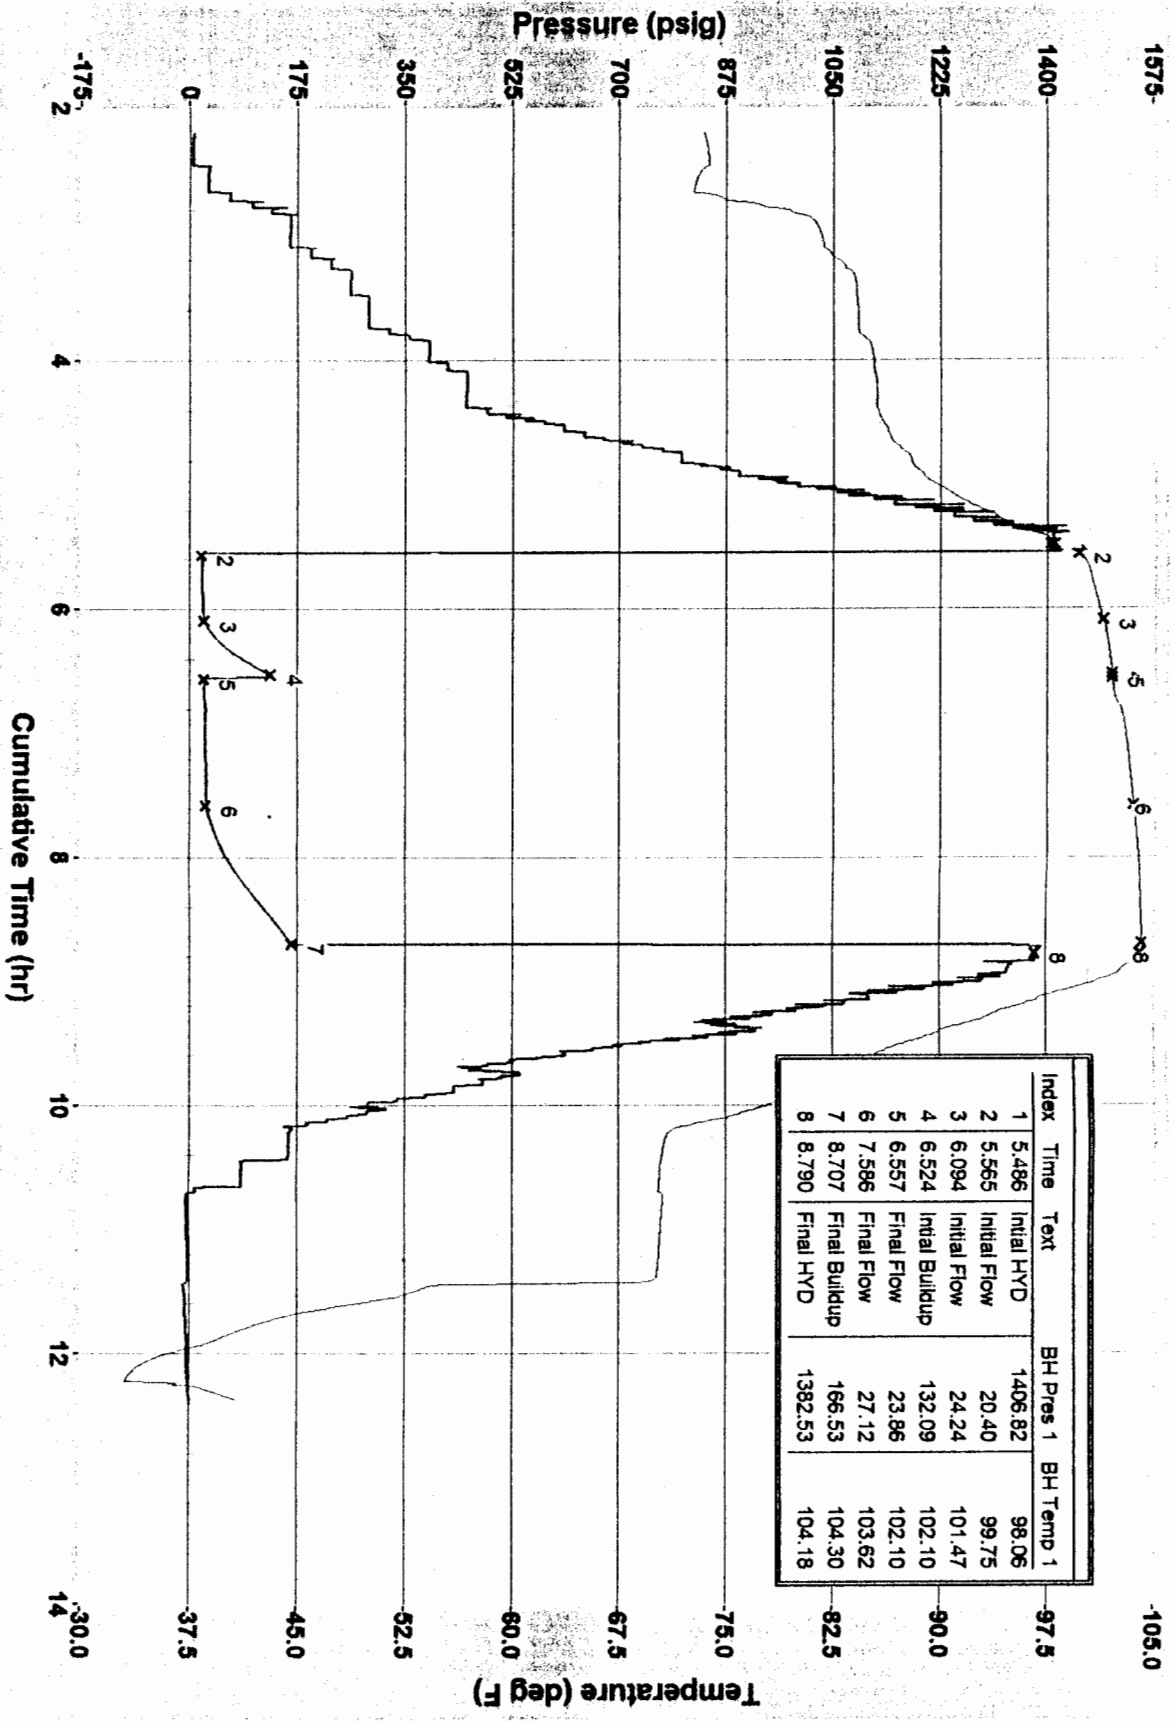

Company Name Flowers Production Company, Inc.
Well Name Flowers Pottorff 1-29 DST #1
Type of Test DST #1 2795 to 2810
Date(s) of Test 3-20-2006

Date	Time	Cum.Time BH1	BH Pres 1	BH Temp 1
		hr	psig	deg F
2006/03/20	03:52:45	7.8778	47.700	103.843
2006/03/20	03:55:00	7.9153	51.171	103.863
2006/03/20	03:57:45	7.9611	55.731	103.899
2006/03/20	04:00:15	8.0028	60.375	103.919
2006/03/20	04:02:30	8.0403	64.776	103.950
2006/03/20	04:05:15	8.0861	70.510	103.982
2006/03/20	04:07:30	8.1236	75.385	104.005
2006/03/20	04:10:15	8.1694	81.886	104.029
2006/03/20	04:12:30	8.2069	87.523	104.045
2006/03/20	04:15:15	8.2528	94.537	104.083
2006/03/20	04:17:45	8.2944	101.168	104.099
2006/03/20	04:20:15	8.3361	107.937	104.122
2006/03/20	04:22:45	8.3778	114.753	104.142
2006/03/20	04:25:00	8.4153	121.075	104.158
2006/03/20	04:27:45	8.4611	128.395	104.191
2006/03/20	04:30:00	8.4986	134.554	104.203
2006/03/20	04:32:45	8.5444	141.957	104.227
2006/03/20	04:35:15	8.5861	148.523	104.243
2006/03/20	04:37:45	8.6278	154.883	104.265
2006/03/20	04:40:15	8.6694	161.212	104.281
Final Buildup				
2006/03/20	04:42:30	8.7069	166.529	104.301
2006/03/20	04:42:45	8.7111	1342.697	104.360
2006/03/20	04:45:15	8.7528	1385.593	104.301
Final HYD				
2006/03/20	04:47:30	8.7903	1382.535	104.178
2006/03/20	04:50:15	8.8361	1381.191	104.054
2006/03/20	04:52:45	8.8778	1340.972	103.165
2006/03/20	04:55:15	8.9194	1335.406	102.742
2006/03/20	04:57:45	8.9611	1319.159	102.144
2006/03/20	05:00:15	9.0028	1293.908	101.084
2006/03/20	05:02:45	9.0444	1245.853	100.008
2006/03/20	05:05:15	9.0861	1153.536	98.605
2006/03/20	05:07:45	9.1278	1107.081	97.196
2006/03/20	05:10:00	9.1653	1062.427	96.672
2006/03/20	05:12:45	9.2111	1028.494	95.182
2006/03/20	05:15:15	9.2528	948.188	94.091
2006/03/20	05:17:45	9.2944	913.363	93.259
2006/03/20	05:20:15	9.3361	822.622	92.212
2006/03/20	05:22:45	9.3778	889.377	90.631
2006/03/20	05:25:15	9.4194	890.960	89.807
2006/03/20	05:27:30	9.4569	844.726	88.855
2006/03/20	05:30:15	9.5028	724.502	87.512
2006/03/20	05:32:30	9.5403	657.292	86.569
2006/03/20	05:35:15	9.5861	610.499	85.536
2006/03/20	05:37:45	9.6278	544.896	84.835
2006/03/20	05:40:15	9.6694	485.742	83.946
2006/03/20	05:42:45	9.7111	468.442	82.949
2006/03/20	05:45:00	9.7486	538.405	82.238
2006/03/20	05:47:45	9.7944	478.377	81.504

RECEIVED
JUL 13 2006
KCC WICHITA

Company Name Flowers Production Company, Inc.
 Well Name Flowers Pottorff 1-29 DST #1
 Type of Test DST #1 2795 to 2810
 Date(s) of Test 3-20-2006

Date	Time	Cum. Time BH1	BH Pres 1	BH Temp 1
		hr	psig	deg F
2006/03/20	02:05:15	6.0861	23.422	101.439
Initial Flow				
2006/03/20	02:05:45	6.0944	24.237	101.471
2006/03/20	02:07:45	6.1278	27.888	101.552
2006/03/20	02:10:00	6.1653	32.699	101.628
2006/03/20	02:12:45	6.2111	39.993	101.701
2006/03/20	02:15:00	6.2486	47.105	101.757
2006/03/20	02:17:45	6.2944	57.437	101.820
2006/03/20	02:20:00	6.3319	67.464	101.872
2006/03/20	02:22:45	6.3778	81.173	101.930
2006/03/20	02:25:00	6.4153	93.674	101.979
2006/03/20	02:27:45	6.4611	109.807	102.027
2006/03/20	02:30:15	6.5028	124.700	102.081
Initial Buildup				
2006/03/20	02:31:30	6.5236	132.094	102.097
2006/03/20	02:32:30	6.5403	25.130	102.101
Final Flow				
2006/03/20	02:33:30	6.5569	23.863	102.101
2006/03/20	02:35:15	6.5861	23.552	102.124
2006/03/20	02:37:30	6.6236	23.515	102.164
2006/03/20	02:40:15	6.6694	23.620	102.211
2006/03/20	02:42:30	6.7069	24.207	102.297
2006/03/20	02:45:15	6.7528	25.403	102.483
2006/03/20	02:47:30	6.7903	26.026	102.697
2006/03/20	02:50:15	6.8361	25.844	102.810
2006/03/20	02:52:45	6.8778	25.881	102.902
2006/03/20	02:55:00	6.9153	25.673	102.952
2006/03/20	02:57:45	6.9611	25.643	103.010
2006/03/20	03:00:00	6.9986	25.626	103.053
2006/03/20	03:02:45	7.0444	25.658	103.113
2006/03/20	03:05:00	7.0819	25.795	103.158
2006/03/20	03:07:45	7.1278	25.865	103.203
2006/03/20	03:10:00	7.1653	25.911	103.231
2006/03/20	03:12:45	7.2111	25.926	103.271
2006/03/20	03:15:15	7.2528	26.053	103.312
2006/03/20	03:17:30	7.2903	26.217	103.345
2006/03/20	03:20:15	7.3361	26.332	103.399
2006/03/20	03:22:30	7.3736	26.409	103.435
2006/03/20	03:25:15	7.4194	26.506	103.471
2006/03/20	03:27:30	7.4569	26.603	103.507
2006/03/20	03:30:15	7.5028	26.689	103.550
2006/03/20	03:32:30	7.5403	26.828	103.581
Final Flow				
2006/03/20	03:35:15	7.5861	27.120	103.620
2006/03/20	03:37:45	7.6278	29.318	103.663
2006/03/20	03:40:00	7.6653	31.622	103.683
2006/03/20	03:42:45	7.7111	34.617	103.721
2006/03/20	03:45:00	7.7486	37.137	103.744
2006/03/20	03:47:45	7.7944	40.749	103.786
2006/03/20	03:50:00	7.8319	43.665	103.807

RECEIVED
 JUL 13 2006
 KCC WICHITA

Company Name Flowers Production Company, Inc.
Well Name Flowers Pottorff 1-29 DST #1
Type of Test DST #1 2795 to 2810
Date(s) of Test 3-20-2006

Date	Time	Cum. Time BH1	BH Pres 1	BH Temp 1
		hr	psig	deg F
2006/03/20	00:10:15	4.1694	450.215	85.498
2006/03/20	00:12:45	4.2111	450.013	85.523
2006/03/20	00:15:15	4.2528	449.774	85.528
2006/03/20	00:17:45	4.2944	449.513	85.528
2006/03/20	00:20:15	4.3361	449.268	85.519
2006/03/20	00:22:45	4.3778	482.535	85.516
2006/03/20	00:25:00	4.4153	482.692	85.663
2006/03/20	00:27:45	4.4611	545.294	85.847
2006/03/20	00:30:00	4.4986	577.115	86.056
2006/03/20	00:32:45	4.5444	609.092	86.281
2006/03/20	00:35:15	4.5861	641.385	86.421
2006/03/20	00:37:45	4.6278	672.246	86.572
2006/03/20	00:40:15	4.6694	731.785	86.925
2006/03/20	00:42:30	4.7069	768.859	87.314
2006/03/20	00:45:15	4.7528	801.304	87.822
2006/03/20	00:47:30	4.7903	800.393	87.969
2006/03/20	00:50:15	4.8361	832.511	88.133
2006/03/20	00:52:30	4.8736	894.666	88.464
2006/03/20	00:55:15	4.9194	895.012	88.853
2006/03/20	00:57:45	4.9611	958.670	89.339
2006/03/20	01:00:00	4.9986	991.371	89.895
2006/03/20	01:02:45	5.0444	1055.064	90.550
2006/03/20	01:05:00	5.0819	1085.621	91.054
2006/03/20	01:07:45	5.1278	1149.990	91.737
2006/03/20	01:10:00	5.1653	1182.285	92.275
2006/03/20	01:12:45	5.2111	1214.611	93.285
2006/03/20	01:15:00	5.2486	1246.984	93.960
2006/03/20	01:17:45	5.2944	1278.832	94.527
2006/03/20	01:20:15	5.3361	1429.936	95.216
2006/03/20	01:22:30	5.3736	1376.763	96.256
2006/03/20	01:25:15	5.4194	1408.961	97.480
2006/03/20	01:27:30	5.4569	1407.850	97.875
Initial HYD				
2006/03/20	01:29:15	5.4861	1406.815	98.064
2006/03/20	01:30:15	5.5028	1407.075	98.154
2006/03/20	01:32:30	5.5403	1421.182	98.814
Initial Flow				
2006/03/20	01:34:00	5.5653	20.396	99.752
2006/03/20	01:35:15	5.5861	20.316	100.011
2006/03/20	01:37:30	5.6236	20.049	100.227
2006/03/20	01:40:15	5.6694	20.206	100.447
2006/03/20	01:42:45	5.7111	20.022	100.537
2006/03/20	01:45:00	5.7486	19.943	100.614
2006/03/20	01:47:45	5.7944	20.353	100.701
2006/03/20	01:50:00	5.8319	21.069	100.801
2006/03/20	01:52:45	5.8778	21.690	100.913
2006/03/20	01:55:15	5.9194	21.788	101.030
2006/03/20	01:57:30	5.9569	21.770	101.111
2006/03/20	02:00:15	6.0028	21.893	101.201
2006/03/20	02:02:30	6.0403	23.182	101.311

RECEIVED
 JUL 13 2006
 KCC WICHITA

Company Name	Flowers Production Company, Inc.
Well Name	Flowers Pottorff 1-29 DST #1
Type of Test	DST #1 2795 to 2810
Date(s) of Test	3-20-2006

COMMENTS

Reported By

Jimmy Ricketts

Weak blow building to 1" initial flow period. Surface blow throughout final flow period. Recovery - 20' drilling mud.

RECEIVED
JUL 13 2006
KCC WICHITA
