

Company **Tomco Oil, Inc.**
 Address **P.O. Box 280**
 CSZ **Douglass, KS 67039**
 Attn. **Tom Blair**

Lease Name **Bossi**
 Lease # **2**
 Legal Desc **NW NE NE**
 Section **15**
 Township **35s**
 County **Cowley**
 Drilling Cont **Gulick Drilling #1**

Job Ticket **4025**
 Range **4e**
 State **KS**

Comments **Times: 30-30-30-30**

15-035-24269

15-35s-4e

GENERAL INFORMATION

Test # 1
 Tester **Richard Holtz**
 Test Type **Conventional Bottom Hole Successful Test**

of Packers **2.0** Packer Size **6 3/4**

Mud Type **Gel Chem**
 Mud Weight **9.4** Viscosity **44.0**
 Filtrate **11.8** Chlorides **1400**

Drill Collar Len **330.0**
 Wght Pipe Len **0**

Formation **Pawnee**
 Interval Top **2920.0** Bottom **2959.0**
 Anchor Len Below **39.0** Between **0**

Total Depth **2959.0**
 Blow Type **Initial Flow, surface blow not building. Final Flow, surface blow dieing to no blow.**

Chokes **3/4** Hole Size **7 7/8**
 Top Recorder # **W1023**
 Mid Recorder #
 Bott Recorder # **13564**


Mileage **80** Approved By
 Standby Time **0**
 Extra Equipmnt
 Time on Site **5:15 PM**
 Tool Picked Up **7:30 PM**
 Tool Layed Dwn **3:30 AM**

Elevation **0** Kelley Bushings **0**

Start Date/Time **6/10/2007 6:49 PM**
 End Date/Time **6/11/2007 3:37 AM**

RECOVERY

Feet	Description	Gas	Oil	Water	Mud
20	mud	0% 0ft	0% 0ft	0% 0ft	100% 20ft
DST Fluids 0					

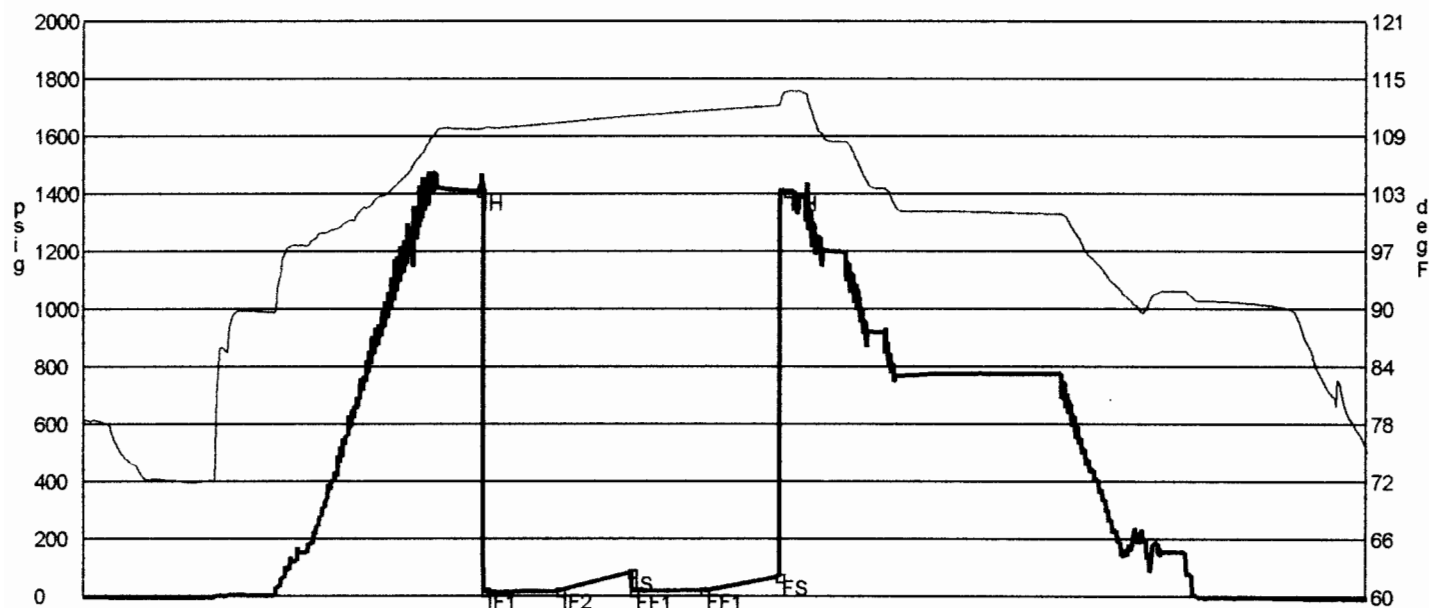

	Date	Time	Pressure	Temp	
IH	6/10/2007 9:31:30 PM	2.7	1409.536	109.6	Initial Hydro-static
IF1	6/10/2007 9:33:30 PM	2.733333	18.964	109.717	Initial Flow (1)
IF2	6/10/2007 10:04:15 PM	3.245833	19.392	110.271	Initial Flow (2)
IS	6/10/2007 10:34:00 PM	3.741667	83.123	110.989	Initial Shut-In
FF1	6/10/2007 10:34:45 PM	3.754167	17.799	111.008	Final Flow (1)
FF1	6/10/2007 11:03:45 PM	4.2375	21.022	111.547	Final Flow (1)
FS	6/10/2007 11:34:45 PM	4.754167	68.203	112.08	Final Shut-In
FH	6/10/2007 11:38:00 PM	4.808333	1406.811	113.566	Final Hydro-static

GAS FLOWS

Min Into IFP Min Into FFP Gas Flows Pressure Choke
