


15-163-23581

30-10s-20w



DRILL STEM TEST REPORT

Prepared For: **American Warrior**

PO Box 399
Garden City KS 67847

ATTN: Marc Downing

30 10 20W Rooks KS

Schneider A #5-30

Start Date: 2006.12.13 @ 08:53:07

End Date: 2006.12.13 @ 13:13:50

Job Ticket #: 26018 DST #: 1

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

American Warrior

PO Box 399
Garden City KS 67847

ATTN: Marc Downing

Schneider A #5-30

30 10 20W Rooks KS

Job Ticket: 26018

DST#: 1

Test Start: 2006.12.13 @ 08:53:07

GENERAL INFORMATION:

Formation: **LKC, H-K**

Deviated: **No** Whipstock: **ft (KB)**

Time Tool Opened: 11:40:00

Time Test Ended: 13:13:50

Test Type: **Conventional Bottom Hole**

Tester: **Michael Shinn**

Unit No: **8**

Interval: **3545.00 ft (KB) To 3635.00 ft (KB) (TVD)**

Total Depth: **3635.00 ft (KB) (TVD)**

Hole Diameter: **7.80 inches** Hole Condition: **Fair**

Reference Elevations: **2155.00 ft (KB)**

2150.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 6672 **Inside**

Press@RunDepth: **psig @ 3546.00 ft (KB)**

Start Date: **2006.12.13**

End Date:

2006.12.13

Capacity: **7000.00 psig**

Last Calib.:

2006.12.13

Start Time: **08:53:07**


End Time:

13:13:50

Time On Btm: **2006.12.13 @ 11:02:20**

Time Off Btm: **2006.12.13 @ 11:03:20**

TEST COMMENT: **Ms-Run**

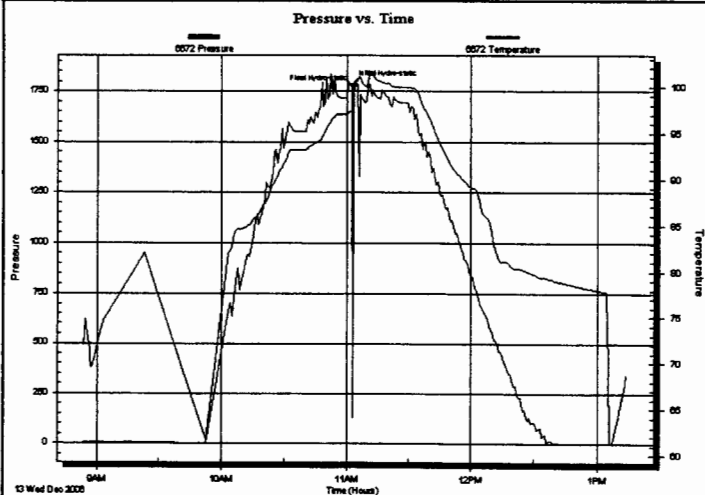

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1783.01	97.39	Initial Hydro-static
1	1762.85	100.30	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
378.00	Mud 100%M	3.61

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

American Warrior

Schneider A #5-30

PO Box 399
Garden City KS 67847

30 10 20W Rooks KS

Job Ticket: 26018

DST#: 1

ATTN: Marc Downing

Test Start: 2006.12.13 @ 08:53:07

Tool Information

Drill Pipe:	Length: 3357.00 ft	Diameter: 3.80 inches	Volume: 47.09 bbl	Tool Weight: 1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 2.25 inches	Volume: 0.00 bbl	Weight set on Packer: 25000.00 lb
Drill Collar:	Length: 186.00 ft	Diameter: 2.25 inches	Volume: 0.91 bbl	Weight to Pull Loose: 34000.00 lb
			Total Volume: 48.00 bbl	Tool Chased 0.00 ft
Drill Pipe Above KB:	18.00 ft			String Weight: Initial 30000.00 lb
Depth to Top Packer:	3545.00 ft			Final 31000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	90.00 ft			
Tool Length:	110.00 ft			
Number of Packers:	1	Diameter:	inches	
Tool Comments:				

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Shut In Tool	5.00			3530.00	
Hydraulic tool	5.00			3535.00	
Packer	5.00			3540.00	20.00 Bottom Of Top Packer
Packer	5.00			3545.00	
Change Over Sub	1.00			3546.00	
Recorder	0.00	6672	Inside	3546.00	
Drill Pipe	63.00			3609.00	
Change Over Sub	1.00			3610.00	
Perforations	20.00			3630.00	
Recorder	0.00	11020	Inside	3630.00	
Bullnose	5.00			3635.00	90.00 Bottom Packers & Anchor

Total Tool Length: 110.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior

Schneider A #5-30

PO Box 399
Garden City KS 67847

30 10 20W Rooks KS

Job Ticket: 26018

DST#: 1

ATTN: Marc Downing

Test Start: 2006.12.13 @ 08:53:07

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 54.00 sec/qt

Cushion Volume:

bbl

Water Loss: 10.98 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2600.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
378.00	Mud 100%M	3.608

Total Length: 378.00 ft

Total Volume: 3.608 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


Serial #: 6672


Inside

American Warrior

30 10 20W Rooks KS

DST Test Number: 1

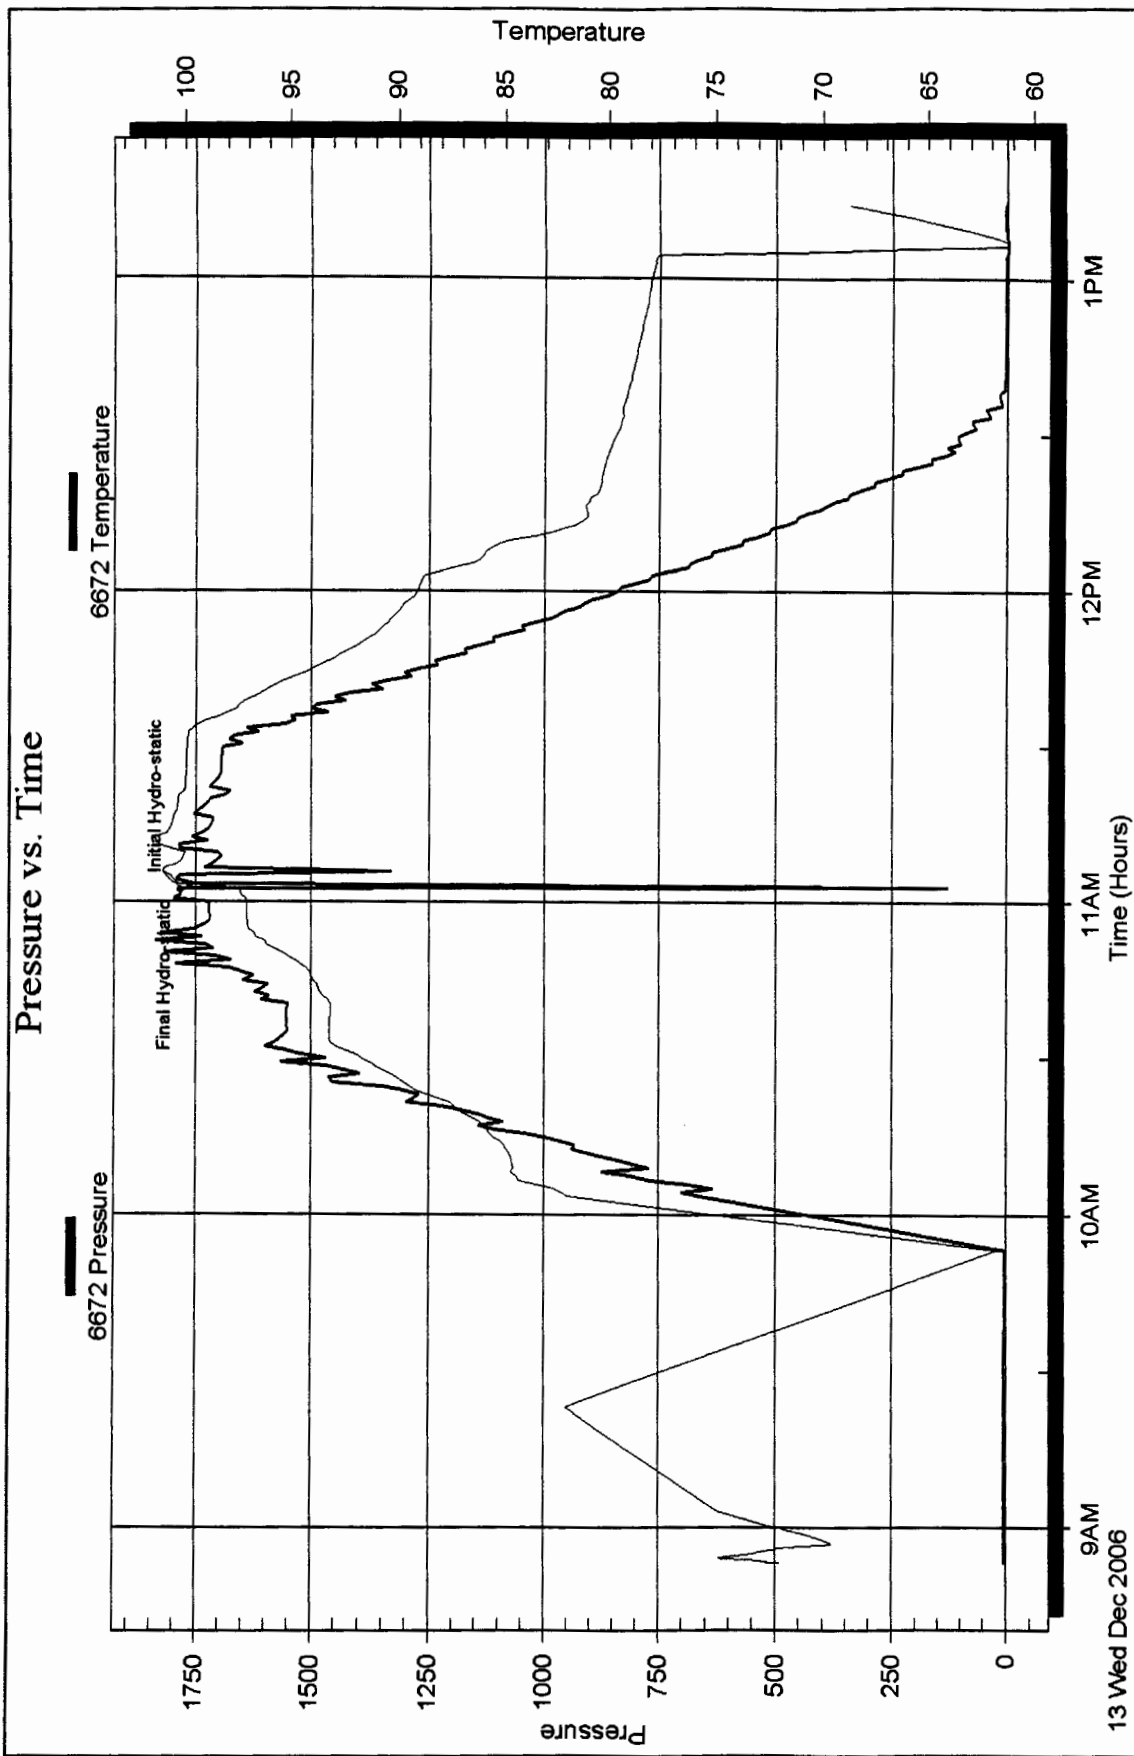



DRILL STEM TEST REPORT

Prepared For: **American Warrior**

PO Box 399
Garden City KS 67847

ATTN: Marc Downing

30 10 20W Rooks KS

Schneider A #5-30

Start Date: 2006.12.13 @ 14:09:46

End Date: 2006.12.13 @ 19:33:59

Job Ticket #: 26019 DST #: 2

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

American Warrior
PO Box 399
Garden City KS 67847
ATTN: Marc Downing

Schneider A #5-30
30 10 20W Rocks KS
Job Ticket: 26019 **DST#: 2**
Test Start: 2006.12.13 @ 14:09:46

GENERAL INFORMATION:

Formation: **LKC, H-K**
Deviated: **No** Whipstock: **ft (KB)**
Time Tool Opened: 15:45:59
Time Test Ended: 19:33:59

Test Type: **Conventional Bottom Hole**
Tester: **Michael Shinn**
Unit No: **8**

Interval: **3537.00 ft (KB) To 3635.00 ft (KB) (TVD)**
Total Depth: **3635.00 ft (KB) (TVD)**
Hole Diameter: **7.80 inches** Hole Condition: **Fair**

Reference Elevations: **2155.00 ft (KB)**
2150.00 ft (CF)
KB to GR/CF: **5.00 ft**


Serial #: 6672

Inside

Press@RunDepth: **28.60 psig @ 3538.00 ft (KB)**
Start Date: **2006.12.13** End Date:
Start Time: **14:09:46** End Time:

Capacity: **7000.00 psig**
Last Calib.: **2006.12.13**
Time On Btm: **2006.12.13 @ 15:45:44**
Time Off Btm: **2006.12.13 @ 17:47:29**

TEST COMMENT: IF Return blow to 1/4 in.
IS No return
FF Weak surface blow
SI No return

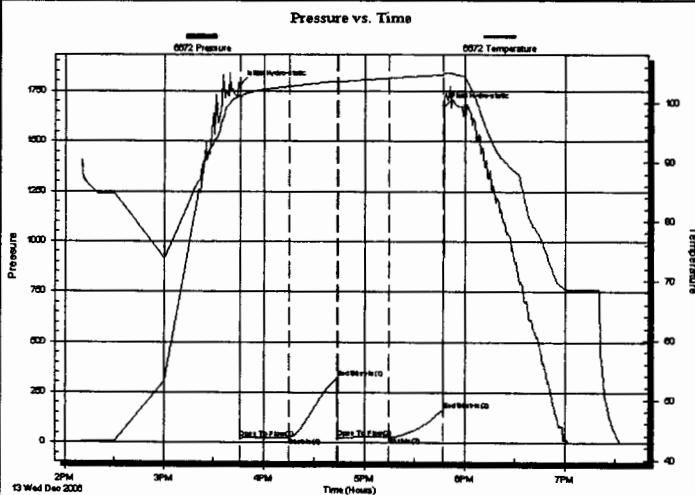

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1781.87	101.31	Initial Hydro-static
1	21.95	100.72	Open To Flow (1)
29	24.50	102.80	Shut-In (1)
58	322.53	103.67	End Shut-In (1)
59	25.88	103.53	Open To Flow (2)
89	28.60	104.19	Shut-In (2)
122	165.11	104.80	End Shut-In (2)
122	1673.85	105.03	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
20.00	Mud 100%M	0.10

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

American Warrior

PO Box 399
Garden City KS 67847

ATTN: Marc Downing

Schneider A #5-30

30 10 20W Rooks KS

Job Ticket: 26019

DST#: 2

Test Start: 2006.12.13 @ 14:09:46

Tool Information

Drill Pipe:	Length: 3353.00 ft	Diameter: 3.80 inches	Volume: 47.03 bbl	Tool Weight:	1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 2.25 inches	Volume: 0.00 bbl	Weight set on Packer:	25000.00 lb
Drill Collar:	Length: 186.00 ft	Diameter: 2.25 inches	Volume: 0.91 bbl	Weight to Pull Loose:	32000.00 lb
		Total Volume:	47.94 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	22.00 ft			String Weight: Initial	30000.00 lb
Depth to Top Packer:	3537.00 ft			Final	30000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	98.00 ft				
Tool Length:	118.00 ft				
Number of Packers:	1	Diameter:	inches		
Tool Comments:					

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Shut In Tool	5.00			3522.00	
Hydraulic tool	5.00			3527.00	
Packer	5.00			3532.00	20.00 Bottom Of Top Packer
Packer	5.00			3537.00	
Change Over Sub	1.00			3538.00	
Recorder	0.00	6672	Inside	3538.00	
Drill Pipe	63.00			3601.00	
Change Over Sub	1.00			3602.00	
Perforations	28.00			3630.00	
Recorder	0.00	11020	Inside	3630.00	
Bullnose	5.00			3635.00	98.00 Bottom Packers & Anchor

Total Tool Length: 118.00



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior

Schneider A #5-30

PO Box 399
Garden City KS 67847

30 10 20W Rooks KS

Job Ticket: 26019

DST#: 2

ATTN: Marc Downing

Test Start: 2006.12.13 @ 14:09:46

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 54.00 sec/qt

Cushion Volume:

bbl

Water Loss: 10.98 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2600.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
20.00	Mud 100%M	0.098

Total Length: 20.00 ft

Total Volume: 0.098 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


Serial #: 6672


Inside

American Warrior

30 10 20W Rocks KS

DST Test Number: 2

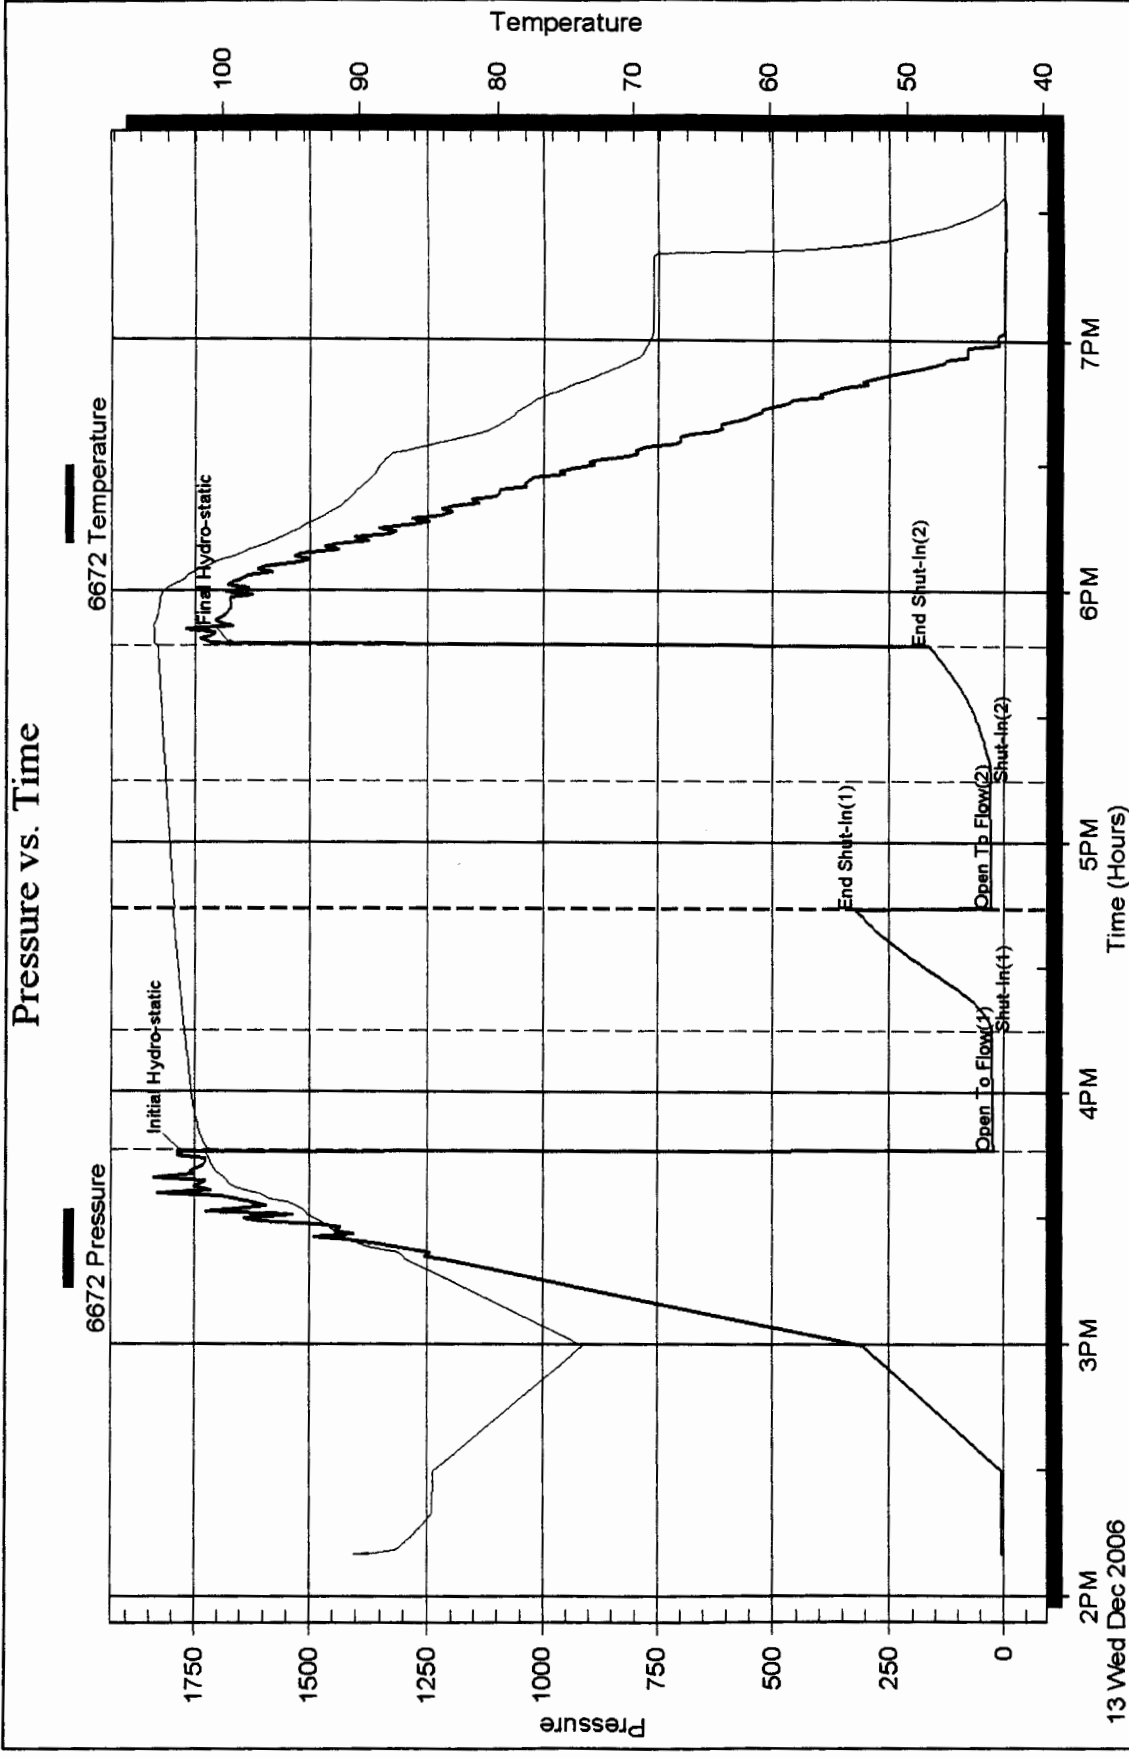



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Prepared For: **American Warrior**

PO Box 399
Garden City KS 67847

ATTN: Marc Downing

30 10 20W Rooks KS

Schneider A #5-30

Start Date: 2006.12.14 @ 06:21:18


End Date: 2006.12.14 @ 12:52:12

Job Ticket #: 25256 DST #: 3

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

American Warrior

PO Box 399
Garden City KS 67847

ATTN: Marc Downing

Schneider A #5-30

30 10 20W Rocks KS

Job Ticket: 25256

DST#: 3

Test Start: 2006.12.14 @ 06:21:18

GENERAL INFORMATION:

Formation: **Arbuckle**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 08:27:13

Time Test Ended: 12:52:12

Test Type: Conventional Bottom Hole

Tester: Ray Schwager

Unit No: 28

Interval: **3684.00 ft (KB) To 3728.00 ft (KB) (TVD)**

Total Depth: 3728.00 ft (KB) (TVD)

Hole Diameter: 7.80 inches Hole Condition: Fair

Reference Elevations: 2155.00 ft (KB)

2150.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 6753

Inside

Press@RunDepth: 41.49 psig @ 3689.01 ft (KB)

Start Date: 2006.12.14

End Date:

2006.12.14

Capacity: 7000.00 psig

Last Calib.: 2006.12.14

Start Time: 06:21:18

End Time:

12:52:12


Time On Btm: 2006.12.14 @ 08:26:43

Time Off Btm: 2006.12.14 @ 11:00:12

TEST COMMENT: IFP Wk bl thru-out 1/4 " to 1 " bl

FFP No bl

Times 45 45 30 30

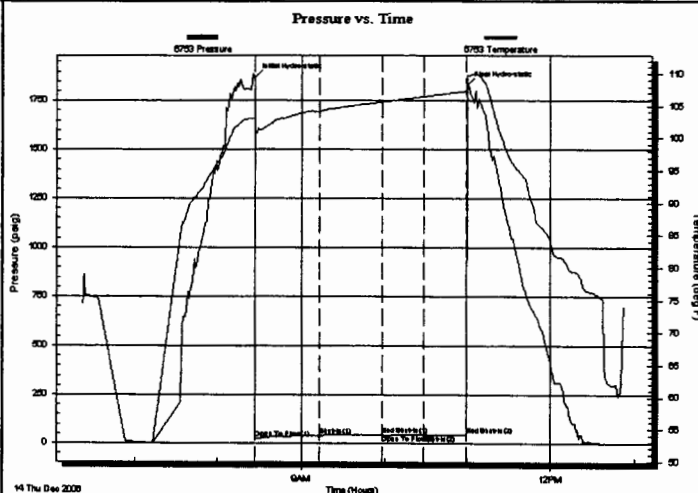

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1868.18	103.11	Initial Hydro-static
1	22.38	100.72	Open To Flow (1)
46	39.01	104.10	Shut-In(1)
91	44.39	105.61	End Shut-In(1)
92	41.87	105.62	Open To Flow(2)
122	41.49	106.45	Shut-In(2)
153	43.95	107.30	End Shut-In(2)
154	1829.49	109.66	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
15.00	SOQM 3%O 97%M	0.07

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

TOOL DIAGRAM

American Warrior

Schneider A #5-30

PO Box 399
Garden City KS 67847

30 10 20W Rooks KS

ATTN: Marc Downing

Job Ticket: 25256 **DST#: 3**

Test Start: 2006.12.14 @ 06:21:18

Tool Information

Drill Pipe:	Length: 3513.00 ft	Diameter: 3.80 inches	Volume: 49.28 bbl	Tool Weight:	2200.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	25000.00 lb
Drill Collar:	Length: 180.00 ft	Diameter: 2.25 inches	Volume: 0.89 bbl	Weight to Pull Loose:	45000.00 lb
		Total Volume:	50.17 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	30.00 ft			String Weight: Initial	30000.00 lb
Depth to Top Packer:	3684.00 ft			Final	30000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	44.02 ft				
Tool Length:	65.02 ft				
Number of Packers:	2	Diameter:	6.75 inches		

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			3664.00	
Shut In Tool	5.00			3669.00	
Hydraulic tool	5.00			3674.00	
Packer	5.00			3679.00	21.00 Bottom Of Top Packer
Packer	5.00			3684.00	
Stubb	1.00			3685.00	
Perforations	4.00			3689.00	
Recorder	0.01	6753	Inside	3689.01	
Perforations	4.00			3693.01	
Recorder	0.01	13534	Outside	3693.02	
Blank Spacing	32.00			3725.02	
Bullnose	3.00			3728.02	44.02 Bottom Packers & Anchor

Total Tool Length: 65.02



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior

Schneider A #5-30

PO Box 399
Garden City KS 67847

30 10 20W Rooks KS

Job Ticket: 25256

DST#: 3

ATTN: Marc Downing

Test Start: 2006.12.14 @ 06:21:18

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 56.00 sec/qt

Cushion Volume:

bbl

Water Loss: 7.59 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 2600.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
15.00	SOCM 3%O 97%M	0.074

Total Length: 15.00 ft

Total Volume: 0.074 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


Serial #: 6753


Inside

American Warrior

30 10 20W Rocks KS

DST Test Number: 3

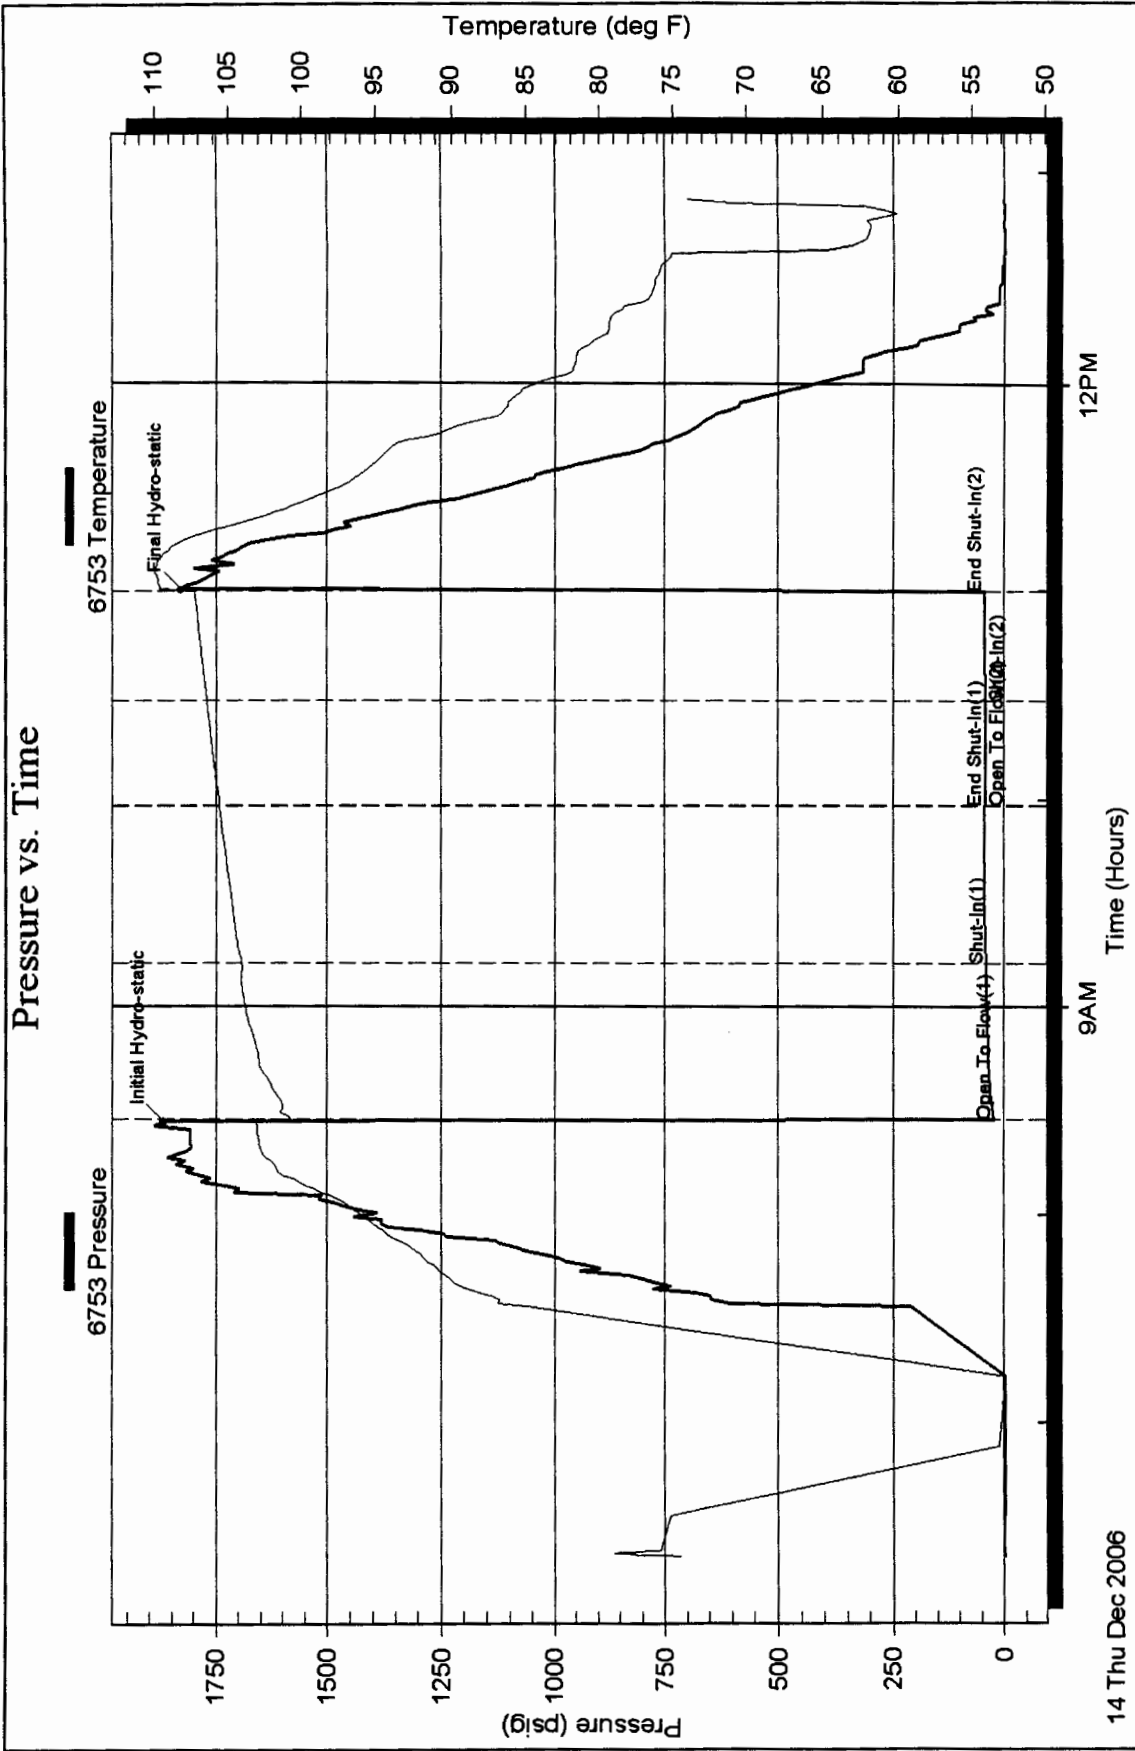



TRILOBITE TESTING INC.

P.O. Box 362 • Hays, Kansas 67601

9649

26018

Test Ticket

Well Name & No. <u>Schneider # A 5-30</u>	Test No. <u>1</u>	Date <u>12-13-06</u>
Company <u>American Warrior</u>	Zone Tested <u>LBK, H-K</u>	
Address <u>P.O. Box 399, Garden City, KS 67846</u>	Elevation <u>2155</u> KB <u>2150</u> GL	
Co. Rep / Geo. <u>Marc Penning</u>	Rig <u>Shelby Pulling Rig #8</u>	
Location: Sec. <u>30</u> Twp. <u>90S</u> Rge. <u>20W</u>	Co. <u>hanks</u> State <u>KS</u>	
Comment: _____		Release date / time: _____

Interval Tested <u>3545'</u>	<u>3635'</u>	Initial Str Wt./Lbs. <u>30,000</u>	Unseated Str Wt./Lbs. <u>31,000</u>
Anchor Length <u>90'</u>		Wt. Set Lbs. <u>25,000</u>	Wt. Pulled Loose/Lbs. <u>34,000</u>
Top Packer Depth <u>3540'</u>		Tool Weight <u>1500</u>	
Bottom Packer Depth <u>3545'</u>		Hole Size 7 7/8" <u>✓</u>	Rubber Size 6 3/4" <u>✓</u>
Total Depth <u>3635'</u>		Wt. Pipe Run <u>✓</u>	Drill Collar Run <u>186'</u>
Mud Wt. <u>9.0</u> LCM <u>20</u> Vis. <u>54</u> WL <u>11.0</u>		Drill Pipe Size <u>4 1/2 XH</u>	Ft. Run <u>3357'</u>
Blow Description <u>ML-RUN</u>			

Recovery - Total Feet <u>378'</u>	GIP <u>0</u>	Ft. in DC _____	Ft. in DP <u>328'</u>
Rec. _____	Feet of _____	%gas _____	%oil _____
Rec. _____	Feet of _____	%gas _____	%oil _____
Rec. _____	Feet of _____	%gas _____	%oil _____
Rec. _____	Feet of _____	%gas _____	%oil _____
Rec. _____	Feet of _____	%gas _____	%oil _____
BHT _____	*F Gravity _____	*API D @ _____	*F Corrected Gravity _____
RW _____	@ _____	*F Chlorides _____	ppm Recovery _____
		Chlorides <u>2,600</u>	ppm System _____

(A) Initial Hydrostatic Mud _____	AK-1 <u>1783</u> PSI	Alpine _____	Recorder No. <u>6672</u>	Test <u>x 1/1000. 0.900</u>
(B) First Initial Flow Pressure _____	_____ PSI	(depth) _____	<u>3550'</u>	Jars _____
(C) First Final Flow Pressure _____	_____ PSI	Recorder No. _____		Safety Jt. _____
(D) Initial Shut-In Pressure _____	_____ PSI	(depth) _____		Circ Sub <u>X N/C</u>
(E) Second Initial Flow Pressure _____	_____ PSI	Recorder No. <u>11020</u>		Sampler _____
(F) Second Final Flow Pressure _____	_____ PSI	(depth) <u>3630'</u>		Straddle _____
(G) Final Shut-In Pressure _____	_____ PSI	Initial Opening _____		Ext. Packer _____
(Q) Final Hydrostatic Mud _____	<u>1763</u> PSI	Initial Shut-In _____		Shale Packer _____

TRILOBITE TESTING INC. SHALL NOT BE LIABLE FOR DAMAGED OF ANY KIND OF THE PROPERTY OR PERSONNEL OF THE ONE FOR WHOM A TEST IS MADE, OR FOR ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH THE USE OF ITS EQUIPMENT, OR ITS STATEMENTS OR OPINION CONCERNING THE RESULTS OF ANY TEST. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT COST BY THE PARTY FOR WHOM THE TEST IS MADE.


Final Flow _____	T-On Location <u>09:00 a.m.</u>	Sub Total: _____
Final Shut-In _____	T-Started <u>09:30 a.m.</u>	Std. By _____
	T-Open <u>11:40 a.m.</u>	Acc. Chg: _____
	T-Pulled <u>11:50 a.m.</u>	Other: <u>\$990</u>
	T-Out <u>13:50 p.m.</u>	Total: _____


Approved By _____

Our Representative [Signature]

CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

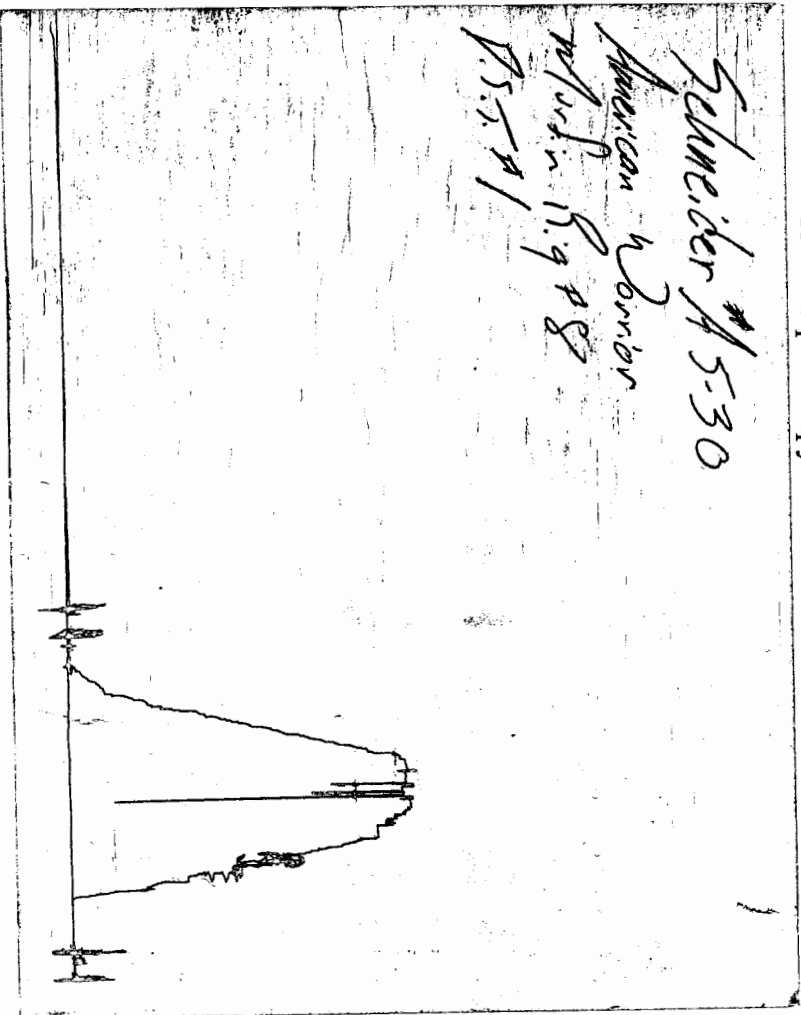



TRILOBITE TESTING INC.

P.O. Box 362 • Hays, Kansas 67601

26019

Test Ticket

Well Name & No. Schneider #A5-30 Test No. 2 Date 12-13-06
 Company American Warrior Zone Tested LCR, H-K
 Address P.O. Box 399 Garden City, KS 67846 Elevation 255 KB 2150 GL
 Co. Rep / Geo. Mark Downing Rig Lucifer R. 4 #8
 Location: Sec. 30 Twp. 10s Rge. 20w Co. Reels State KS
 Comment: _____ Release date / time: _____

Interval Tested 3537' 3635' Initial Str Wt./Lbs. 30000 Unseated Str Wt./Lbs. 30000
 Anchor Length 98' Wt. Set Lbs. 25000 Wt. Pulled Loose/Lbs. 32,000
 Top Packer Depth 3532' Tool Weight 1800
 Bottom Packer Depth 3537' Hole Size 7 7/8" ✓ Rubber Size 6 3/4" ✓
 Total Depth 3635' Wt. Pipe Run ✓ Drill Collar Run 186'
 Mud Wt. 9.0 LCM 2nd Vis. 54 WL 11.0 Drill Pipe Size 4 1/2 x H Ft. Run 3353'

Blow Description 14" Return blow to 4 in.

15" No Return
16" Weak Surface blow
18" No Return

Recovery - Total Feet 30' GIP 0 Ft. in DC 0 Ft. in DP 20'
 Rec. 20' Feet of mud %gas %oil %water 100 %mud
 Rec. _____ Feet of _____ %gas %oil %water %mud
 Rec. _____ Feet of _____ %gas %oil %water %mud
 Rec. _____ Feet of _____ %gas %oil %water %mud
 Rec. _____ Feet of _____ %gas %oil %water %mud
 BHT _____ °F Gravity _____ °API D @ _____ °F Corrected Gravity _____ °API
 RW _____ @ _____ °F Chlorides _____ ppm Recovery _____ Chlorides 2600 ppm System

(A) Initial Hydrostatic Mud	AK-1	Alpine	Recorder No.	Test
(B) First Initial Flow Pressure	1782	PSI	(depth)	Jars
(C) First Final Flow Pressure	22	PSI	Recorder No.	Safety Jt.
(D) Initial Shut-In Pressure	25	PSI	(depth)	Circ Sub <u>x N/C</u>
(E) Second Initial Flow Pressure	323	PSI	Recorder No. <u>11020</u>	Sampler
(F) Second Final Flow Pressure	26	PSI	(depth)	Straddle
(G) Final Shut-In Pressure	29	PSI	Initial Opening <u>30</u>	Ext. Packer
(Q) Final Hydrostatic Mud	1674	PSI	Initial Shut-In <u>30</u>	Shale Packer
			Final Flow <u>30</u>	Ruined Packer <u>x200.00</u>
			Final Shut-In <u>30</u>	Mileage <u>0</u>

TRILOBITE TESTING INC. SHALL NOT BE LIABLE FOR DAMAGED OF ANY KIND OF THE PROPERTY OR PERSONNEL OF THE ONE FOR WHOM A TEST IS MADE, OR FOR ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH THE USE OF ITS EQUIPMENT, OR ITS STATEMENTS OR OPINION CONCERNING THE RESULTS OF ANY TEST. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT COST BY THE PARTY FOR WHOM THE TEST IS MADE.

Approved By _____

Our Representative [Signature]


T-On Location


T-Started 14.00 p.m.
 T-Open 14.20 p.m.
 T-Pulled 15.55 p.m.
 T-Out 17.55 p.m.

Sub Total: _____
 Std. By _____
 Acc. Chg: 1300
 Other: _____
 Total: _____

CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

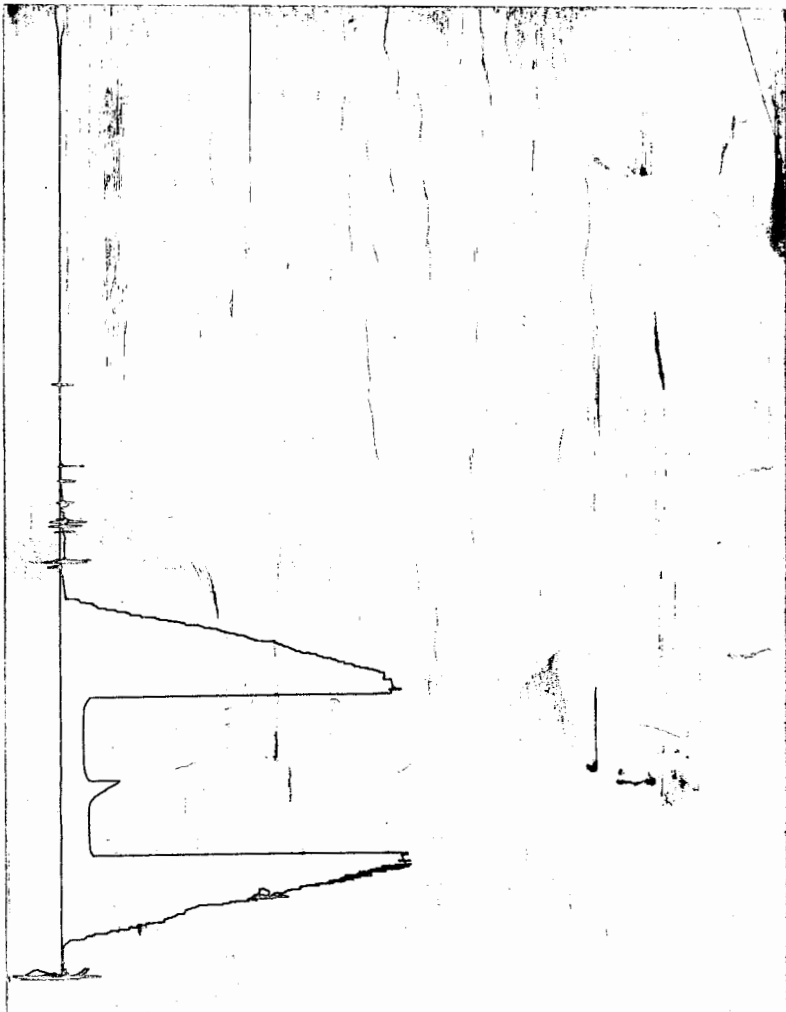



TRILOBITE TESTING INC.

P.O. Box 362 • Hays, Kansas 67601

25256

Test Ticket

Well Name & No.	Schneider 'A' # 5-30		Test No.	3	Date	12-14-06
Company	AMERICAN WARRIOR INC		Zone Tested	Arbuckle		
Address	P.O. Box 399 Garden City, Ks 67846-0399		Elevation	2155	KB	2150 GL
Co. Rep / Geo.	MARC Downing		Rig	MURFIN 8		
Location: Sec.	30	Twp.	10 ^s	Rge.	20 ^w	Co. Rooks State Ks
Comment:	Release date / time:					

Interval Tested	3684-3728		Initial Str Wt./Lbs.	30000	Unseated Str Wt./Lbs.	30000
Anchor Length	44		Wt. Set Lbs.	25000	Wt. Pulled Loose/Lbs.	45000
Top Packer Depth	3679		Tool Weight	2200		
Bottom Packer Depth	3684		Hole Size 7 7/8"	-	Rubber Size 6 3/4"	-
Total Depth	3728		Wt. Pipe Run	-	Drill Collar Run	180
Mud Wt.	9.1	LCM 2 [#]	Vis. 56	WL 7.6	Drill Pipe Size	4 1/2 X H
Blow Description	IFP - WEAK Blow thru-out 1/4" To 1" Blow					
	FFP - NO BLOW					

Recovery - Total Feet	15	GIP	-	Ft. in DC	15	Ft. in DP	
Rec.	15	Feet of	50 CM	%gas	3	%oil	%water 97 %mud
Rec.		Feet of		%gas		%oil	%water %mud
Rec.		Feet of		%gas		%oil	%water %mud
Rec.		Feet of		%gas		%oil	%water %mud
Rec.		Feet of		%gas		%oil	%water %mud
BHT	107	*F Gravity	-	*API D @	-	*F Corrected Gravity	*API
RW	-	@	-	*F	Chlorides	ppm Recovery	Chlorides 2600 ppm System

	AK-1	Alpine	Recorder No.	Test
(A) Initial Hydrostatic Mud	1807	PSI	6753	✓ 1100
(B) First Initial Flow Pressure	22	PSI	3689	Jars
(C) First Final Flow Pressure	39	PSI	13534	Safety Jt.
(D) Initial Shut-In Pressure	44	PSI	3693	Circ Sub
(E) Second Initial Flow Pressure	41	PSI	-	Sampler
(F) Second Final Flow Pressure	41	PSI	-	Straddle
(G) Final Shut-In Pressure	44	PSI	45	Ext. Packer
(Q) Final Hydrostatic Mud	1760	PSI	45	Shale Packer
			30	Ruined Packer
			30	Mileage ✓ 72 RT 90
			0545	Sub Total:
			0621	Std. By
			0825	Acc. Chg:
			1055	Other:
			1252	Total:

Approved By _____

Our Representative

RAY SCHWAGER Thank you

TRILOBITE TESTING INC. SHALL NOT BE LIABLE FOR DAMAGED OF ANY KIND OF THE PROPERTY OR PERSONNEL OF THE ONE FOR WHOM A TEST IS MADE, OR FOR ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH THE USE OF ITS EQUIPMENT, OR ITS STATEMENTS OR OPINION CONCERNING THE RESULTS OF ANY TEST. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT COST BY THE PARTY FOR WHOM THE TEST IS MADE.

CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

