

DATE 1-2-62

TICKET NO. 403

COMPANY Davis Bros. CONTRACTOR Transit Corp.

WELL NO. 'B' 1 LEASE Wilson COUNTY Rooks SEC. 34 RG. 18 TWP. 10

TEST NO. 1 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4" FH

ANCHOR LENGTH 134' AIR CHAMBER LENGTH --- SIZE CHOKE 1/4"

FORMATION TESTED Cong. Simp. INTERVAL TESTED 3452' - 3586' ELEVATION 1989' DF T. D. 3586'
Arb.

MUD WEIGHT 10.4 VISCOSITY 43 WATER LOSS 15.4cc


TOOL OPEN 2 hrs. IBHP SHUT IN TIME 20 min. FBHP SHUT IN TIME 30 min.

BLOW Weak steady blow through out test.

RECOVERY 330' of water cut mud.

REMARKS _____

APPROVED BY J. R. Green TESTER T. C. Skinner

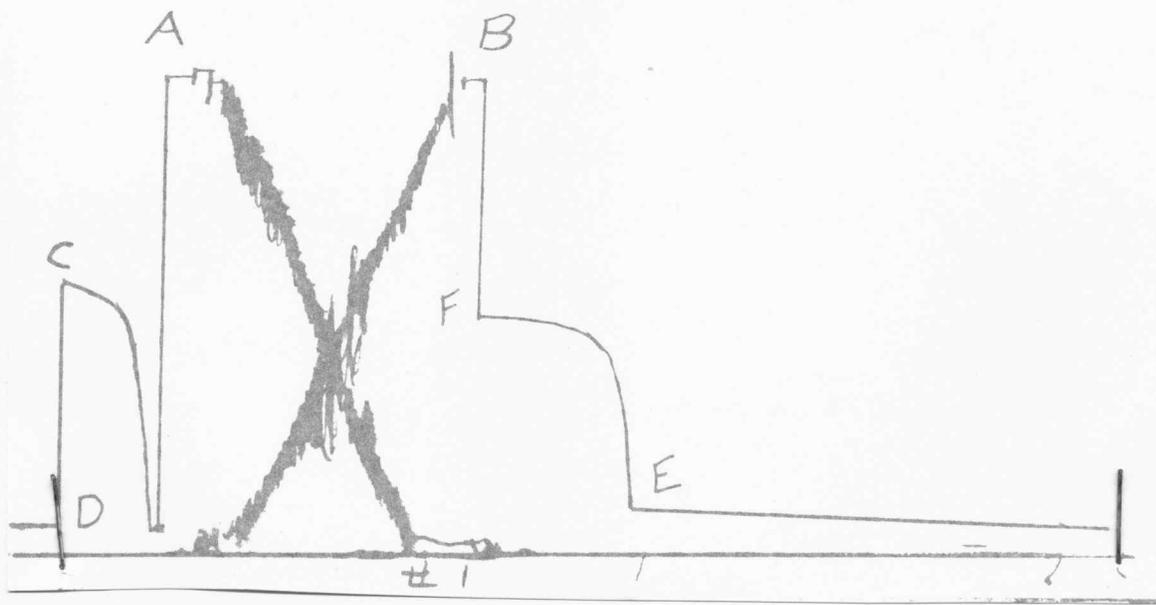

PRESSURE READINGS	
A. Initial Hyd. Pressure	2050
B. Final Hyd. Pressure	2030
C. Initial BHP	1190
D. Initial Flow Pressure	170
E. Final Flow Pressure	240
F. Final BHP	1050
