




DRILL STEM TEST REPORT

Prepared For: **Ritchie Exploration**

8100 East 22nd Street North
#700 Wichita Kansas 67278

ATTN: Max Lovely

Van Eaton 10B

10-12s-31w-Gove


Start Date: 2011.11.06 @ 04:35:00

End Date: 2011.11.06 @ 10:48:00

Job Ticket #: 17231 DST #: 1

Superior Testers Enterprises LLC
PO Box 138 Great Bend KS 67530
1-800-792-6902

Printed: 2011.11.06 @ 23:05:44



DRILL STEM TEST REPORT

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17231

DST#: 1

ATTN: Max Lovely

Test Start: 2011.11.06 @ 04:35:00

GENERAL INFORMATION:

Formation: **Lansing H**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 06:36:00

Time Test Ended: 10:48:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Dustin Ellis

Unit No: 3315-GB-225 miles

Interval: ft (KB) To ft (KB) (TVD)

Total Depth: 4216.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2969.00 ft (KB)

2960.00 ft (CF)

KB to GR/CF: 9.00 ft

Serial #: 6806

Inside

Press@RunDepth: 49.74 psia @ 4212.00 ft (KB)

Start Date: 2011.11.06

End Date:

2011.11.06

Start Time: 04:35:00

End Time:

10:48:00


Capacity: 5000.00 psia

Last Calib.: 2011.11.06

Time On Btm: 2011.11.06 @ 06:35:30

Time Off Btm: 2011.11.06 @ 09:06:30

TEST COMMENT: 1st Open 30 minutes Very weak surface blow
1st Shut in 45 minutes No blow back
2nd Open 30 minutes Dead
2nd Shut in 45 minutes No blow back

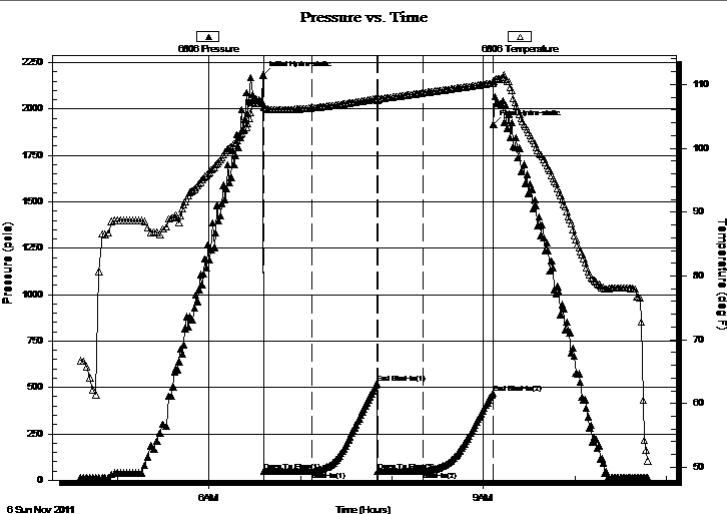

PRESSURE SUMMARY


Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	2182.56	107.13	Initial Hydro-static
1	46.76	106.48	Open To Flow (1)
32	46.66	106.33	Shut-In(1)
75	521.81	107.78	End Shut-In(1)
75	48.02	107.58	Open To Flow (2)
105	49.74	108.69	Shut-In(2)
151	468.30	110.23	End Shut-In(2)
151	1914.59	110.52	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
1.00	Mud 100%	0.00

Gas Rates

Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
----------------	-----------------	------------------



DRILL STEM TEST REPORT

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17231

DST#: 1

ATTN: Max Lovely

Test Start: 2011.11.06 @ 04:35:00

GENERAL INFORMATION:

Formation: **Lansing H**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 06:36:00

Time Test Ended: 10:48:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Dustin Ellis

Unit No: 3315-GB-225 miles

Interval: ft (KB) To ft (KB) (TVD)

Total Depth: 4216.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2969.00 ft (KB)

2960.00 ft (CF)

KB to GR/CF: 9.00 ft

Serial #: 6663 Outside

Press@RunDepth: 469.46 psia @ 4213.00 ft (KB)

Start Date: 2011.11.06

End Date:

2011.11.06

Capacity: 5000.00 psia

Last Calib.: 2011.11.06

Start Time: 04:35:00

End Time:


10:48:00

Time On Btm: 2011.11.06 @ 06:35:30

Time Off Btm: 2011.11.06 @ 09:06:30

TEST COMMENT: 1st Open 30 minutes Very weak surface blow
1st Shut in 45 minutes No blow back
2nd Open 30 minutes Dead
2nd Shut in 45 minutes No blow back

Pressure vs. Time

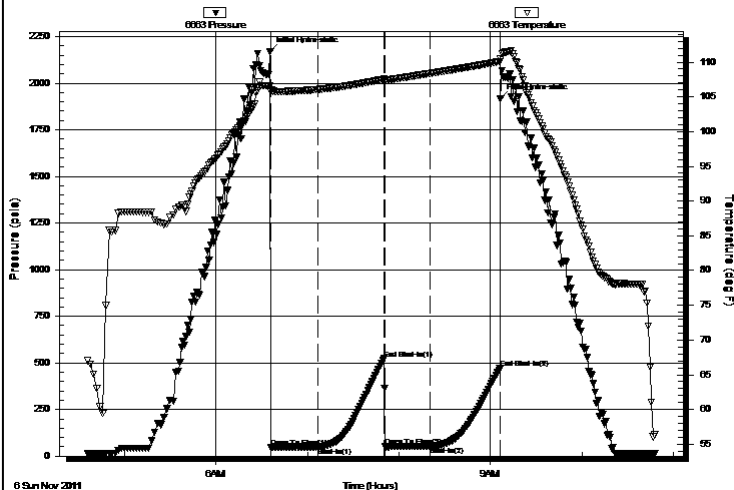

PRESSURE SUMMARY


Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	2171.55	106.56	Initial Hydro-static
1	48.57	105.70	Open To Flow (1)
32	49.81	106.08	Shut-In(1)
75	522.88	107.54	End Shut-In(1)
76	50.59	107.41	Open To Flow (2)
105	51.81	108.38	Shut-In(2)
151	469.46	110.09	End Shut-In(2)
151	1918.15	110.50	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
1.00	Mud 100%	0.00

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



DRILL STEM TEST REPORT

TOOL DIAGRAM

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17231

DST#: 1

ATTN: Max Lovely


Test Start: 2011.11.06 @ 04:35:00

Tool Information

Drill Pipe:	Length:	3606.00 ft	Diameter:	3.80 inches	Volume:	50.58 bbl	Tool Weight:	2000.00 lb
Heavy Wt. Pipe:	Length:	0.00 ft	Diameter:	0.00 inches	Volume:	0.00 bbl	Weight set on Packer:	20000.00 lb
Drill Collar:	Length:	569.00 ft	Diameter:	2.25 inches	Volume:	2.80 bbl	Weight to Pull Loose:	64000.00 lb
					Total Volume:	53.38 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:		27.00 ft					String Weight: Initial	62000.00 lb
Depth to Top Packer:		4176.00 ft					Final	62000.00 lb
Depth to Bottom Packer:		ft						
Interval between Packers:		40.00 ft						
Tool Length:		68.00 ft						
Number of Packers:		2	Diameter:	6.25 inches				
Tool Comments:								

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Shut-In Tool	5.00			4153.00	
Hydrolic Tool	5.00			4158.00	
Jars	6.00			4164.00	
Safety Joint	2.00			4166.00	
Packer	5.00			4171.00	28.00 Bottom Of Top Packer
Packer	5.00			4176.00	
Perforations	35.00			4211.00	
Recorder	1.00	6806	Inside	4212.00	
Recorder	1.00	6663	Outside	4213.00	
Bull Plug	3.00			4216.00	40.00 Bottom Packers & Anchor
Total Tool Length:	68.00				



DRILL STEM TEST REPORT

FLUID SUMMARY

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17231

DST#: 1

ATTN: Max Lovely

Test Start: 2011.11.06 @ 04:35:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 52.00 sec/qt

Water Loss: 71.96 in³

Resistivity: ohm.m

Salinity: 1200.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psia

Oil API:

Water Salinity:

deg API

ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
1.00	Mud 100%	0.005

Total Length: 1.00 ft Total Volume: 0.005 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

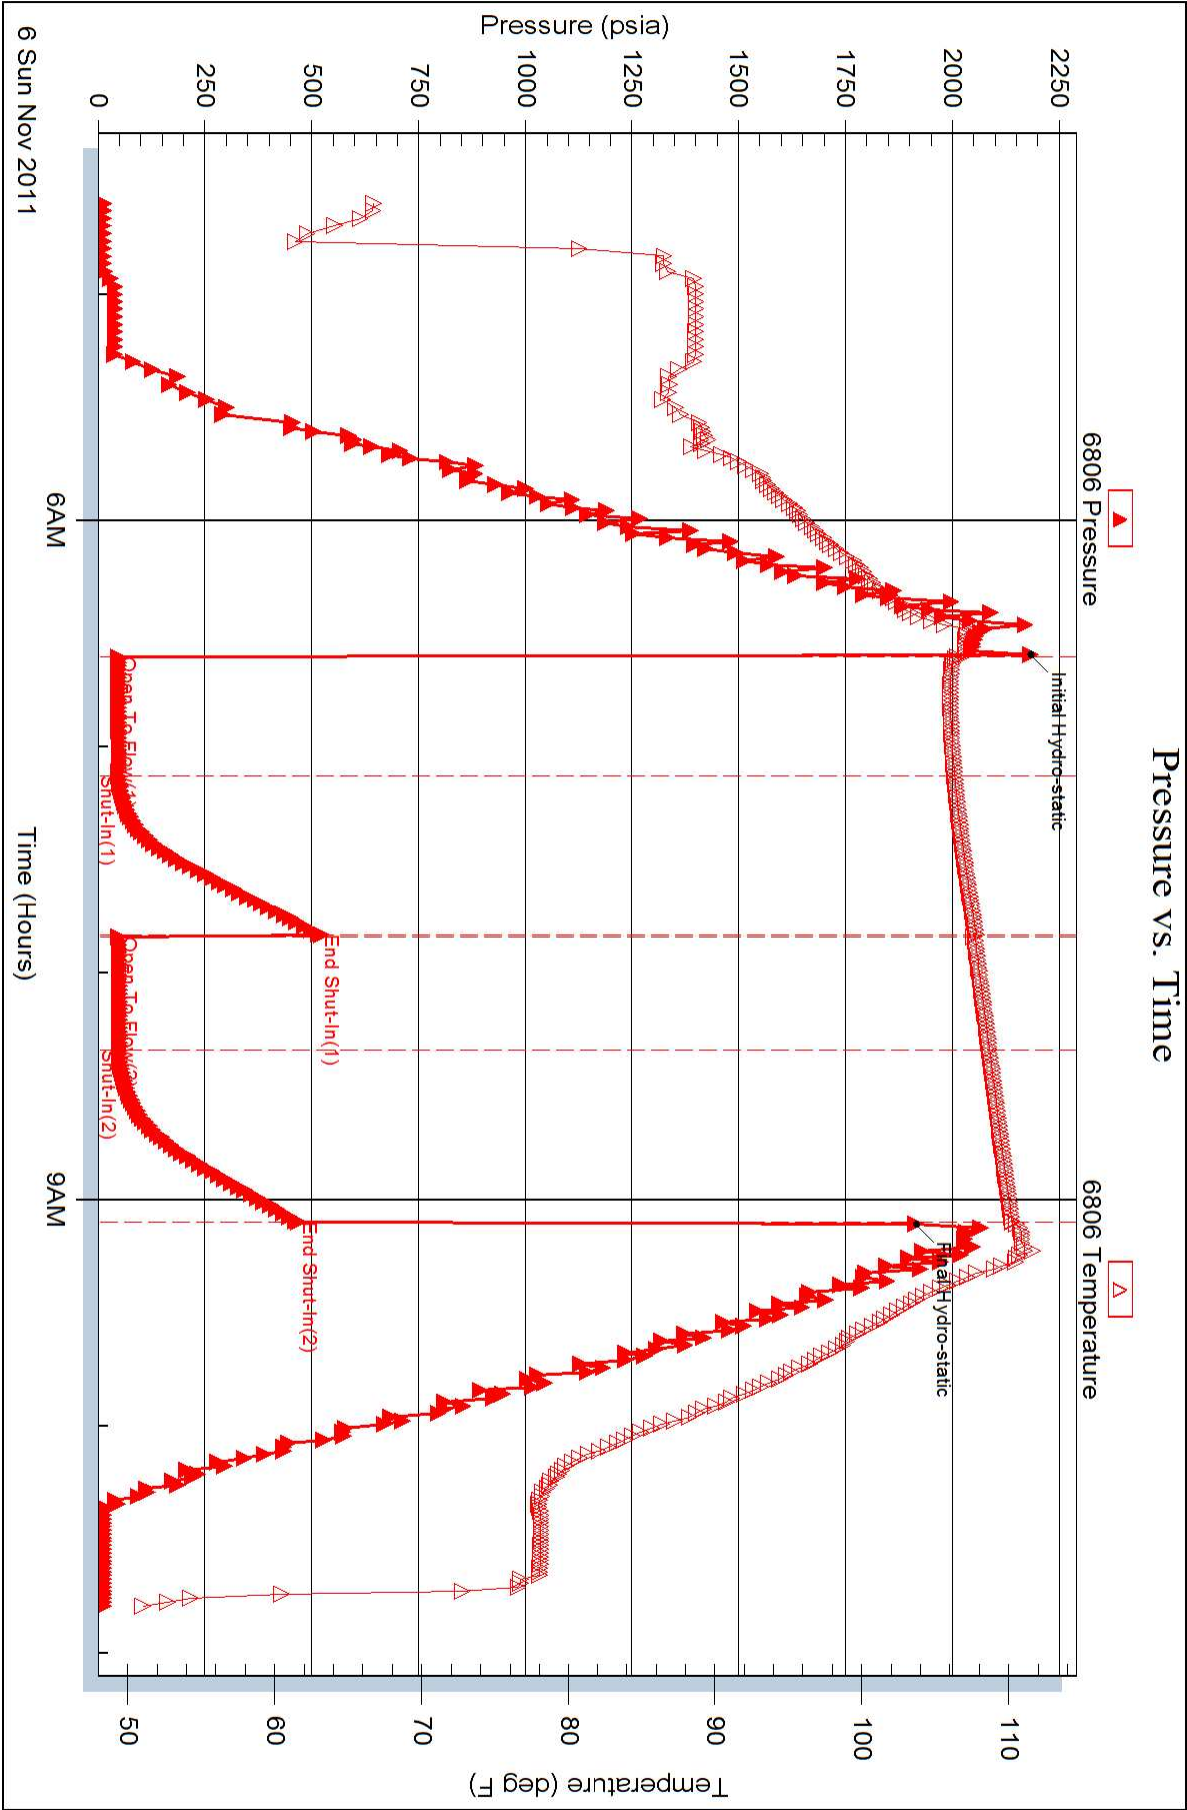



Serial #: 6663

Outside Ritchie Exploration

Van Eaton 10B

DST Test Number: 1

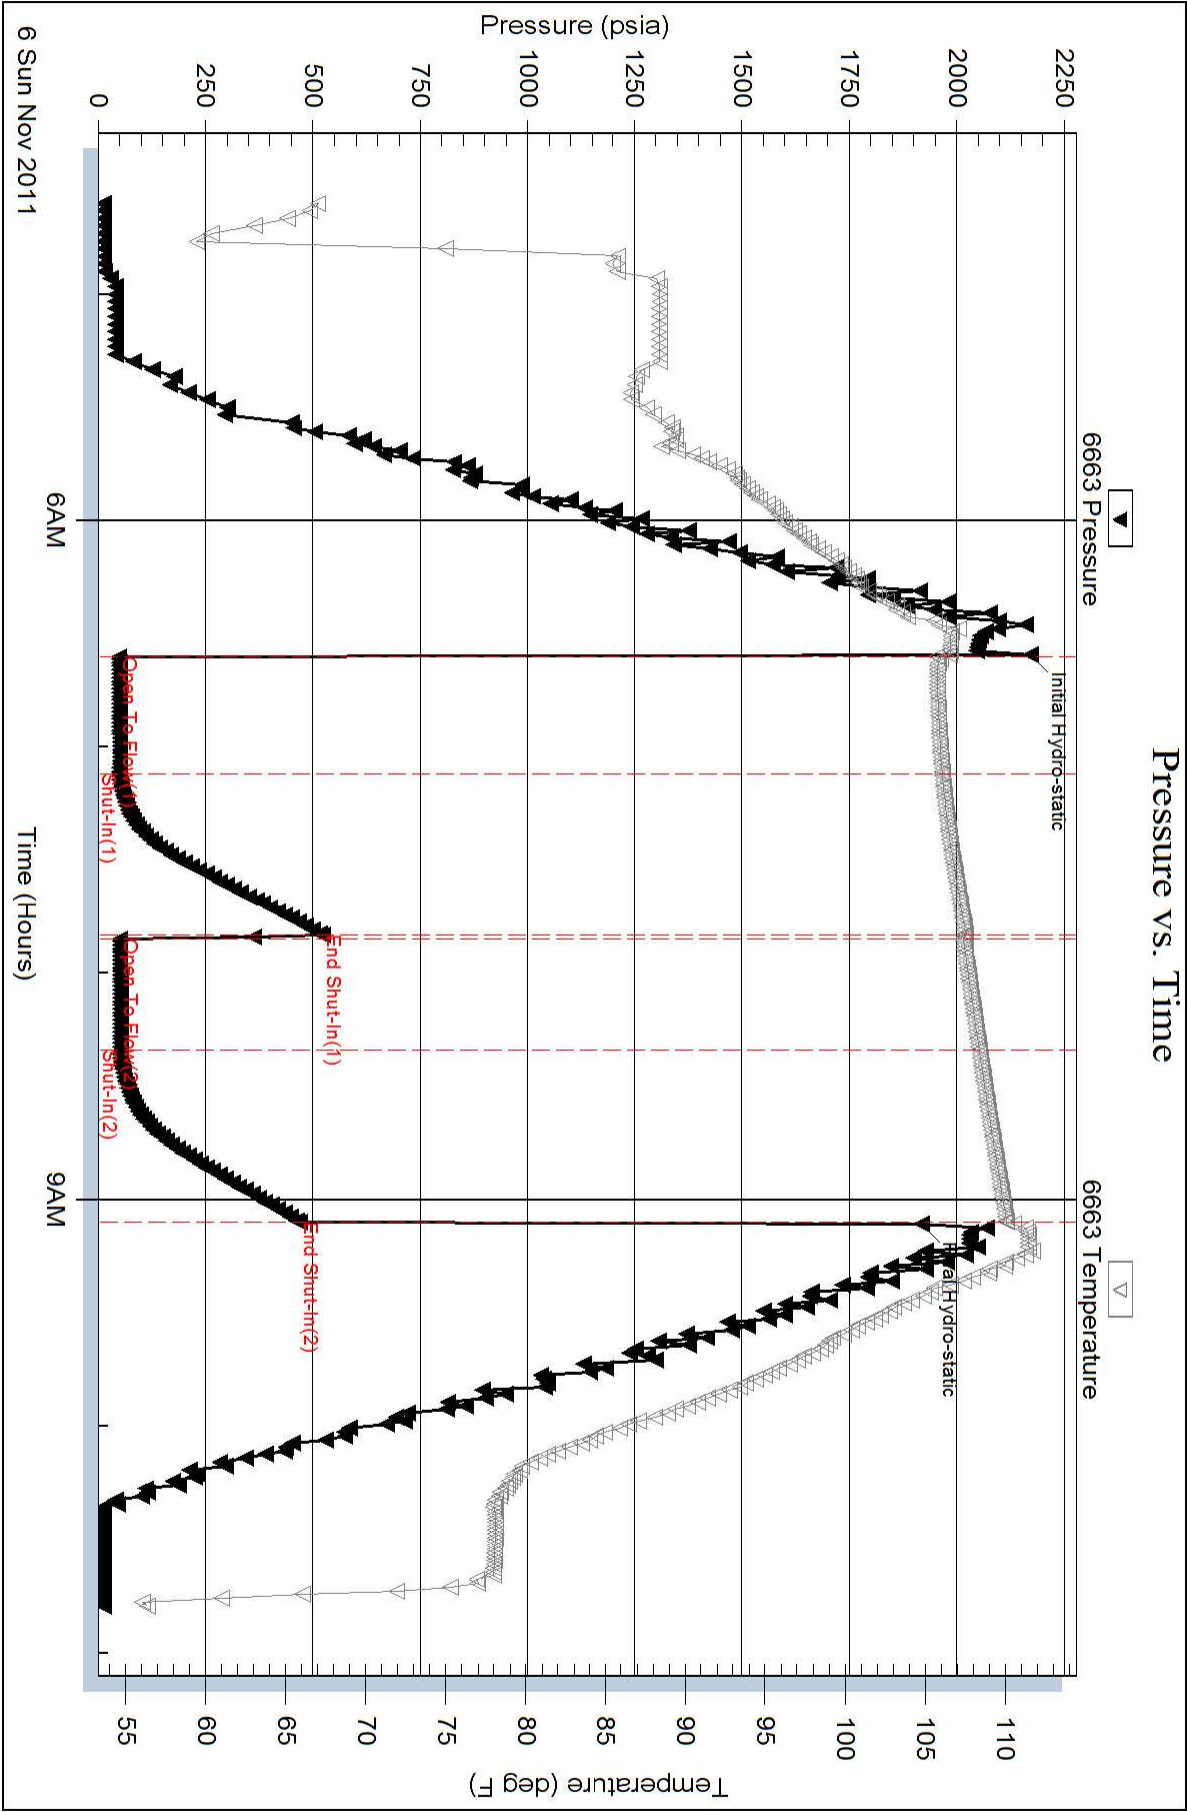



DRILL STEM TEST REPORT

Prepared For: **Ritchie Exploration**

8100 East 22nd Street North
#700 Wichita Kansas 67278

ATTN: Max Lovely

Van Eaton 10B

10-12s-31w-Gove


Start Date: 2011.11.07 @ 09:50:00

End Date: 2011.11.07 @ 16:02:30

Job Ticket #: 17232 DST #: 2

Superior Testers Enterprises LLC
PO Box 138 Great Bend KS 67530
1-800-792-6902

Printed: 2011.11.07 @ 16:16:59



DRILL STEM TEST REPORT

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17232

DST#: 2

ATTN: Max Lovely

Test Start: 2011.11.07 @ 09:50:00

GENERAL INFORMATION:

Formation: **Lansing I&J**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 11:52:30

Time Test Ended: 16:02:30

Test Type: Conventional Bottom Hole (Initial)

Tester: Dustin Ellis

Unit No: 3315-GB-225 miles

Interval: ft (KB) To ft (KB) (TVD)

Total Depth: 4262.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2969.00 ft (KB)

2960.00 ft (CF)

KB to GR/CF: 9.00 ft

Serial #: 6806

Inside

Press@RunDepth: 53.55 psia @ 4258.00 ft (KB)

Start Date: 2011.11.07

End Date:

2011.11.07

Start Time: 09:50:00

End Time:

16:02:30


Capacity: 5000.00 psia

Last Calib.: 2011.11.07

Time On Btm: 2011.11.07 @ 11:51:30

Time Off Btm: 2011.11.07 @ 14:23:30

TEST COMMENT: 1st Open 30 minutes Weak surface blow
1st Shut in 45 minutes No blow back
2nd Open 30 minutes Very weak initial blow then died off
2nd Shut in 45 minutes No blow

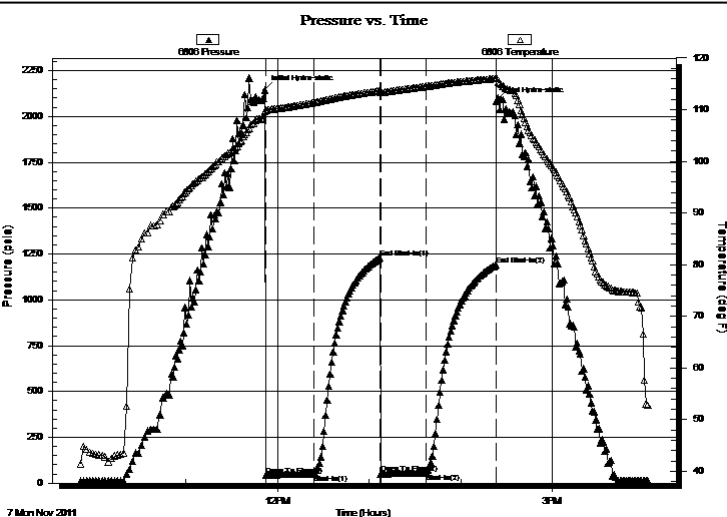

PRESSURE SUMMARY


Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	2144.03	109.57	Initial Hydro-static
1	44.49	109.88	Open To Flow (1)
32	48.77	111.33	Shut-In(1)
76	1227.63	113.63	End Shut-In(1)
76	50.93	113.38	Open To Flow (2)
106	53.55	114.47	Shut-In(2)
152	1189.84	116.02	End Shut-In(2)
152	2083.40	116.24	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	Mud 100%	0.02

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



DRILL STEM TEST REPORT

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17232

DST#: 2

ATTN: Max Lovely

Test Start: 2011.11.07 @ 09:50:00

GENERAL INFORMATION:

Formation: **Lansing I&J**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 11:52:30

Time Test Ended: 16:02:30

Test Type: Conventional Bottom Hole (Initial)

Tester: Dustin Ellis

Unit No: 3315-GB-225 miles

Interval: ft (KB) To ft (KB) (TVD)

Total Depth: 4262.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2969.00 ft (KB)

2960.00 ft (CF)

KB to GR/CF: 9.00 ft

Serial #: 6663 Outside

Press@RunDepth: 1191.78 psia @ 4259.00 ft (KB)

Start Date: 2011.11.07

End Date:

2011.11.07

Start Time: 09:50:00

End Time:

16:02:00


Capacity: 5000.00 psia

Last Calib.: 2011.11.07

Time On Btm: 2011.11.07 @ 11:51:00

Time Off Btm: 2011.11.07 @ 14:23:30

TEST COMMENT: 1st Open 30 minutes Weak surface blow
1st Shut in 45 minutes No blow back
2nd Open 30 minutes Very weak initial blow then died off
2nd Shut in 45 minutes No blow

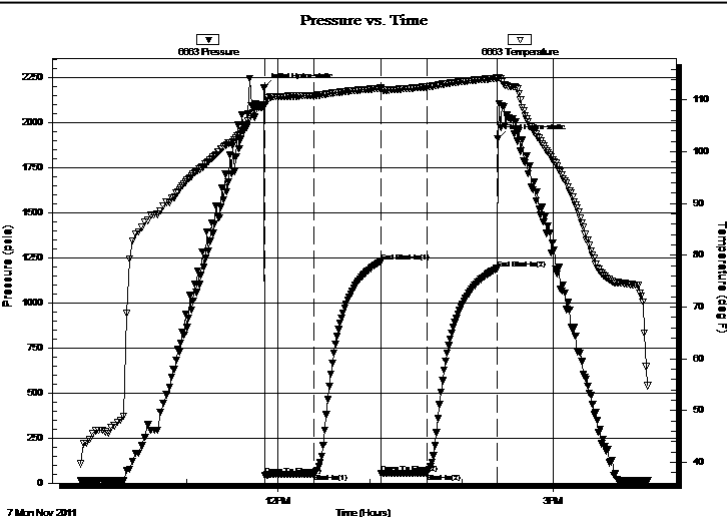

PRESSURE SUMMARY


Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	2194.31	108.83	Initial Hydro-static
1	44.85	109.16	Open To Flow (1)
33	51.66	110.90	Shut-In(1)
76	1229.65	112.29	End Shut-In(1)
77	53.00	111.96	Open To Flow (2)
106	56.86	112.56	Shut-In(2)
152	1191.78	114.22	End Shut-In(2)
153	1911.57	114.38	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	Mud 100%	0.02

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



DRILL STEM TEST REPORT

TOOL DIAGRAM

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17232

DST#: 2


ATTN: Max Lovely

Test Start: 2011.11.07 @ 09:50:00

Tool Information

Drill Pipe:	Length: 3637.00 ft	Diameter: 3.80 inches	Volume: 51.02 bbl	Tool Weight: 2000.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 20000.00 lb
Drill Collar:	Length: 569.00 ft	Diameter: 2.25 inches	Volume: 2.80 bbl	Weight to Pull Loose: 70000.00 lb
		Total Volume:	53.82 bbl	Tool Chased 0.00 ft
Drill Pipe Above KB:	5.00 ft			String Weight: Initial 62000.00 lb
Depth to Top Packer:	4229.00 ft			Final 62000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	33.00 ft			
Tool Length:	61.00 ft			
Number of Packers:	2	Diameter: 6.25 inches		
Tool Comments:				

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Shut-In Tool	5.00			4206.00	
Hydrolic Tool	5.00			4211.00	
Jars	6.00			4217.00	
Safety Joint	2.00			4219.00	
Packer	5.00			4224.00	28.00 Bottom Of Top Packer
Packer	5.00			4229.00	
Perforations	28.00			4257.00	
Recorder	1.00	6806	Inside	4258.00	
Recorder	1.00	6663	Outside	4259.00	
Bull Plug	3.00			4262.00	33.00 Bottom Packers & Anchor
Total Tool Length:	61.00				



DRILL STEM TEST REPORT

FLUID SUMMARY

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17232

DST#: 2

ATTN: Max Lovely

Test Start: 2011.11.07 @ 09:50:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 57.00 sec/qt

Water Loss: 6.40 in³

Resistivity: ohm.m

Salinity: 2200.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psia

Oil API:

Water Salinity:

deg API

ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
5.00	Mud 100%	0.025

Total Length: 5.00 ft Total Volume: 0.025 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

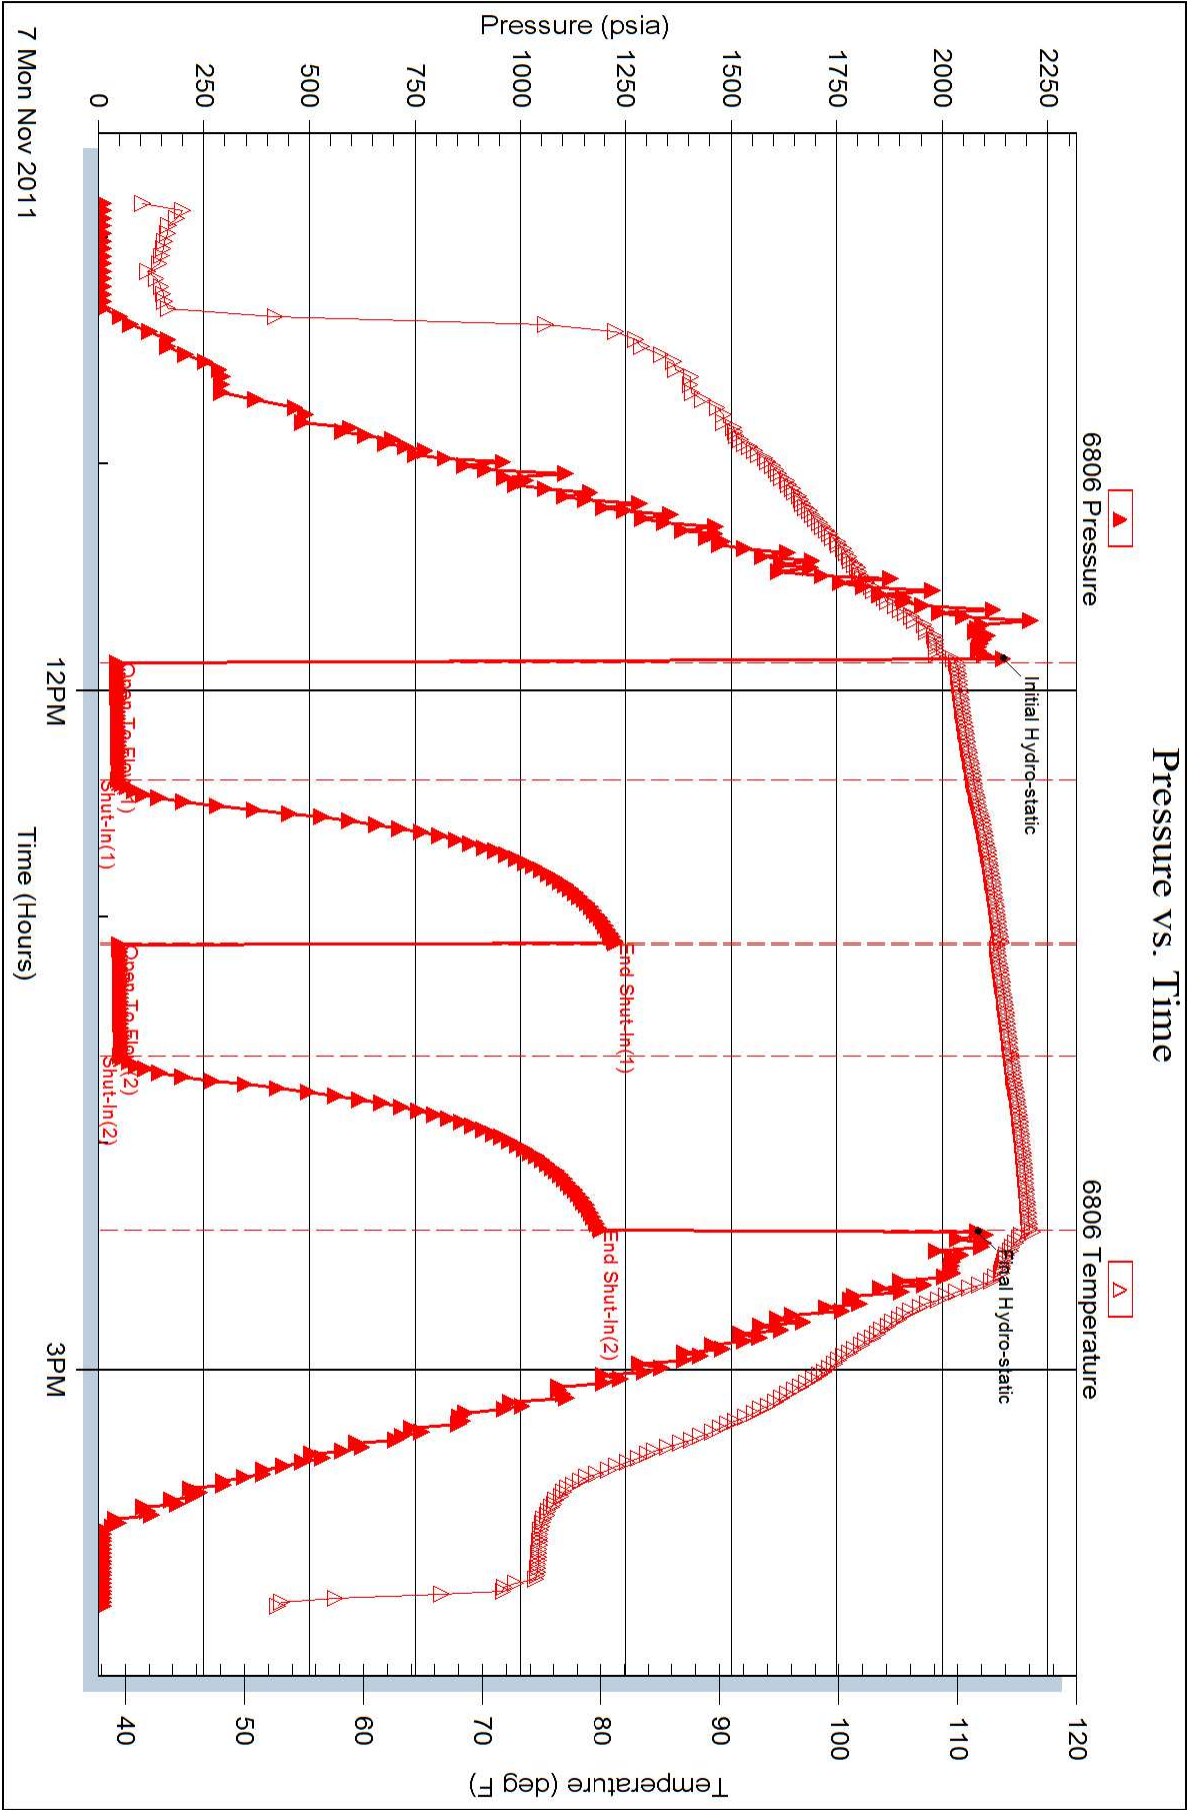



Serial #: 6663

Outside Ritchie Exploration

Van Eaton 10B

DST Test Number: 2

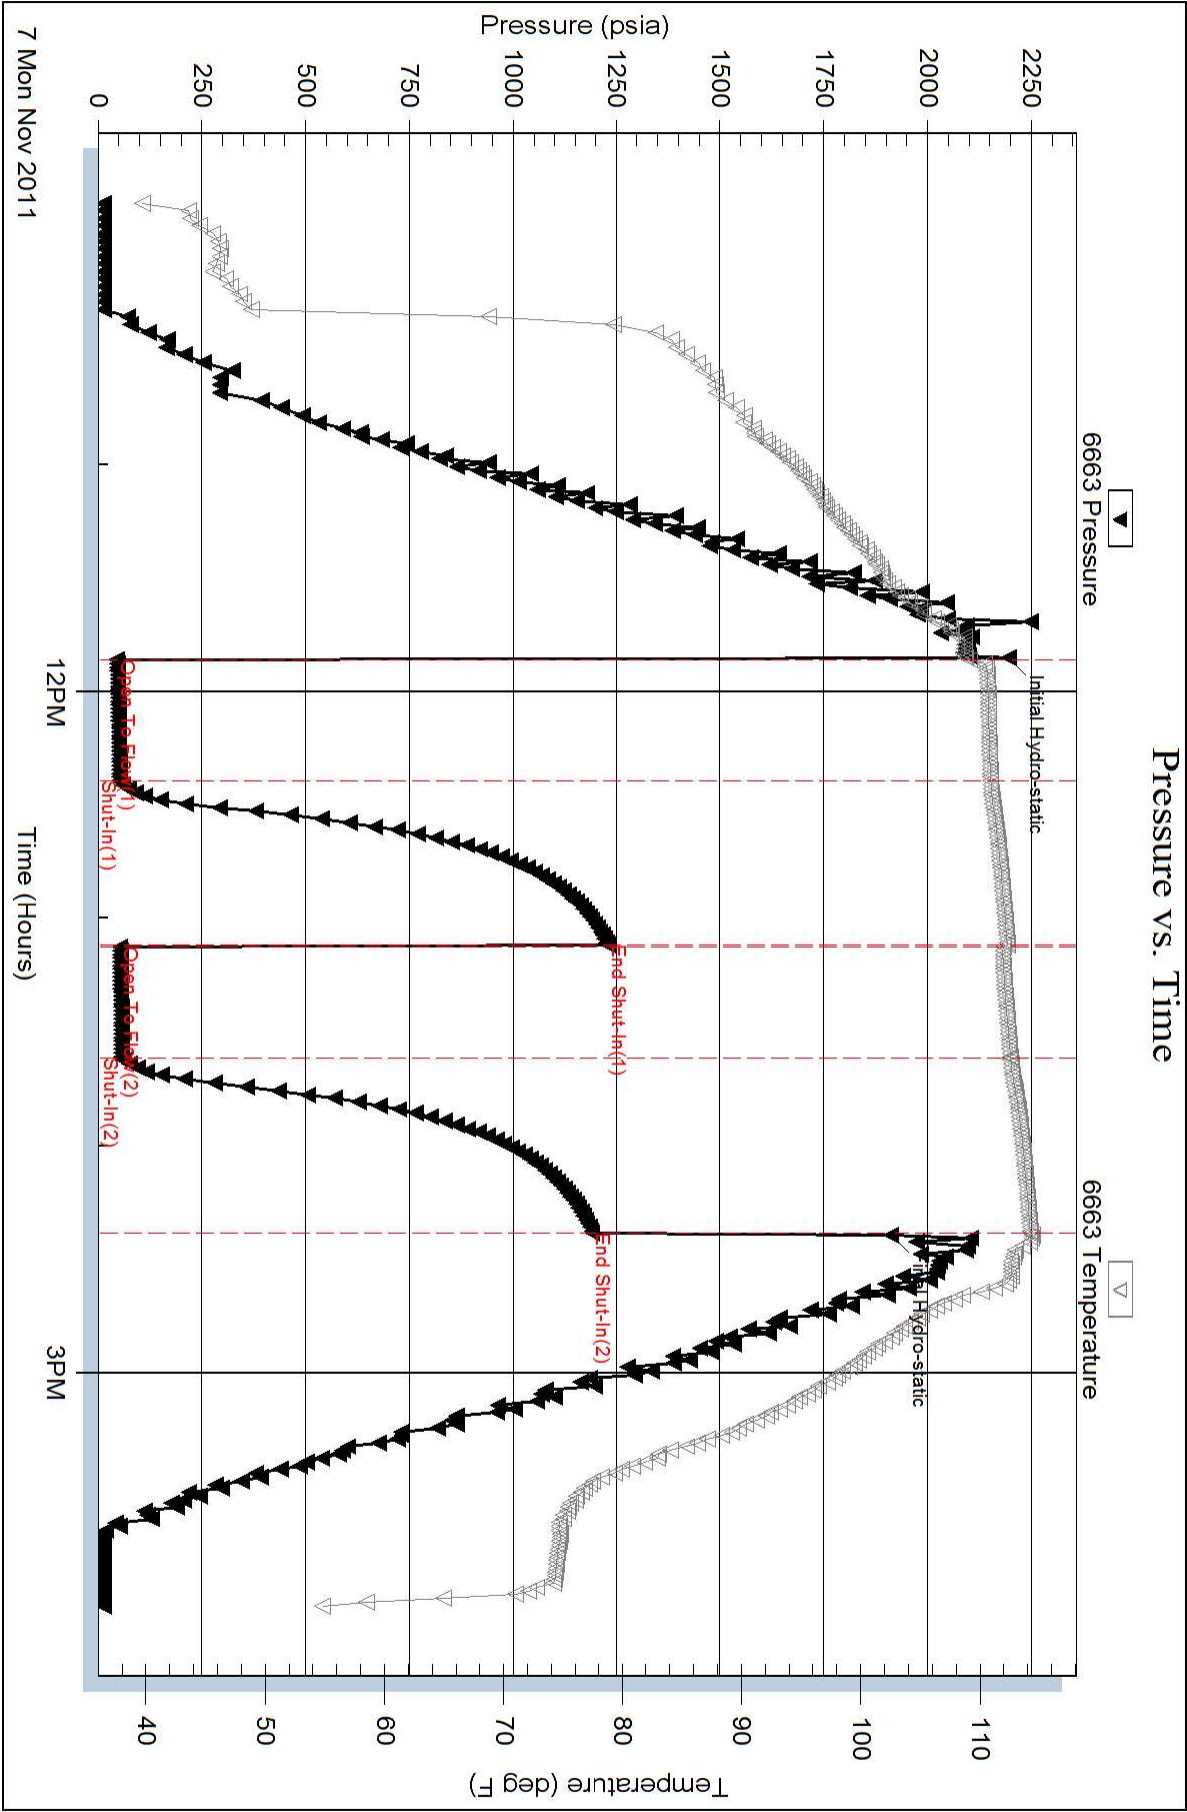



DRILL STEM TEST REPORT

Prepared For: **Ritchie Exploration**

8100 East 22nd Street North
#700 Wichita Kansas 67278

ATTN: Max Lovely

Van Eaton 10B

10-12s-31w-Gove

Start Date: 2011.11.09 @ 03:52:00


End Date: 2011.11.09 @ 09:21:00

Job Ticket #: 17233 DST #: 3

Superior Testers Enterprises LLC
PO Box 138 Great Bend KS 67530
1-800-792-6902

Printed: 2011.11.09 @ 10:12:04

Ritchie Exploration
10-12s-31w-Gove
Van Eaton 10B
DST # 3
Johnson
2011.11.09



DRILL STEM TEST REPORT

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17233

DST#: 3

ATTN: Max Lovely

Test Start: 2011.11.09 @ 03:52:00

GENERAL INFORMATION:

Formation: **Johnson**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 06:30:30

Time Test Ended: 09:21:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Dustin Ellis

Unit No: 3315-GB-225 miles

Interval: ft (KB) To ft (KB) (TVD)

Total Depth: 4599.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2969.00 ft (KB)

2960.00 ft (CF)

KB to GR/CF: 9.00 ft

Serial #: 6806 Inside

Press@RunDepth: psia @ 4595.00 ft (KB)

Start Date: 2011.11.09

End Date:

2011.11.09

Capacity: 5000.00 psia

Last Calib.: 2011.11.09

Start Time: 03:53:00


End Time:

09:21:00

Time On Btm: 2011.11.09 @ 06:30:00

Time Off Btm: 2011.11.09 @ 06:48:00

TEST COMMENT: 1st Open 15 minutes no blow then flushed the tool lost fluid we come out of hole then.

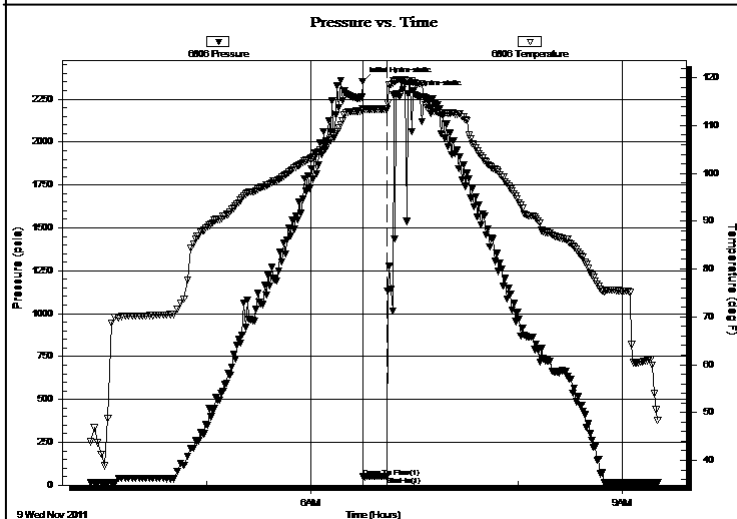

PRESSURE SUMMARY


Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	2352.50	113.49	Initial Hydro-static
1	48.71	113.33	Open To Flow (1)
14	49.98	113.46	Shut-In(1)
19	2274.66	119.28	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
2360.00	Mud 100%	27.92

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



DRILL STEM TEST REPORT

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17233

DST#: 3

ATTN: Max Lovely

Test Start: 2011.11.09 @ 03:52:00

GENERAL INFORMATION:

Formation: **Johnson**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 06:30:30

Time Test Ended: 09:21:00

Test Type: Conventional Bottom Hole (Initial)

Tester: Dustin Ellis

Unit No: 3315-GB-225 miles

Interval: ft (KB) To ft (KB) (TVD)

Total Depth: 4599.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2969.00 ft (KB)

2960.00 ft (CF)

KB to GR/CF: 9.00 ft

Serial #: 6663 Outside

Press@RunDepth: psia @ 4596.00 ft (KB)

Start Date: 2011.11.09

End Date:

2011.11.09

Capacity: 5000.00 psia

Last Calib.: 2011.11.09

Start Time: 03:53:00


End Time:

09:21:00

Time On Btm: 2011.11.09 @ 06:29:30

Time Off Btm: 2011.11.09 @ 06:47:30

TEST COMMENT: 1st Open 15 minutes no blow then flushed the tool lost fluid we come out of hole then.

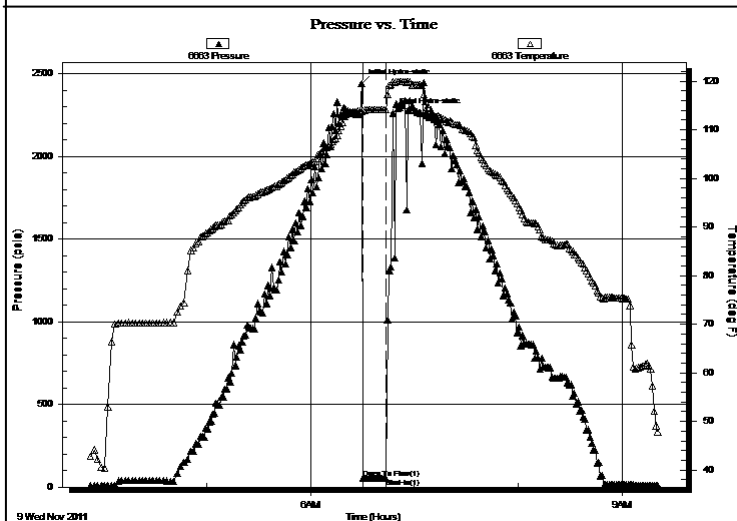

PRESSURE SUMMARY


Time (Min.)	Pressure (psia)	Temp (deg F)	Annotation
0	2441.47	113.76	Initial Hydro-static
1	52.28	113.91	Open To Flow (1)
14	52.43	114.08	Shut-In(1)
18	2262.76	119.91	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
2360.00	Mud 100%	27.92

Gas Rates

	Choke (inches)	Pressure (psia)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



DRILL STEM TEST REPORT

TOOL DIAGRAM

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17233

DST#: 3

ATTN: Max Lovely


Test Start: 2011.11.09 @ 03:52:00

Tool Information

Drill Pipe:	Length:	3995.00 ft	Diameter:	3.80 inches	Volume:	56.04 bbl	Tool Weight:	2000.00 lb
Heavy Wt. Pipe:	Length:	0.00 ft	Diameter:	0.00 inches	Volume:	0.00 bbl	Weight set on Packer:	20000.00 lb
Drill Collar:	Length:	569.00 ft	Diameter:	2.25 inches	Volume:	2.80 bbl	Weight to Pull Loose:	120000.0 lb
					Total Volume:	58.84 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:		28.00 ft					String Weight: Initial	62000.00 lb
Depth to Top Packer:		4564.00 ft					Final	70000.00 lb
Depth to Bottom Packer:		ft						
Interval between Packers:		35.00 ft						
Tool Length:		63.00 ft						
Number of Packers:		2	Diameter:	6.25 inches				

Tool Comments: Packers ripped off down the hole.

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Shut-In Tool	5.00			4541.00	
Hydrolic Tool	5.00			4546.00	
Jars	6.00			4552.00	
Safety Joint	2.00			4554.00	
Packer	5.00			4559.00	28.00 Bottom Of Top Packer
Packer	5.00			4564.00	
Perforations	30.00			4594.00	
Recorder	1.00	6806	Inside	4595.00	
Recorder	1.00	6663	Outside	4596.00	
Bull Plug	3.00			4599.00	35.00 Bottom Packers & Anchor
Total Tool Length:	63.00				



DRILL STEM TEST REPORT

FLUID SUMMARY

Ritchie Exploration

10-12s-31w-Gove

8100 East 22nd Street North
#700 Wichita Kansas 67278

Van Eaton 10B

Job Ticket: 17233

DST#: 3

ATTN: Max Lovely

Test Start: 2011.11.09 @ 03:52:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 58.00 sec/qt

Water Loss: 7.60 in³

Resistivity: ohm.m

Salinity: 2700.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psia

Oil API:

Water Salinity:

deg API

ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
2360.00	Mud 100%	27.921

Total Length: 2360.00 ft

Total Volume: 27.921 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


Serial #: 6806

Inside

Ritchie Exploration

Van Eaton 10B

DST Test Number: 3

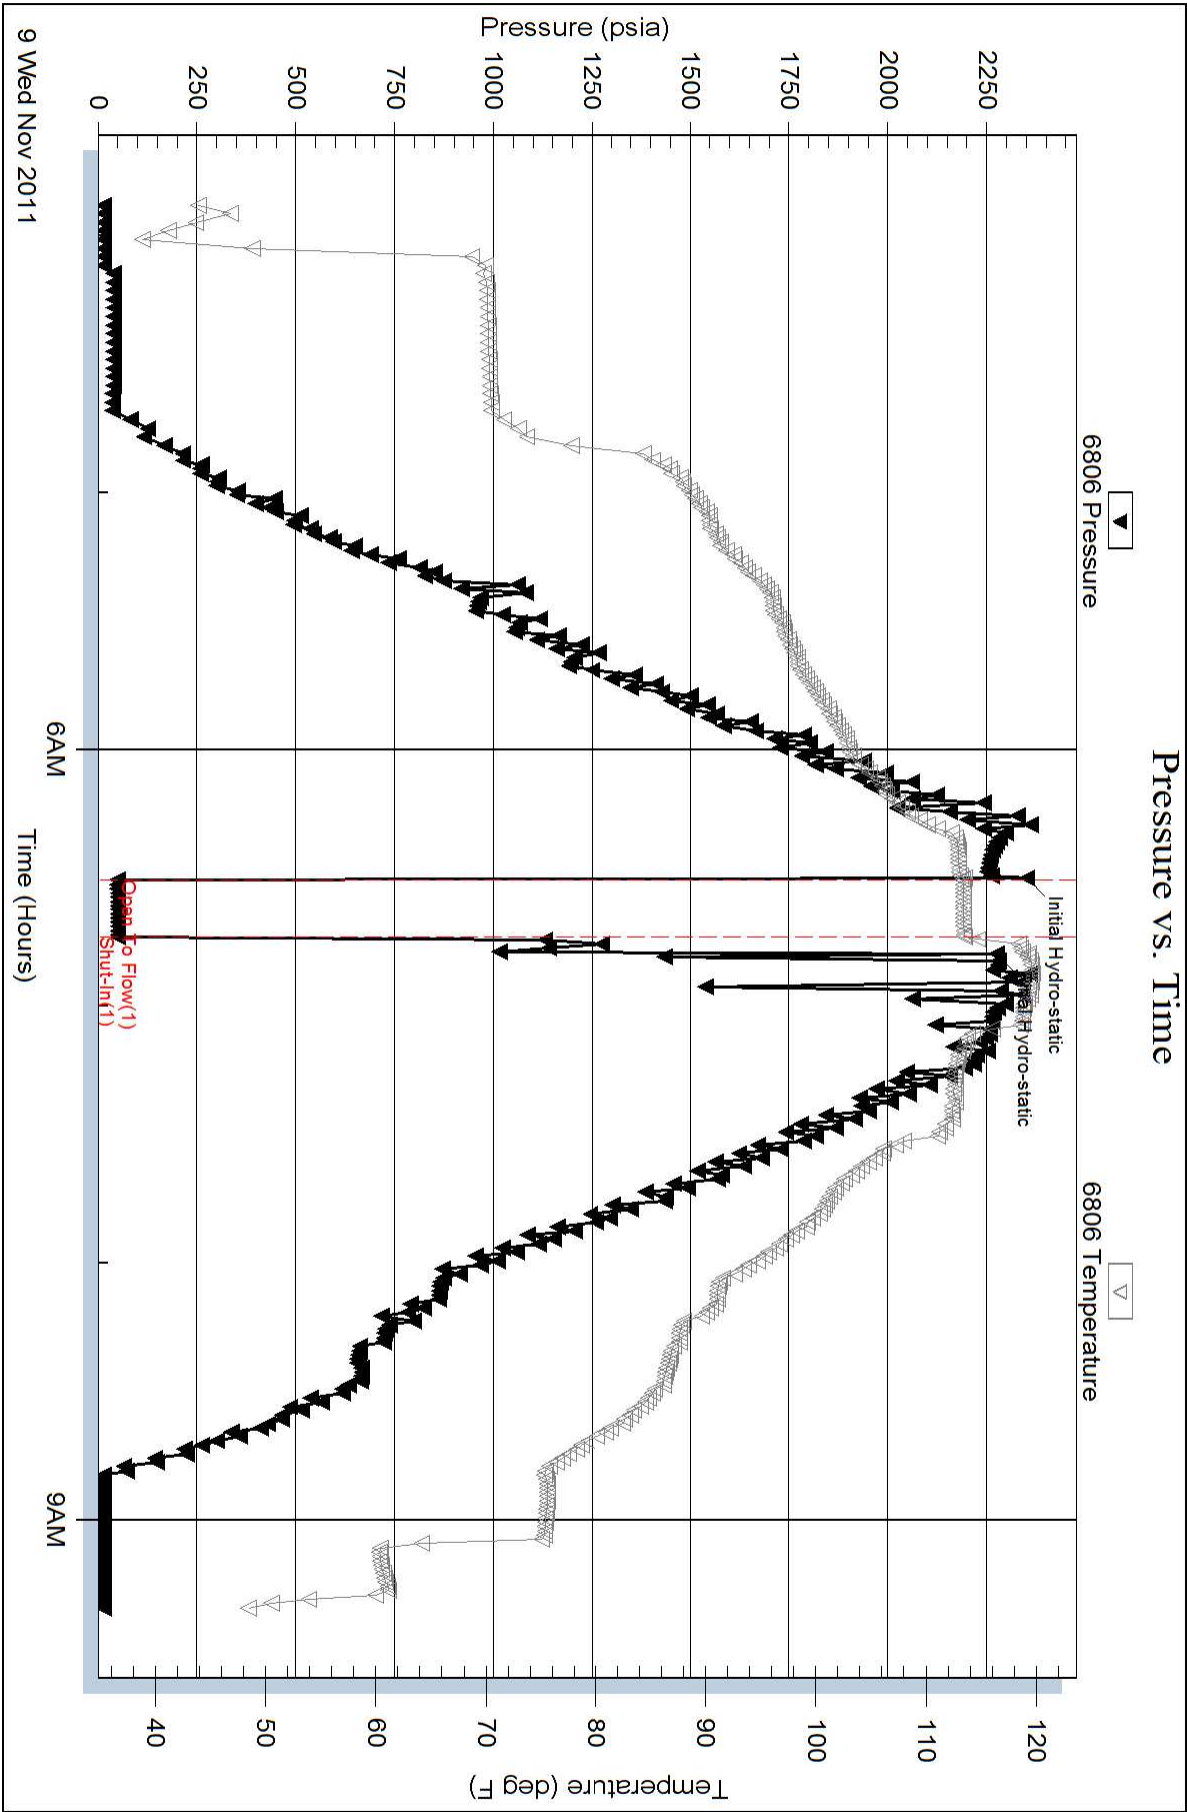

Serial #: 6663

Outside

Ritchie Exploration

Van Eaton 10B

DST Test Number: 3

Pressure vs. Time

