

Date 8-18-64

Ticket No. 3995

Company Solar Oil Co. Contractor Red Tiger Drlg. Co.

Well No. 1 Lease Dumler County Russell Sec. 29 Rg. 13 Twp. 15

Test No. 1 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 21' Depth Well 3005'

Interval Tested From 2984' To 3005'

Size Choke 5/8 Tool Open 70 min.

IBHP Shut in time 20 min. FBHP Shut in time 20 min.

Blow Weak thruout test

Recovery 125' Sl. Oil Cut water

Remarks _____

Approved Waite Tester Weathusin

K9S Dr.
5/3/2024


A. Initial Hyd. Pressure	<u>1549¹¹</u>
B. Final Hyd. Pressure	<u></u>
C. Initial BHP	<u>938¹¹</u>
D. Initial Flow Pressure	<u>29¹¹</u>
E. Final Flow Pressure	<u>89¹¹</u>
F. Final BHP	<u>853¹¹</u>



Sun DILWELL CEMENTING, INC.

POST OFFICE BOX 89
HAYS, KANSAS

3995

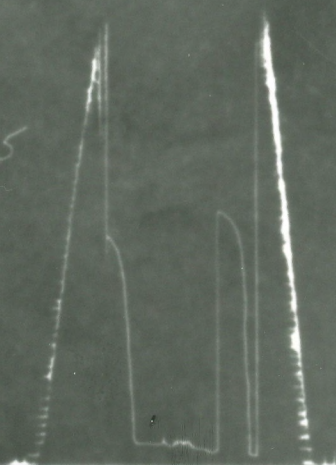

Date 8-19-64

Ticket No. 3996

Company Solar Cil Co. Contractor Red Tiger Drlg. Co.

Well No. 1 Lease Dumler County Russell Sec. 29 Rg. 13 Tw. 15

Test No. 2 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 33' Depth Well 3125'

Interval Tested From 3092' To 3125'

Size Choke 5/8 Tool Open 70 min.

IBHP Shut in time 20 min. FBHP Shut in time 20 min.

Blow Weak thruout test

Recovery 340' Muddy salt water

Remarks _____

Approved Waite Tester Nesthusin

A. Initial Hyd. Pressure 1679#
B. Final Hyd. Pressure _____
C. Initial BHP 743#
D. Initial Flow Pressure 51#
E. Final Flow Pressure 168#
F. Final BHP 543#

Sun




OILWELL CEMENTING, INC.

POST OFFICE BOX 89

HAYS, KANSAS

3996

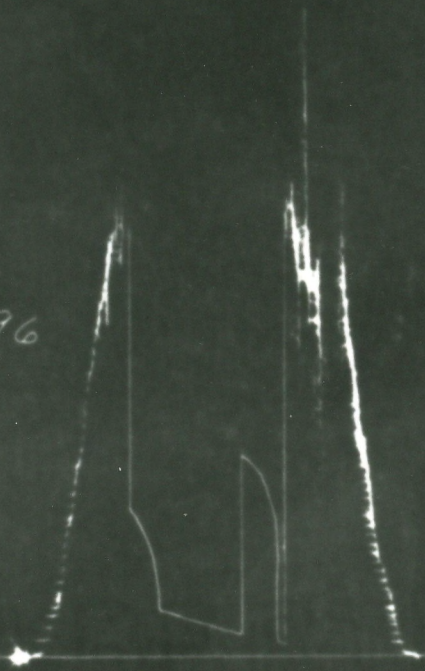

Date 8 - 29-64

Ticket No. 3997

Company Solar oil Co. Contractor Red Tiger Drlg. Co.

Well No. 1 Lease Dumler County Russell Sec. 29 Rg. 13 Tw. 15

Test No. 3 Size Hole 7 7/8 Tool Joint 1 1/2

Anchor Length 53' Depth Well 3295'

Interval Tested From 3242' To 3295'

Size Choke 5/8 Tool Open 60 min.

IBHP Shut in time 20 min. FBHP Shut in time 20 min.

Blow Fair thruout test

Recovery 180' Muddy Salt water

Remarks _____

Approved Waite Tester Westhusin


A. Initial Hyd. Pressure	1796#
B. Final Hyd. Pressure	
C. Initial BHP	923#
D. Initial Flow Pressure	54#
E. Final Flow Pressure	125#
F. Final BHP	826#



Sun OILWELL CEMENTING, INC.

POST OFFICE BOX 89
HAYS, KANSAS

3997

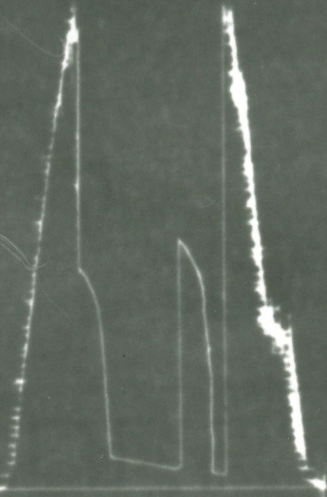

Date 8-21-64

Ticket No. 3998

Company Solar Oil Co. Contractor Red Tiger Drilg. Co.

Well No. 1 Lease Dumler County Russell Sec. 29 Rg. 13 Tw. 15

Test No. 4 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 32' Depth Well 3361'

Interval Tested From 3329' To 3361'

Size Choke 5/8 Tool Open 30 min.

IBHP Shut in time 20 min. FBHP Shut in time 20 min.

Blow Very weak for 6 min. flushed tool weak surge

Recovery 12' Drilg. Mud

Remarks _____

Approved Waite Tester Westhusin

A. Initial Hyd. Pressure 1799[#]
B. Final Hyd. Pressure _____
C. Initial BHP 108[#]
D. Initial Flow Pressure 38[#]
E. Final Flow Pressure 38[#]
F. Final BHP 61[#]

Sun




OSWELL CEMENTING, INC.

POST OFFICE BOX 89

HAYS, KANSAS

3998

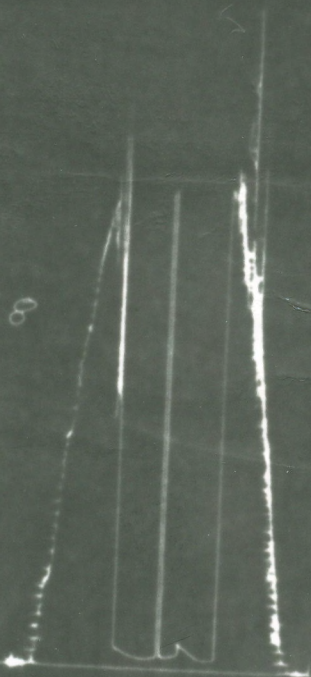

Date 8-21-64

Ticket No. 3999

Company Solar Cil Co. Contractor Red Tiger Drlg. Co.

Well No. 1 Lease Dumler County Russell Sec. 29 Rg. 13 Tw. 15

Test No. 5 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 13' Depth Well 3379'

Interval Tested From 3366' To 3379'

Size Choke 5/8 Tool Open 40 min.

IBHP Shut in time 20 min. FBHP Shut in time 20 min.

Blow Fairly strong thru cut test

Recovery 750' Sulfur water

Remarks _____

Approved Waite Tester Westhusin

A. Initial Hyd. Pressure	<u>1803#</u>
B. Final Hyd. Pressure	<u> </u>
C. Initial BHP	<u>982#</u>
D. Initial Flow Pressure	<u>102#</u>
E. Final Flow Pressure	<u>333#</u>
F. Final BHP	<u>96#</u>

Sun



OILWELL CEMENTING, INC.

POST OFFICE BOX 89

HAYS, KANSAS

3999

