




DRILL STEM TEST REPORT

Prepared for

Starr F Schlobohm
47 Micavanic Rd #3D
Sanbornville, NH 03872-3787

Staab
9-13S-17W
Ellis Co Kansas

Trilobite Testing, Inc
PO Box 362 - Hays, Kansas - 67601
ph: 785-625-4778 fax: 785-625-5620
e-mail: trilobite@eaglecom.net



TRILOBITE TESTING, INC.

DRILL STEM TEST REPORT

Starr F Schlobohm

47 Micavanic Rd #3D

Sanbornville, NH 03872-3787

Well name#:	Staab	Date:	8/27/2003
Location#:	9-13S-17W Ellis Co Kansas	Ticket #:	17137
		DST#	1

General Informaion:


Formation:	Arbuckle	Test Type:	Conventional	BHT:	104
Interval:	3537-3595	Tester:	Gary Pevoteaux	OIL API:	
Total Depth:	3595	Elevation:	2033 ft(KB)	H2O Salinity:	
Hole Diameter:	7 7/8"		2028 ft(CF)		

Start Data:	8/27/2003	Tool Weight:	2100	Mud Type:	Chemical
Start Time:	12:30:00	Weight Set on Packers:	20000	Mud Weight:	9
Time tool opened:	16:00:00	Weight to Pull Loose:	63000	Viscosity:	50
Time Off Btm:	17:10:00	Initial String Weight:	42000	Water Loss:	8.8
End Date:	8/27/03	Final String Weight:	42000	Resistivity;	
End Time:	19:40:00	Drill Pipe Length:	3548	Salinity:	
		Drill Collar Length:			
		Wt. Pipe Length:			

Test Comment:	IF: Weak blow. 1/4" Dead in 16 min. ISI: No blow. FF: No blow. FSI: None
Recovery Length(ft):	5 Drilling Mud

Gas Volume Report

Recorder #:	13788	Min:	Ins. Of water	Orifice	MCF/D
Pressure Summary:	Time:(min)		PSIG	size	
Initial Hydro-static:	1730				
Open to Flow (1):	35 30				
Shut-in (1):	35 30				
End Shut-in (1):	116				
Open to Flow (2):	38 10				
Shut-in (2):	38 none				
End Shut-in (2):	none				
Final Hydro-static:	1696				



**TRILOBITE
TESTING INC.**

P.O. Box 362 • Hays, Kansas 67601

No 17137

12/02

Test Ticket

Well Name & No. STAAB Test No. 1 Date 8-27-03
Company Starr F. Scholobohm Zone Tested Arbuckle
Address 47 Michaumie Rd. #30, Sanbornville, N.H. Elevation 2033 KB 2028 GL
Co. Rep / Geo. Dave Mummakes Cont. Vonfeldt Drilling Est. Ft. of Pay _____ Por. _____ %
Location: Sec. 9 Twp. 13 S Rge. 17 W Co. Ellis State Ko.
No. of Copies 5 Distribution Sheet (Y, N) N Turnkey (Y, N) _____ Evaluation (Y, N) _____

Interval Tested 3537 - 3595' Initial Str Wt./Lbs. 42,000 Unseated Str Wt./Lbs. 42,000
Anchor Length 58' Wt. Set Lbs. 20,000 Wt. Pulled Loose/Lbs. 63,000
Top Packer Depth 3532' Tool Weight 2100 lb
Bottom Packer Depth 3537' Hole Size 7 7/8" ✓ Rubber Size 6 3/4" ✓
Total Depth 3595' Wt. Pipe Run None Drill Collar Run None
Mud Wt. 9.0 LCM 4# Vis. 50 WL 8.8 sec Drill Pipe Size 4 1/2" x 11' Ft. Run 3548'
Blow Description IF: Work below. 1/4" Dead in 16 mins. IS: No blow.

FF: No blow.

Recovery - Total Feet 5 GIP 0 Ft. in DC 0 Ft. in DP 5
Rec. 5 Feet of Dreg. Mud.
Rec. _____ Feet of _____
Rec. _____ Feet of _____
Rec. _____ Feet of _____
Rec. _____ Feet of _____
BHT 104 °F Gravity N/A °API D @ 2 °F Corrected Gravity N/A °API
RW P.C. @ _____ °F Chlorides 6,000 ppm Recovery _____ Chlorides 6,000 ppm System

	AK-1	Alpine			
(A) Initial Hydrostatic Mud	<u>1730</u>	PSI	Recorder No.	<u>13788</u>	Test <u>✓ 760 90</u>
(B) First Initial Flow Pressure	<u>35</u>	PSI	(depth)	<u>3587'</u>	Elec. Rec. _____
(C) First Final Flow Pressure	<u>35</u>	PSI	Recorder No.	<u>13212</u>	Jars _____
(D) Initial Shut-In Pressure	<u>116</u>	PSI	(depth)	<u>3592'</u>	Safety Jt. _____
(E) Second Initial Flow Pressure	<u>38</u>	PSI	Recorder No.	<u>_____</u>	Circ Sub _____
(F) Second Final Flow Pressure	<u>38</u>	PSI	(depth)	<u>_____</u>	Sampler _____
(G) Final Shut-In Pressure	<u>None</u>	PSI	Initial Opening	<u>30</u>	Straddle _____
(Q) Final Hydrostatic Mud	<u>1696</u>	PSI	Initial Shut-In	<u>30</u>	Ext. Packer _____
			Final Flow	<u>10</u>	Shale Packer _____
			Final Shut-In	<u>None</u>	Mileage <u>✓ 15</u>
			T-On Location	<u>1130</u>	Sub Total: _____
			T-Started	<u>1230</u>	Std. By _____
			T-Open	<u>1600</u>	Other _____
			T-Pulled	<u>1710</u>	Total: <u>✓ 71500</u>
			T-Out	<u>1940</u>	

TRILOBITE TESTING INC. SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND OF THE PROPERTY OR PERSONNEL OF THE ONE FOR WHOM A TEST IS MADE, OR FOR ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH THE USE OF ITS EQUIPMENT, OR ITS STATEMENTS OR OPINION CONCERNING THE RESULTS OF ANY TEST. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT COST BY THE PARTY FOR WHOM THE TEST IS MADE.

Approved By [Signature]
Our Representative Cory Pivota

CHART PAGE

This is a photocopy of the actual AK-1 recorder chart

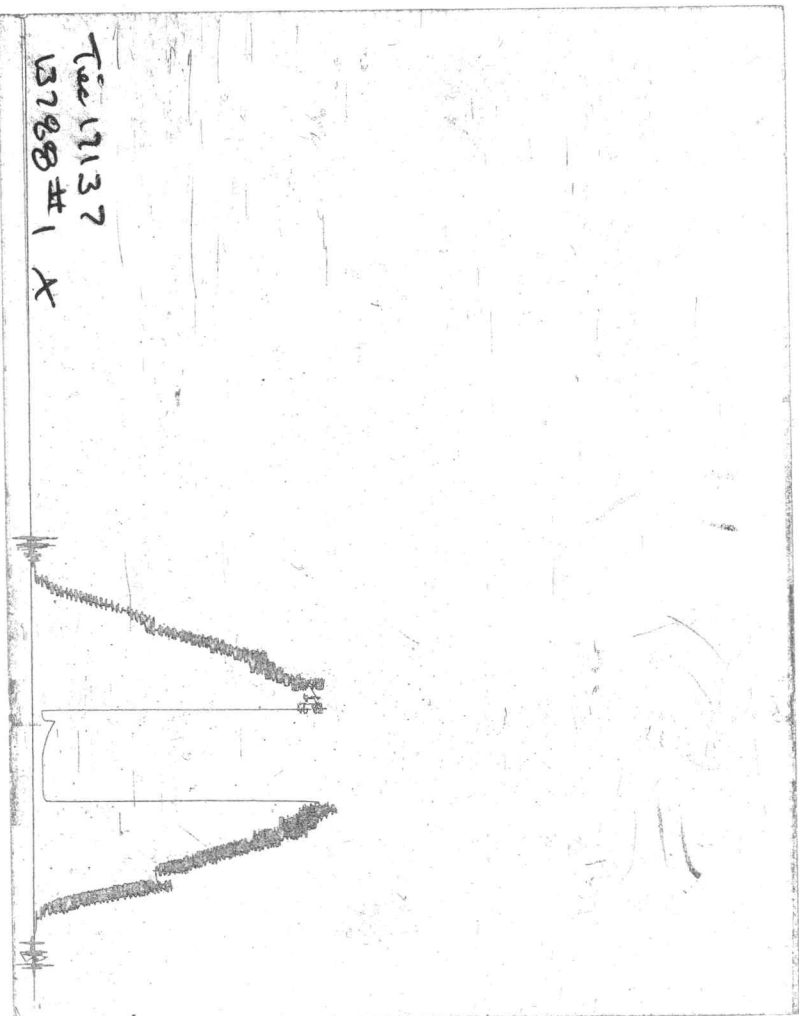


CHART PAGE

This is a photocopy of the actual AK-1 recorder chart

