




OIL WELL CEMENTING INC.

Date 8-11-68

DRILL STEM TEST RECOVERY REPORT

Ticket No. 5846

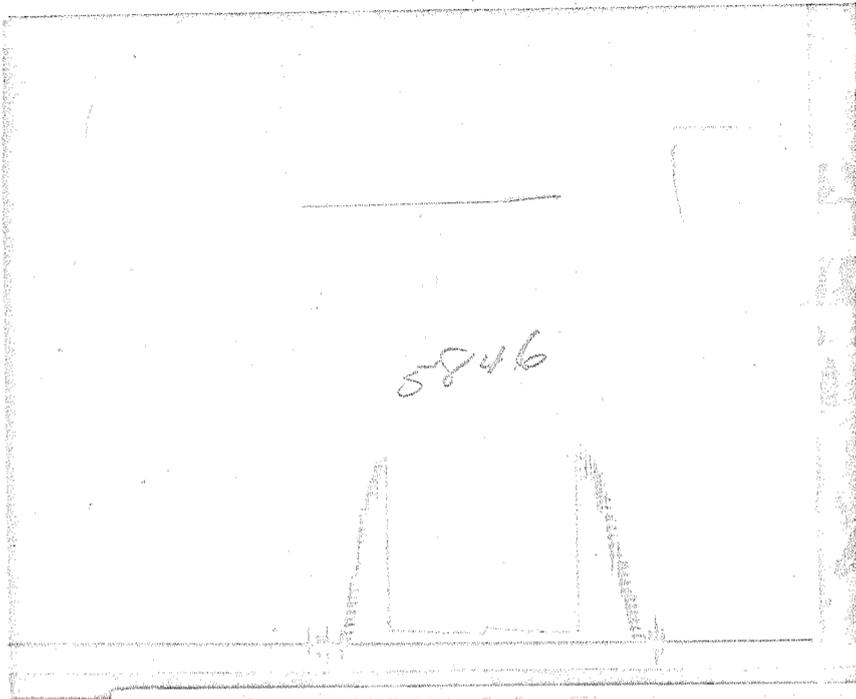

Company Ash & American Oil Co. Contractor American Drlg Co.

Well No. 3 Lease Krathy County Ellsworth Sec. 20 Twp 14 Rng 10

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 Xh

Interval Tested From 1306 To 1350 Depth of Well 1350 Size Choke 5/8

Fluid Recovered In Flexweight Temp. 85 Elev. 1676 KB

Initial Hyd. 716 P.S.I. Final Hyd. 716 P.S.I.

First Initial Flow Pressure 33 P.S.I. Opened Tool 2:15 ~~###~~ P.M.

First Final Flow Pressure 33 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 58 P.S.I. Initial Closed-in Pres. 45 Min.

Second Initial Flow Pressure 33 P.S.I. Second Flow Pres. 30 Min.

Second Final Flow Pressure 33 P.S.I. Final Closed-in Pres. 45 Min.

Final Closed-in Pressure 41 P.S.I.

Blow Very weak thru-out test

Recovery 5' Gas & oil cut mud slight show of oil

Remarks

Approved By Stephenson Tester Lewis
