



DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

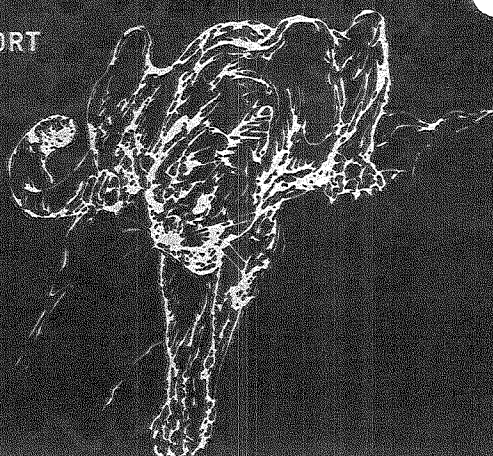

Date 8-14-71

Ticket No. 318

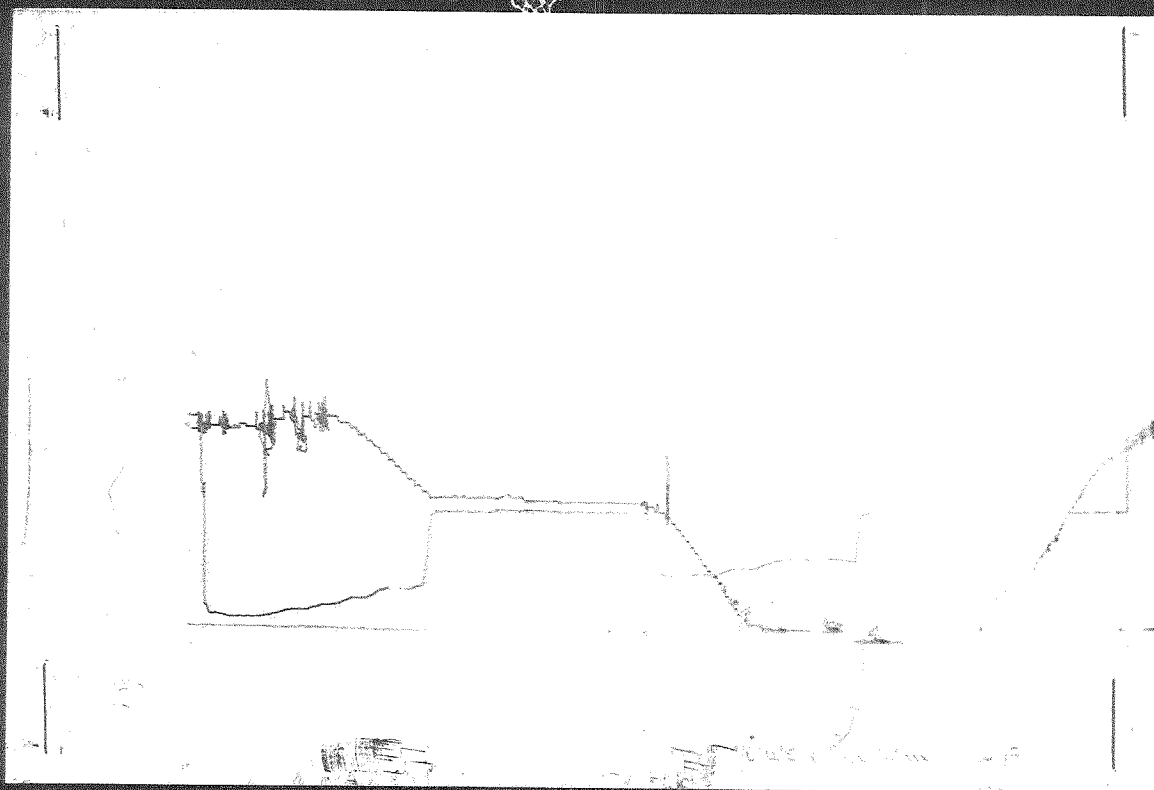

Company INTERNATIONAL RESOURCES CORP. Contractor H. 30- DRILL CO.
 Well No. A-1 Lease BAKER County ELLSWORTH Sec 16 Rg 14 Twp 10
 Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 P.H.
 Interval Tested From 2438 To 2470 Depth of Well 2470 Size Choke 1/2
 Fluid Recovered In FLECKWIGHT Temp. 94 Elev. 1724 K.B.
 Initial Hyd. _____ P.S.I. Final Hyd. _____ P.S.I.
 First Initial Flow Pressure 93 P.S.I. Opened Tool 5:45 A.M./P.M.
 First Final Flow Pressure 375 P.S.I. First Flow Pres. 60 Min.
 Initial Closed-in Pressure 810 P.S.I. Initial Closed-in Pres. 60 Min.
 Second Initial Flow Pressure 395 P.S.I. Second Flow Pres. 60 Min.
 Second Final Flow Pressure 460 P.S.I. Final Closed-in Pres. 60 Min.
 Final Closed-in Pressure 810 P.S.I.
 Blow STRONG BLOW. GAS TO SURFACE IN 2 1/2 MIN. T.S.T.M.
 Recovery FLOVED OIL IN 1 HR. 20 MIN.

Remarks

Approved By


DICK FOLLY

Tester

ED PHILBORN


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

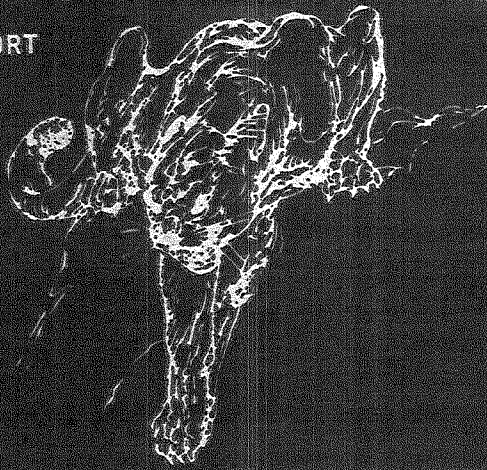

Date 8-15-71

Ticket No. 319

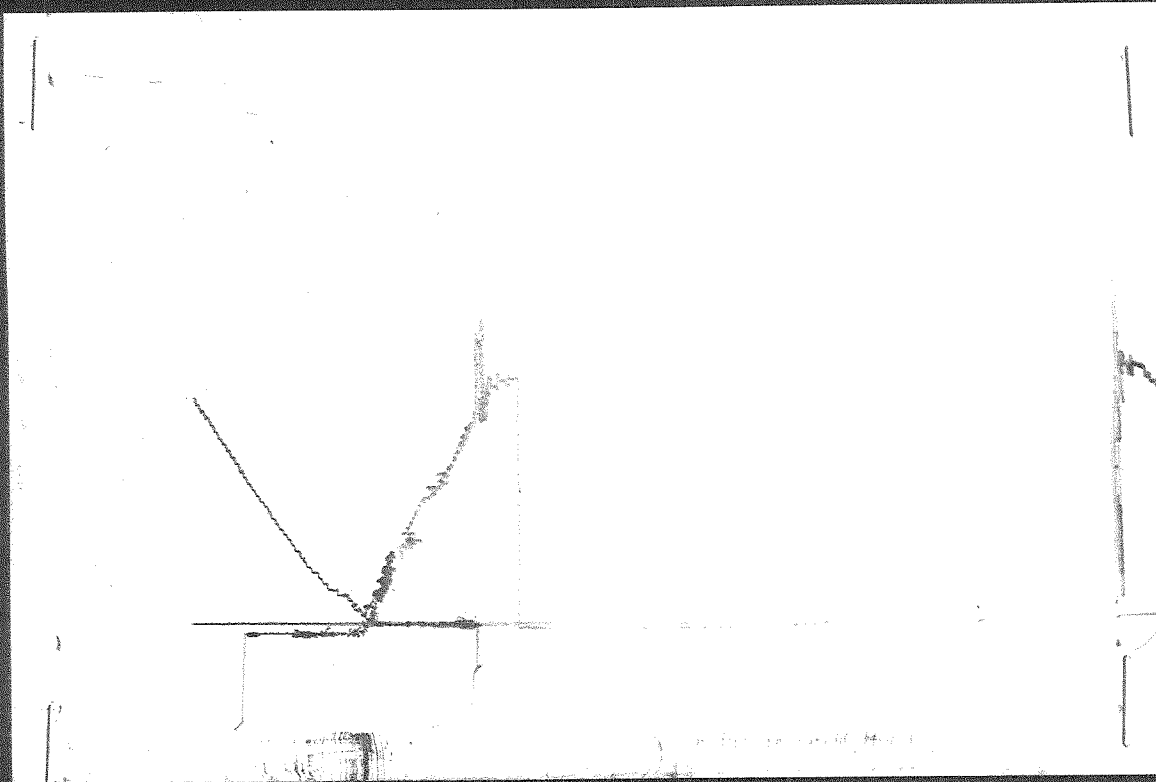

Company INTERNATIONAL RESOURCES CORP. Contractor H -30- DRILL CO.
 Well No. A-1 Lease BAKER County ELLSWORTH Sec. 16 Rg. 14 Twp. 10
 Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 F.H.
 Interval Tested From 2340 To 2369 Depth of Well 2369 Size Choke 1/2
 Fluid Recovered In FLEXWEIGHT Temp. 101 Elev. _____
 Initial Hyd. _____ P.S.I. Final Hyd. _____ P.S.I.
 First Initial Flow Pressure 10 P.S.I. Opened Tool 7:25 4 M / P.M.
 First Final Flow Pressure 10 P.S.I. First Flow Pres. 60 Min.
 Initial Closed-in Pressure 130 P.S.I. Initial Closed-in Pres. 60 Min.
 Second Initial Flow Pressure 10 P.S.I. Second Flow Pres. 240 Min.
 Second Final Flow Pressure 10 P.S.I. Final Closed-in Pres. 60 Min.
 Final Closed-in Pressure 130 P.S.I.
 Blow WEAK TO FAIR BLOW ON INIT. FAIR TO STRONG ON FINAL FLOW.


Recovery 240 FT. GAS IN PIPE.
30 FT H.O.& G.G.M.
30 FT. BLACK MUDDY CASSY OILY EMULSION.

Remarks

Approved By DICK TOLAY Tester ED PHILBORN


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

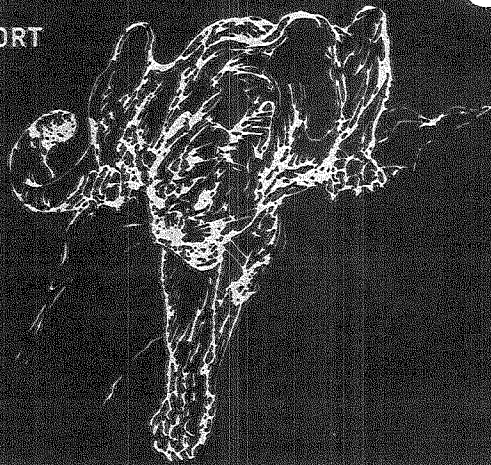

Date 8-16-71

Ticket No. 320

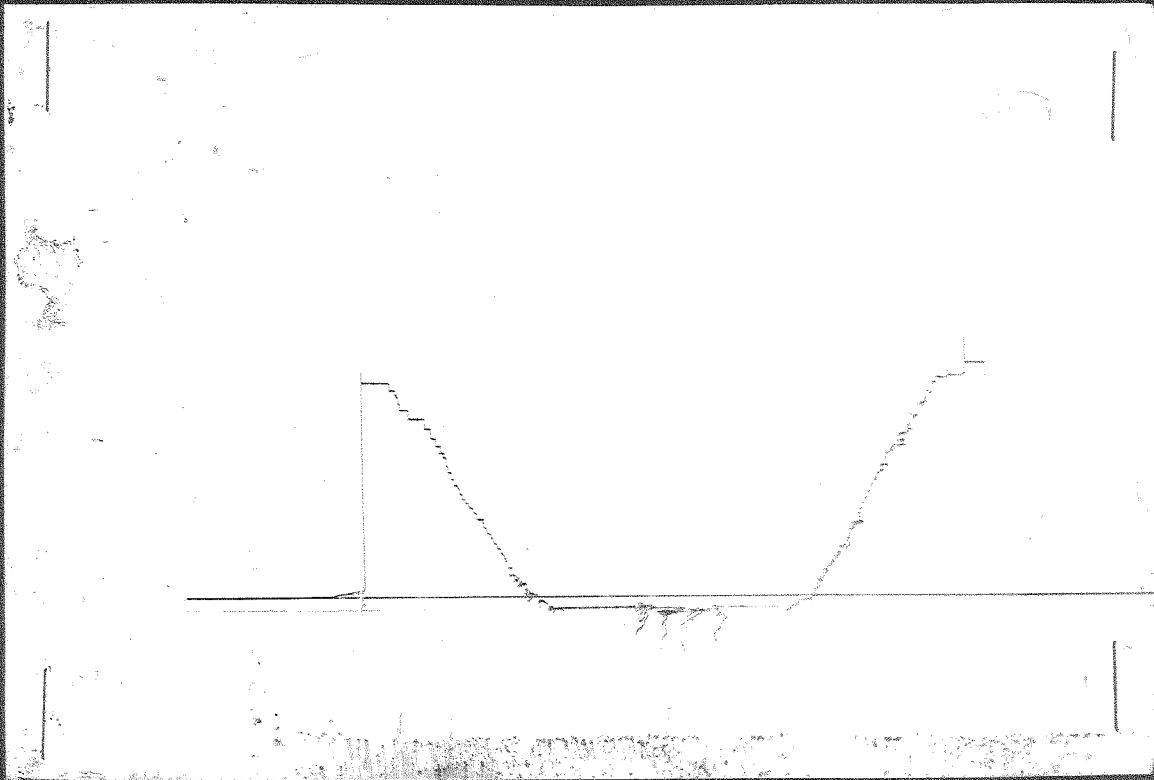

Company INTERNATIONAL RESOURCES CORP. Contractor H-30-DRILL CO.
 Well No. A-1 Lease BAKER County ELLISWORTH Sec 16 Rg 14 Twp 10
 Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 P.H.
 Interval Tested From 2826 To 2836 Depth of Well 2836 Size Choke 1/2
 Fluid Recovered In FLEX/WEIGHT Temp. 102 Elev. _____
 Initial Hyd. _____ P.S.I. Final Hyd. _____ P.S.I.
 First Initial Flow Pressure 20 P.S.I. Opened Tool 4:53 A.M./P.M.
 First Final Flow Pressure 20 P.S.I. First Flow Pres. 30 Min.
 Initial Closed-in Pressure 20 P.S.I. Initial Closed-in Pres. 30 Min.
 Second Initial Flow Pressure 20 P.S.I. Second Flow Pres. 30 Min.
 Second Final Flow Pressure 20 P.S.I. Final Closed-in Pres. 30 Min.
 Final Closed-in Pressure 20 P.S.I.
 Blow VERY WEAK BLOW THRU INIT.

Recovery 10 FT. WATERY DRILL MUD.

Remarks _____

Approved By DICK FOLEY Tester ED PHILBERT
