


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

Date 11-23-70

Ticket No. 230

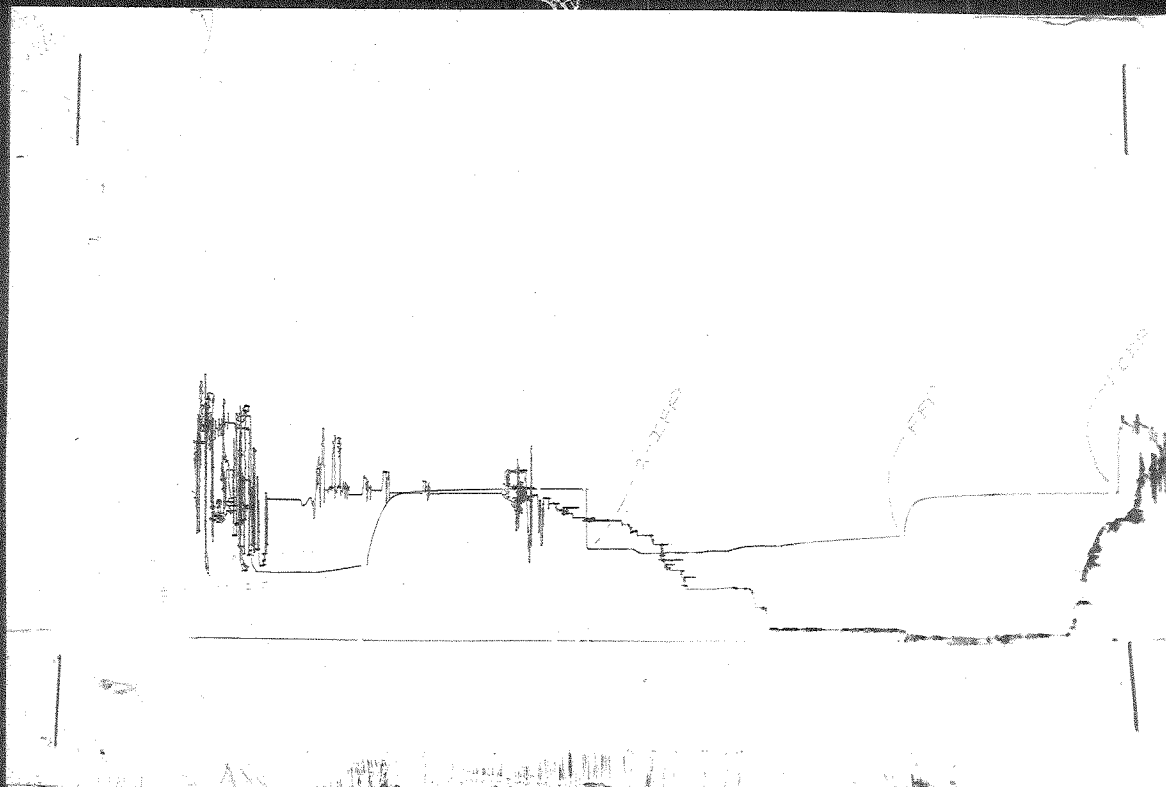

Company AMERICAN DRILLING CO. NATURAL RECOUPERS AMERICAN DRILLING CO.

Well No. 1 Lease BAKER County ELIZABETH Sec. 16 R. 10 Twp. 14

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 44 XH

Interval Tested From 2449 To 2480 Depth of Well 2480 Size Choke 1

Fluid Recovered In FLEXFIGHT Temp. 93 Elev.

Initial Hyd. 1590 P.S.I. Final Hyd. 1590 P.S.I.

First Initial Flow Pressure 470 P.S.I. Opened Tool 12:35 XX P.M.

First Final Flow Pressure 470 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 1080 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure 730 P.S.I. Second Flow Pres. 90 Min.

Second Final Flow Pressure 730 P.S.I. Final Closed-in Pres. 60 Min.

Final Closed-in Pressure 1030 P.S.I.

Blow STRONG BLOW THRU-OUT TEST

Recovery GAS TO SURFACE IN 11 MIN.

1600 FT. GASSY MUDDY OIL

NO WATER


Remarks

Approved By RICHARD M. FOLEY

Tester ED PHILBORN


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

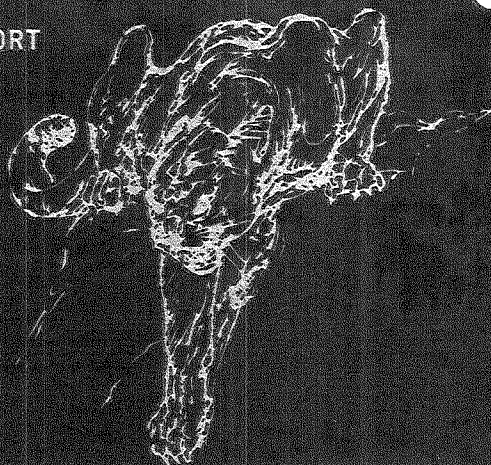

Date 11-23-70

Ticket No. 231

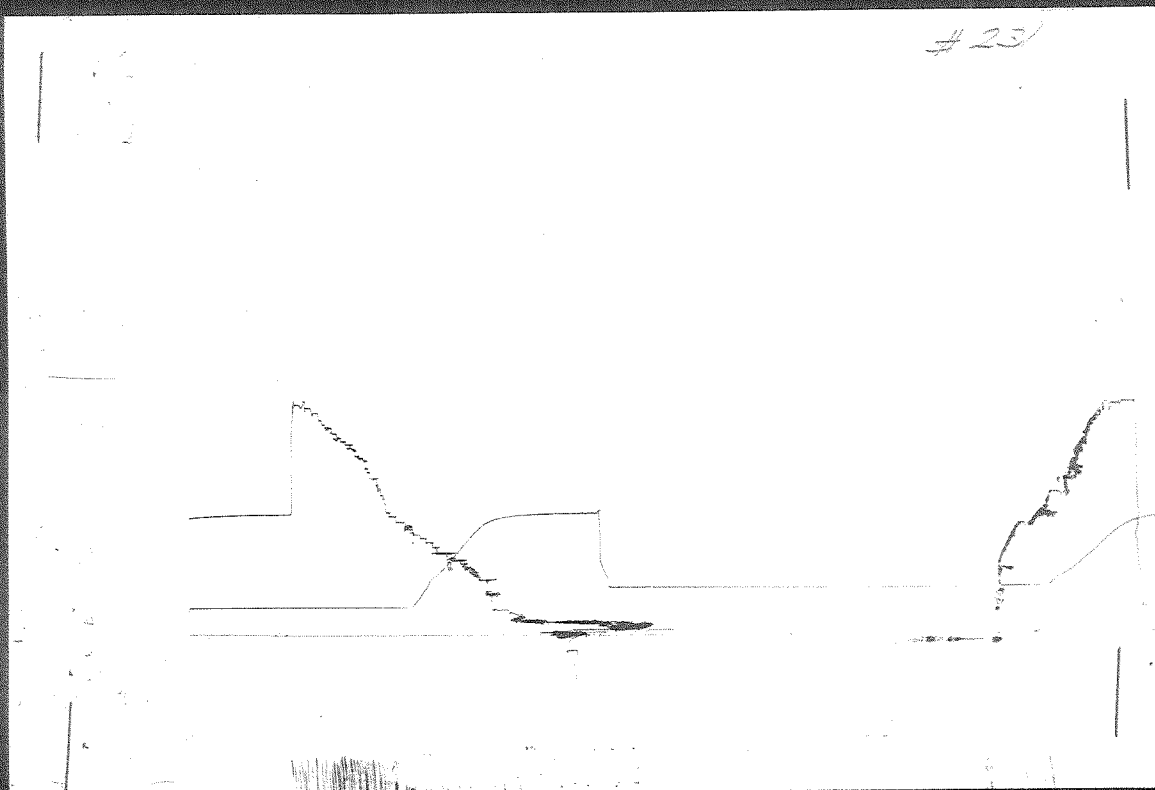

Company AMERICAN DRILG. CO. & NATURAL RESOURCES AMERICAN DRILG. CO.

Well No. 1 Lease BAKER County ELLSWORTH Sec. 16 Rg. 10 Twp. 14

Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 XH

Interval Tested From 2842 To 2870 Depth of Well 2870 Size Choke 1/2

Fluid Recovered In PLEXWEIGHT Temp. 98 Elev. _____

Initial Hyd.	~~XXXX~~ 1710	PSI	Final Hyd.	1710	PSI
First Initial Flow Pressure	110	PSI	Opened Tool	2:35	A.M. ~~XXX~~
First Final Flow Pressure	110	PSI	First Flow Pres.	60	Min.
Initial Closed-in Pressure	845	PSI	Initial Closed-in Pres.	60	Min.
Second Initial Flow Pressure	275	PSI	Second Flow Pres.	120	Min.
Second Final Flow Pressure	275	PSI	Final Closed-in Pres.	60	Min.
Final Closed-in Pressure	845	PSI			

Blow WEAK INCREASING TO STRONG THRU-OUT TEST

Recovery 1100 FT. GAS IN PIPE

160FT. VERY HEAVY MUDDY & GASSY OIL


NO WATER

Remarks _____

Approved By RICHARD M. FOLEY Tester ED PHILBERN


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

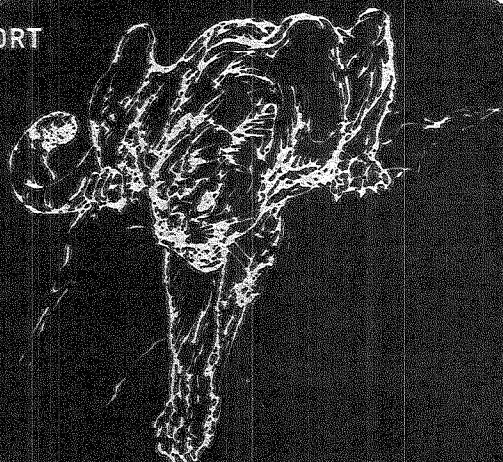

Date 11-23-70

Ticket No. 232

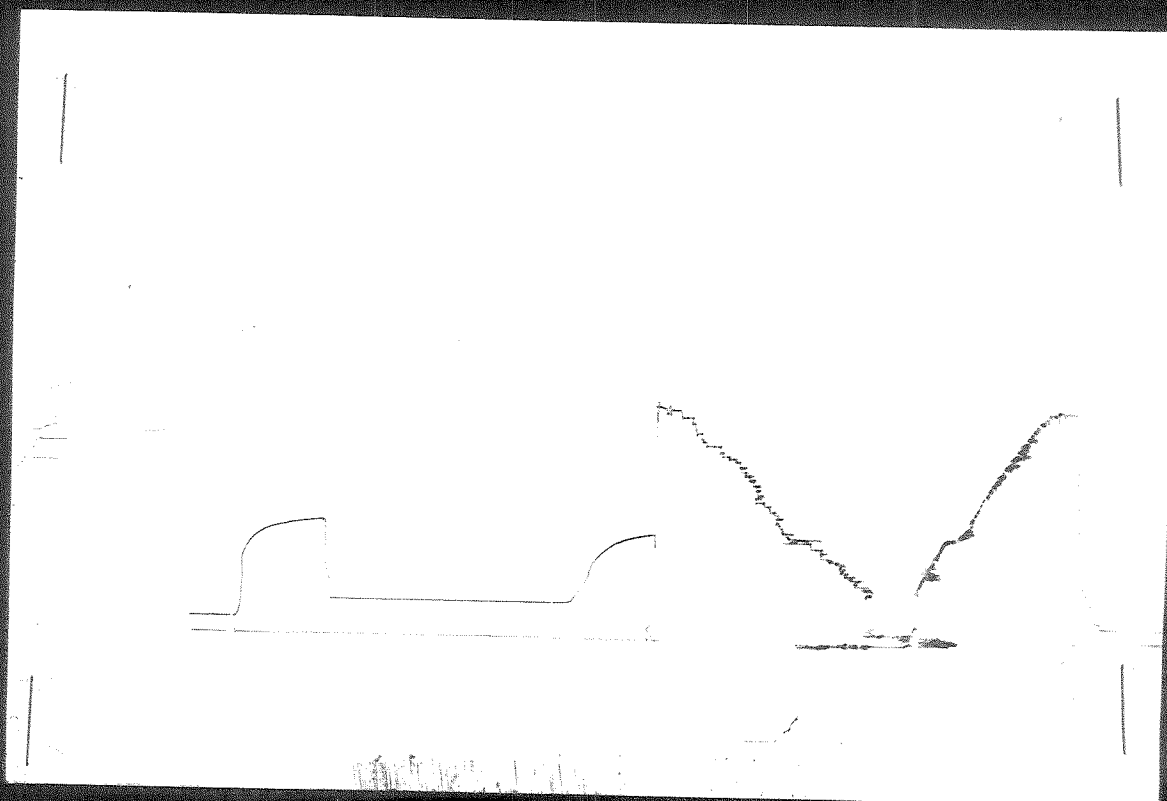

Company AMERICAN DRILG. CO. & NATURAL RES. Contractor AMERICAN DRILG. CO.
 Well No. 1 Lease BAKER County ELLISWORTH Sec. 16 Rg 10 Twp 14
 Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 XH
 Interval Tested From 2894 To 2924 Depth of Well 2924 Size Choke 1/2
 Fluid Recovered In FLEXWEIGHT Temp. 98 Elev. _____
 Initial Hyd. 1740 P.S.I. Final Hyd. 1740 P.S.I.
 First Initial Flow Pressure 50 P.S.I. Opened Tool 6:35 ~~XXX~~ P.M.
 First Final Flow Pressure 50 P.S.I. First Flow Pres. 30 Min.
 Initial Closed-in Pressure 805 P.S.I. Initial Closed-in Pres. 30 Min.
 Second Initial Flow Pressure 190 P.S.I. Second Flow Pres. 60 Min.
 Second Final Flow Pressure 190 P.S.I. Final Closed-in Pres. 30 Min.
 Final Closed-in Pressure 720 P.S.I.
 Blow WET STEADY BLOW THRU-TEST

Recovery 45FT. VERY SLIGHT OIL CUT MUD
WITH FREE OIL IN TOP OF TEST TOOL


Remarks _____

Approved By RICHARD M. FOLEY

Tester ED PHILBORN


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

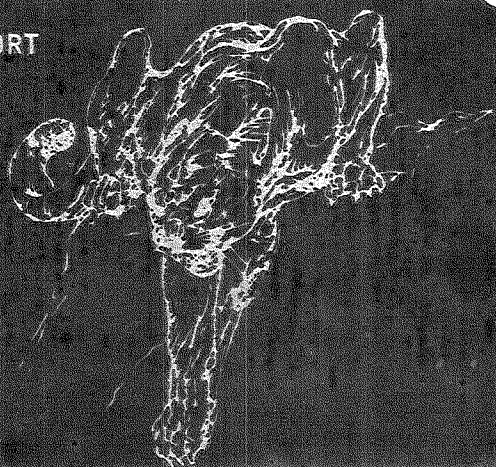

Date 11-23-70

Ticket No. 233

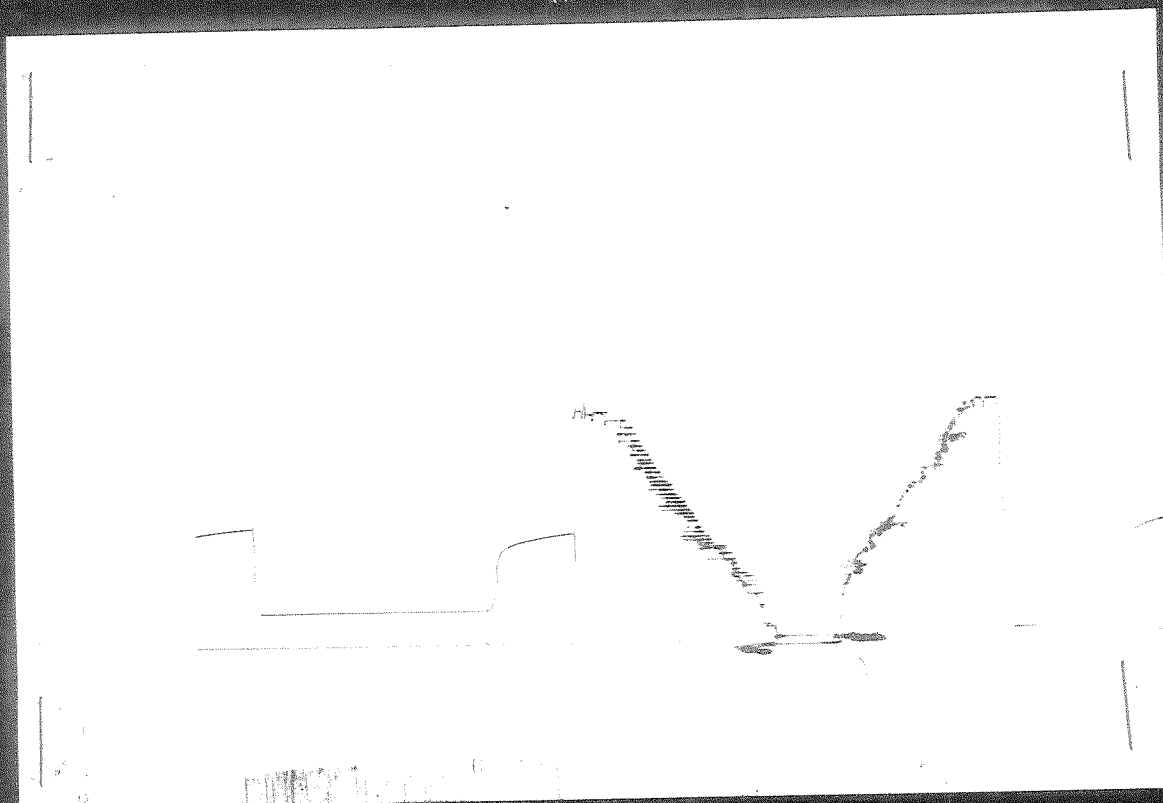

Company AMERICAN DRILG. CO. & NATURAL RES. Contractor AMERICAN DRILG. CO.

Well No. 1 Lease BAKER County ELLISWORTH Sec 16 Rg. 10 Twp. 14

Test No. 4 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 XII

Interval Tested From 2931 To 2942 Depth of Well 2942 Size Choke 1/2

Fluid Recovered In FLEXIBIGHT Temp. 101 Elev. _____

Initial Hyd. 1750 P.S.I. Final Hyd. 1750 P.S.I.

First Initial Flow Pressure 20 P.S.I. Opened Tool 5:45 A.M. XXI

First Final Flow Pressure 20 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 840 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 155 P.S.I. Second Flow Pres. 60 Min.

Second Final Flow Pressure 155 P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 740 P.S.I.

Blow WEAK BLOW THRU-TEST

Recovery 50 FT. MUDDY WATER

Remarks _____

Approved By RICHARD M. FOLEY

Tester ED PHILBERN
