



WILDCAT TESTING COMPANY

P. O. BOX 617

PHONE 793-9278

GREAT BEND, KANSAS

DRILL STEM TEST REPORT

LEASE Soukup WELL NO. I

MAR 23 1971

DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

XXXXXXXXXXXXXXXXXXXX

XXXXXXXXXXXXXXXXXXXX


658-5151

R.R.1 BOX 83

WILSON, KS.

Date 2-13-71

Ticket No. 271

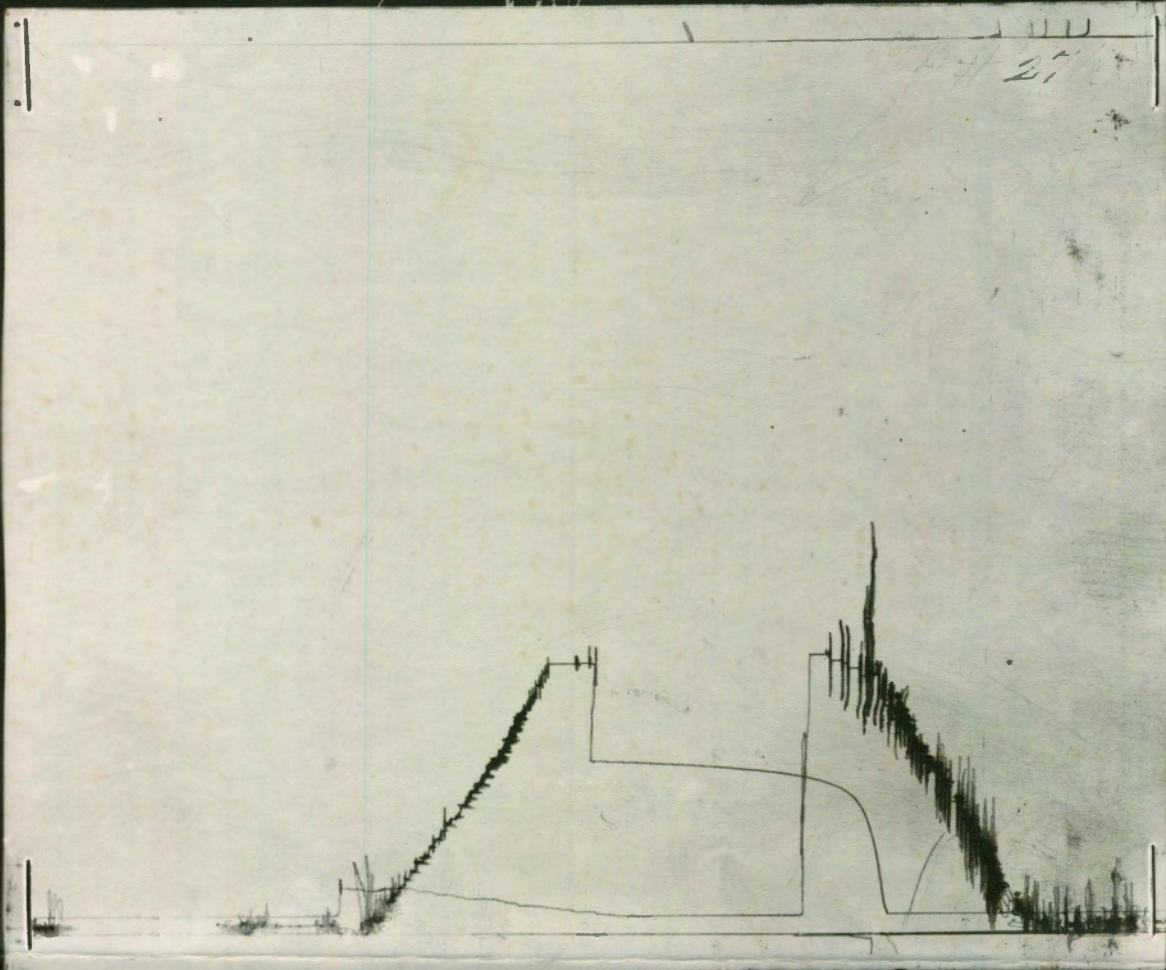

Company GLEN RUPE & GORSKI Contractor RED TIGER RIG #1

Well No. 1 Lease SOUKUP County ELLSWORTH Sec. Rg. Twp.

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 X.H.

Interval Tested From 2118 To 2140 Depth of Well 2140 Size Choke 1/2

Fluid Recovered In FLEXWEIGHT Temp. Elev. 1748

Initial Hyd. 1160 P.S.I. Final Hyd. 1160 P.S.I.

First Initial Flow Pressure 208 80 P.S.I. Opened Tool 6:30 AM P.M.

First Final Flow Pressure 80 80 P.S.I. First Flow Pres. 60 Min.

Initial Closed-in Pressure 80 208 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure 70 80 P.S.I. Second Flow Pres. 120 Min.

Second Final Flow Pressure 95 80 P.S.I. Final Closed-in Pres. 60 Min.

Final Closed-in Pressure 80 253 P.S.I.

Blow STRONG BLOW.GAS TO SURFACE IN 1 HR.

Recovery 20 FT. WATERY MUD

Remarks

Approved By RICHARD M.FOLEY Tester ED PHILBERN


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY
XXXXXXXXXXXX
XXXXXXXXXXXX



Date 2-17-71

Ticket No. 272

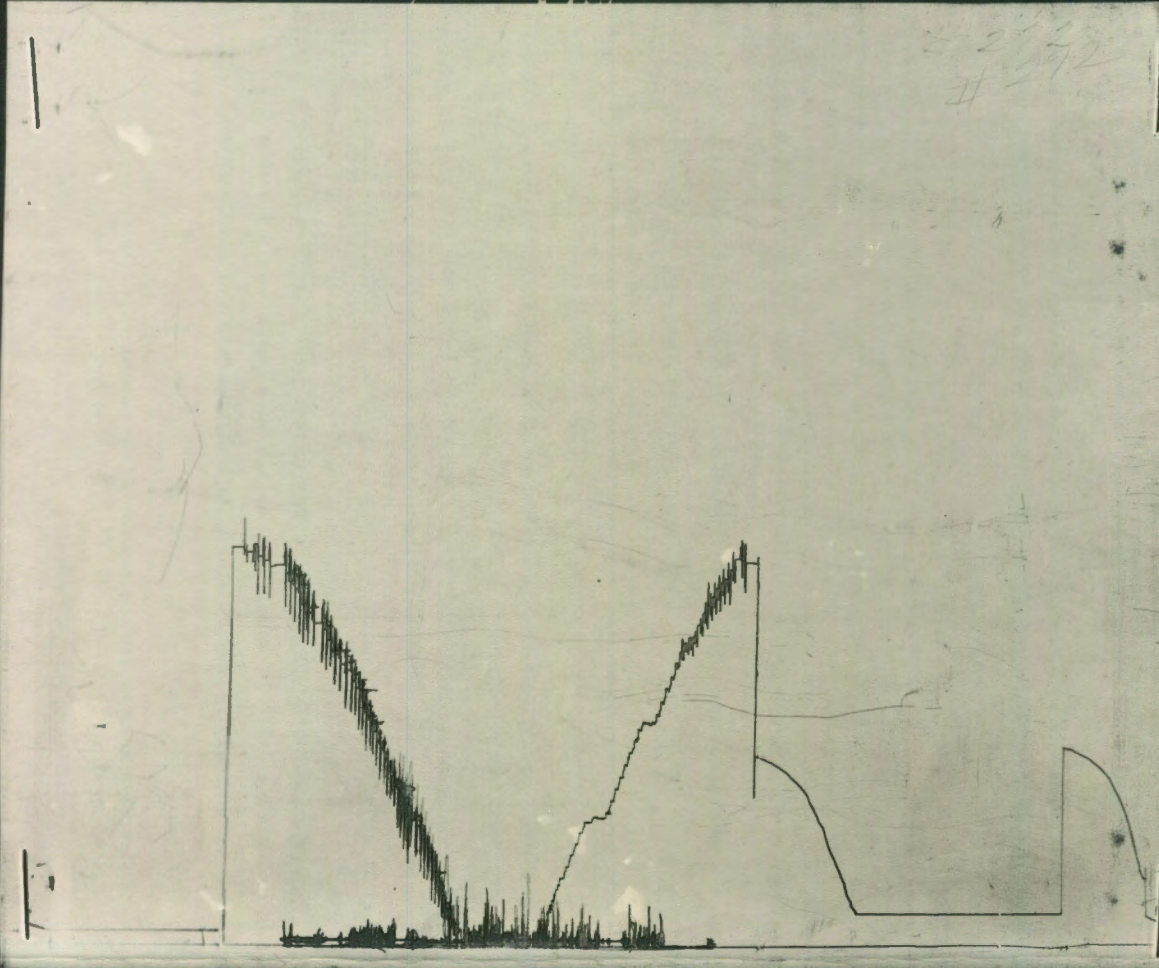

Company	GLEN RUPE & GORSKI		Contractor	TED FINGER		RIG	#1		
Well No.	1	Lease	SOUKUP		County	ELIZABETH		Sec. 22 Rg. 10 Twp. 14	
Test No.	2	Size Hole	7 7/8		Packer Size	6 3/4		Drill Pipe Size 4 1/2 X.H.	
Interval Tested From	2931		To	2940		Depth of Well	2940		Size Choke 1/2
Fluid Recovered In	FLEXWEIGHT		Temp.			Elev.	1748		
Initial Hyd.	1710		P.S.I.			Final Hyd.	1710		P.S.I.
First Initial Flow Pressure	852		P.S.I.	90		Opened Tool	5:27		A.M. XXXXX
First Final Flow Pressure	852		P.S.I.	90		First Flow Pres.	30		Min.
Initial Closed-in Pressure	30		P.S.I.	30		Initial Closed-in Pres.	30		Min.
Second Initial Flow Pressure	850		P.S.I.	90		Second Flow Pres.	30		Min.
Second Final Flow Pressure	860		P.S.I.	90		Final Closed-in Pres	30		Min.
Final Closed-in Pressure	850		P.S.I.	90					
Blow	WEAK STEADY BLOW								
Recovery	60 FT. GAS IN PIPE								
	90 FT. MUDDY WATER								
	WITH SCUM OF OIL ON TOP OF FLUID								
Remarks									
Approved By	RICHARD M. FOLEY				Tester	ED PHILBURN			


DRILL STEM TEST RECOVERY REPORT

WILDCAT TESTING COMPANY

XXXXXXXXXXXXXXXXXXXX
XXXXXXXXXXXXXXXXXXXX
658-5151
R.R. BOX 83
WILSON, KS.

Date 2-17-71

Ticket No. 273

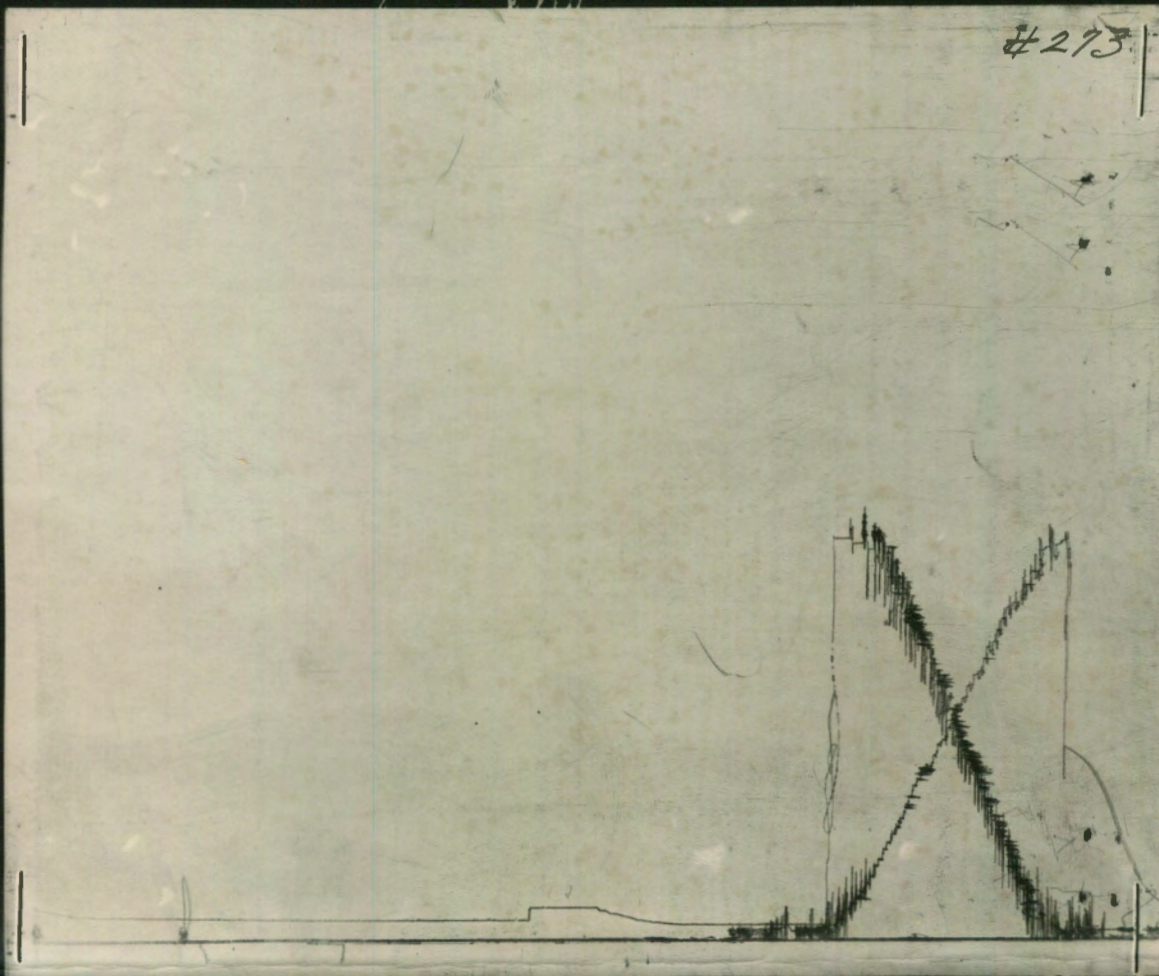

Company GLEN RUPE & GORSKI Contractor RED TIGER RIG #1

Well No. 1 Lease SOUKUP County ELLSWORTH Sec. 22 Rg. 10 Twp. 14

Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 X.H.

Interval Tested From 2930 To 2940 Depth of Well 2940 Size Choke 1/2

Fluid Recovered In FLEXWEIGHT Temp. Elev. 1748

Initial Hyd. 1370 P.S.I. Final Hyd. 1370 P.S.I.

First Initial Flow Pressure 84 P.S.I. Opened Tool 2:15 XXX P.M.

First Final Flow Pressure 84 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 170 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 113 P.S.I. Second Flow Pres. 90 Min.

Second Final Flow Pressure 113 P.S.I. Final Closed-in Pres. 30 Min.

Final Closed in Pressure 860 P.S.I.

Blow WEAK STEADY BLOW THRU-OUT TEST

Recovery 100 FT. MUDDY WATER

Remarks

Approved By RICHARD M. FOLEY Tester ED PHILBERN
