



POST OFFICE BOX 169


GREAT BEND, KANSAS 67530

DRILL-STEM TEST DATA


Well Name	Sebesta	Test No.	1
Well Number	1-A	Zone Tested	Tarkio
Company	Will P. Ash	Date	3/27/72
Comp. Rep.	Schmidt	Tester	Williams
Contractor	Sage Drlg.	Ticket No.	7751
Location	24-14-11	Elevation	

Recorder No.	3500	Clock Range	12 Hr.	Recorder No.	3000	Clock Range	12 Hr.
Depth	2079	Depth	2094				
Initial Hydro Mud Press.	1155	Initial Hydro Mud Press.	1161				
Initial Shut-in Press.	635	Initial Shut-in Press.	628				
Initial Flow Press.	25-34	Initial Flow Press.	21-31				
Final Flow Press.	37-41	Final Flow Press.	35-39				
Final Shut-in Press.	488	Final Shut-in Press.	480				
Final Hydro Mud Press.	1121	Final Hydro Mud Press.	1092				
Temperature	#### 86	Tool Open Before I. S. I.	90			Mins.	
Mud Weight	9.8	Initial Shut-in	90			Mins.	
Viscosity	41	Flow Period	90			Mins.	
Interval Tested	2080-2100	Final Shut-in	90			Mins.	
Top Packer Depth	2080	Surface Choke Size	5/8				
Bottom Packer Depth		Bottom Choke Size	5/8				
Total Depth	2100	Main Hole Size	7 7/8				
Drill Pipe Size	4 1/2 F.H.	Rubber Size	6 3/4				
Wt.							
Drill Collar I. D.							
Ft. Run							
Recovery—Total Feet							
Recovered	730	Feet Of	Gas In Pipe				
Recovered	50	Feet Of	Muddy Gassy Oil				
Recovered	60	Feet Of	Hvy. Oil & Gas Cut Mud				
Recovered		Feet Of					
Remarks							
	Weak		& Good In 45 Min. Thru-Out Test				

Test # 1 7751

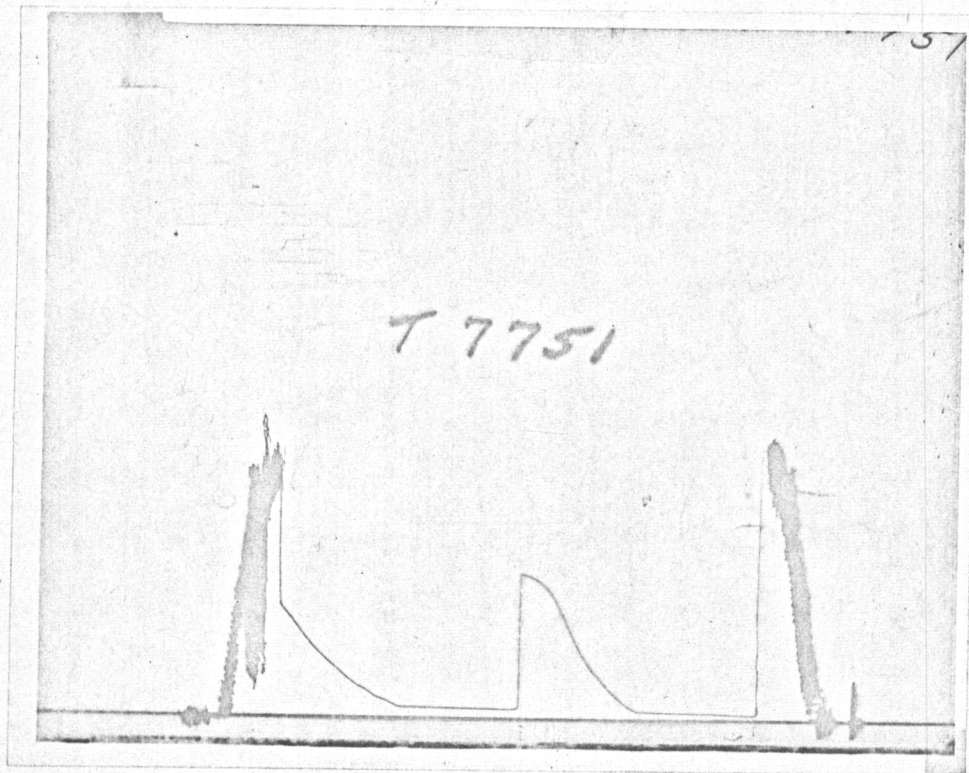

Top Recorder

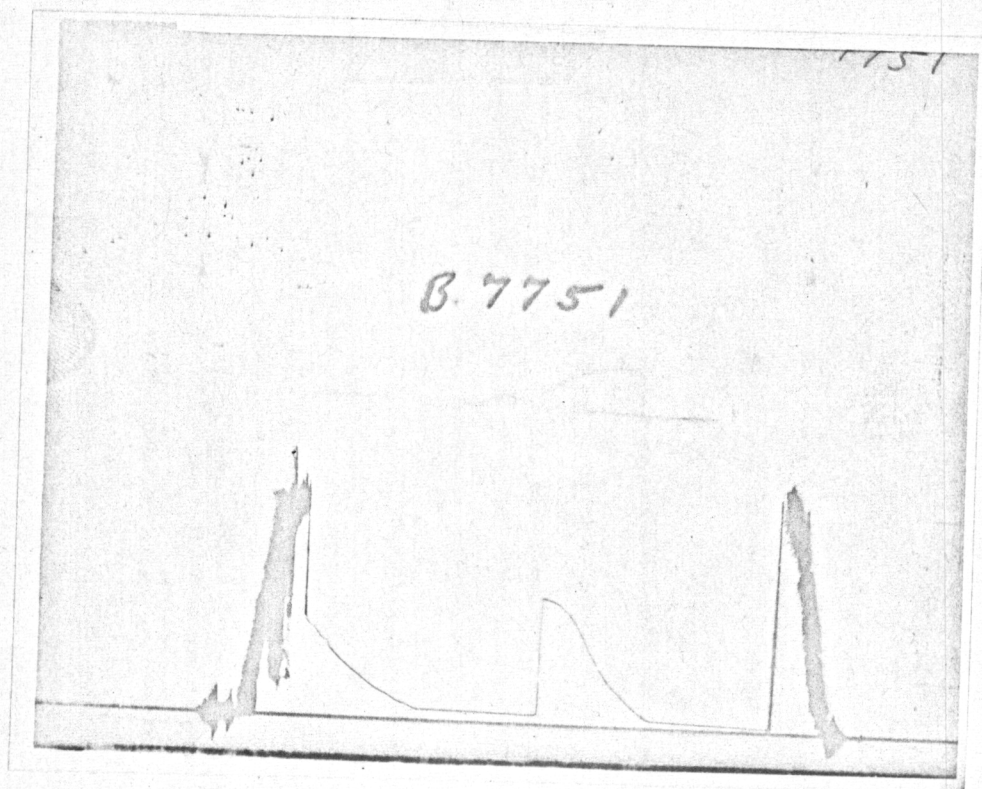

Bottom Recorder
