




OIL WELL CEMENTING INC.

Date 12/11/70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 7263

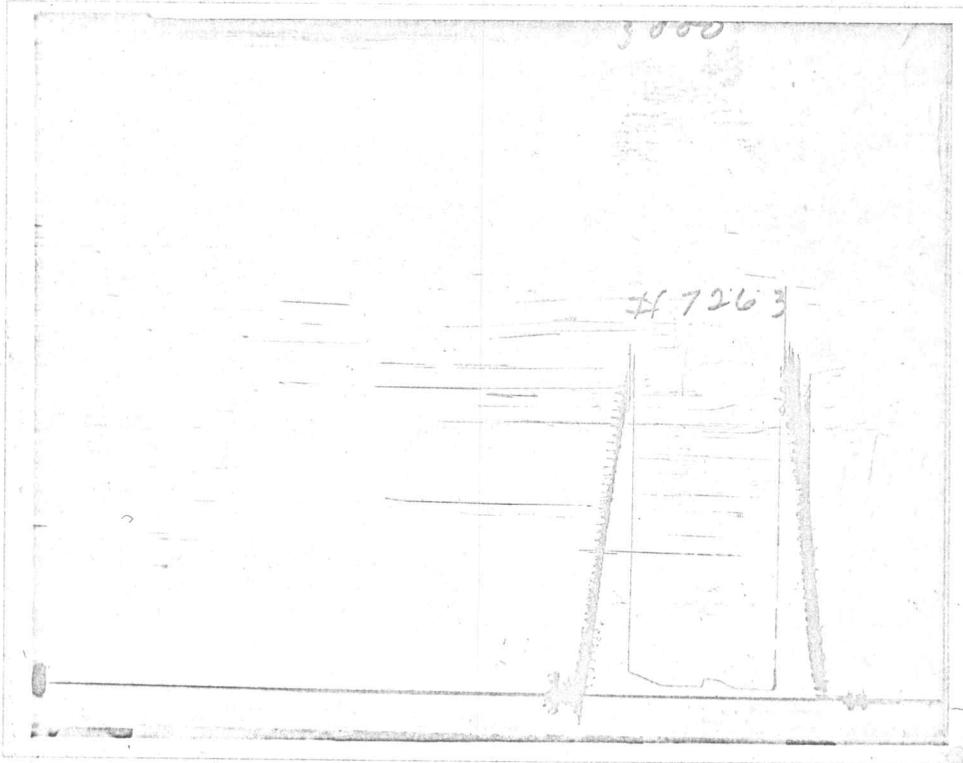

Company Rupe & GORSKI Contractor LEBEN DRILLING CO. RIG #7

Well No. 1 Lease K. VOPAT County ELLSWORTH Sec. 16 Twp 14 Rng 10

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2FH

Interval Tested From 2456 To 2490 Depth of Well 2490 Size Choke 5/8

Fluid Recovered In Flexweight Temp. 89 Elev. \_\_\_\_\_

Initial Hyd. 1423 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.

First Initial Flow Pressure 22 P.S.I. Opened Tool 5:25 ~~XXX~~ P.M.

First Final Flow Pressure \_\_\_\_\_ P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 90 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 52 P.S.I. Second Flow Pres. 30 Min.

Second Final Flow Pressure \_\_\_\_\_ P.S.I. Final Closed-in Pres. 30 Min.


Final Closed-in Pressure 90 P.S.I.

Blow FAIR BLOW THRU\*OUT TEST 4 in.

Recovery 50' Mud with scum of oil on top

Remarks \_\_\_\_\_

Approved By RICHARD M. FOLEY Tester SANDERS #014




OIL WELL CEMENTING INC.

Date 12-13-70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6628

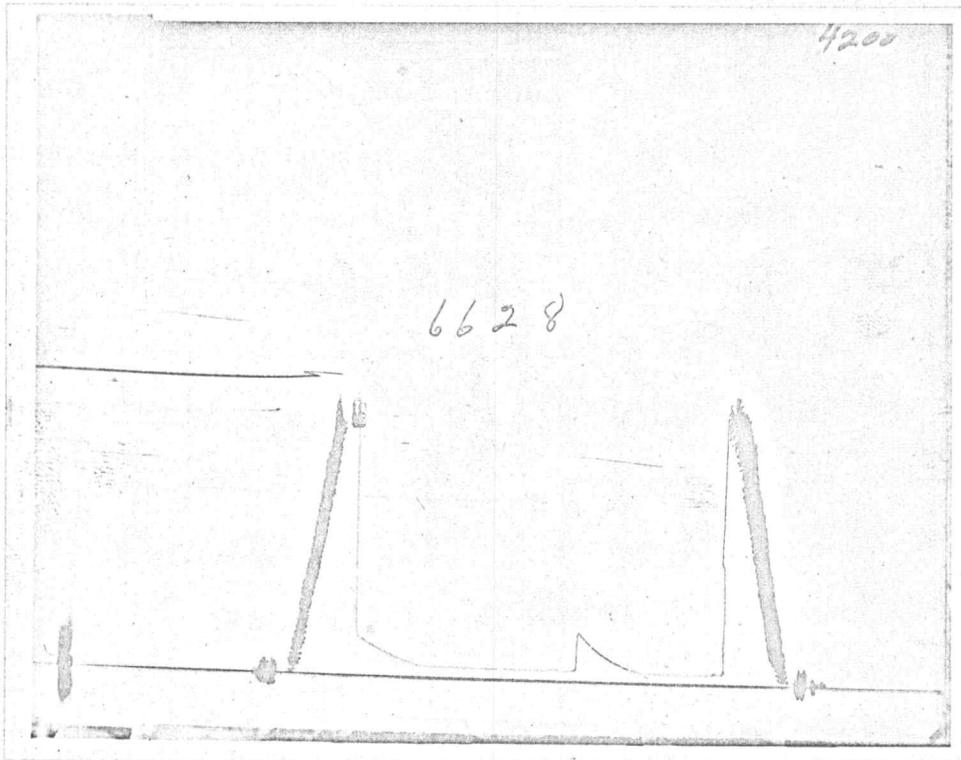

Company RUPE & GORSKI Contractor LEBEN DRILLING CO. RIG # 7  
 Well No. 1 Lease K. VOPAT County ELLSWORTH Sec. 16 Twp 14 Rng 10  
 Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 PH  
 Interval Tested From 2862 To 2888 Depth of Well 2888 Size Choke 5/8  
 Fluid Recovered In \_\_\_\_\_ Temp. 98 Elev. \_\_\_\_\_  
 Initial Hyd. 1638 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.  
 First Initial Flow Pressure 25 P.S.I. Opened Tool 3:12 A.M. ~~PM~~  
 First Final Flow Pressure \_\_\_\_\_ P.S.I. First Flow Pres. 60 Min.  
 Initial Closed-in Pressure 276 P.S.I. Initial Closed-in Pres. 60 Min.  
 Second Initial Flow Pressure 41 P.S.I. Second Flow Pres. 120 Min.  
 Second Final Flow Pressure \_\_\_\_\_ P.S.I. Final Closed-in Pres. 60 Min.  
 Final Closed-in Pressure 217 P.S.I.


Blow WEAK BLOW THRU-OUT TEST

Recovery 180' GAS IN PIPE

50' THIN OIL CUT WATERY MUD

Remarks \_\_\_\_\_

Approved By RICHARD M. FOLEY Tester SMITH #013



OIL WELL CEMENTING INC.

Date 12-13-70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6629



Company RUPE & GORSKI Contractor LEBEN DRILLING CO. RIG# 7

Well No. 1 Lease K. VOPAT County ELLSWORTH Sec. 16 Twp 14 Rng 10

Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 FH

Interval Tested From 2936 To 2950 Depth of Well 2950 Size Choke 5/8

Fluid Recovered In \_\_\_\_\_ Temp. 100 Elev. \_\_\_\_\_

Initial Hyd. 1690 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.

First Initial Flow Pressure 16 P.S.I. Opened Tool 8:35 XXX P.M.

First Final Flow Pressure \_\_\_\_\_ P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 754 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 41 P.S.I. Second Flow Pres. 60 Min.

Second Final Flow Pressure \_\_\_\_\_ P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 712 P.S.I.

Blow WEAK BLOW FOR 30 MIN. VERY WEAK ON FINIAL FLOW

Recovery 70' MUDDY WATER

Remarks \_\_\_\_\_

Approved By RICHARD M. FOLEY Tester SMITH #013
