




OIL WELL CEMENTING INC.

Date 7/29/70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 7163

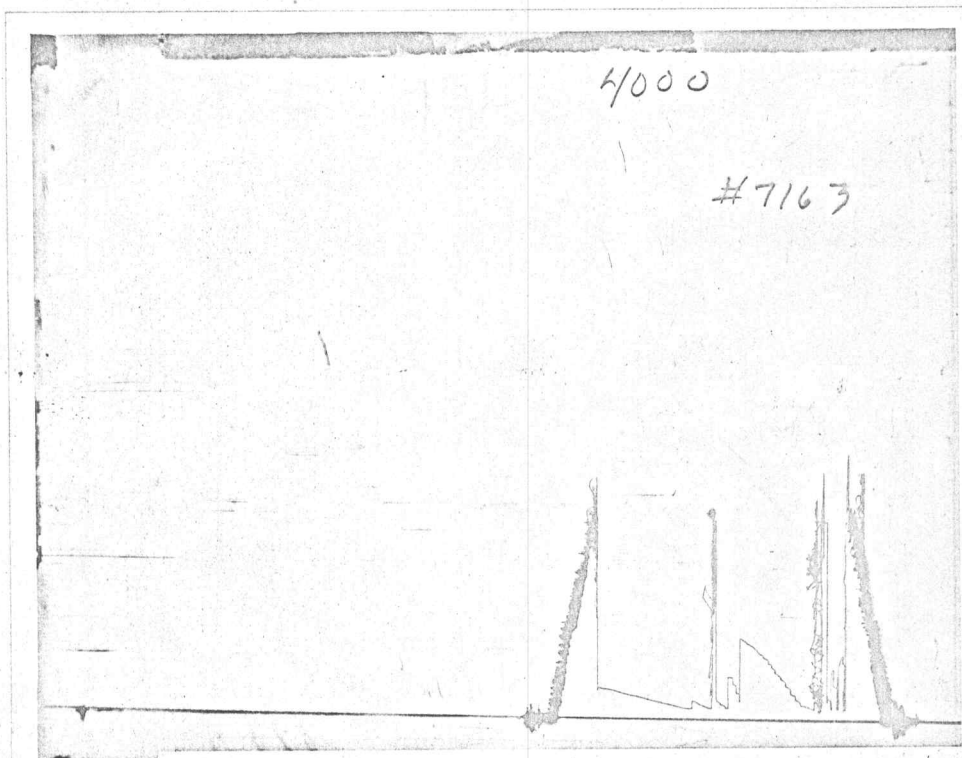

Company A.J. Gorski Contractor American Drlg. Co.

Well No. 1 Lease Stiles County Ellsworth Sec. 21 Twp 14 Rng 10

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 F.H.

Interval Tested From 2066 To 2088 Depth of Well 2088 Size Choke 5/8

Fluid Recovered In _____ Temp. 86 Elev. _____

Initial Hyd. _____ P.S.I. Final Hyd. _____ P.S.I.

First Initial Flow Pressure 37 P.S.I. Opened Tool 10:15 A.M. ###

First Final Flow Pressure _____ P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 443 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure _____ P.S.I. Second Flow Pres. 60 Min.

Second Final Flow Pressure 55 P.S.I. Final Closed-in Pres. 60 Min.

Final Closed-in Pressure 138 P.S.I.

Blow Very Weak For 8 Mins. Flushed Tool 3 Times

Recovery 10' Mud

Remarks Some Plugging Action

Approved By Elster Tester Sanders




OIL WELL CEMENTING INC.

Date 7/30/70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 7164

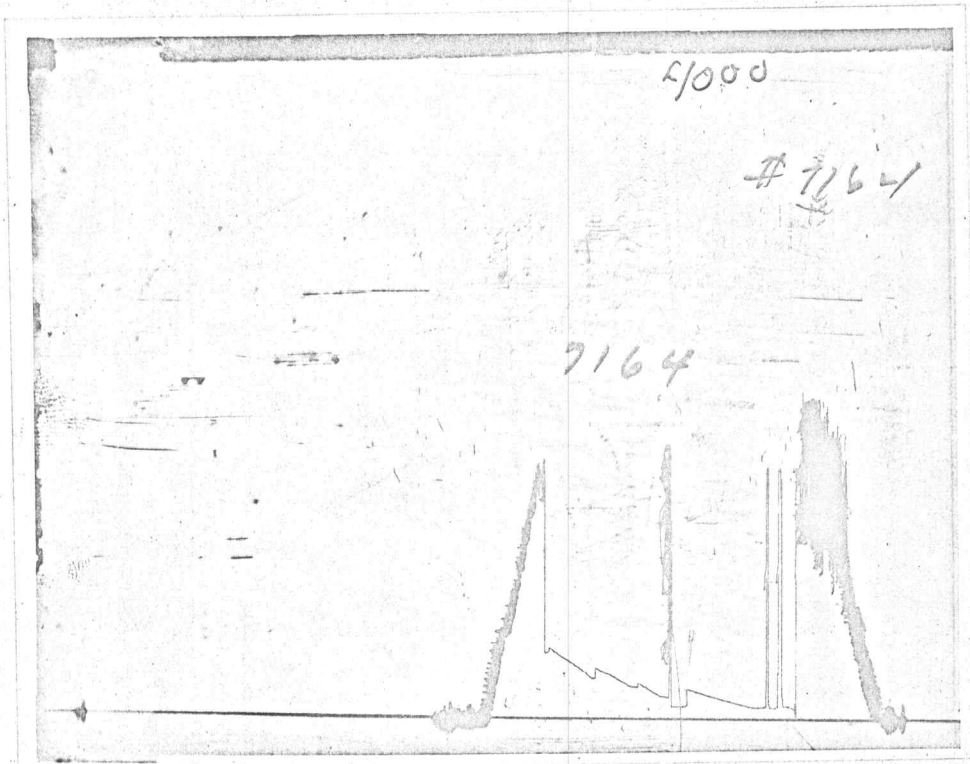

Company A.J. Gorski Contractor American Drlg. Co.

Well No. 1 Lease Stiles County Ellsworth Sec. 21 Twp 14 Rng 10

Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 F.H.

Interval Tested From 2420 To 2450 Depth of Well 2450 Size Choke 5/8

Fluid Recovered In _____ Temp. 89 Elev. _____

Initial Hyd. 1508 P.S.I. Final Hyd. _____ P.S.I.

First Initial Flow Pressure 20 P.S.I. Opened Tool 12:15 ~~AM~~ P.M.

First Final Flow Pressure _____ P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 144 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure _____ P.S.I. Second Flow Pres. 60 Min.

Second Final Flow Pressure 48 P.S.I. Final Closed-in Pres. 60 Min.

Final Closed-in Pressure 336 P.S.I.

Blow Very Weak Blow For 8 Mins. Flushed Tool

Recovery 30' Mud

Remarks _____

Approved By Elster Tester Sanders



OIL WELL CEMENTING INC.

Date 8/1/70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 7165



Company A.J. Gorski Contractor American Drlg Co.

Well No. 1 Lease Stiles County Ellsworth Sec. 21 Twp 14 Rng 10

Test No. 3 Size Hole. 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 F.H.

Interval Tested From 2883 To 2891 Depth of Well 2891 Size Choke 5/8

Fluid Recovered In _____ Temp. 98 Elev. _____

Initial Hyd. 1690 P.S.I. Final Hyd. _____ P.S.I.

First Initial Flow Pressure 46 P.S.I. Opened Tool 3:25 A.M. #P.M.

First Final Flow Pressure _____ P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 844 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure _____ P.S.I. Second Flow Pres. 90 Min.

Second Final Flow Pressure 231 P.S.I. Final Closed-in Pres. 60 Min.

Final Closed-in Pressure 798 P.S.I.

Blow Fair Blow Thru-out Test

Recovery 400' Salt Water

Remarks _____

Approved By Elster Tester Sanders
