

32-145-30w

(800) 792-6902

Ticket No 15173


SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Temperature / Pressure Data

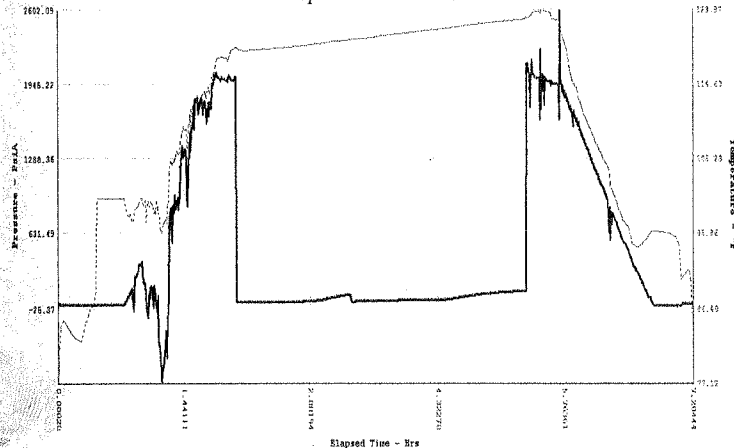

1	Initial Hydrostatic Pressure	2010
2	Initial Flow Pressure	29
3	Final Initial Flow Pressure	36
4	Initial Shut-In Pressure	97
5	Initial Final Flow Pressure	36
6	Final Flow Pressure	51
7	Final Shut-In Pressure	126
8	Final Hydrostatic Pressure	2125

Maximum Temperature 123

GENERAL INFORMATION

COMPANY NAME	 GLOBE OPERATING INC	LEASE AND WELL NUMBER	 PORTER #3
TEST DATE	 6/22/07	FORMATION TESTED	 MYRICK STATION
SECTION-TOWN-RANGE	 32-14-30W	DRILL STEM TEST NUMBER	 1
STATE	 KANSAS	REPORT NUMBER	 #####
COUNTY	 GROVE	ELEVATION KELLY BUSHINGS	 2734
ELEVATION GROUND LEVEL	 2726	TESTING ENGINEER	 JARED SCHECK
COMPANY REPRESENTATIVE	 JIM MUSGOVE		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	 4284	TOP PACKER DEPTH	 4279
TEST INTERVAL (to)	 4321	BOTTOM PACKER DEPTH	 4284
ANCHOR LENGTH	 37	NUMBER OF PACKERS	 2
TOTAL DEPTH (ft)	 4321	PACKER SIZE	 6 3/4
		HOLE SIZE	 7 7/8

FLOW TIMES

INITIAL OPEN		FINAL OPEN	
TOOL OPEN (from)	 1:15P	TOOL OPEN (from)	 2:30
TOOL OPEN (to)	 2:00P	TOOL OPEN (to)	 3:30
DURATION (min.)	 45	DURATION (min.)	 60
INITIAL SHUT-IN		FINAL SHUT-IN	
TOOL CLOSED (from)	 2:00	TOOL CLOSED (from)	 3:30
TOOL CLOSED (to)	 2:30	TOOL CLOSED (to)	 4:30
DURATION (min.)	 30	DURATION (min.)	 60

INITIAL FLOW WEAK BUT BUILDING BLOW BUILT 2 INCHS INTO BUCKET IN 30 MIN
NO BLOW BACK

FINAL FLOW WEAK BUT BUILDING BLOW BUILT 4 1/4 INCHS IN 60 MIN
NO BLOW BACK

30 W
 Company: GLOBE OPERATING INC
 Lease & Well No. PORTER #3
 Test #: 1
 Date: 6-22-07
 SEC. 32
 TWP. 14
 RGE.

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC	LEASE AND WELL NUMBER	PORTER #3
TEST DATE	6/22/07	FORMATION TESTED	MYRICK STATION
SECTION-TOWN-RANGE	32-14-30W	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	15173
COUNTY	GROVE	ELEVATION KELLY BUSHINGS	2734
ELEVATION GROUND LEVEL	2726	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
270	MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	4317	BOTTOM RECORDER DEPTH	4318
RECORDER NUMBER	91986	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DISCOVERY DRILLING CO INC		
DRILL PIPE LENGTH	4265	DRILL COLLAR LENGTH	
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.


COMMENTS

Recovery Sample Description

Great Bend, Kansas 67530

[illegible]

Temperature / Pressure Data

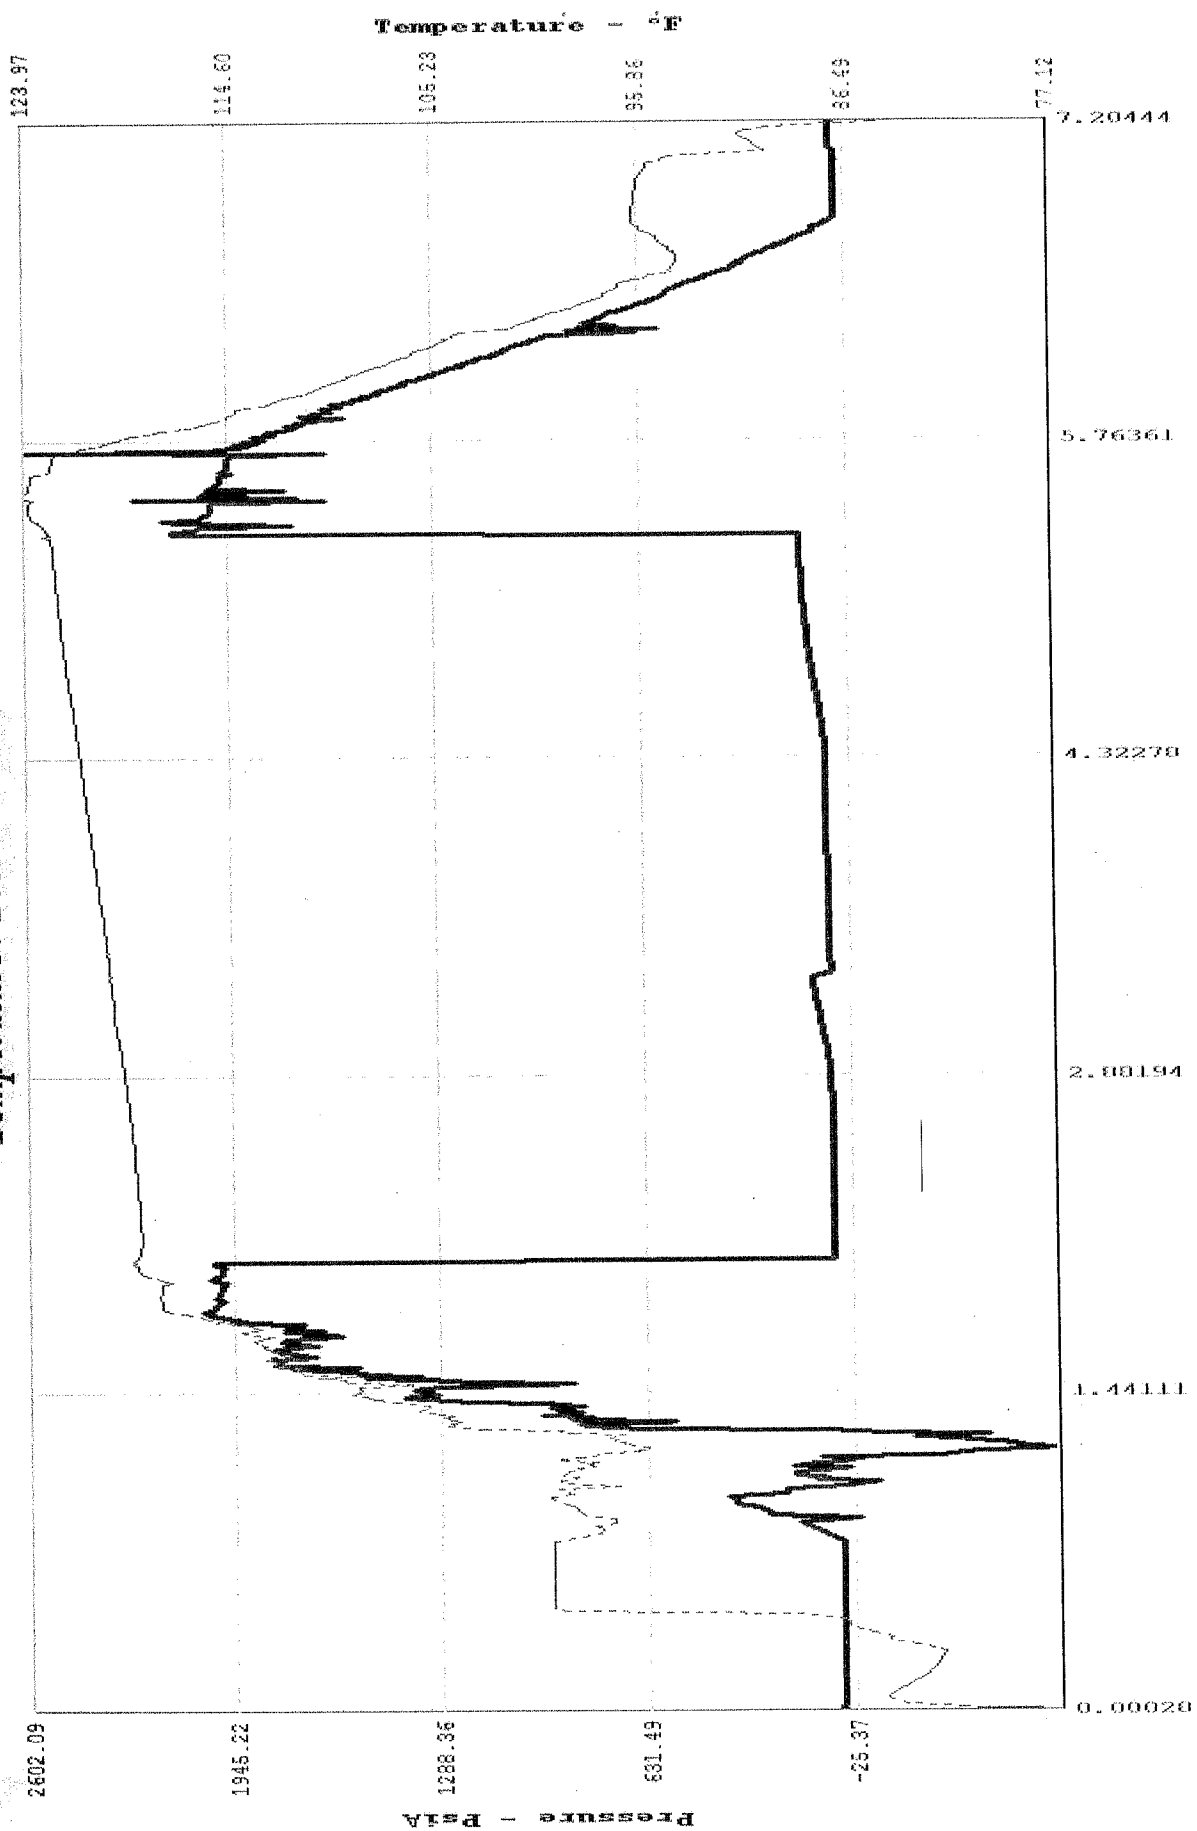

DST #1

6-22-07

32-14-30W

PORTER #3

GLOBE OPERATING INC

Superior Testers Enterprises L.L.C.

P.O. Box 138, Great Bend, Kansas 67530

(800) 792-6902

Company Globe Operating Inc
 Address PO Box 12 Great Bend KS 67530
 Lease & # Porter #3 Sec. 32 Twp 14 Rng 30W
 Date 6-23-2007 County Gove Elevation 2726 G.L. 2734 K.B.
 Drilling Contractor Discovery Drilling Co
 Drill Pipe Length 4321 I.D. of Drill Pipe 3.8 Tool Joint Size 9 1/2 X 11
 Drill Collar Length I.D. of Drill Collars Tool Joint Size
 Mud Weight 9.5 Viscosity 4.6 Filtrate 10.4 Chlorides-Pits 2,000 DST
 Top Packer Depth 4335 Bottom Packer Depth 4340 Number of Packers 2
 Tested From 4340 to 4410 Total Depth 4410 Anchor Length 70
 Test # 2 Formation Tested Johnson Hole Size 7 7/8
 Initial Blow Weak Building Blow Built 2 inches into Bucket

Blow back on the 1st Shut-in NO Blow Back
 Final Blow Weak ~~Build~~ Surface Blow Built 1/2 inch into Bucket in 45 min
 Blow back on the 2nd Shut-in NO Blow Back
 Initial Hydrostatic 2095 P.S.I. Final Hydrostatic 2074 P.S.I. Maximum Temp. 128 F

Initial Opening	<u>56</u>	P.S.I. to	<u>59</u>	P.S.I. from	<u>7:01 am</u> to	<u>7:46 am</u>	<u>45</u>	minutes
Initial Shut-in	<u>526</u>	P.S.I. from	<u>7:46 am</u>	to	<u>8:16 am</u>	<u>30</u>	minutes	
Final Opening	<u>67</u>	P.S.I. to	<u>76</u>	P.S.I. from	<u>8:16 am</u>	to	<u>9:01 am</u>	<u>45</u> minutes
Final Shut-in	<u>699</u>	P.S.I. from	<u>9:01 am</u>	to	<u>10:01 am</u>	<u>60</u>	minutes	

Feet	Recovery Description	% Gas	% Oil	% Mud	% Water
<u>30</u>	<u>Gas in pipe</u>				
<u>30</u>	<u>Slight lay oil cut mud</u>		<u>5</u>	<u>95</u>	

Total Feet Recovered Recovery Chlorides Rw. ohms @ Degrees
 Gravity of oil Corrected Gas to Surface in minutes into the
 Max. Gas Gauged MCF/day See Gas Flow Report Was a gas sample taken
 Comments


Extra Equipment-Jars Safety Joint Circulating Sub Straddle
 Electronic Recorder No. 3088 Depth 4406 Extra Packer (3rd) Hook Wall
 Bottom Recorder No. 47441 Depth 4407 Extra Packer (4th) Sampler
 Tool Operator [Signature] Approved By

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

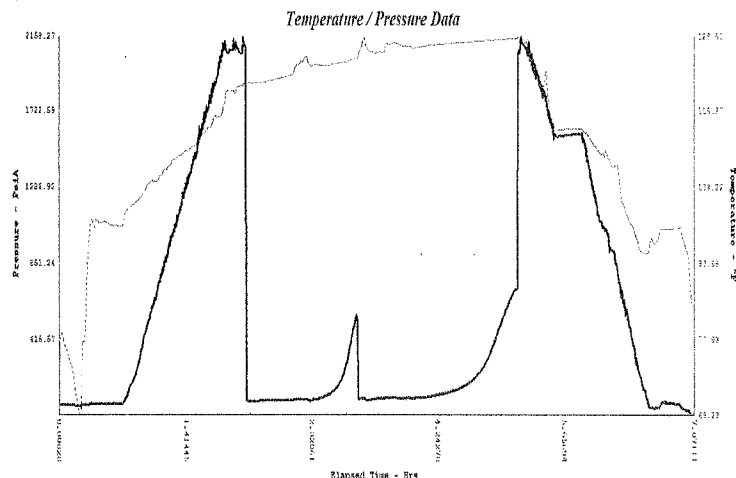

1	Initial Hydrostatic Pressure	2095
2	Initial Flow Pressure	56
3	Final Initial Flow Pressure	59
4	Initial Shut-In Pressure	526
5	Initial Final Flow Pressure	67
6	Final Flow Pressure	76
7	Final Shut-In Pressure	699
8	Final Hydrostatic Pressure	2074

Maximum Temperature 128

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC

TEST DATE 6/23/07

SECTION-TOWN-RANGE 32-14-30W

STATE KANSAS

COUNTY GROVE

ELEVATION GROUND LEVEL

COMPANY REPRESENTATIVE

LEASE AND WELL NUMBER PORTER #3

FORMATION TESTED JOHNSON

DRILL STEM TEST NUMBER 2

REPORT NUMBER #####

ELEVATION KELLY BUSHINGS 2734

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4340

TEST INTERVAL (to) 4410

ANCHOR LENGTH 70

TOTAL DEPTH (ft) 4410

TOP PACKER DEPTH 4335

BOTTOM PACKER DEPTH 4340

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 7:01A

TOOL OPEN (to) 7:46A

DURATION (min.) 45

INITIAL SHUT-IN

TOOL CLOSED (from) 7:46

TOOL CLOSED (to) 8:16

DURATION (min.) 30

FINAL OPEN

TOOL OPEN (from) 8:16

TOOL OPEN (to) 9:01

DURATION (min.) 45

FINAL SHUT-IN

TOOL CLOSED (from) 9:01

TOOL CLOSED (to) 10:01

DURATION (min.) 60

INITIAL FLOW

WEAK BUILDING BLOW BUILT 2 INCHS IN 45 MIN
NO BLOW BACK

FINAL FLOW

WEAK SURFACE BLOW BUILT 1/2 INTO BUCKET IN 45 MIN
NO BLOW BACK

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC	LEASE AND WELL NUMBER	PORTER #3
TEST DATE	6/23/07	FORMATION TESTED	JOHNSON
SECTION-TOWN-RANGE	32-14-30W	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	14174
COUNTY	GROVE	ELEVATION KELLY BUSHINGS	2734
ELEVATION GROUND LEVEL	2726	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	270 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	4406	BOTTOM RECORDER DEPTH	4407
RECORDER NUMBER	91986	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DISCOVERY DRILLING	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4321	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS

[illegible]

Temperature / Pressure Data

