

P.O. Box 138, Great Bend, Kansas 67530
(800) 792-6902

(800) 792-6902

Company Trans Pacific Oil Corporation
Address 100 S. Main Suite 200 Wichita KS 67202
Lease & # Leiker 7-18
Date 10-5-2007 County Ellis Sec. 18 Twp 15 Rng 17
Drilling Contractor Shelds Elevation 1989 G.L. 1992 K.B.
Drill Pipe Length 3259 I.D. of Drill Pipe 3.80
Drill Collar Length — I.D. of Drill Collars 3.25 Tool Joint Size —
Mud Weight 8.6 Viscosity 49 Filtrate 7.2 Tool Joint Size —
Top Packer Depth 3273 Chlorides-Pits 4.500 DST —
Tested From 3278 to 3307 Bottom Packer Depth 3278 Number of Packers 2
Test # 1 Formation Tested Upper Lansing Total Depth 3307 Anchor Length 29
Initial Blow Weak Building Blow Built to 3 inch int Hole Size 7 7/8

Test # 1 Formation Tested Upper Lansing Total Depth 3307 Number of Packers 2
Initial Blow Weak Building Blow Built to 3 inch into water in 30 min Anchor Length 29
Final Blow Weak Building Blow Built to 2 inch into water in 45 min Hole Size 7 7/8
Initial Hydrostatic 1646 PSI Final Hydrostatic 1646 PSI Blow back on the 1st Shut-in 16
Blow back on the 2nd Shut-in 16

Initial Hydrostatic	1646	P.S.I.	Final Hydrostatic	1595	P.S.I.	Blow back on the 2nd Shut-in	NO
Initial Opening	39	P.S.I.	to	57	P.S.I.	Maximum Temp.	107 F
Initial Shut-in	698	P.S.I.	from	12:35 A	m to	1:05	m 30 minutes
Final Opening	63	P.S.I.	to	74	P.S.I.	from	1:05 m to 1:30 m 45 minutes
Final Shut-in	281	P.S.I.	from	1:50	m to	2:50	m 60 minutes
		P.S.I.	from	2:50	m to	3:50 A	m 60 minutes

[illegible]

Total Feet Recovered _____ Recovery Chlorides _____ Rw. _____ ohms @ _____ Degrees
 Gravity of oil _____ Corrected Gas to Surface in _____ minutes into the _____
 Max. Gas Gauged _____ MCF/day See Gas Flow Report
 Comments _____ Was a gas sample taken _____

Extra Equipment-Jars _____ Safety Joint _____
Electronic Recorder No. 91986 Depth 3302
Bottom Recorder No. 4337 Depth 3303
Tool Operator [Signature] Circulating Sub _____
Extra Packer (3rd) _____ Straddle _____
Extra Packer (4th) _____ Hook Wall _____
Approved By _____ Sampler _____

Ticket No. 15415

Ticket No. 15415


SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Temperature / Pressure Data

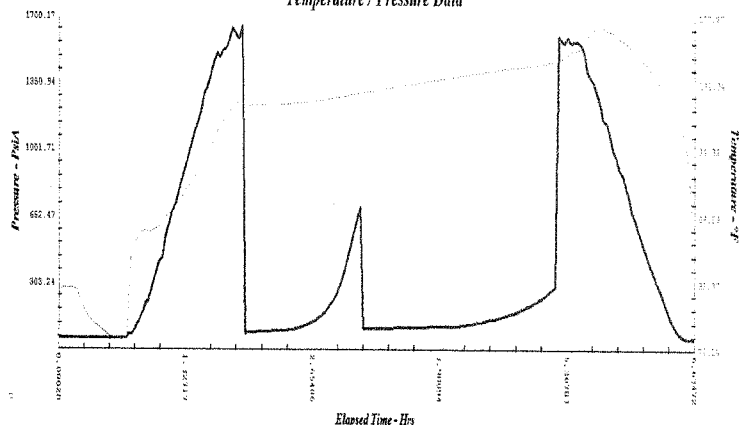

Drill serial number: 91716
Test Start: 10/05/2007 08:42:00

1	Initial Hydrostatic Pressure	1646
2	Initial Flow Pressure	39
3	Final Initial Flow Pressure	57
4	Initial Shut-In Pressure	698
5	Initial Final Flow Pressure	63
6	Final Flow Pressure	76
7	Final Shut-In Pressure	281
8	Final Hydrostatic Pressure	1595

Maximum Temperature 107

GENERAL INFORMATION

COMPANY NAME TRANS PACIFIC OIL CORPORATION

TEST DATE 10/5/07

SECTION-TOWN-RANGE 18-15-17

STATE KANSAS

COUNTY ELLIS

ELEVATION GROUND LEVEL 1989

COMPANY REPRESENTATIVE BETH

LEASE AND WELL NUMBER LEIKER 7-18

FORMATION TESTED UPPER LANSING

DRILL STEM TEST NUMBER 1

REPORT NUMBER 15415

ELEVATION KELLY BUSHINGS 1992

TESTING ENGINEER DAVID NICHOLS

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3278

TEST INTERVAL (to) 3307

ANCHOR LENGTH 29

TOTAL DEPTH (ft) 3307

TOP PACKER DEPTH 3273

BOTTOM PACKER DEPTH 3278

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 12:35

TOOL OPEN (to) 1:05

DURATION (min.) 30

FINAL OPEN

TOOL OPEN (from) 1:50

TOOL OPEN (to) 2:50

DURATION (min.) 60

INITIAL SHUT-IN

TOOL CLOSED (from) 1:05

TOOL CLOSED (to) 1:50

DURATION (min.) 45

FINAL SHUT-IN

TOOL CLOSED (from) 2:50

TOOL CLOSED (to) 3:50

DURATION (min.) 60

INITIAL FLOW

WEAK BUILDING BLOW BUILT TO 3 INCHES INTO WATER IN 30 MIN

FINAL FLOW

WEAK BUILDING BLOW BUILT TO 2 INCHES INTO WATER IN 60 MIN

Company: TRANS PACIFIC OIL CORPORATION
TWP. 15 RGE. 17

Lease & Well No. LEIKER 7-18 Test #: 1 Date: 10-5-07 SEC. 18

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	TRANS PACIFIC OIL CORPORATION	LEASE AND WELL NUMBER	LEIKER 7-18
TEST DATE	10/5/07	FORMATION TESTED	UPPER LANSING
SECTION-TOWN-RANGE	18-15-17	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	15415
COUNTY	ELLIS	ELEVATION KELLY BUSHINGS	1992
ELEVATION GROUND LEVEL	1989	TESTING ENGINEER	DAVID NICHOLS
COMPANY REPRESENTATIVE	BETH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	NO	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	36 MILES ROUND TRIP FROM	HAYS	
TOP RECORDER DEPTH	3302	BOTTOM RECORDER DEPTH	3303
RECORDER NUMBER	91986	RECORDER NUMBER	3088

WELL INFORMATION

DRILLING CONTRACTOR	SHIELDS	DRILL COLLAR LENGTH	0
DRILL PIPE LENGTH	3259	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS


Recovery Sample Description

1-800-792-6902

Great Bend, Kansas 67530

Drill Pipe	I.D.	Feet		Recovery Description For Drill Pipe	Gas	Oil	Mud	Water	Total bbls.
4 1/2	3.82	90	MUD WITH A VERY SLIGHT SHOW OF OIL			1%	99%		1.2780
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
Drill Collars	I.D.			Recovery Description For Drill Collars	0.0000	0.0128	1.2652	0.0000	
	2.25								0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
Total Recovery	90	Feet		Total bbls. Recovered From Drill Pipe	0.0000	0.0128	1.2652	0.0000	Total
				Total bbls. Recovered From Drill Collars	0.0000	0.0000	0.0000	0.0000	bbls
				Total bbls Recovered	0.0000	0.0128	1.2652	0.0000	1.2780
					Gravity Corrected				
MUD WEIGHT #GAL	8.6			Resistivity		ohms @		Degrees	
VISCOSITY	49			Recovery Chlorides		ppm			
WATER LOSS	7.2			Pit Chlorides	4,500	ppm			
				4 1/2 inch Drill Pipe 3.83 I.D. Drill Collars 2.25 I.D					
			TRANS PACIFIC OIL CORPORATION	18-15-17	LIEKER 7-18	10-5-07	DST#1	UPPER LANSING	

Temperature / Pressure Data

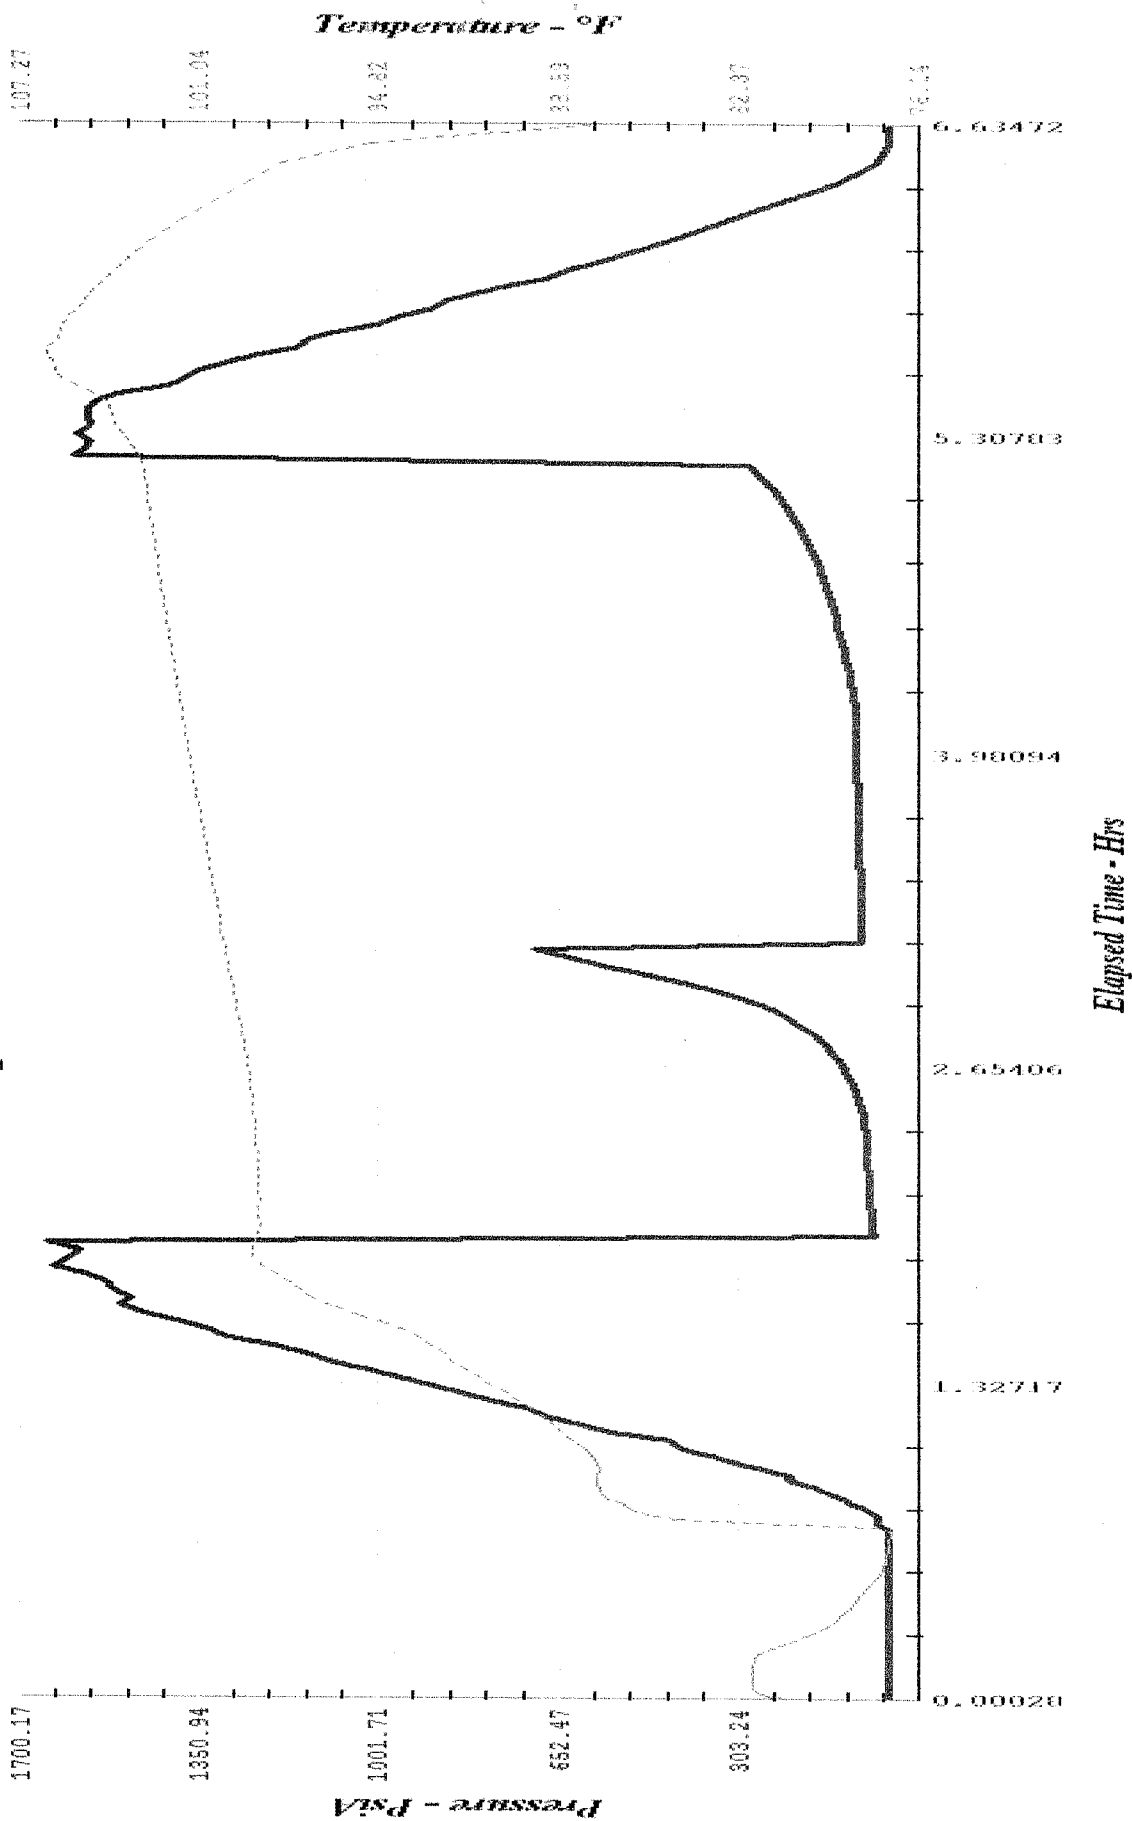

Tool serial number: 91716
 Test start: 10/05/2007 05:42:00

P.O. Box 138, Great Bend, Kansas 67530
(800) 792-6002

(800) 792-6902

Lease # Leiker 7-18 Date 10-3-2007 County Ellis Sec. 18 Twp 15 Rng 17
Drilling Contractor Sheilds Elevation 1989 G.L. 1982 K.B.
Drill Pipe Length 3289

Drill Collar Length 4 I.D. of Drill Pipe 3.80
Mud Weight 9.3 Viscosity 11 I.D. of Drill Collars — Tool Joint Size 4 1/2 x 1 1/2

Top Packer Depth 330.3 viscosity 34 Filtrate 8.4 Tool Joint Size
Tested From 330.8 Bottom Packer Depth 330.8 Chlorides-Pits 4.700 DST

Test # 2 Formation Tested Lansing Total Depth 3360 Number of Packers 2
Initial Blow 1 Anchor Length

Weak Building Blow Built to 7 inches in 3 min

Initial Hydrostatic 1073

Initial Shut-in 394 P.S.I. from 3:36 p m to 6:25 m 30 minutes
Final Opening 39 P.S.I. to 65 P.S.I. from 6:25 m to 7:10 m 45 minutes

Feet	Recovery Description	%			
10					
20					
30					
40					
50					
60					
70					
80					
90					
100					

[illegible][illegible][illegible]

Gas Gauged _____ Gas to Surface in _____ minutes into the _____ @ _____ Degrees
 _____ MCF/day See Gas Flow Report _____

Electronic Recorder No. 91954 Safety Joint _____
Depth 3356 Circulating Sub _____ Straddle _____

ket No. 15416

Ticket No. 15416

Extra Packer (3rd) _____ Straddle _____
Extra Packer _____ Hook Wall _____

Extra Packer (4th) _____ Sampler _____
Approved By _____

Prepared By _____

SUPERIOR TESTERS ENTERPRISES L.L.C.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: TRANSPACIFIC OIL CORPORATION
18 TWP. 15 RGE. 17
Lease & Well No. LIEKER 7-18 Test #: 2 Date: 10-5-07 SEC.

Temperature / Pressure Data

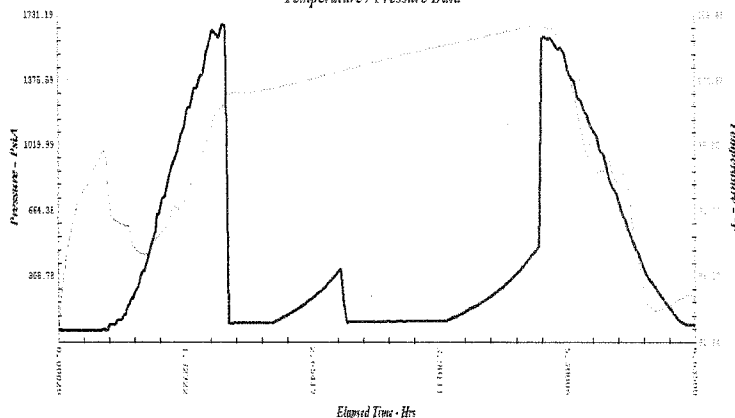

Tool serial number: 51714
Test start: 10/05/2007 20:39:17

1	Initial Hydrostatic Pressure	1673
2	Initial Flow Pressure	50
3	Final Initial Flow Pressure	56
4	Initial Shut-In Pressure	344
5	Initial Final Flow Pressure	59
6	Final Flow Pressure	64
7	Final Shut-In Pressure	465
8	Final Hydrostatic Pressure	1610

Maximum Temperature 105

GENERAL INFORMATION

COMPANY NAME	TRANSPACIFIC OIL CORPORATION	LEASE AND WELL NUMBER	LIEKER 7-18
TEST DATE	10/5/07	FORMATION TESTED	LANSING
SECTION-TOWN-RANGE	18-15-17	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	15416
COUNTY	ELLIS	ELEVATION KELLY BUSHINGS	1992
ELEVATION GROUND LEVEL	1989	TESTING ENGINEER	DAVID NICHOLS
COMPANY REPRESENTATIVE	BETH		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	3308	TOP PACKER DEPTH	3303
TEST INTERVAL (to)	3360	BOTTOM PACKER DEPTH	3308
ANCHOR LENGTH	52	NUMBER OF PACKERS	2
TOTAL DEPTH (ft)	3360	PACKER SIZE	6 3/4
		HOLE SIZE	7 7/8

FLOW TIMES

INITIAL OPEN		FINAL OPEN	
TOOL OPEN (from)	5:55	TOOL OPEN (from)	7:10
TOOL OPEN (to)	6:25	TOOL OPEN (to)	8:10
DURATION (min.)	30	DURATION (min.)	60
INITIAL SHUT-IN		FINAL SHUT-IN	
TOOL CLOSED (from)	6:25	TOOL CLOSED (from)	8:10
TOOL CLOSED (to)	7:10	TOOL CLOSED (to)	9:10
DURATION (min.)	45	DURATION (min.)	60

INITIAL FLOW

WEAK BUILDING BLOW BUILT TO 7 INCHES INTO WATER IN 30 MIN

FINAL FLOW

FAIR BLOW BOTTOM OF BUCKET IN 5 MIN

SUPERIOR TESTERS ENTERPRISES L.L.C.
DRILL STEM TEST REPORT
GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	TRANSPACIFIC OIL CORPATION	LEASE AND WELL NUMBER	LIEKER 7-18
TEST DATE	10/5/07	FORMATION TESTED	LANSING
SECTION-TOWN-RANGE	18-15-17	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	15416
COUNTY	ELLIS	ELEVATION KELLY BUSHINGS	1992
ELEVATION GROUND LEVEL	1989	TESTING ENGINEER	DAVID NICHOLS
COMPANY REPRESENTATIVE	BETH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	NO	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
36 ROUND TRIP FROM HAYS			
TOP RECORDER DEPTH	3356	BOTTOM RECORDER DEPTH	3357
RECORDER NUMBER	91986	RECORDER NUMBER	3088


WELL INFORMATION

DRILLING CONTRACTOR	SHIELDS	DRILL COLLAR LENGTH	0
DRILL PIPE LENGTH	3289	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS

Drill Pipe	I.D.	Feet	Recovery Description For Drill Pipe	Gas	Oil	Mud	Water	Total bbls.
4 1/2	3.82	50	OIL CUT MUD		7%	93%		0.7100
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
Drill Collars	I.D.		Recovery Description For Drill Collars	0.0000	0.0497	0.6603	0.0000	
	2.25							0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
								0.0000
Total Recovery	50	Feet	Total bbls. Recovered From Drill Pipe	0.0000	0.0497	0.6603	0.0000	Total
			Total bbls. Recovered From Drill Collars	0.0000	0.0000	0.0000	0.0000	bbls
			Total bbls Recovered	0.0000	0.0497	0.6603	0.0000	0.7100
				Gas	Oil	Mud	Water	
			Gravity Corrected					
MUD WEIGHT #/GAL	9.3		Resistivity		ohms @		Degrees	
VISCOSITY	54		Recovery Chlorides		ppm			
WATER LOSS	8.4		Pit Chlorides	4,700	ppm			
			4 1/2 inch Drill Pipe 3.83 I.D. Drill Collars 2.25 I.D					
			TRANS PACIFIC OIL CORPATION	18-15-17	LIEKER 7-18	10-5-07	DST#2	LANSING

Temperature / Pressure Data

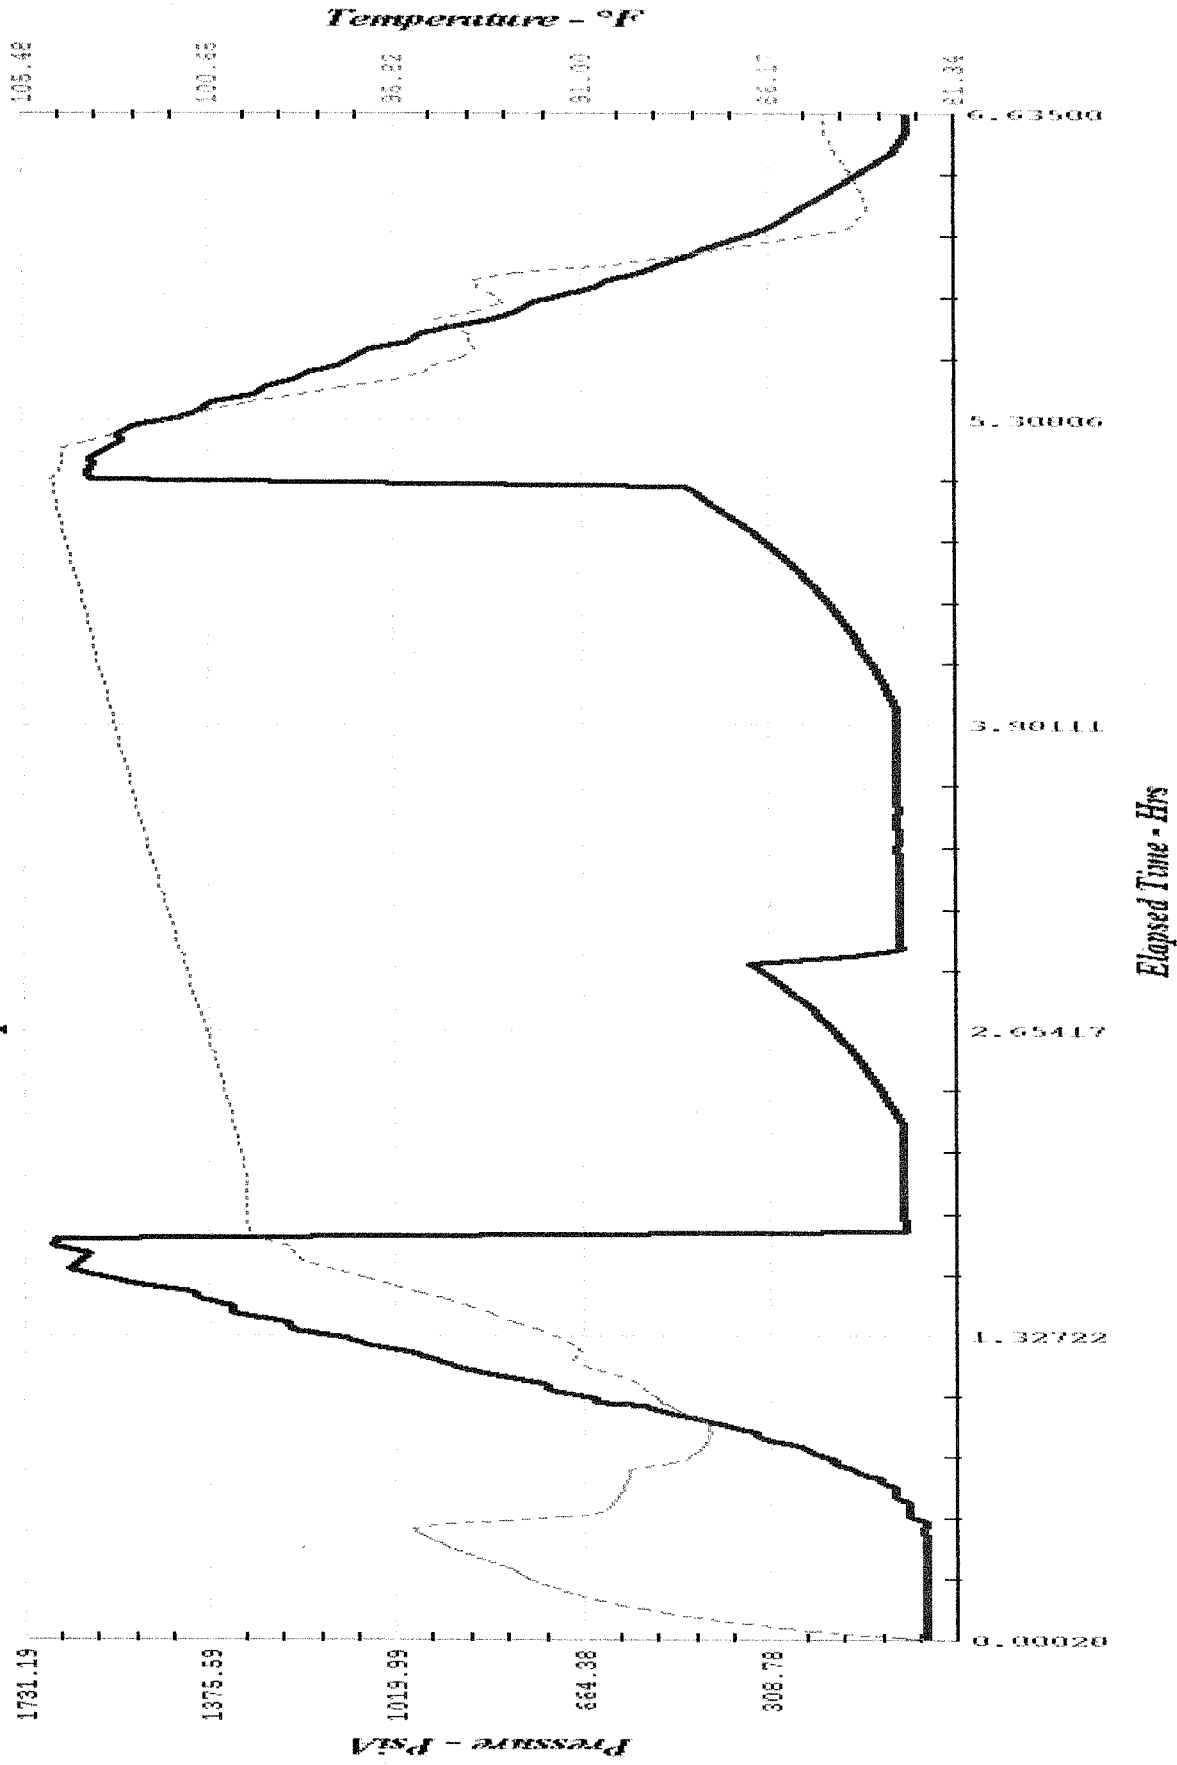

Tool serial number: 91716


Test start: 10/05/2007 23:09:17

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

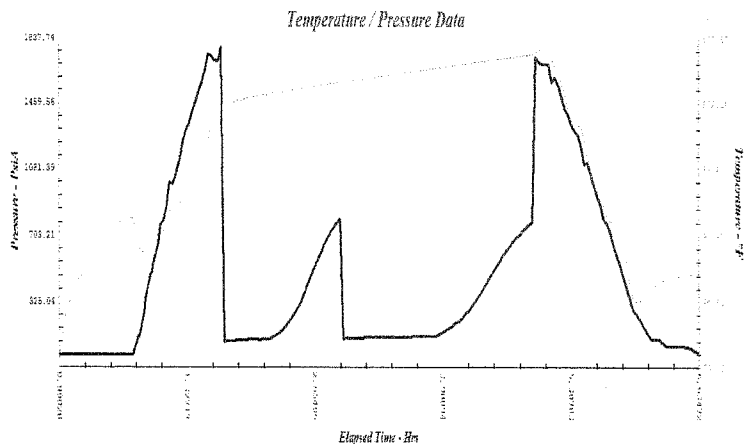

1	Initial Hydrostatic Pressure	1779
2	Initial Flow Pressure	94
3	Final Initial Flow Pressure	105
4	Initial Shut-In Pressure	793
5	Initial Final Flow Pressure	110
6	Final Flow Pressure	124
7	Final Shut-In Pressure	776
8	Final Hydrostatic Pressure	1721

Maximum Temperature 108

GENERAL INFORMATION

COMPANY NAME **TRANS PACIFIC OIL CORPORATION**

TEST DATE **10/6/07**

SECTION-TOWN-RANGE **18-15-17**

STATE **KANSAS**

COUNTY **ELLIS**

ELEVATION GROUND LEVEL **1989**

COMPANY REPRESENTATIVE **BETH**

LEASE AND WELL NUMBER **LIEKER 7-18**

FORMATION TESTED **LOWER LANSING**

DRILL STEM TEST NUMBER **3**

REPORT NUMBER **15417**

ELEVATION KELLY BUSHINGS **1992**

TESTING ENGINEER **DAVID NICHOLS**

TOOL SETTING INFORMATION

TEST INTERVAL (From) **3380**

TEST INTERVAL (to) **3505**

ANCHOR LENGTH **125**

TOTAL DEPTH (ft) **3505**

TOP PACKER DEPTH **3375**

BOTTOM PACKER DEPTH **3380**

NUMBER OF PACKERS **2**

PACKER SIZE **6 3/4**

HOLE SIZE **7 7/8**

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) **4:20**

TOOL OPEN (to) **4:50**

DURATION (min.) **30**

FINAL OPEN

TOOL OPEN (from) **5:35**

TOOL OPEN (to) **6:35**

DURATION (min.) **60**

INITIAL SHUT-IN

TOOL CLOSED (from) **4:50**

TOOL CLOSED (to) **5:35**

DURATION (min.) **45**

FINAL SHUT-IN

TOOL CLOSED (from) **6:35**

TOOL CLOSED (to) **7:35**

DURATION (min.) **60**

INITIAL FLOW

WEAK BLOW BUILT TO 3 INCHES INTO WATER IN 30 MIN

FINAL FLOW

WEAK BUILDING BLOW BUILT TO BOTTOM OF BUCKET IN 40 MIN

Company: **TRANS PACIFIC OIL CORPORATION** SEC. 18 TWP. 15 RGE. 17 Lease & Well No. **LIEKER 7-18** Test #: **3** Date: **10-6-07**

SUPERIOR TESTERS ENTERPRISES L.L.C.
DRILL STEM TEST REPORT
GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	TRANS PACIFIC OIL CORPORATION	LEASE AND WELL NUMBER	LIEKER 7-18
TEST DATE	10/6/07	FORMATION TESTED	LOWER LANSING
SECTION-TOWN-RANGE	18-15-17	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	15417
COUNTY	ELLIS	ELEVATION KELLY BUSHINGS	1992
ELEVATION GROUND LEVEL	1989	TESTING ENGINEER	DAVID NICHOLS
COMPANY REPRESENTATIVE	BETH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	NO	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	36 MILES ROUND TRIP FROM	HAYS	
TOP RECORDER DEPTH	3501	BOTTOM RECORDER DEPTH	3502
RECORDER NUMBER	91986	RECORDER NUMBER	3088


WELL INFORMATION

DRILLING CONTRACTOR	SHIELDS	DRILL COLLAR LENGTH	0
DRILL PIPE LENGTH	3161	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS

[illegible]

Temperature / Pressure Data

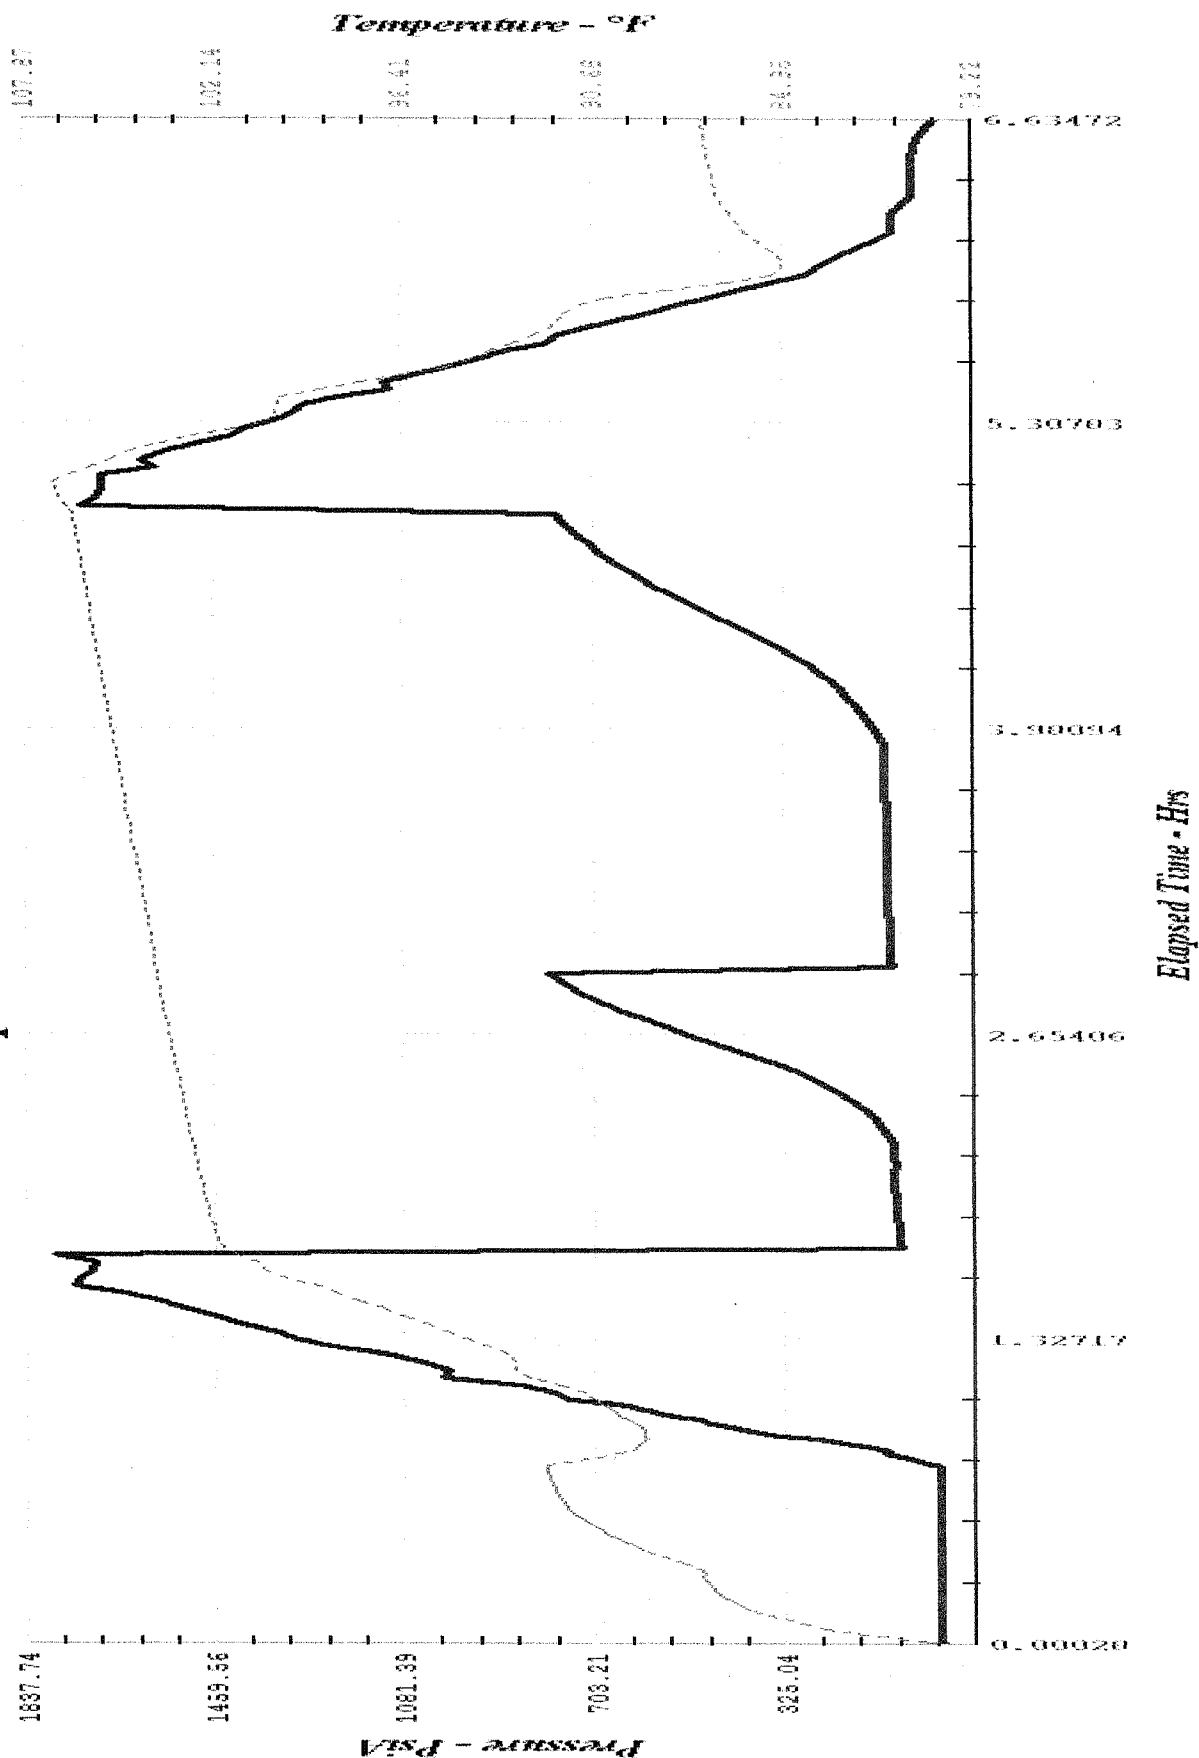

Tool serial number: 91716
 Test start: 10/06/2007 21:34:27

P.O. Box 138, Great Bend, Kansas 67530

(800) 792-6902

Final Blow good Blow Bottom Bucket in 9min Blow back on the 1st Shut-in NO

Initial Hydrostatic	1744	P.S.I.	Final Hydrostatic	1722	Blow back on the 2nd Shut-in	YES
Initial Opening	85	P.S.I. to	267	P.S.I.	Maximum Temp.	117 F
Initial Shut-in	1156	P.S.I.	from	10:30 p.m.	to	11:00 p.m.
Final Opening	2660	P.S.I. to	425	P.S.I.	from	11:00 m to 11:45 m
Final Shut-in	1120	P.S.I.	from	11:45 m to 12:45 m	to	1:45 p.m.
		P.S.I.	from	12:45 m to		

[illegible]

Total Feet Recovered 1080 Recovery Chlorides _____ Rw. _____ ohms @ _____ Degrees
Gravity of oil 34 Corrected _____ Gas to Surface in _____ minutes into the _____
Max. Gas Gauged _____ MCF/day See Gas Flow Report _____
Comments _____ Was a gas sample taken _____

Extra Equipment-Jars _____ Safety Joint _____
Electronic Recorder No. 91986 Depth 3562 Circulating Sub _____ Straddle _____
Bottom Recorder No. 9337 Depth 3563 Extra Packer (3rd) _____ Hook Wall _____
Tool Operator Sanford Extra Packer (4th) _____ Sampler _____
Approved By _____
Ticket No. 15410


Ticket No. 15418

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

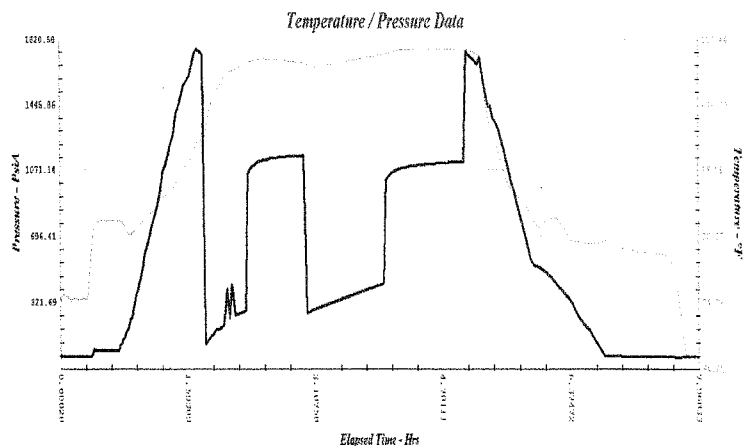

1	Initial Hydrostatic Pressure	1744
2	Initial Flow Pressure	85
3	Final Initial Flow Pressure	267
4	Initial Shut-In Pressure	1156
5	Initial Final Flow Pressure	266
6	Final Flow Pressure	425
7	Final Shut-In Pressure	1120
8	Final Hydrostatic Pressure	1722

Maximum Temperature 117

GENERAL INFORMATION

COMPANY NAME		TRANS PACIFIC OIL CORPORATION			
TEST DATE		10/7/07	LEASE AND WELL NUMBER		LEIKER 7-18
SECTION-TOWN-RANGE		18-15-17	FORMATION TESTED		ARBUCKLE
STATE		KANSAS	DRILL STEM TEST NUMBER		4
COUNTY		ELLIS	REPORT NUMBER		15418
ELEVATION GROUND LEVEL		1989	ELEVATION KELLY BUSHINGS		1992
COMPANY REPRESENTATIVE		BETH	TESTING ENGINEER		DAVID NICHOLS

TOOL SETTING INFORMATION

TEST INTERVAL (From)		3497	TOP PACKER DEPTH		3492
TEST INTERVAL (to)		3566	BOTTOM PACKER DEPTH		3497
ANCHOR LENGTH		69	NUMBER OF PACKERS		2
TOTAL DEPTH (ft)		3566	PACKER SIZE		6 3/4
			HOLE SIZE		7 7/8

FLOW TIMES

INITIAL OPEN		FINAL OPEN			
TOOL OPEN (from)		10:30	TOOL OPEN (from)		11:45
TOOL OPEN (to)		11:00	TOOL OPEN (to)		12:45
DURATION (min.)		30	DURATION (min.)		60
INITIAL SHUT-IN		FINAL SHUT-IN			
TOOL CLOSED (from)		11:00	TOOL CLOSED (from)		12:45
TOOL CLOSED (to)		11:45	TOOL CLOSED (to)		1:45
DURATION (min.)		45	DURATION (min.)		60

INITIAL FLOW

GOOD BLOW BOTTOM OF THE BUCKET IN 8 MIN

FINAL FLOW

GOOD BLOW BOTTOM OF THE BUCKET IN 9 MIN

Company: TRANS PACIFIC OIL CORPORATION
SEC. 18 TWP. 15 RGE. 17
Lease & Well No. LEIKER 7-18 Test #: 4 Date: 10-7-07

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	TRANS PACIFIC OIL CORPORATION	LEASE AND WELL NUMBER	LEIKER 7-18
TEST DATE	10/7/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	18-15-17	DRILL STEM TEST NUMBER	4
STATE	KANSAS	REPORT NUMBER	15418
COUNTY	ELLIS	ELEVATION KELLY BUSHINGS	1992
ELEVATION GROUND LEVEL	1989	TESTING ENGINEER	DAVID NICHOLS
COMPANY REPRESENTATIVE	BETH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	NO	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	36 MILES ROUND TRIP FROM	HAYS	
TOP RECORDER DEPTH	3562	BOTTOM RECORDER DEPTH	3563
RECORDER NUMBER	91986	RECORDER NUMBER	3088


WELL INFORMATION

DRILLING CONTRACTOR	SHEILDS	DRILL COLLAR LENGTH	0
DRILL PIPE LENGTH	3478	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS

[illegible]

Temperature / Pressure Data

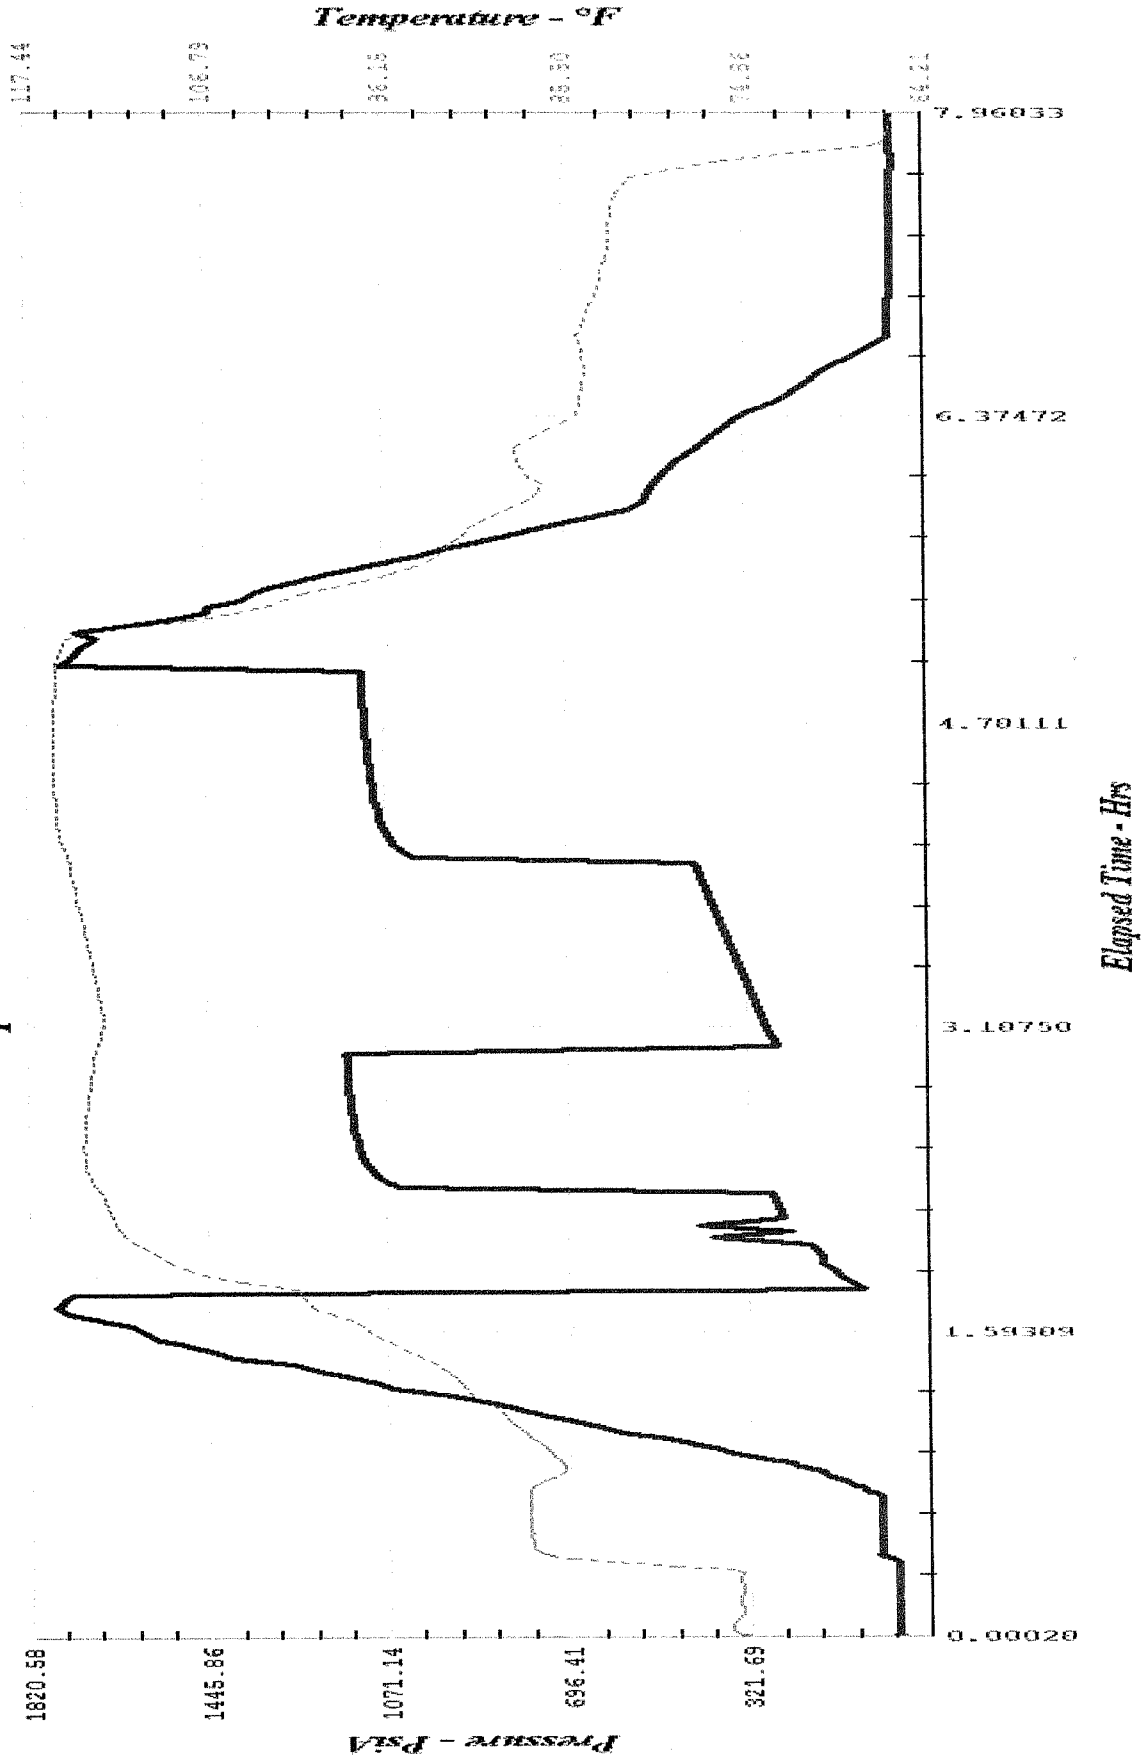

Tool serial number: 91716

Test start: 10/07/2007 16:55:51
