

15-053-20153

3-165-10w




OIL WELL CEMENTING INC.

Date 9/9/70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6984

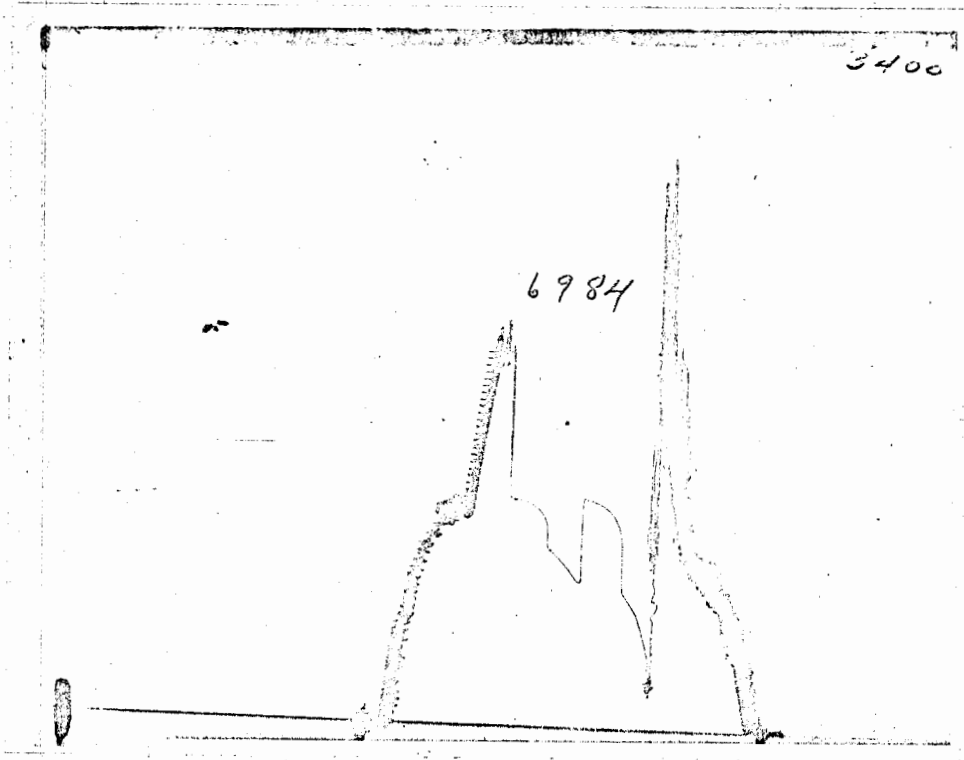

Company Kenneth Rupp Contractor Red Tiger Drlg.

Well No. 1 Lease Bednasek County Ellsworth Sec. 3 Twp 16 Rng 10

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 F.H.

Interval Tested From ~~3447~~ 3447 To 3452 Depth of Well 3452 Size Choke 5/8

Fluid Recovered In _____ Temp. _____ Elev. _____

Initial Hyd. 1949 P.S.I. Final Hyd. _____ P.S.I.

First Initial Flow Pressure 167 P.S.I. Opened Tool 12:00 ~~###~~ P.M.

First Final Flow Pressure 628 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 1091 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 679 P.S.I. Second Flow Pres. 30 Min.

Second Final Flow Pressure 838 P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 1083 P.S.I.

Blow Strong Thru-Out Test

Recovery 1800' Salt Water

Remarks _____

Approved By Salgle Tester Smith
