

GARVEY DRILLING COMPANY

TESTING DIVISION

No 3207

Company Pet. Inc. Lease & Well No. Stetsonberg #1

Elevation _____ Ticket Number _____

Date 9-29-68 Sec. _____ Twp. _____ Range _____ County Barton State Kansas

Test Approved by Jay Dirks Garvey Representative Doyle Folkerts

Formation Test No. 1 O.K. ☒ Misrun ☐ Interval Tested From 2977 to 3028 Total Depth 3028

Size Main Hole 7 7/8 Rat Hole ☐ Conv. ☒ B.T. ☐ Damaged ☐ Yes ☐ No ☐ Conv. ☐ B.T. ☐ Damaged ☐ Yes ☐ No ☐

Packer Depth 2977 Ft. Size 6 7/8 Packer Depth _____ Ft. Size _____

Straddle ☐ Yes ☒ No ☐ Conv. ☐ B.T. ☐ Damaged ☐ Yes ☐ No ☐

Packer Depth _____ Ft. Size _____

Tool Size 5" Tool Jt. Size 5 1/2" Anchor Length 51 Ft. Size 4 1/2 FH

RECORDERS Depth 2982 Ft. Clock No. 8701 Depth 2984 Ft. Clock No. 118

Top Make Kuster Cap. 4300 No. 2774 Inside ☐ Outside ☐ Bottom Make Wester Cap. 4000 No. 51 Inside ☐ Outside ☐

Below Straddle: Depth _____ Clock No. _____ Inside ☐ Outside ☐

Top Make _____ Cap. _____ No. _____ Inside ☐ Outside ☐ Bottom Make _____ Cap. _____ No. _____ Inside ☐ Outside ☐

Time Set Packer 1:58 A.M.

Tool Open I.F.P. From 2:00 M. to 2:30 M. Hr. 30 Min. From (B) 23 P.S.I. To (C) 23 P.S.I.

Tool Closed I.C.I.P. From 2:30 M. to 3:00 M. Hr. 30 Min. (D) 57 P.S.I.

Tool Open F.F.P. From 3:00 M. to 3:30 M. Hr. 30 Min. From (E) 34 P.S.I. To (F) 34 P.S.I.

Tool Closed F.C.I.P. From 3:30 M. to 4:00 M. Hr. 30 Min. (G) 37 P.S.I.

Initial Hydrostatic Pressure (A) 1645 P.S.I. Final Hydrostatic Pressure (H) 1645 P.S.I.

SURFACE Size Choke 2 1/2 In. Max. Press. P.S.I. _____ Time _____ Description of Flow _____

INFORMATION _____ M. _____

_____ M. _____

_____ M. _____

BLOW Weak Bottom Choke Size 2 In.

Did Well Flow ☐ Yes ☒ No. Recovery Total Ft. 30' 19 1/2'

Reversed Out ☐ Yes ☒ No Mud Type 5 to 6 Viscosity 42 Weight 10.1 Maximum Temp. 108 °F

EXTRA EQUIPMENT: Dual Packers NO Safety Joint NO Jars: Size _____ Make _____ Ser. No. _____

Type Circ. Sub. 1 1/2" Liberator Did Tool Plug? NO Where? _____ Did Packer Hold? YES


Length Drill Pipe 1460 ft. I. D Drill Pipe 3 1/2 in. Length Weight Pipe 1000 ft. I. D. Weight Pipe 2 1/2 in. Length Drill Collars _____ ft.

I. D. Drill Collars _____ in. Length D. S. T. Tool 68 ft.

Remarks _____

22-165-10W
SW-NW-SE

3207

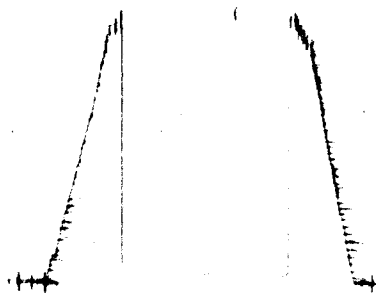

GARVEY DRILLING COMPANY

TESTING DIVISION

Nº 3208

Company Pet. Inc. Lease & Well No. Stellenberg #1

Elevation _____ Ticket Number _____

Date 9-30-68 Sec. _____ Twp. _____ Range _____ County Ellsworth State Kansas

Test Approved by Jay Dirks Garvey Representative Doyle Folkerts

Formation Test No. 2 O.K. ☒ Misrun ☐ Interval Tested From 3289 to 3315 Total Depth 3315

Size Main Hole 7 7/8 Rat Hole ☐ Conv. ☒ B.T. ☐ Damaged ☐ Yes ☒ No ☐ Conv. ☐ B.T. ☐ Damaged ☐ Yes ☐ No ☐

Packer Depth 3289 Ft. Size 4 1/2 Packer Depth _____ Ft. Size _____

Straddle ☐ Yes ☒ No ☐ Conv. ☐ B.T. ☐ Damaged ☐ Yes ☐ No ☐

Packer Depth _____ Ft. Size _____

Tool Size 5" Tool Jt. Size 5 1/2" Anchor Length 26 Ft. Size 4 1/2 FM

RECORDERS Depth 3294 Ft. Clock No. 8701 Depth 3297 Ft. Clock No. 118

Top Make Kuster Cap 4300 No. 2714 Inside Outside Bottom Make Western Cap 4000 No. 51 Inside Outside

Below Straddle: Depth _____ Clock No. _____ Inside Outside Depth _____ Ft. Clock No. _____ Inside Outside

Top Make _____ Cap _____ No. _____ Inside Outside Bottom Make _____ Cap _____ No. _____ Inside Outside

Time Set Packer 5:43 P

Tool Open I.F.P. From 5:45 M. to 6:15 M. Hr. 30 Min. From (B) 123 P.S.I. To (C) 765 P.S.I.

Tool Closed I.C.I.P. From 6:15 M. to 6:45 M. Hr. 30 Min. (D) 1053 P.S.I.

Tool Open F.F.P. From 6:45 M. to 7:15 M. Hr. 30 Min. From (E) 820 P.S.I. To (F) 931 P.S.I.

Tool Closed F.C.I.P. From 7:15 M. to 7:45 M. Hr. 30 Min. (G) 1053 P.S.I.

Initial Hydrostatic Pressure (A) 1809 P.S.I. Final Hydrostatic Pressure (H) 1809 P.S.I.

SURFACE Size Choke 4 In. Max. Press. P.S.I. _____ Time _____ Description of Flow _____

INFORMATION _____ M. _____

_____ M. _____

_____ M. _____

BLOW Good Bottom Choke Size 4 In.

Did Well Flow ☒ Yes ☐ No Recovery Total Ft. 2230' Sulphur Water with Scum & Oil

Reversed Out ☒ Yes ☐ No Mud Type Steady Viscosity 41 Weight 10 Maximum Temp. 118 °F

EXTRA EQUIPMENT: Dual Packers NO Safety Joint NO Jars: Size _____ Make _____ Ser. No. _____

Type Circ. Sub. Halliburton Did Tool Plug? NO Where? _____ Did Packer Hold? Yes

Length Drill Pipe 2262 ft. I. D Drill Pipe 3 1/2 In. Length Weight Pipe 1000 ft. I. D. Weight Pipe 2 1/2 In. Length Drill Collars _____ ft.

I. D. Drill Collars _____ In. Length D. S. T. Tool 5.3 ft.

Remarks _____

22-165-10W
SW-NW-SE

3208

