


Telephone
(316) 793-6347

Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424

Company NATIONAL DEVELOPMENT Date SEPTEMBER 29, 1982
Address RIVERFRONT PLACE 833 N. WACO WICHITA, KANSAS 67203
Drilling Contractor DUKE DRILLING Rig No. 2
Lease, Well No. LAMBERT # 1 County BARTON Sec 17 Twp. 16 Rng 12
Size Hole 7 7/8 Size Pipe 4 1/2 FH - XH Size Tool 3 1/2 FH
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 FH
Interval Tested 2880 to 2897 Total Depth 2897
Test No. 1 Successful No. 1 Misrun No. 0
Formation Tested TOPEKA Time Packer Set 6:55 A.M. Time Tool Opened 7:00 A.M.
Tool Open 45-45 Min. Initial Shut-in-Time 30 Min. Final Shut-in-Time 30 Min.
Blow BLEW OFF BOTTOM OF BUCKET IN 1 MIN.
STRONG BLOW ON SECOND OPEN.
Recovery 20' OIL CUT MUDDY WATER; 2280' GAS CUT MUDDY WATER (SHOW OF OIL)
Remarks TEMPERATURE 108 DEGREES
Initial BHP 1368# IFP 138# - 677# FFP 740# - 1004# Final BHP 1358#
Hydrastatic Press. 1472#-1462# Mud Wt. 9.7 Vis. 43 Water Loss 9.6cc
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester GARY A. SHOOK Approved By JIM MUSGROVE Ticket No. 1494

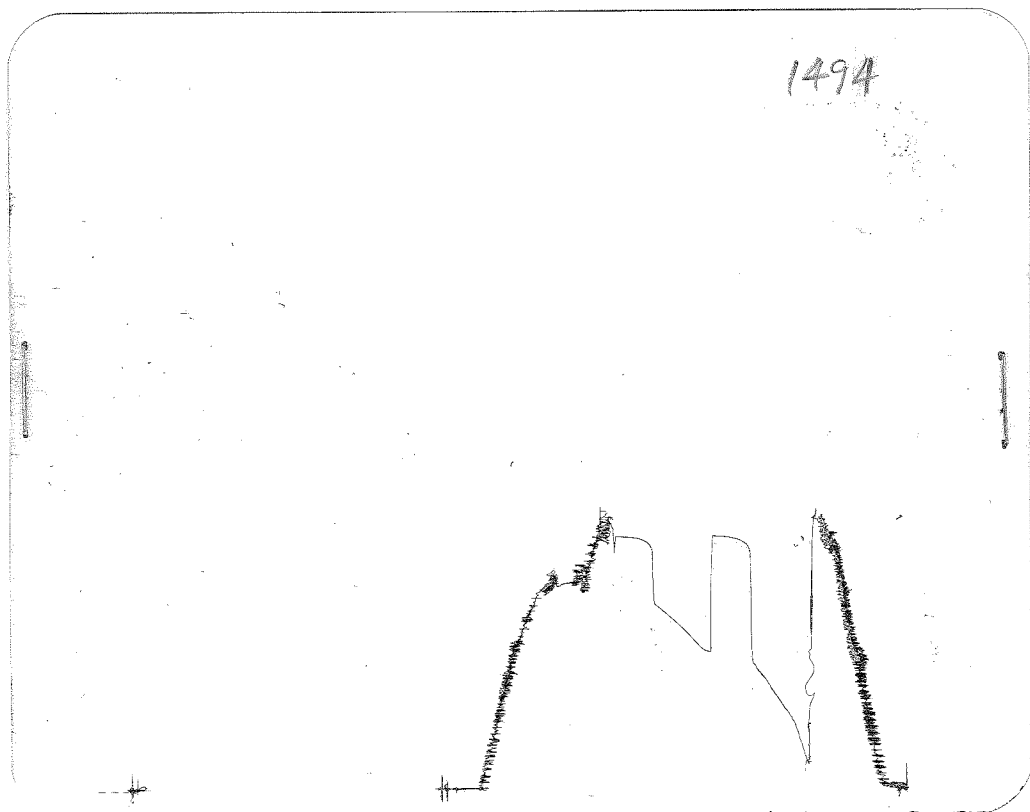


Telephone
(316) 793-6347

Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424

Company NATIONAL DEVELOPMENT Date SEPTEMBER 29, 1982
Address RIVERFRONT PLACE, 833 N. WAGO WICHITA, KANSAS 67203
Drilling Contractor DUKE DRILLING Rig No. 2
Lease, Well No. LAMBERT #1 County BARTON Sec 17 Twp 16 Rng 12
Size Hole 7 7/8 Size Pipe 4 1/2 FH-XH Size Tool 3 1/2 FH
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 FH
Interval Tested 3045 to 3084 Total Depth 3084
Test No. 2 Successful No. 2 Misrun No. 0
Formation Tested KC Time Packer Set 2:55 A.M. Time Tool Opened 3:00 A.M.
Tool Open 45-45 Min. Initial Shut-in-Time 45 Min. Final Shut-in-Time 45 Min.
Blow BLEW OFF BOTTOM OF BUCKET IN 1 MIN.
STRONG BLOW ON SECOND OPEN.
Recovery 2400' OIL, GAS CUT WATER
Remarks "75% WATER 25% OIL"
TEMPERATURE 108 DEGREES
Initial BHP 1369# IFP 85# - 793# FFP 878# - 1108# Final BHP 1358#
Hydrastatic Press. 1631 # - 1631# Mud Wt. 9.7 Vis. 44 Water Loss 9.6cc
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester GARY A. SHOOK Approved By ROD TREMBLAY Ticket No. 1495

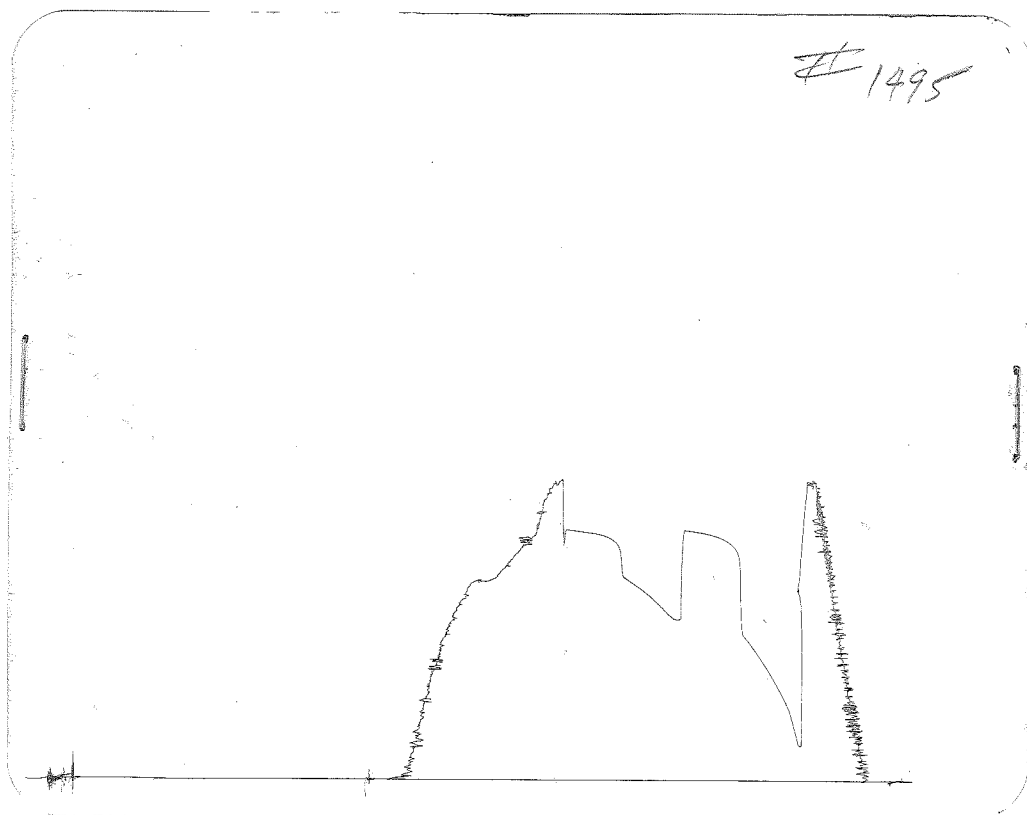

Telephone
(316) 793-6347

Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424

Company NATIONAL DEVELOPMENT Date SEPTEMBER 29, 1982

Address RIVERFRONT PLACE, 833 N. WACO, WICHITA, KANSAS 67203

Drilling Contractor DUKE DRILLING Rig No. 2

Lease, Well No. LAMBERT #1 County B ARTON Sec 17 Twp. 16 Rng 12

Size Hole 7 7/8 Size Pipe 4 1/2 FH-XH Size Tool 3 1/2 FH

Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 FH

Interval Tested 3127 to 3140 Total Depth 3140

Test No. 3 Successful No. 3 Misrun No. 0

Formation Tested KC Time Packer Set 6:05 P.M. Time Tool Opened 6:10 P.M.

Tool Open 45-45 Min. Initial Shut-in-Time 45 Min. Final Shut-in-Time 45 Min.

Blow BLEW OFF BOTTOM OF BUCKET IN 2 MIN. ON FIRST OPEN.

STRONG BLOW ON SECOND OPEN.

Recovery 1930' GAS - CUT WATER (NO SHOW OF OIL)


Remarks TEMPERATURE 104 DEGREES

Initial BHP 1108# IFP 106# -519# FFP 667# - 835# Final BHP 1129#

Hydrastatic Press. 1652# - 1620# Mud Wt. 9.5 Vis. 44 Water Loss 21.2cc

Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____

Tester GARY A. SHOOK Approved By JIM MUSGROVE Ticket No. 1496

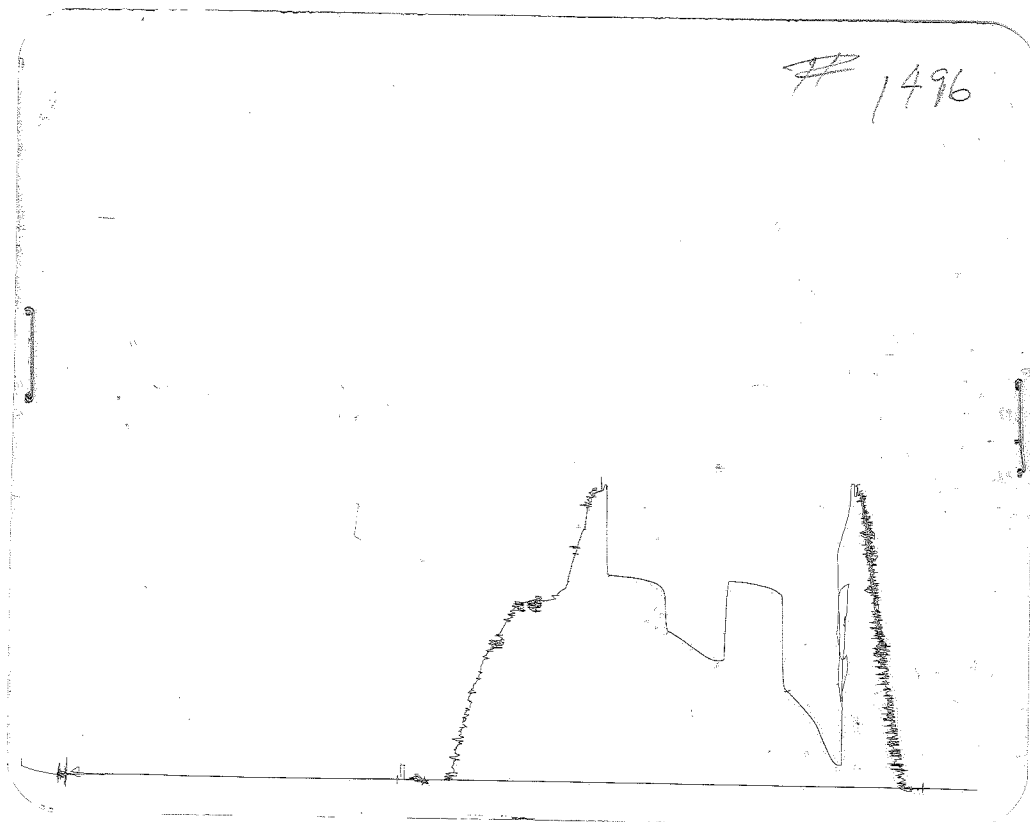

Telephone
(316) 793-6347

Mobil — (316) 793-7859
Unit 7076



Company NATIONAL DEVELOPMENT Date SEPTEMBER 29, 1982
Address RIVERFRONT PLACE, 833 N. WACO, WICHITA, KANSAS 67203
Drilling Contractor DUKE DRILLING Rig No. 2
Lease, Well No. LAMBERT #1 County BARTON Sec 17 Twp. 16 Rng 12
Size Hole 2 7/8 Size Pipe 4 1/2 FH - XH Size Tool 3 1/2 FH
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 FH
Interval Tested 3178 to 3220 Total Depth 3220
Test No. 4 Successful No. 4 Misrun No. 0
Formation Tested KC Time Packer Set 12:20 P.M. Time Tool Opened 12:25 P.M.
Tool Open 30-30 Min. Initial Shut-in-Time 30 Min. Final Shut-in-Time 30 Min.
Blow BLEW OFF BOTTOM OF BUCKET IN 20 MIN. ON FIRST OPEN.
STRONG BLOW ON SECOND OPEN.
Recovery 660' GAS IN PIPE: 35' SLIGHTLY OIL CUT MUD; 60' OIL CUT MUD; 60' HEAVY
OIL CUT MUD.
Remarks TEMPERATURE 98 DEGREES

Initial BHP 413# IFP 64#-64# FFP 95# - 85# Final BHP 530#
Hydrastatic Press. 1715# - 1705# Mud Wt. 9.7 Vis. 48 Water Loss 11.2cc
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester GARY A. SHOOK Approved By JIM MUSGROVE Ticket No. _____

1497

