

TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Larson Operating**

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lewellyn

33 16S 27W Lane KS

Anderson #1-33

Start Date: 2006.12.04 @ 14:14:00

End Date: 2006.12.04 @ 21:31:45

Job Ticket #: 25646 DST #: 1

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Larson Operating

562 W Hwy 4
Olmritz KS 67564-8561

ATTN: Bob Lewellyn

Anderson #1-33

33 16S 27W Lane KS

Job Ticket: 25646

DST#: 1

Test Start: 2006.12.04 @ 14:14:00

GENERAL INFORMATION:

Formation: **L/KC "A"**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 16:30:00

Time Test Ended: 21:31:45

Test Type: Conventional Bottom Hole

Tester: Chuck Smith

Unit No: 37

Interval: **3963.00 ft (KB) To 3980.00 ft (KB) (TVD)**

Total Depth: 3980.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2687.00 ft (KB)

2682.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 8017

Inside

Press@RunDepth: 55.66 psig @ 3966.00 ft (KB)

Start Date: 2006.12.04

End Date:

2006.12.04

Start Time: 14:14:01

End Time:

21:31:45


Capacity: 7000.00 psig

Last Calib.: 2006.12.04

Time On Btm: 2006.12.04 @ 16:29:45

Time Off Btm: 2006.12.04 @ 18:53:45

TEST COMMENT: IF Weak surface blow
ISI No return
FF Weak surface blow
FSI No return

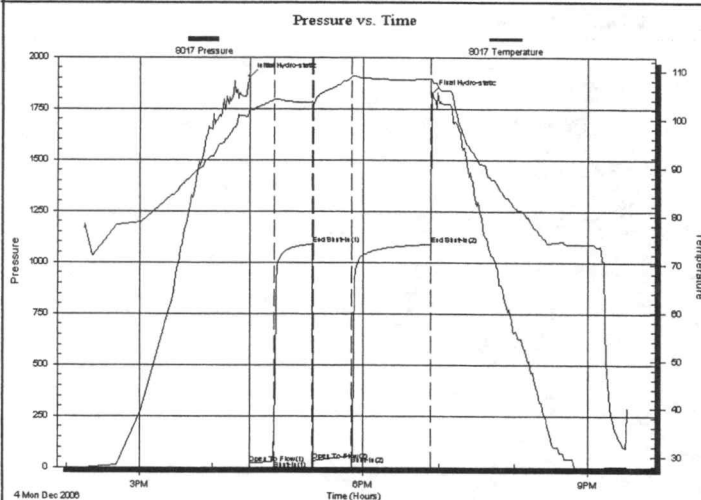

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1904.75	102.45	Initial Hydro-static
1	18.04	101.74	Open To Flow (1)
20	31.18	103.98	Shut-In (1)
50	1089.66	103.71	End Shut-In (1)
51	32.68	103.44	Open To Flow (2)
81	55.66	108.71	Shut-In (2)
144	1088.44	108.40	End Shut-In (2)
144	1824.92	108.42	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	M 100%M	0.02
85.00	MCW 10%M 90%W	0.42

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Operating

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lew ellyn

Anderson #1-33

33 16S 27W Lane KS

Job Ticket: 25646

DST#: 1

Test Start: 2006.12.04 @ 14:14:00

Tool Information

Drill Pipe:	Length: 3814.00 ft	Diameter: 3.80 inches	Volume: 53.50 bbl	Tool Weight:	1800.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	34000.00 lb
Drill Collar:	Length: 125.00 ft	Diameter: 2.25 inches	Volume: 0.61 bbl	Weight to Pull Loose:	75000.00 lb
		Total Volume:	54.11 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	4.00 ft			String Weight: Initial	54000.00 lb
Depth to Top Packer:	3963.00 ft			Final	55000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	17.00 ft				
Tool Length:	45.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		
Tool Comments:					
Tool slid 15 feet.					

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			3936.00	
Shut In Tool	5.00			3941.00	
Hydraulic tool	5.00			3946.00	
Jars	5.00			3951.00	
Safety Joint	3.00			3954.00	
Packer	5.00			3959.00	28.00 Bottom Of Top Packer
Packer	4.00			3963.00	
Stubb	1.00			3964.00	
Perforations	2.00			3966.00	
Recorder	0.00	8017	Inside	3966.00	
Perforations	9.00			3975.00	
Recorder	0.00	13309	Inside	3975.00	
Bullnose	5.00			3980.00	17.00 Bottom Packers & Anchor

Total Tool Length: 45.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Operating

Anderson #1-33

562 W Hwy 4
Olmitz KS 67564-8561

33 16S 27W Lane KS

Job Ticket: 25646

DST#: 1

ATTN: Bob Lewellyn

Test Start: 2006.12.04 @ 14:14:00

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

36000 ppm

Viscosity: 45.00 sec/qt

Cushion Volume:

bbl

Water Loss: 5.59 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 1900.00 ppm

Filter Cake: 1.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
5.00	M 100%M	0.025
85.00	MCW 10%M 90%W	0.418

Total Length: 90.00 ft

Total Volume: 0.443 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0


Serial #:


Laboratory Name:

Laboratory Location:

Recovery Comments: RW; .389 @ 36 degrees F = 36000 chlorides.

Pressure vs. Time

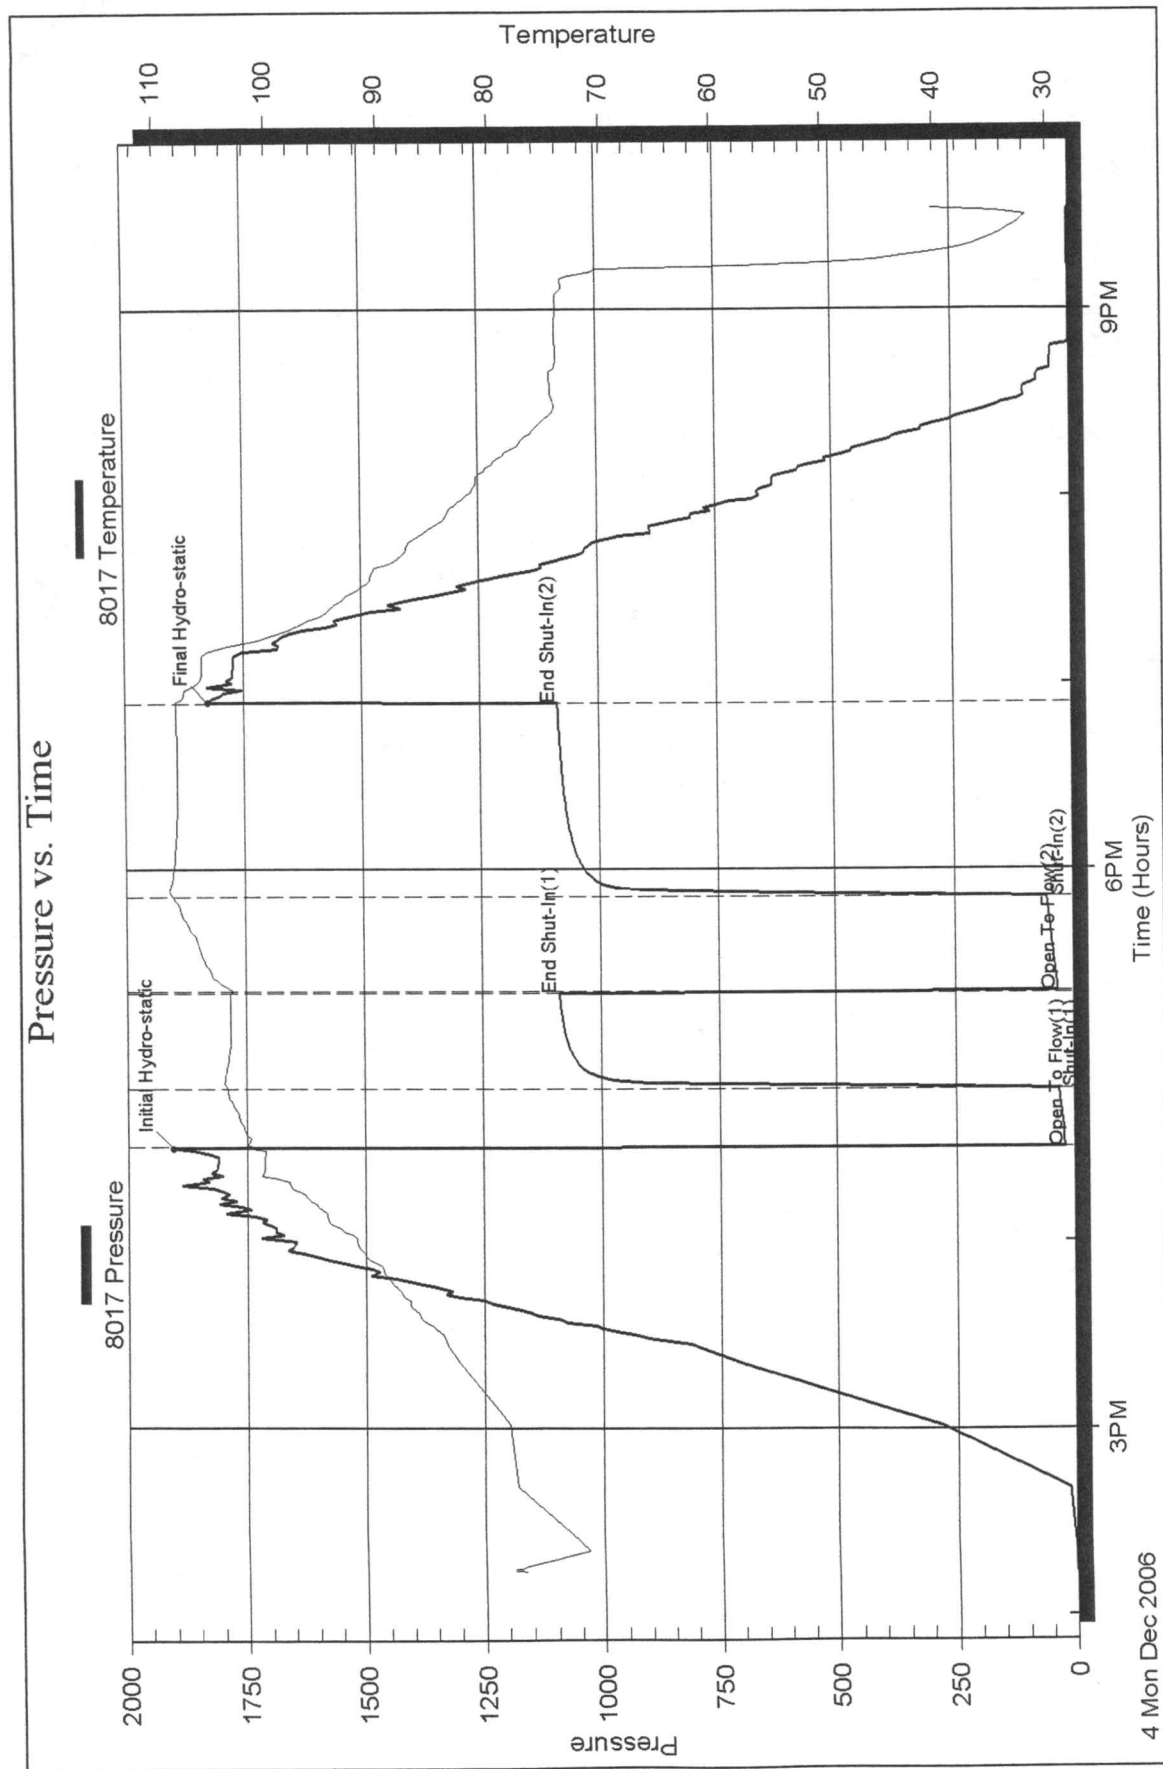



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Larson Operating**

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lewellyn

33 16S 27W Lane KS

Anderson #1-33

Start Date: 2006.12.06 @ 14:45:00

End Date: 2006.12.06 @ 22:53:30

Job Ticket #: 25647 DST #: 2

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Larson Operating

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lewellyn

Anderson #1-33

33 16S 27W Lane KS

Job Ticket: 25647

DST#: 2

Test Start: 2006.12.06 @ 14:45:00

GENERAL INFORMATION:

Formation: **Altamont**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 18:02:45

Time Test Ended: 22:53:30

Test Type: Conventional Bottom Hole

Tester: Chuck Smith

Unit No: 37

Interval: **4344.00 ft (KB) To 4384.00 ft (KB) (TVD)**

Total Depth: 4384.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2687.00 ft (KB)

2682.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 8017

Inside

Press@RunDepth: 22.65 psig @ 4347.00 ft (KB)

Start Date: 2006.12.06

End Date:

2006.12.06

Start Time: 14:45:01

End Time:

22:53:30

Capacity: 7000.00 psig

Last Calib.: 2006.12.06

Time On Btm: 2006.12.06 @ 18:02:30


Time Off Btm: 2006.12.06 @ 20:24:00

TEST COMMENT: IF Weak surface blow died @ 14 min.

ISI No return

FF No blow

FSI No return

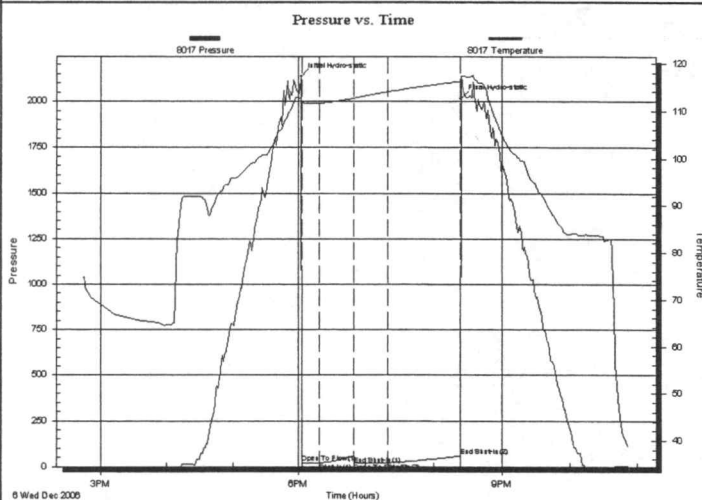

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2136.07	112.59	Initial Hydro-static
1	20.14	111.74	Open To Flow (1)
16	21.54	111.61	Shut-In (1)
47	59.87	112.68	End Shut-In (1)
47	21.23	112.67	Open To Flow (2)
78	22.65	114.05	Shut-In (2)
141	58.94	116.26	End Shut-In (2)
142	2016.90	117.45	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
3.00	M 100%M	0.01

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Operating

562 W Hwy 4
Olmritz KS 67564-8561

ATTN: Bob Lewellyn

Anderson #1-33

33 16S 27W Lane KS

Job Ticket: 25647

DST#: 2

Test Start: 2006.12.06 @ 14:45:00

Tool Information

Drill Pipe:	Length: 4221.00 ft	Diameter: 3.80 inches	Volume: 59.21 bbl	Tool Weight: 1800.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 125.00 ft	Diameter: 2.25 inches	Volume: 0.61 bbl	Weight to Pull Loose: 80000.00 lb
		Total Volume: 59.82 bbl		Tool Chased 0.00 ft
Drill Pipe Above KB:	30.00 ft			String Weight: Initial 57000.00 lb
Depth to Top Packer:	4344.00 ft			Final 57000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	40.00 ft			
Tool Length:	68.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		
Tool Comments:				

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			4317.00	
Shut In Tool	5.00			4322.00	
Hydraulic tool	5.00			4327.00	
Jars	5.00			4332.00	
Safety Joint	3.00			4335.00	
Packer	5.00			4340.00	28.00 Bottom Of Top Packer
Packer	4.00			4344.00	
Stubb	1.00			4345.00	
Perforations	2.00			4347.00	
Recorder	0.00	8017	Inside	4347.00	
Perforations	32.00			4379.00	
Recorder	0.00	13309	Inside	4379.00	
Bullnose	5.00			4384.00	40.00 Bottom Packers & Anchor

Total Tool Length: 68.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Operating

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lewellyn

Anderson #1-33

33 16S 27W Lane KS

Job Ticket: 25647

DST#: 2

Test Start: 2006.12.06 @ 14:45:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 50.00 sec/qt

Water Loss: 6.79 in³

Resistivity: 0.00 ohm.m

Salinity: 2500.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psig

Oil API:

Water Salinity:

0 deg API

0 ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
3.00	M 100%M	0.015

Total Length: 3.00 ft

Total Volume: 0.015 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

Pressure vs. Time

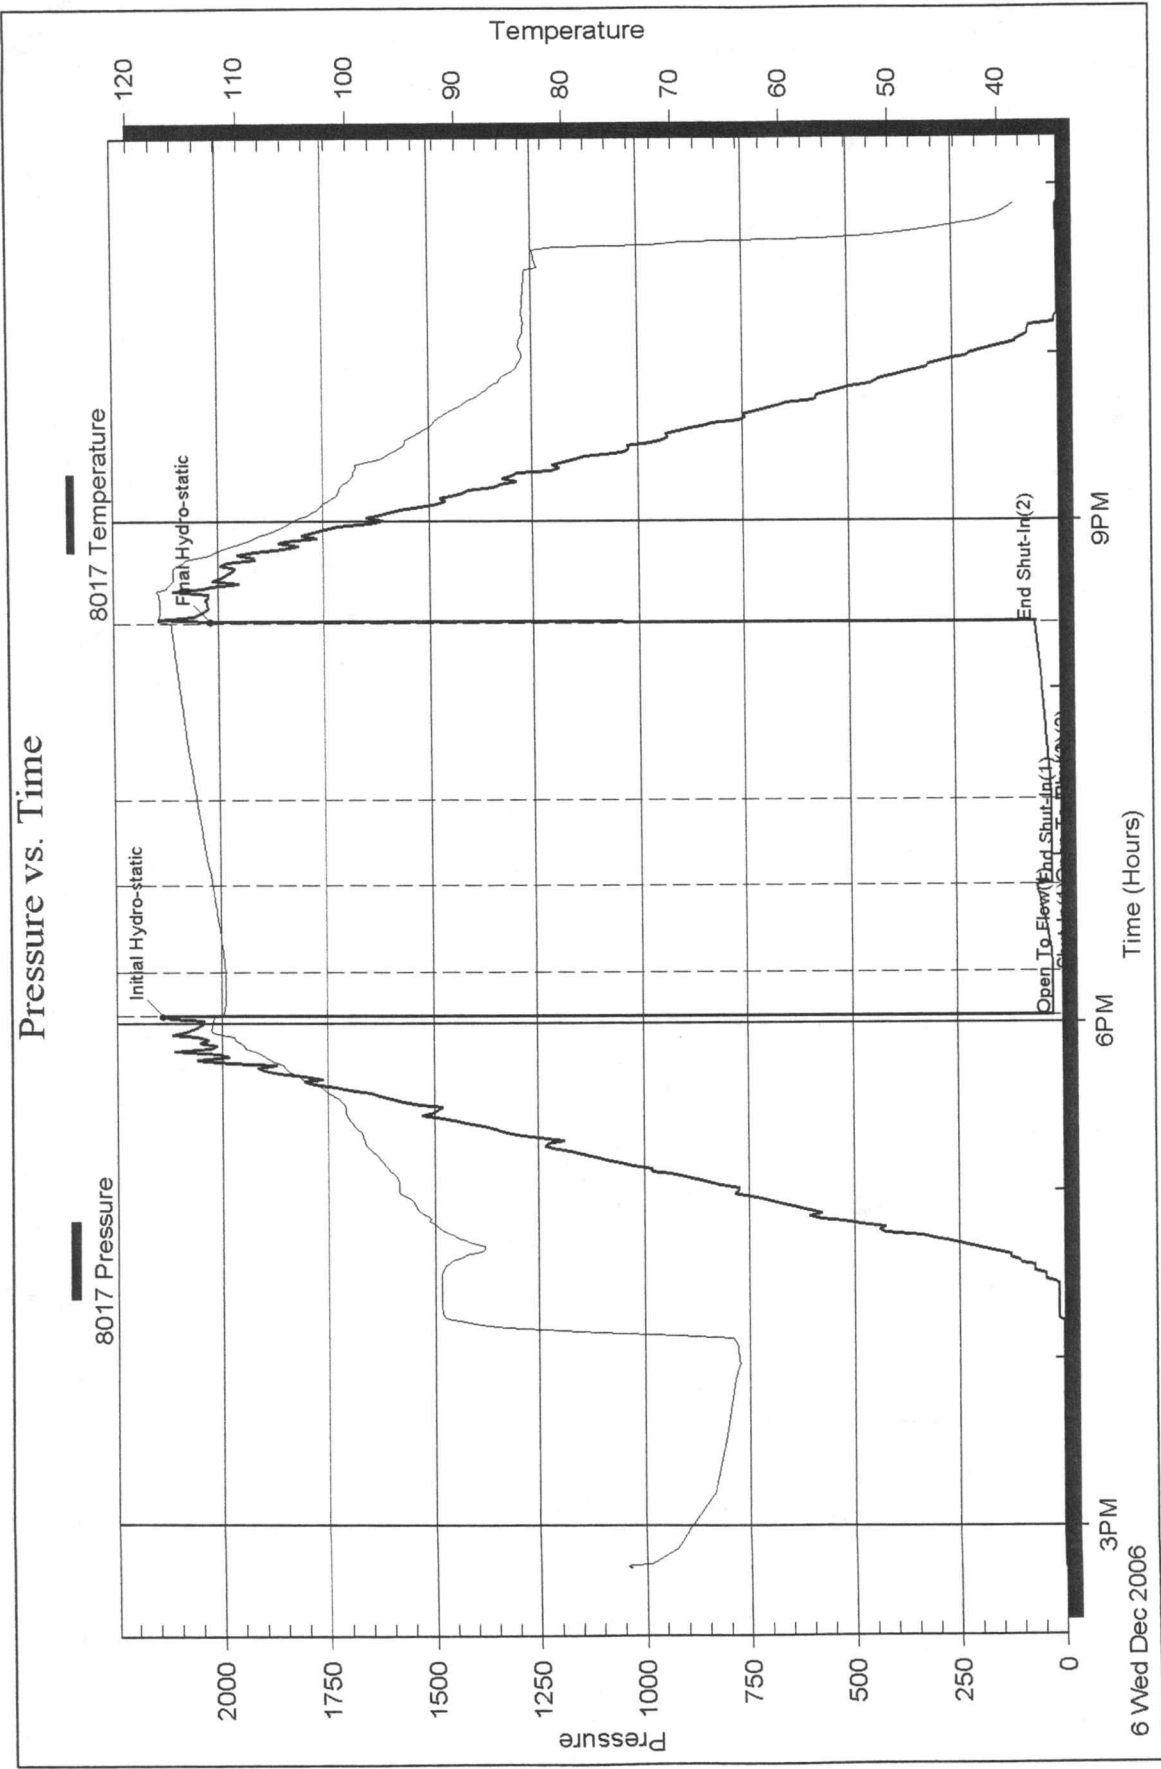



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Larson Operating**

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lewellyn

33 16S 27W Lane KS

Anderson #1-33

Start Date: 2006.12.07 @ 15:25:00

End Date: 2006.12.07 @ 23:00:30

Job Ticket #: 25648 DST #: 3

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Larson Operating

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lewellyn

Anderson #1-33

33 16S 27W Lane KS

Job Ticket: 25648

DST#: 3

Test Start: 2006.12.07 @ 15:25:00

GENERAL INFORMATION:

Formation: **Ft. Scott**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 17:49:15

Time Test Ended: 23:00:30

Test Type: Conventional Bottom Hole

Tester: Chuck Smith

Unit No: 37

Interval: **4438.00 ft (KB) To 4512.00 ft (KB) (TVD)**

Total Depth: 4512.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2687.00 ft (KB)

2682.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 8017

Inside

Press@RunDepth: 21.38 psig @ 4442.00 ft (KB)

Start Date: 2006.12.07

End Date:

2006.12.07

Capacity: 7000.00 psig

Last Calib.: 2006.12.07

Start Time: 15:25:01

End Time:

23:00:30

Time On Btm: 2006.12.07 @ 17:49:00


Time Off Btm: 2006.12.07 @ 20:08:45

TEST COMMENT: IF Weak surface blow

ISI No return

FF No blow

FSI No return

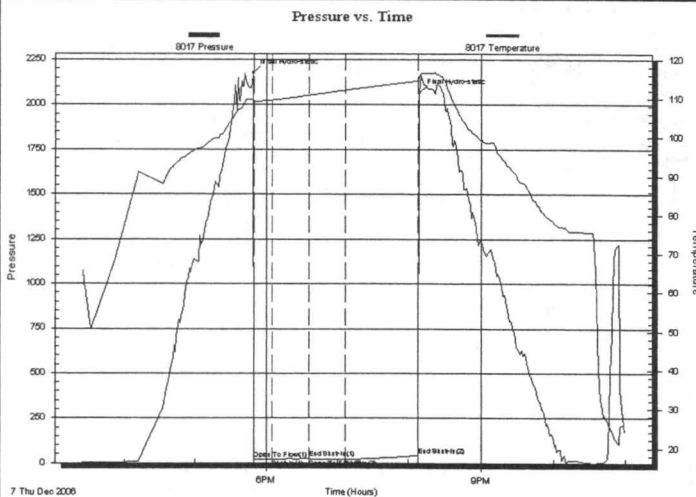

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2174.38	109.87	Initial Hydro-static
1	19.70	108.83	Open To Flow (1)
16	20.11	109.65	Shut-In(1)
47	26.53	110.85	End Shut-In(1)
48	19.93	110.86	Open To Flow (2)
78	21.38	112.16	Shut-In(2)
139	42.30	114.53	End Shut-In(2)
140	2065.04	115.66	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
3.00	M 100%M	0.01

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Operating

Anderson #1-33

562 W Hwy 4
Olmritz KS 67564-8561

33 16S 27W Lane KS

Job Ticket: 25648

DST#: 3

ATTN: Bob Lewellyn

Test Start: 2006.12.07 @ 15:25:00

Tool Information

Drill Pipe:	Length: 4283.00 ft	Diameter: 3.80 inches	Volume: 60.08 bbl	Tool Weight:	1800.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	30000.00 lb
Drill Collar:	Length: 125.00 ft	Diameter: 2.25 inches	Volume: 0.61 bbl	Weight to Pull Loose:	70000.00 lb
		Total Volume:	60.69 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	29.00 ft			String Weight: Initial	60000.00 lb
Depth to Top Packer:	4438.00 ft			Final	60000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	74.00 ft				
Tool Length:	133.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		
Tool Comments:					

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	32.00			4411.00	
Shut In Tool	5.00			4416.00	
Hydraulic tool	5.00			4421.00	
Jars	5.00			4426.00	
Safety Joint	3.00			4429.00	
Packer	5.00			4434.00	59.00 Bottom Of Top Packer
Packer	4.00			4438.00	
Stubb	1.00			4439.00	
Perforations	3.00			4442.00	
Recorder	0.00	8017	Inside	4442.00	
Perforations	32.00			4474.00	
Change Over Sub	1.00			4475.00	
Drill Pipe	31.00			4506.00	
Change Over Sub	1.00			4507.00	
Recorder	0.00	13276	Inside	4507.00	
Bullnose	5.00			4512.00	74.00 Bottom Packers & Anchor
Total Tool Length:		133.00			



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Operating

Anderson #1-33

562 W Hwy 4
Olmitz KS 67564-8561

33 16S 27W Lane KS

Job Ticket: 25648

DST#: 3

ATTN: Bob Lewellyn

Test Start: 2006.12.07 @ 15:25:00

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 48.00 sec/qt

Cushion Volume:

bbl

Water Loss: 7.19 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2600.00 ppm

Filter Cake: 1.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
3.00	M 100%M	0.015

Total Length: 3.00 ft Total Volume: 0.015 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

Pressure vs. Time

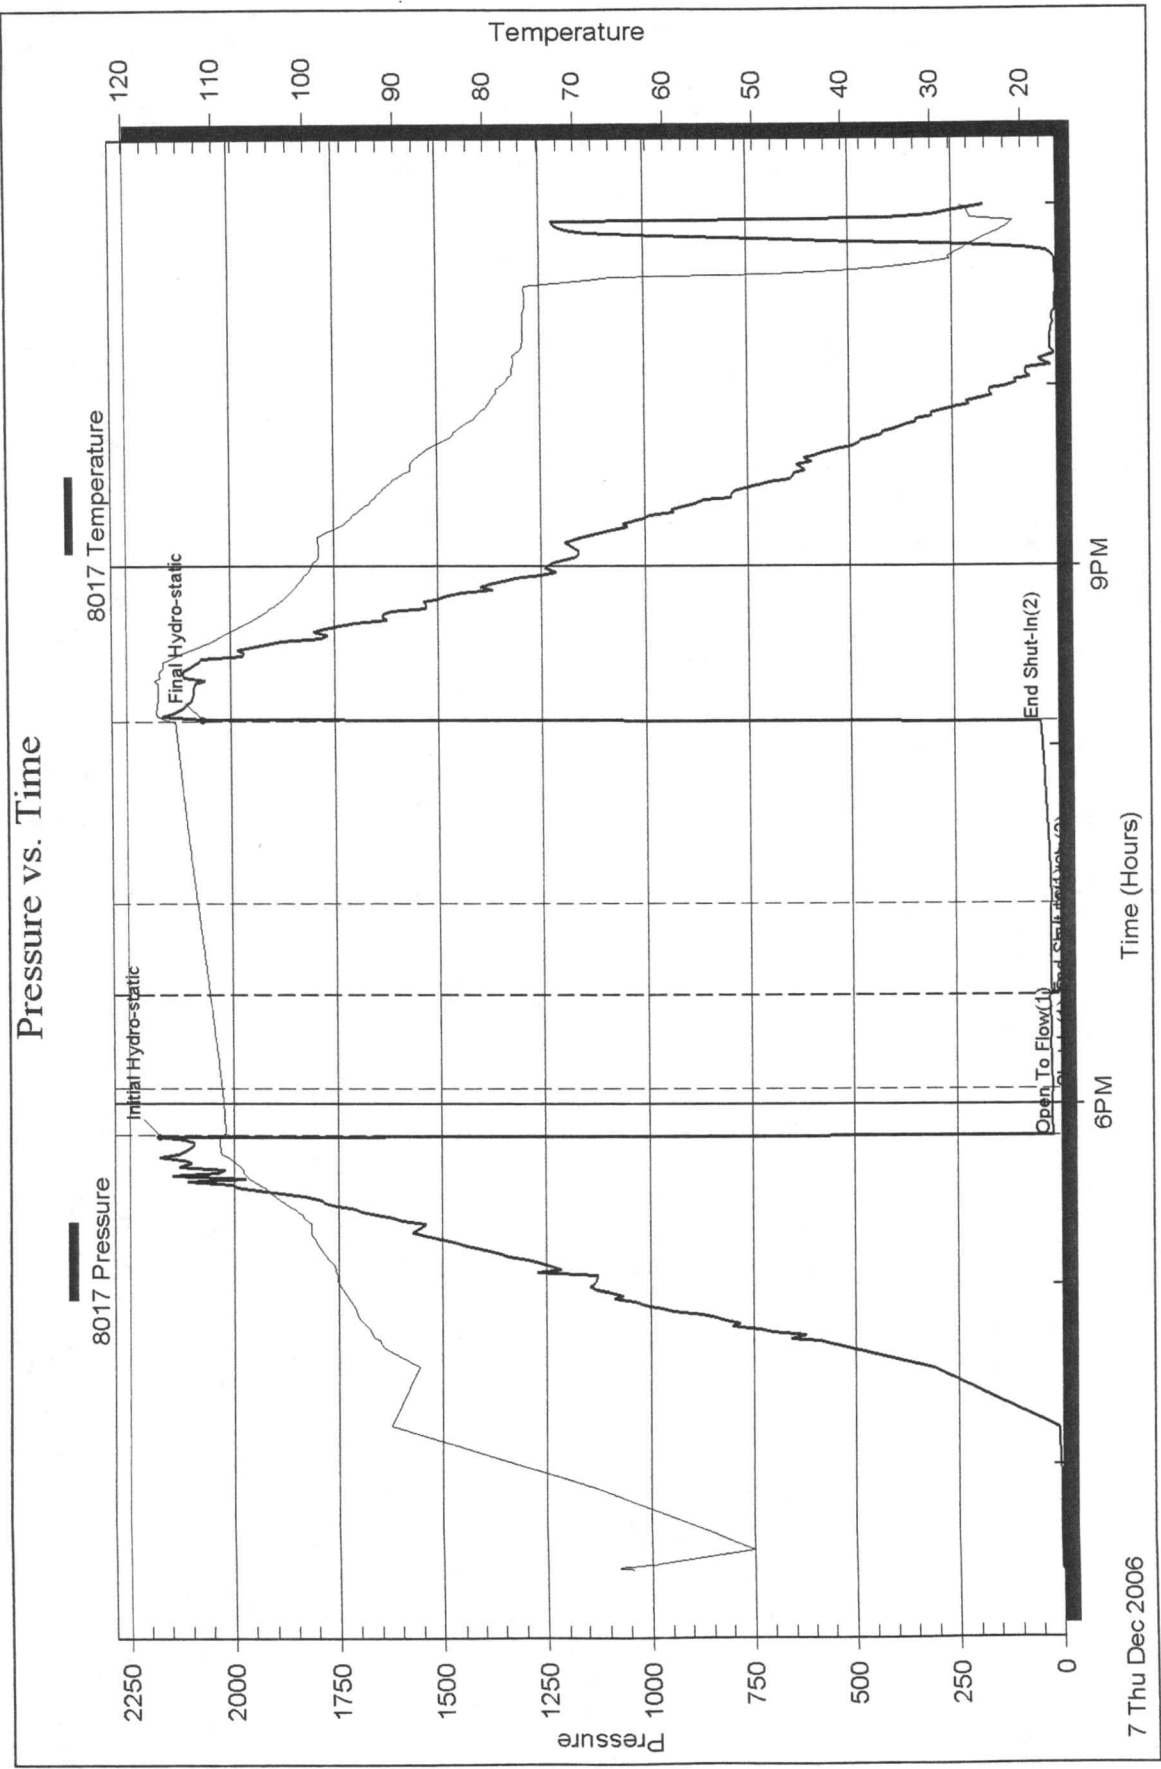



DRILL STEM TEST REPORT

Prepared For: **Larson Operating**

562 W Hwy 4
Olmits KS 67564-8561

ATTN: Bob Lewellyn

33 16S 27W Lane KS

Anderson #1-33

Start Date: 2006.12.09 @ 00:40:29

End Date: 2006.12.09 @ 08:11:08

Job Ticket #: 25544 DST #: 4

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Larson Operating
562 W Hwy 4
Olmitz KS 67564-8561
ATTN: Bob Lewellyn

Anderson #1-33
33 16S 27W Lane KS
Job Ticket: 25544 **DST#: 4**
Test Start: 2006.12.09 @ 00:40:29

GENERAL INFORMATION:

Formation: **LKC-J**
Deviated: **No** Whipstock: **ft (KB)**
Time Tool Opened: 02:55:09
Time Test Ended: 08:11:08

Test Type: Conventional Straddle
Tester: Brandon Turley
Unit No: 35

Interval: **4190.00 ft (KB) To 4225.00 ft (KB) (TVD)**
Total Depth: **4640.00 ft (KB) (TVD)**
Hole Diameter: **7.88 inches** Hole Condition: **Good**

Reference Elevations: **2687.00 ft (KB)**
2682.00 ft (CF)
KB to GR/CF: **5.00 ft**

Serial #: 6772


Inside

Press@RunDepth: **19.55 psig @ 4191.00 ft (KB)**
Start Date: **2006.12.09** End Date: **2006.12.09**
Start Time: **00:40:29** End Time: **08:11:08**

Capacity: **7000.00 psig**
Last Calib.: **2006.12.09**
Time On Btm: **2006.12.09 @ 02:54:54**
Time Off Btm: **2006.12.09 @ 05:12:08**

TEST COMMENT: IF 1/4 blow died in 7 min.
IS No return
FF No blow
FS No return

Pressure vs. Time

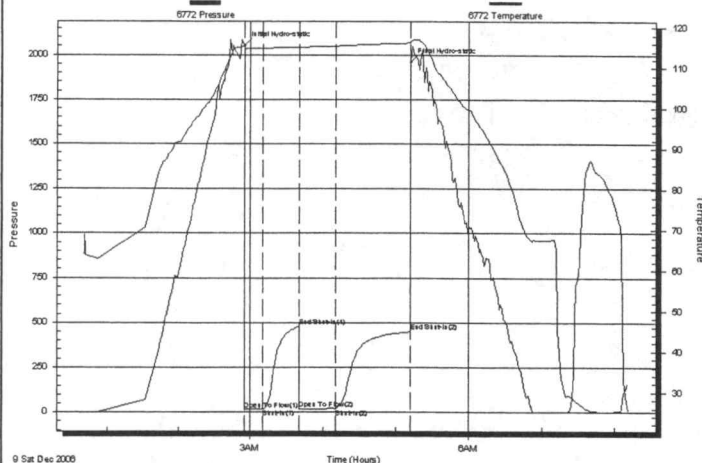

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2050.16	115.41	Initial Hydro-static
1	14.40	114.34	Open To Flow (1)
16	17.23	114.88	Shut-In(1)
46	478.64	115.23	End Shut-In(1)
46	17.92	115.08	Open To Flow (2)
76	19.55	115.43	Shut-In(2)
137	448.75	116.20	End Shut-In(2)
138	1958.45	116.57	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	Mud 100%M	0.02

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Operating

562 W Hwy 4
Olmitz KS 67564-8561

ATTN: Bob Lewellyn

Anderson #1-33

33 16S 27W Lane KS

Job Ticket: 25544

DST#: 4

Test Start: 2006.12.09 @ 00:40:29

Tool Information

Drill Pipe:	Length: 4066.00 ft	Diameter: 3.80 inches	Volume: 57.04 bbl	Tool Weight: 1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 126.00 ft	Diameter: 2.25 inches	Volume: 0.62 bbl	Weight to Pull Loose: 82000.00 lb
		Total Volume:	57.66 bbl	Tool Chased 0.00 ft
Drill Pipe Above KB:	29.00 ft			String Weight: Initial 62000.00 lb
Depth to Top Packer:	4190.00 ft			Final 62000.00 lb
Depth to Bottom Packer:	4221.00 ft			
Interval between Packers:	31.00 ft			
Tool Length:	477.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		
Tool Comments:				

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Stubb	1.00			4164.00	
Shut In Tool	5.00			4169.00	
Hydraulic tool	5.00			4174.00	
Jars	5.00			4179.00	
Safety Joint	2.00			4181.00	
Packer	5.00			4186.00	27.00 Bottom Of Top Packer
Packer	4.00			4190.00	
Stubb	1.00			4191.00	
Recorder	0.00	6772	Inside	4191.00	
Perforations	29.00			4220.00	
Recorder	0.00	7437	Outside	4220.00	
Blank Off Sub	1.00			4221.00	31.00 Tool Interval
Packer	4.00			4225.00	
Stubb	1.00			4226.00	
Perforations	4.00			4230.00	
Change Over Sub	1.00			4231.00	
Drill Pipe	403.00			4634.00	
Change Over Sub	1.00			4635.00	
Recorder	0.00	10248	Below	4635.00	
Bullnose	5.00			4640.00	419.00 Bottom Packers & Anchor
Total Tool Length:		477.00			



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Operating

Anderson #1-33

562 W Hwy 4
Olmritz KS 67564-8561

33 16S 27W Lane KS

Job Ticket: 25544

DST#: 4

ATTN: Bob Lewellyn

Test Start: 2006.12.09 @ 00:40:29

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 50.00 sec/qt

Cushion Volume:

bbl

Water Loss: 7.98 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2900.00 ppm

Filter Cake: 1.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
5.00	Mud 100%M	0.025

Total Length:

5.00 ft

Total Volume:

0.025 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

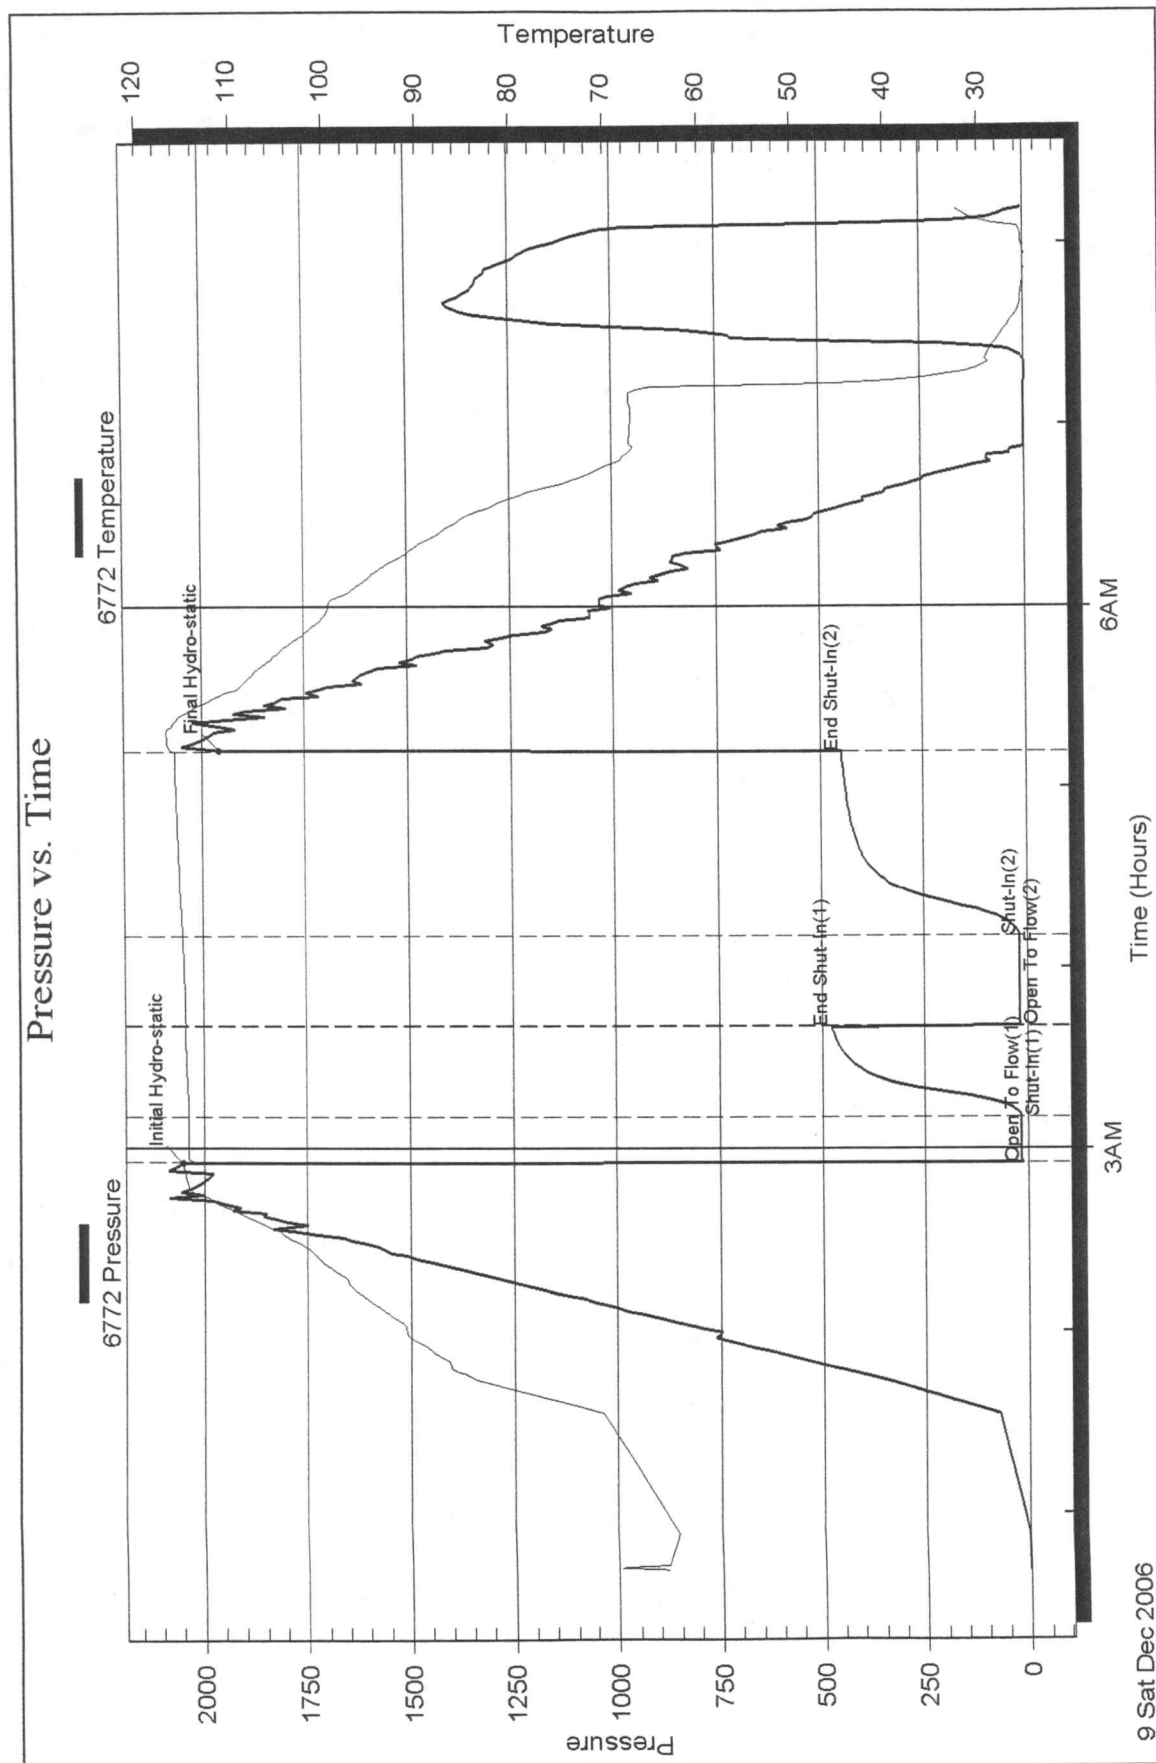


CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

Larson Operating Anderson #1-33 25646 437001

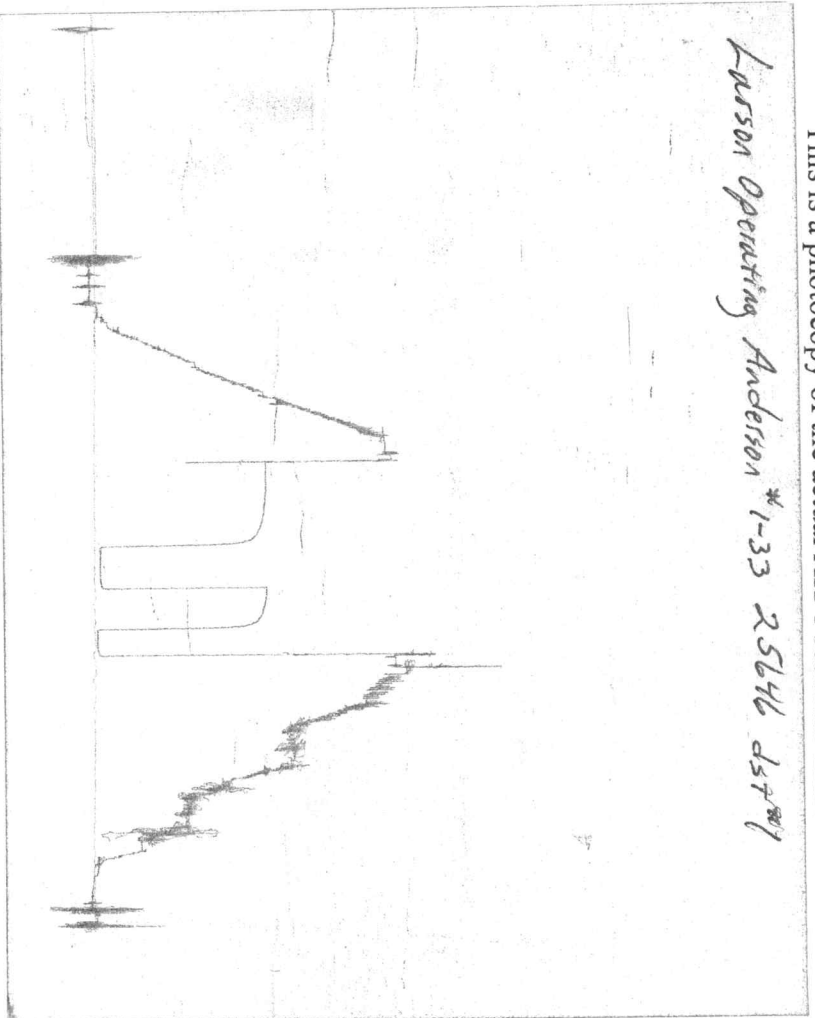


CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

Larson Operating Anderson #1-33 25647 d17#2

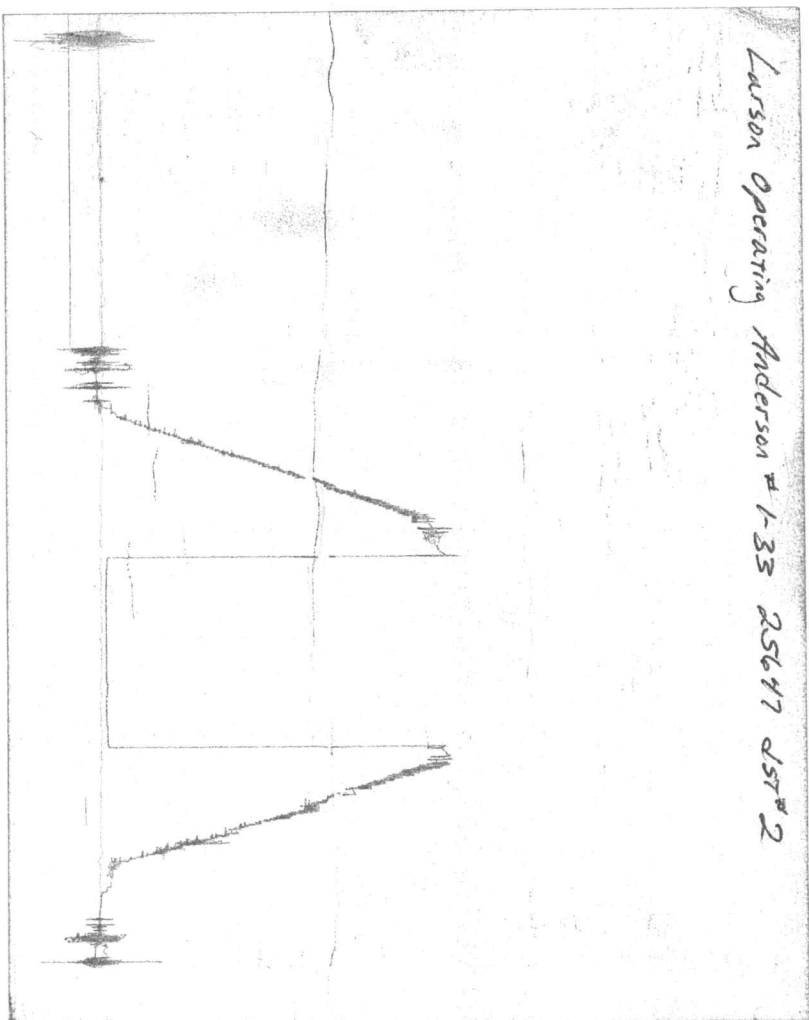


CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

Larson Operating Anderson #1-33 25648 dsr #3

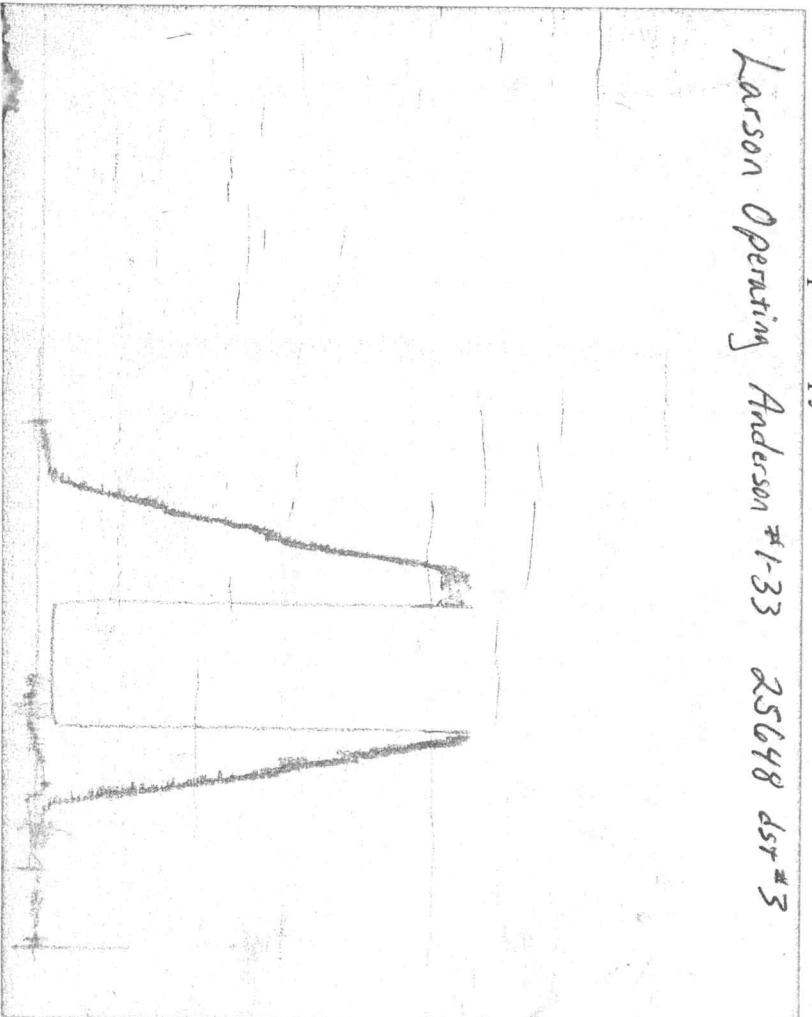


CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

10248 Lanson Operating
#4 Anderson 1-33

Top

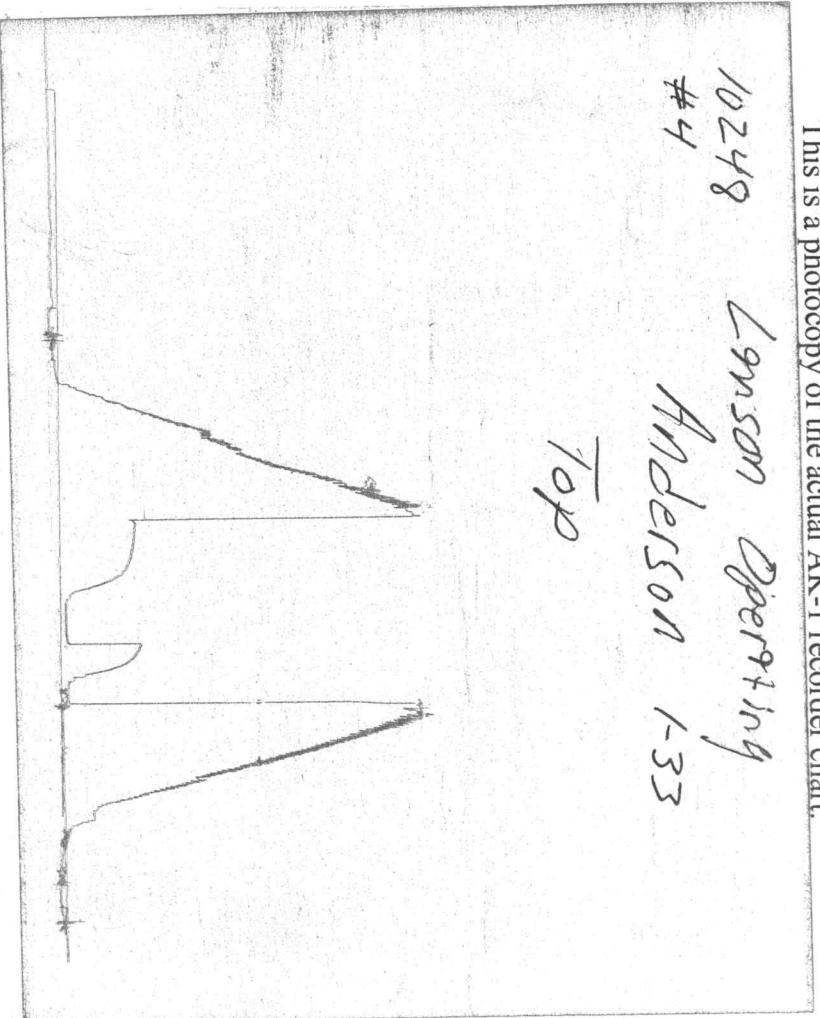


CHART PAGE

This is a photocopy of the actual AK-1 recorder chart.

3437 Larson operating
#4 Anderson 1-33

Bottom

