

CHENEY TESTING COMPANY

P. O. BOX 845 3 GREAT BEND, KANSAS 67530

Hill City, Kansas 67642

DRILL-STEM TEST DATA

Well Name	Waddell	Test No.	1
Well Number	1	Zone Tested	Lansing
Company	Asso. Oil & Gas	Date	2-18-76
Comp. Rep.	Bob Lewellyn	Tester	Kirk Cheney
Contractor	Abercrombie Drlg. Inc.	Ticket No.	157
Location	Sec. 29-16S-29W Lane County, Kan.	Elevation	2794 K.B.

Recorder No. 3695	Clock Range 12 hr	Recorder No. 203	Clock Range 4 hr
Depth 4129		Depth 4132	
Initial Hydro Mud Press. 2095		Initial Hydro Mud Press.	
Initial Shut-in Press. 39		Initial Shut-in Press.	
Initial Flow Press. 39-39		Initial Flow Press.	
Final Flow Press. 39-39		Final Flow Press.	
Final Shut-in Press. 39		Final Shut-in Press.	
Final Hydro Mud Press. 2082		Final Hydro Mud Press.	
Temperature 126		Tool Open Before I. S. I. 30	Mins.
Mud Weight 9.5	Viscosity 46	Initial Shut-in 30	Mins.
Fluid Loss 8.0		Flow Period 30	Mins.
Interval Tested 4067-4135		Final Shut-in 30	Mins.
Top Packer Depth 4062		Surface Choke Size 1"	
Bottom Packer Depth 4067		Bottom Choke Size 1/2"	
Total Depth 4135		Main Hole Size 7 7/8"	
Drill Pipe Size 4 1/2 F.H.	Wt. 4 1/2 Ex. H.	Rubber Size 6 3/4"	
Drill Collar I. D.	Ft. Run		
Recovery—Total Feet 5			
Recovered 5	Feet Of Mud		
Recovered	Feet Of		
Recovered	Feet Of		
Recovered	Feet Of		

Remarks

Tool open @ 4:50 A.M. Blow-weak died in 15 minutes.

THIS ORDER MUST BE SIGNED BEFORE WORK IS COMMENCED.


CONDITIONS: It is expressly understood and agreed that the above described work shall be done under the exclusive control, direction and supervision of the owner or contractor. As a part of the consideration for this agreement, it is expressly understood and agreed that Cheney Testing Company shall not be responsible for damages or losses of any kind whatsoever occasioned by or incident to the use of the above described Tools, whether run or operated by customer, or by anyone employed directly or indirectly by Cheney Testing Company, nor whether resulting from

the acts or omissions of Cheney Testing Company, or any of its agents, servants or employees in any way connected with or related to the use of such Tools.

It is expressly understood and agreed that Cheney Testing Company, shall not be bound by any agreement, not herein contained, and no agent or representative connected with or employed by Cheney Testing Company has authority to alter or extend the terms of this agreement. I have read and understand the terms of this agreement and represent that I am authorized to sign the same as agent of customer.

By

Owner, Operator or his Agent

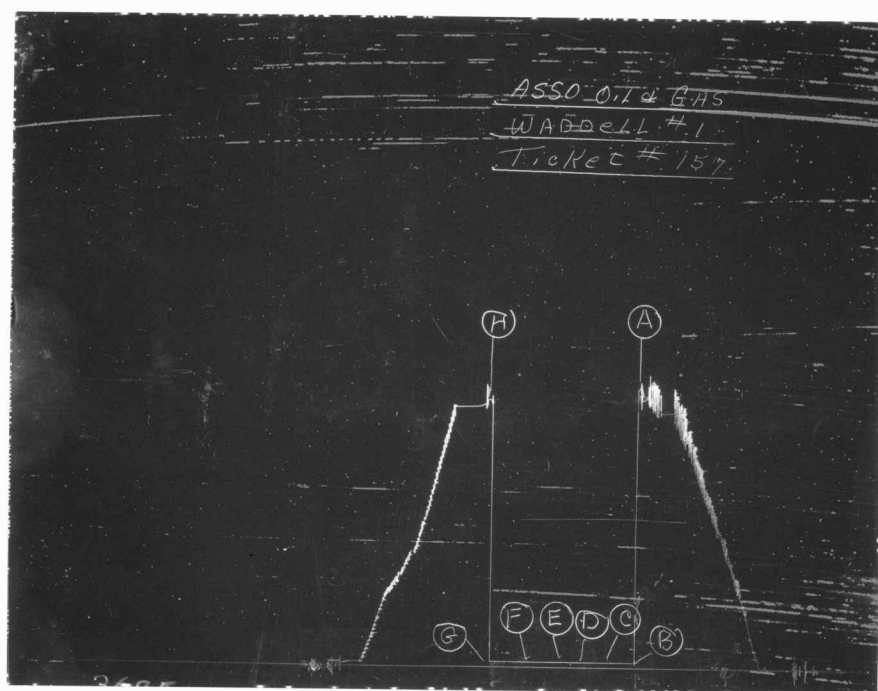

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	2095	PSI
(B) First Initial Flow Pressure	39	PSI
(C) First Final Flow Pressure	39	PSI
(D) Initial Closed-in Pressure	39	PSI
(E) Second Initial Flow Pressure	39	PSI
(F) Second Final Flow Pressure	39	PSI
(G) Final Closed-in Pressure	39	PSI
(H) Final Hydrostatic Mud	2082	PSI

CHENEY TESTING COMPANY

P. O. BOX 845 3 ~~GREAT BEND, KANSAS~~ 67530

Hill City, Kan 67642

DRILL-STEM TEST DATA

Well Name	Waddell	Test No.	2
Well Number	1	Zone Tested	Lansing
Company	Asso. Oil & Gas	Date	2-18-76
Comp. Rep.	Bob Lewellyn	Tester	Kirk Cheney
Contractor	Abercrombie Drlg. Inc.	Ticket No.	158
Location	Sec. 29-16S-29W Lane County, Kan.	Elevation	2794 K.B.

Recorder No. 3695	Clock Range 12 hr	Recorder No. 203	Clock Range 4 hr
Depth 4156		Depth 4159	
Initial Hydro Mud Press. 2109		Initial Hydro Mud Press.	
Initial Shut-in Press. 39		Initial Shut-in Press.	
Initial Flow Press. 39-39		Initial Flow Press.	
Final Flow Press. 39-39		Final Flow Press.	
Final Shut-in Press. 39		Final Shut-in Press.	
Final Hydro Mud Press. 2095		Final Hydro Mud Press.	
Temperature 119		Tool Open Before I. S. I. 30	Mins.
Mud Weight 9.5	Viscosity 47	Initial Shut-in 30	Mins.
Fluid Loss 8.0		Flow Period 30	Mins.
Interval Tested 4135-4162		Final Shut-in 30	Mins.
Top Packer Depth 4130		Surface Choke Size 1"	
Bottom Packer Depth 4135		Bottom Choke Size 1/2"	
Total Depth 4162		Main Hole Size 7 7/8"	
Drill Pipe Size 4 1/2 F.H.	Wt. 4 1/2 Ex. H.	Rubber Size 6 3/4"	
Drill Collar I. D.	Ft. Run 5		
Recovery—Total Feet 5			
Recovered 5	Feet Of watery mud.		
Recovered	Feet Of		
Recovered	Feet Of		
Recovered	Feet Of		

Remarks

Tool open @ 6:38 P.M. Blow-weak, died in 10 minutes.

THIS ORDER MUST BE SIGNED BEFORE WORK IS COMMENCED.


CONDITIONS: It is expressly understood and agreed that the above described work shall be done under the exclusive control, direction and supervision of the owner or contractor. As a part of the consideration for this agreement, it is expressly understood and agreed that Cheney Testing Company shall not be responsible for damages or losses of any kind whatsoever occasioned by or incident to the use of the above described Tools, whether run or operated by customer, or by anyone employed directly or indirectly by Cheney Testing Company, nor whether resulting from

the acts or omissions of Cheney Testing Company, or any of its agents, servants or employees in any way connected with or related to the use of such Tools.

It is expressly understood and agreed that Cheney Testing Company, shall not be bound by any agreement, not herein contained, and no agent or representative connected with or employed by Cheney Testing Company has authority to alter or extend the terms of this agreement. I have read and understand the terms of this agreement and represent that I am authorized to sign the same as agent of customer.

By _____

Owner, Operator or his Agent

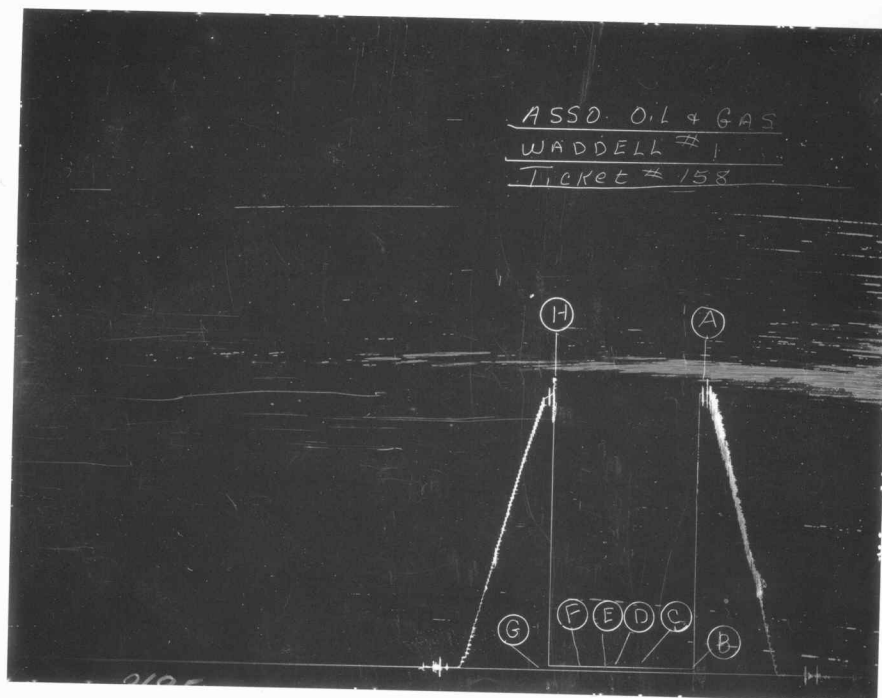

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	2109	PSI
(B) First Initial Flow Pressure	39	PSI
(C) First Final Flow Pressure	39	PSI
(D) Initial Closed-in Pressure	39	PSI
(E) Second Initial Flow Pressure	39	PSI
(F) Second Final Flow Pressure	39	PSI
(G) Final Closed-in Pressure	39	PSI
(H) Final Hydrostatic Mud	2095	PSI

CHENEY TESTING COMPANY

P. O. BOX 845 3 GREAT BEND, KANSAS 67530

Hill City, Kansas 67642

DRILL-STEM TEST DATA

Well Name	Waddell	Test No.	3
Well Number	1	Zone Tested	Kansas City
Company	Asso. Oil & Gas	Date	2-19-76
Comp. Rep.	Bob Lewllyn	Tester	Kirk Cheney
Contractor	Abercrombie Drlg. Inc..	Ticket No.	159
Location	Sec. 29-16S-29W Lane County, Kan.	Elevation	2749 K.B.

Recorder No. 3695 Clock Range 12 hr Recorder No. 203 Clock Range 4 hr

Depth 4181 Depth 4184

Initial Hydro Mud Press. 2135 Initial Hydro Mud Press. _____

Initial Shut-in Press. 436 Initial Shut-in Press. _____

Initial Flow Press. 26-26 Initial Flow Press. _____

Final Flow Press. 39-39 Final Flow Press. _____

Final Shut-in Press. 542 Final Shut-in Press. _____

Final Hydro Mud Press. 2122 Final Hydro Mud Press. _____

Temperature 120 Tool Open Before I. S. I. 30 Mins.

Mud Weight 9.4 Viscosity 46 Initial Shut-in 30 Mins.

Fluid Loss 10.0 Flow Period 30 Mins.

Interval Tested 4162-4187 Final Shut-in 30 Mins.

Top Packer Depth 4157 Surface Choke Size 1"

Bottom Packer Depth 4162 Bottom Choke Size 1/2"

Total Depth 4187 Main Hole Size 7 7/8"

Drill Pipe Size 4 1/2 F.H. Wt. 4 1/2 Ex. H. Rubber Size 6 3/4"

Drill Collar I. D. _____ Ft. Run _____

Recovery—Total Feet 15

Recovered 15 Feet Of watery mud

Recovered _____ Feet Of _____

Recovered _____ Feet Of _____

Recovered _____ Feet Of _____

Remarks Tool open @ 9:20 A.M. Blow-weak for 3 minutes and died.

THIS ORDER MUST BE SIGNED BEFORE WORK IS COMMENCED.


CONDITIONS: It is expressly understood and agreed that the above described work shall be done under the exclusive control, direction and supervision of the owner or contractor. As a part of the consideration for this agreement, it is expressly understood and agreed that Cheney Testing Company shall not be responsible for damages or losses of any kind whatsoever occasioned by or incident to the use of the above described Tools, whether run or operated by customer, or by anyone employed directly or indirectly by Cheney Testing Company, nor whether resulting from

the acts or omissions of Cheney Testing Company, or any of its agents, servants or employees in any way connected with or related to the use of such Tools.

It is expressly understood and agreed that Cheney Testing Company, shall not be bound by any agreement, not herein contained, and no agent or representative connected with or employed by Cheney Testing Company has authority to alter or extend the terms of this agreement. I have read and understand the terms of this agreement and represent that I am authorized to sign the same as agent of customer.

By _____

Owner, Operator or his Agent

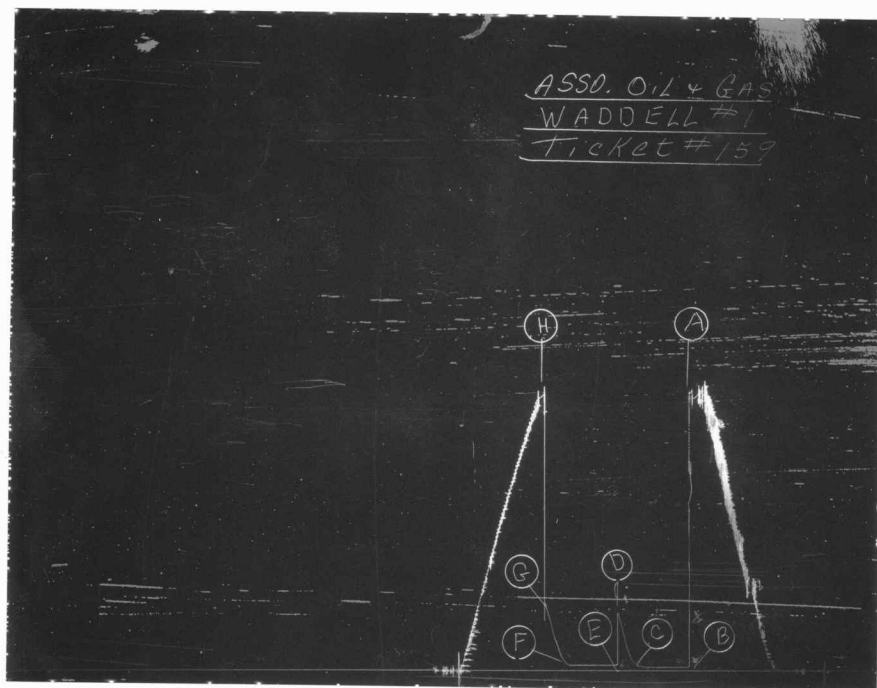

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	2135	PSI
(B) First Initial Flow Pressure	26	PSI
(C) First Final Flow Pressure	26	PSI
(D) Initial Closed-in Pressure	436	PSI
(E) Second Initial Flow Pressure	39	PSI
(F) Second Final Flow Pressure	39	PSI
(G) Final Closed-in Pressure	542	PSI
(H) Final Hydrostatic Mud	2122	PSI

CHENEY TESTING COMPANY

P. O. BOX 845 3 GREAT-BEND, KANSAS 67530

Hill City, Kansas 67642

DRILL-STEM TEST DATA

Well Name	Waddell	Test No.	4
Well Number	1	Zone Tested	Kansas City
Company	Asso. Oil & Gas	Date	2-20-76
Comp. Rep.	Bob Lewellyn	Tester	Kirk Cheney
Contractor	Abercrombie Drlg. Inc.	Ticket No.	160
Location	Sec. 29-16S-29W Lane County, Kan.	Elevation	2794 K.B.

Recorder No. 3695 Clock Range 12 hr Recorder No. 203 Clock Range 4 hr

Depth 4264 Depth 4267

Initial Hydro Mud Press. 2148 Initial Hydro Mud Press.

Initial Shut-in Press. 79 Initial Shut-in Press.

Initial Flow Press. 52-52 Initial Flow Press.

Final Flow Press. 52-52 Final Flow Press.

Final Shut-in Press. 92 Final Shut-in Press.

Final Hydro Mud Press. 2135 Final Hydro Mud Press.

Temperature 120 Tool Open Before I. S. I. 30 Mins.

Mud Weight 9.5 Viscosity 43 Initial Shut-in 30 Mins.

Fluid Loss 11.0 Flow Period 30 Mins.

Interval Tested 4190-4270 Final Shut-in 30 Mins.

Top Packer Depth 4185 Surface Choke Size 1"

Bottom Packer Depth 4190 Bottom Choke Size 1/2"

Total Depth 4270 Main Hole Size 7 7/8"

Drill Pipe Size 4 1/2 F.H. Wt. 4 1/2 Ex. H. Rubber Size 6 3/4"

Drill Collar I. D. Ft. Run

Recovery—Total Feet 5

Recovered 5 Feet Of Mud

Recovered Feet Of

Recovered Feet Of

Recovered Feet Of

Remarks


Tool open @ 6:50 A.M. Blow-weak & died in 15 minutes..

THIS ORDER MUST BE SIGNED BEFORE WORK IS COMMENCED.

CONDITIONS: It is expressly understood and agreed that the above described work shall be done under the exclusive control, direction and supervision of the owner or contractor. As a part of the consideration for this agreement, it is expressly understood and agreed that Cheney Testing Company shall not be responsible for damages or losses of any kind whatsoever occasioned by or incident to the use of the above described Tools, whether run or operated by customer, or by anyone employed directly or indirectly by Cheney Testing Company, nor whether resulting from

the acts or omissions of Cheney Testing Company, or any of its agents, servants or employees in any way connected with or related to the use of such Tools. It is expressly understood and agreed that Cheney Testing Company, shall not be bound by any agreement, not herein contained, and no agent or representative connected with or employed by Cheney Testing Company has authority to alter or extend the terms of this agreement. I have read and understand the terms of this agreement and represent that I am authorized to sign the same as agent of customer.

By _____
Owner, Operator or his Agent

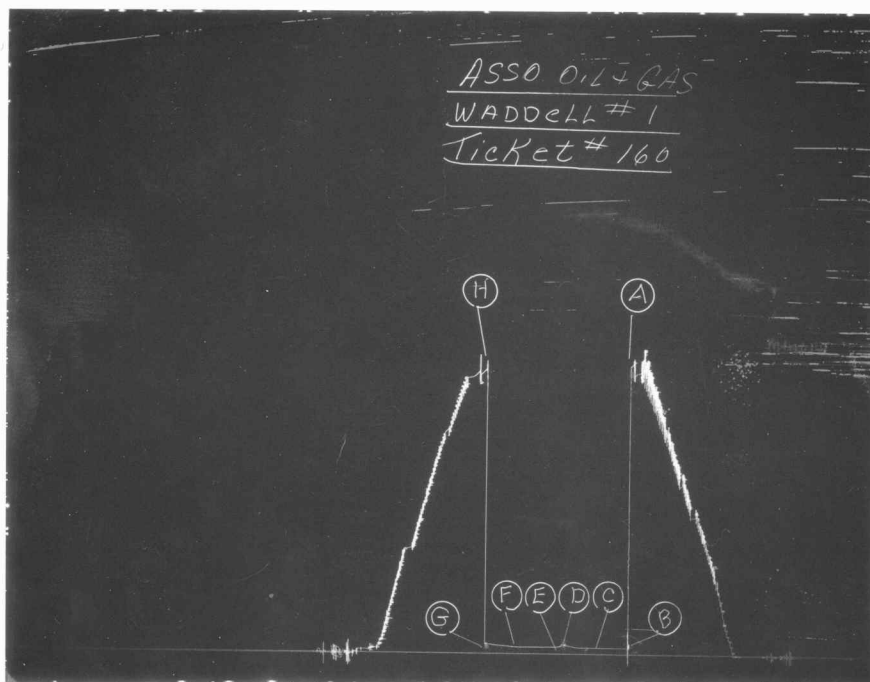

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	2148	PSI
(B) First Initial Flow Pressure	52	PSI
(C) First Final Flow Pressure	52	PSI
(D) Initial Closed-in Pressure	79	PSI
(E) Second Initial Flow Pressure	52	PSI
(F) Second Final Flow Pressure	52	PSI
(G) Final Closed-in Pressure	92	PSI
(H) Final Hydrostatic Mud	2135	PSI

CHENEY TESTING COMPANY

P. O. BOX-845 3 GREAT-BEND, KANSAS 67530

Hill City, Kan. 67642

DRILL-STEM TEST DATA

Well Name Waddell	Test No. 5
Well Number 1	Zone Tested Fort Scott & Cherokee
Company Associates Oil & Gas Inc.	Date 2-22-76
Comp. Rep. Bob Lewellyn	Tester Kirk Cheney
Contractor Abercrombie Drilg. Inc.	Ticket No. 161
Location Sec. 29-16S-29W Lane County, Kan.	Elevation 2794 K.B.

Recorder No. 3695	Clock Range 12 hr	Recorder No. 203	Clock Range 4 hr
Depth 4494		Depth 4497	
Initial Hydro Mud Press. 2215		Initial Hydro Mud Press.	
Initial Shut-in Press. 1188		Initial Shut-in Press.	
Initial Flow Press. 79-132		Initial Flow Press.	
Final Flow Press. 158-251		Final Flow Press.	
Final Shut-in Press. 1175		Final Shut-in Press.	
Final Hydro Mud Press. 2202		Final Hydro Mud Press.	
Temperature 96		Tool Open Before I. S. I. 30	Mins.
Mud Weight 9.4	Viscosity 44	Initial Shut-in 30	Mins.
Fluid Loss 11.5		Flow Period 90	Mins.
Interval Tested 4390-4500		Final Shut-in 60	Mins.
Top Packer Depth 4385		Surface Choke Size 1"	
Bottom Packer Depth 4390		Bottom Choke Size 1 1/4"	
Total Depth 4500		Main Hole Size 7 7/8"	
Drill Pipe Size 4 1/2 F.H.	Wt. 4 1/2 Ex. H.	Rubber Size 6 3/4"	
Drill Collar I. D. 527	Ft. Run		
Recovery—Total Feet			
Recovered 62	Feet Of Watery mud - oil specks		
Recovered 62	Feet Of very slightly oil & gas cut mud		
Recovered 186	Feet Of oil & slightly gas cut mud		
Recovered 217	Feet Of heavy oil & slightly gas cut mud		
Remarks Tool open @ 10:50 A.M. Blow-strong			

THIS ORDER MUST BE SIGNED BEFORE WORK IS COMMENCED.

CONDITIONS: It is expressly understood and agreed that the above described work shall be done under the exclusive control, direction and supervision of the owner or contractor. As a part of the consideration for this agreement, it is expressly understood and agreed that Cheney Testing Company shall not be responsible for damages or losses of any kind whatsoever occasioned by or incident to the use of the above described Tools, whether run or operated by customer, or by anyone employed directly or indirectly by Cheney Testing Company, nor whether resulting from

the acts or omissions of Cheney Testing Company, or any of its agents, servants or employees in any way connected with or related to the use of such Tools.

It is expressly understood and agreed that Cheney Testing Company, shall not be bound by any agreement, not herein contained, and no agent or representative connected with or employed by Cheney Testing Company has authority to alter or extend the terms of this agreement. I have read and understand the terms of this agreement and represent that I am authorized to sign the same as agent of customer.

By _____
Owner, Operator or his Agent

CHENEY TESTING COMPANY


Pressure Data

Date 2-22-76 Test Ticket No. 161
 Recorder No. 3695 Capacity 5300 Location 4494 Ft.
 Clock No. 10413 Elevation 2794 K.B. Well Temperature 96 °F

Point	Pressure		Time Given	Time Computed
A Initial Hydrostatic Mud	<u>2242</u>	P.S.I.	<u>10:50 A.M.</u>	
B First Initial Flow Pressure	<u>74</u>	P.S.I.	<u>30</u>	Mins.
C First Final Flow Pressure	<u>124</u>	P.S.I.	<u>30</u>	Mins.
D Initial Closed-in Pressure	<u>1178</u>	P.S.I.	<u>90</u>	Mins.
E Second Initial Flow Pressure	<u>156</u>	P.S.I.	<u>60</u>	Mins.
F Second Final Flow Pressure	<u>255</u>	P.S.I.		
G Final Closed-in Pressure	<u>1175</u>	P.S.I.		
H Final Hydrostatic Mud	<u>2215</u>	P.S.I.		

PRESSURE BREAKDOWN

First Flow Pressure		Initial Shut-In		Second Flow Pressure		Final Shut-In	
Breakdown: <u>6</u> Inc.		Breakdown: <u>10</u> Inc.		Breakdown: <u>18</u> Inc.		Breakdown: <u>20</u> Inc.	
of <u>5</u> mins. and a		of <u>3</u> mins. and a		of <u>5</u> mins. and a		of <u>3</u> mins. and a	
final inc. of _____ Min.		final inc. of _____ Min.		final inc. of _____ Min.		final inc. of _____ Min.	
Point Mins.	Press.	Point Minutes	Press.	Point Minutes	Press.	Point Minutes	Press.
P 1 <u>0</u>	<u>74</u>	<u>0</u>	<u>124</u>	<u>0</u>	<u>156</u>	<u>0</u>	<u>255</u>
P 2 <u>5</u>	<u>82</u>	<u>3</u>	<u>264</u>	<u>5</u>	<u>156</u>	<u>3</u>	<u>907</u>
P 3 <u>10</u>	<u>92</u>	<u>6</u>	<u>817</u>	<u>10</u>	<u>156</u>	<u>6</u>	<u>1018</u>
P 4 <u>15</u>	<u>100</u>	<u>9</u>	<u>1007</u>	<u>15</u>	<u>156</u>	<u>9</u>	<u>1070</u>
P 5 <u>20</u>	<u>108</u>	<u>12</u>	<u>1086</u>	<u>20</u>	<u>164</u>	<u>12</u>	<u>1097</u>
P 6 <u>25</u>	<u>119</u>	<u>15</u>	<u>1120</u>	<u>25</u>	<u>171</u>	<u>15</u>	<u>1112</u>
P 7 <u>30</u>	<u>124</u>	<u>18</u>	<u>1140</u>	<u>30</u>	<u>179</u>	<u>18</u>	<u>1123</u>
P 8 _____		<u>21</u>	<u>1155</u>	<u>35</u>	<u>190</u>	<u>21</u>	<u>1136</u>
P 9 _____		<u>24</u>	<u>1162</u>	<u>40</u>	<u>194</u>	<u>24</u>	<u>1143</u>
P10 _____		<u>27</u>	<u>1172</u>	<u>45</u>	<u>202</u>	<u>27</u>	<u>1146</u>
P11 _____		<u>30</u>	<u>1178</u>	<u>50</u>	<u>211</u>	<u>30</u>	<u>1152</u>
P12 _____				<u>55</u>	<u>216</u>	<u>33</u>	<u>1158</u>
P13 _____				<u>60</u>	<u>219</u>	<u>36</u>	<u>1162</u>
P14 _____				<u>65</u>	<u>222</u>	<u>39</u>	<u>1165</u>
P15 _____				<u>70</u>	<u>227</u>	<u>42</u>	<u>1167</u>
P16 _____				<u>75</u>	<u>232</u>	<u>45</u>	<u>1168</u>
P17 _____				<u>80</u>	<u>240</u>	<u>48</u>	<u>1170</u>
P18 _____				<u>85</u>	<u>248</u>	<u>51</u>	<u>1173</u>
P19 _____				<u>90</u>	<u>255</u>	<u>54</u>	<u>1174</u>
P20 _____						<u>57</u>	<u>1175</u>
						<u>60</u>	<u>1175</u>

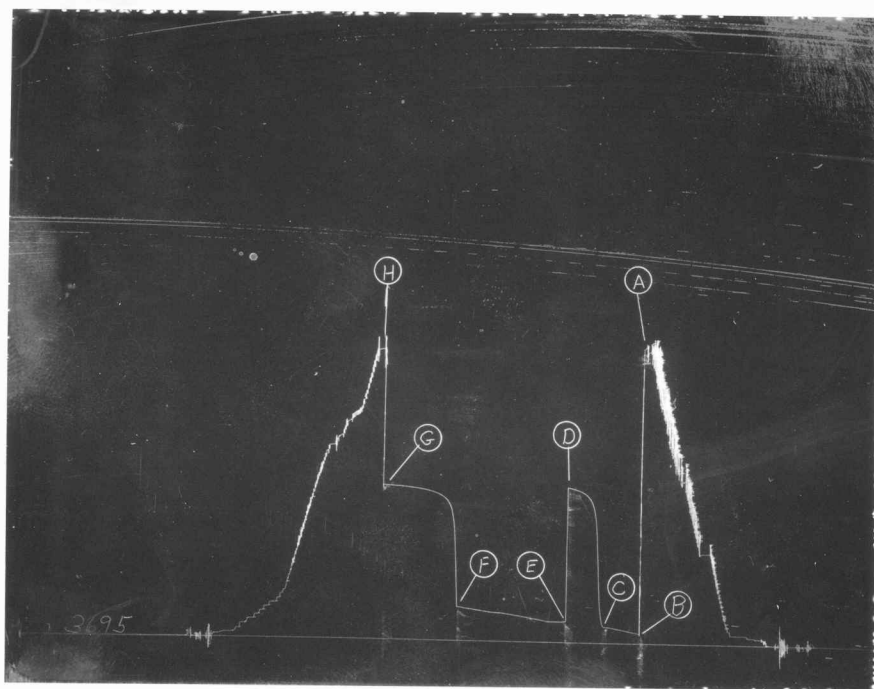

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	2215	2242 PSI
(B) First Initial Flow Pressure	79	74 PSI
(C) First Final Flow Pressure	132	124 PSI
(D) Initial Closed-in Pressure	1188	1178 PSI
(E) Second Initial Flow Pressure	158	156 PSI
(F) Second Final Flow Pressure	251	255 PSI
(G) Final Closed-in Pressure	1175	1175 PSI
(H) Final Hydrostatic Mud	2202	2215 PSI

CHENEY TESTING COMPANY

P. O. BOX 845- 3 GREAT BEND, KANSAS 67530

Hill City, Kansas 67642

DRILL-STEM TEST DATA

Well Name	Waddell	Test No.	6
Well Number	1	Zone Tested	Cherokee
Company	Associates Oil & Gas Inc.	Date	2-22-76
Comp. Rep.	Bob Lewellyn	Tester	Kenneth Cheney
Contractor	Abercrombie Drilg. Inc.	Ticket No.	162
Location	Sec. 29-16S-29W Lane County, Kan.	Elevation	2794 K.B.

Recorder No.	3695	Clock Range	12 hr	Recorder No.	203	Clock Range	4 hr
Depth	4495	Depth	4497				
Initial Hydro Mud Press.	2215	Initial Hydro Mud Press.					
Initial Shut-in Press.	39	Initial Shut-in Press.					
Initial Flow Press.	26-39	Initial Flow Press.					
Final Flow Press.	39-39	Final Flow Press.					
Final Shut-in Press.	39	Final Shut-in Press.					
Final Hydro Mud Press.	2202	Final Hydro Mud Press.					
Temperature	122	Tool Open Before I. S. I.	30	Mins.			
Mud Weight	9.4	Viscosity	44	Initial Shut-in	30	Mins.	
Fluid Loss	11.5	Flow Period	30	Mins.			
Interval Tested	4478-4500	Final Shut-in	30	Mins.			
Top Packer Depth	4473	Surface Choke Size	1"				
Bottom Packer Depth	4478	Bottom Choke Size	1"				
Total Depth	4500	Main Hole Size	7 7/8"				
Drill Pipe Size	4 1/2 F.H.	Rubber Size	6 3/4"				
Drill Collar I. D.	5						
Recovery—Total Feet	5						
Recovered		Feet Of					
Recovered		Feet Of					
Recovered		Feet Of					
Recovered		Feet Of					
Remarks	Tool open @ 9:35 P.M. Blow-weak died in 15 minutes						

THIS ORDER MUST BE SIGNED BEFORE WORK IS COMMENCED.


CONDITIONS: It is expressly understood and agreed that the above described work shall be done under the exclusive control, direction and supervision of the owner or contractor. As a part of the consideration for this agreement, it is expressly understood and agreed that Cheney Testing Company shall not be responsible for damages or losses of any kind whatsoever occasioned by or incident to the use of the above described Tools, whether run or operated by customer, or by anyone employed directly or indirectly by Cheney Testing Company, nor whether resulting from

the acts or omissions of Cheney Testing Company, or any of its agents, servants or employees in any way connected with or related to the use of such Tools.

It is expressly understood and agreed that Cheney Testing Company, shall not be bound by any agreement, not herein contained, and no agent or representative connected with or employed by Cheney Testing Company has authority to alter or extend the terms of this agreement. I have read and understand the terms of this agreement and represent that I am authorized to sign the same as agent of customer.

By

Owner, Operator or his Agent

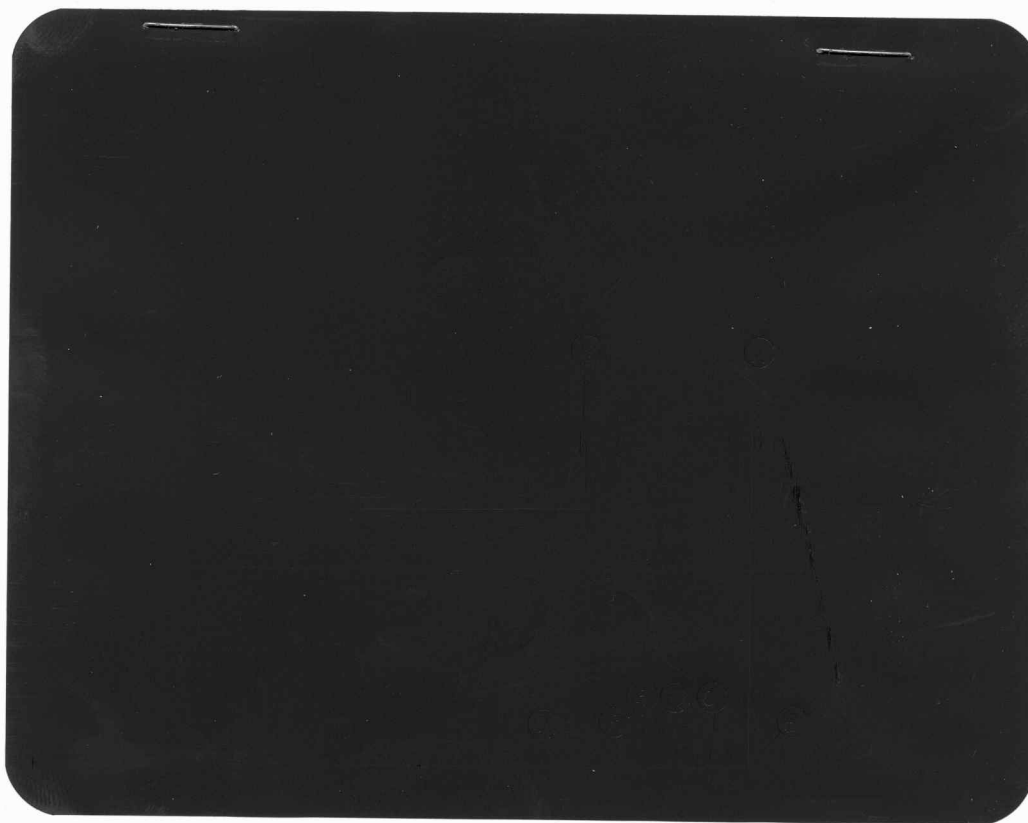

This is an actual photograph of recorder chart.

POINT	PRESSURE	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	2215	PSI
(B) First Initial Flow Pressure	26	PSI
(C) First Final Flow Pressure	39	PSI
(D) Initial Closed-in Pressure	39	PSI
(E) Second Initial Flow Pressure	39	PSI
(F) Second Final Flow Pressure	39	PSI
(G) Final Closed-in Pressure	39	PSI
(H) Final Hydrostatic Mud	2202	PSI
