

API # 15-009-25024-00-00

Wondra 'B' 4

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-31-07 Location 8-17-11w Elevation 1858 County BartonCompany RJM Company INC Number of Copies 5Charts Mailed to PO BOX 256 Claflin KS 67525Drilling Contractor Loyal Drilling INCLength Drill Pipe 3328 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size 4 1/2 XHTop Packer Depth 3309 Bottom Packer Depth 3314 Number of Packers 2 Packer Size 6 3/4TESTED FROM 3314 TO 3369 ANCHOR LENGTH 55 TOTAL DEPTH 3369 Hole Size 7 7/8LEASE & WELL NO. Wondra B-4 FORMATION TESTED Arbuckle TEST NO. 1Mud Weight 9.1 Viscosity 54 Water Loss 9.8 Chlorides - Pits 4000 D.S.T. _____Maximum Temp. 102 °F Initial Hydrostatic Pressure (A) 1560 P.S.I. Final Hydrostatic Pressure (H) 1552 P.S.I.Tool Open I.F.P. from 10:00 A.m. to 10:45 A.m. 45 minTool Closed I.C.I.P. from 10:45 A.m. to 11:30 A.m. 45 minTool Open F.F.P. from 11:30 A.m. to 12:15 p.m. 45 minTool Closed F.C.I.P. from 12:15 p.m. to 1:00 p.m. 45 min

from [B]	<u>31</u>	P.S.I. to [C]	<u>70</u>	P.S.I.
[D]	<u>1097</u>			P.S.I.
from [E]	<u>71</u>	P.S.I. to [F]	<u>114</u>	P.S.I.
[G]	<u>1103</u>			P.S.I.

Initial Blow Weak But Building Blow Built Bottom of Bucket in 35 minFinal Blow Weak TO Fair Blow Built Bottom of Bucket in 28 minTotal Feet Recovered 230 Gravity of Oil 40 Corrected50 Feet of clean oil % Gas 100 % Oil _____ % Mud _____ % Water _____60 Feet of clean oil % Gas 100 % Oil _____ % Mud _____ % Water _____60 Feet of Mud cut oil % Gas 60 % Oil 40 % Mud _____ % Water _____60 Feet of Mud cut oil % Gas 60 % Oil 40 % Mud _____ % Water _____

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 3365 Cir. Sub _____ Sampler _____Bottom Recorder No. 3088 Clock No. 47441 Depth 3366 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14344


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

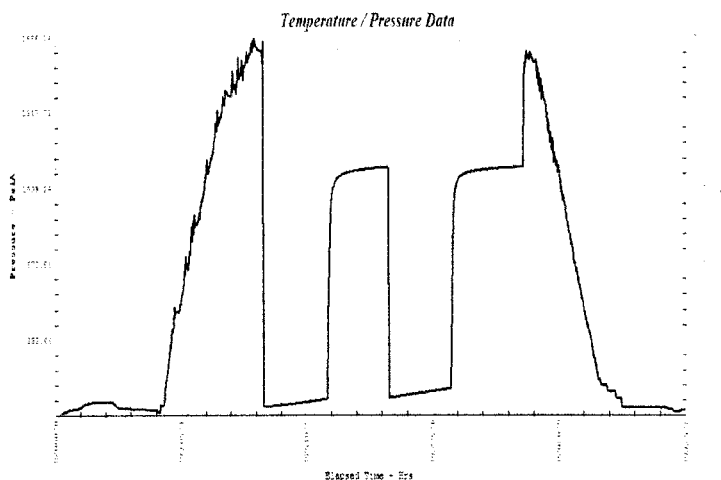

1	Initial Hydrostatic Pressure	1562
2	Initial Flow Pressure	31
3	Final Initial Flow Pressure	70
4	Initial Shut-In Pressure	1097
5	Initial Final Flow Pressure	71
6	Final Flow Pressure	114
7	Final Shut-In Pressure	1103
8	Final Hydrostatic Pressure	1552

Maximum Temperature 102

GENERAL INFORMATION

COMPANY NAME	 RJM COMPANY INC	LEASE AND WELL NUMBER	 WONDRA B-4
TEST DATE	 1/31/07	FORMATION TESTED	 ARBUCKLE
SECTION-TOWN-RANGE	 8-17-11W	DRILL STEM TEST NUMBER	 1
STATE	 KANSAS	REPORT NUMBER	 14344
COUNTY	 BARTON	ELEVATION KELLY BUSHINGS	 1862
ELEVATION GROUND LEVEL	 1858	TESTING ENGINEER	 JARED SCHECK
COMPANY REPRESENTATIVE	 JIM M		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	 3314	TOP PACKER DEPTH	 3309
TEST INTERVAL (to)	 3369	BOTTOM PACKER DEPTH	 3314
ANCHOR LENGTH	 55	NUMBER OF PACKERS	 2
TOTAL DEPTH (ft)	 3369	PACKER SIZE	 6 3/4
		HOLE SIZE	 7 7/8

FLOW TIMES

TOOL OPEN (from)	 10:00A	TOOL OPEN (from)	 11:30
INITIAL OPEN TOOL OPEN (to)	 10:45	FINAL OPEN TOOL OPEN (to)	 12:15P
DURATION (min.)	 45	DURATION (min.)	 45
TOOL CLOSED (from)	 10:45	TOOL CLOSED (from)	 12:15
INITIAL SHUT-IN TOOL CLOSED (to)	 11:30	FINAL SHUT-IN TOOL CLOSED (to)	 1:00P
DURATION (min.)	 45	DURATION (min.)	 45

INITIAL FLOW WEAK BUT BUILDING BLOW BUILT BOTTOM OF BUCKET IN 35 MIN.

FINAL FLOW WEAK TO FAIR BLOW BUILT BOTOM OF BUCKET IN 28 MIN

Feet of Recovery	RESISTIVITY	AT	DEGREES	CHLORIDES				
	RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER	
1) 50	CLEAN GASSY OIL				100			
2) 60	CLEAN GASSY OIL				100			
3) 60	MUD CUT OIL				60	40		
4) 60	MUD CUT OIL				60	40		
5)								

Company: RJM COMPANY INC Lease & Well No. WONDRA B-4 Test #: 1 Date: 1-31-07 SEC 8 TWP. 17 RGE. 11

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	RJM COMPANY INC	LEASE AND WELL NUMBER	WONDRA B-4
TEST DATE	1/31/07	FORMATION TESTED	INTERVAL
SECTION-TOWN-RANGE	B-17-11W	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	14344
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1862
ELEVATION GROUND LEVEL	1858	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	JIM M		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	60 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3365	BOTTOM RECORDER DEPTH	3366
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	ROYAL DRILLING INC	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3328	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	54
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	9.4
		CHLORIDES-PITS	4,000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

