

SUPERIOR TESTERS ENTERPRISES L.L.C.


(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: R.J.M OIL COMPANY INC
 Lease & Well No. WONDRA B #6
 Test #: 1
 Date: 11-27-07
 SEC. 8 TWP. 17
 RGE. 11

Temperature / Pressure Data

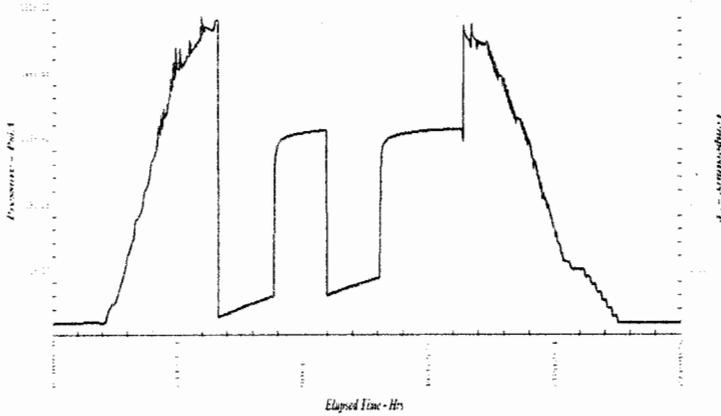

1	Initial Hydrostatic Pressure.....	1743
2	Initial Flow Pressure.....	45
3	Final Initial Flow Pressure.....	168
4	Initial Shut-In Pressure.....	1111
5	Initial Final Flow Pressure.....	176
6	Final Flow Pressure.....	273
7	Final Shut-In Pressure.....	1118
8	Final Hydrostatic Pressure.....	1705
Maximum Temperature.....		108

GENERAL INFORMATION

COMPANY NAME R.J.M OIL COMPANY INC	LEASE AND WELL NUMBER WONDRA B #6
TEST DATE 11/27/07	FORMATION TESTED ARBUCKLE
SECTION-TOWN-RANGE 40772	DRILL STEM TEST NUMBER 1
STATE KANSAS	REPORT NUMBER ####
COUNTY BARTON	ELEVATION KELLY BUSHINGS 1898
ELEVATION GROUND LEVEL 1894	TESTING ENGINEER DAVID NICHOLS
COMPANY REPRESENTATIVE JIM	

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3350	TOP PACKER DEPTH 3345
TEST INTERVAL (to) 3375	BOTTOM PACKER DEPTH 3350
ANCHOR LENGTH 25	NUMBER OF PACKERS 2
TOTAL DEPTH (ft) 3375	PACKER SIZE 6 3/4
	HOLE SIZE 7 7/8


FLOW TIMES

<p><i>INITIAL OPEN</i></p> <p>TOOL OPEN (from) 12:50</p> <p>TOOL OPEN (to) 1:20</p> <p>DURATION (min.) 30</p> <p><i>INITIAL SHUT-IN</i></p> <p>TOOL CLOSED (from) 1:20</p> <p>TOOL CLOSED (to) 1:50</p> <p>DURATION (min.) 30</p>	<p><i>FINAL OPEN</i></p> <p>TOOL OPEN (from) 1:50</p> <p>TOOL OPEN (to) 2:20</p> <p>DURATION (min.) 30</p> <p><i>FINAL SHUT-IN</i></p> <p>TOOL CLOSED (from) 2:20</p> <p>TOOL CLOSED (to) 3:05</p> <p>DURATION (min.) 45</p>
---	--

INITIAL FLOW GOOD BLOW BOTTOM BUCKET IN 6 MIN

FINAL FLOW GOOD BLOW BOTTOM OF BUCKET IN 8 MIN

Temperature / Pressure Data

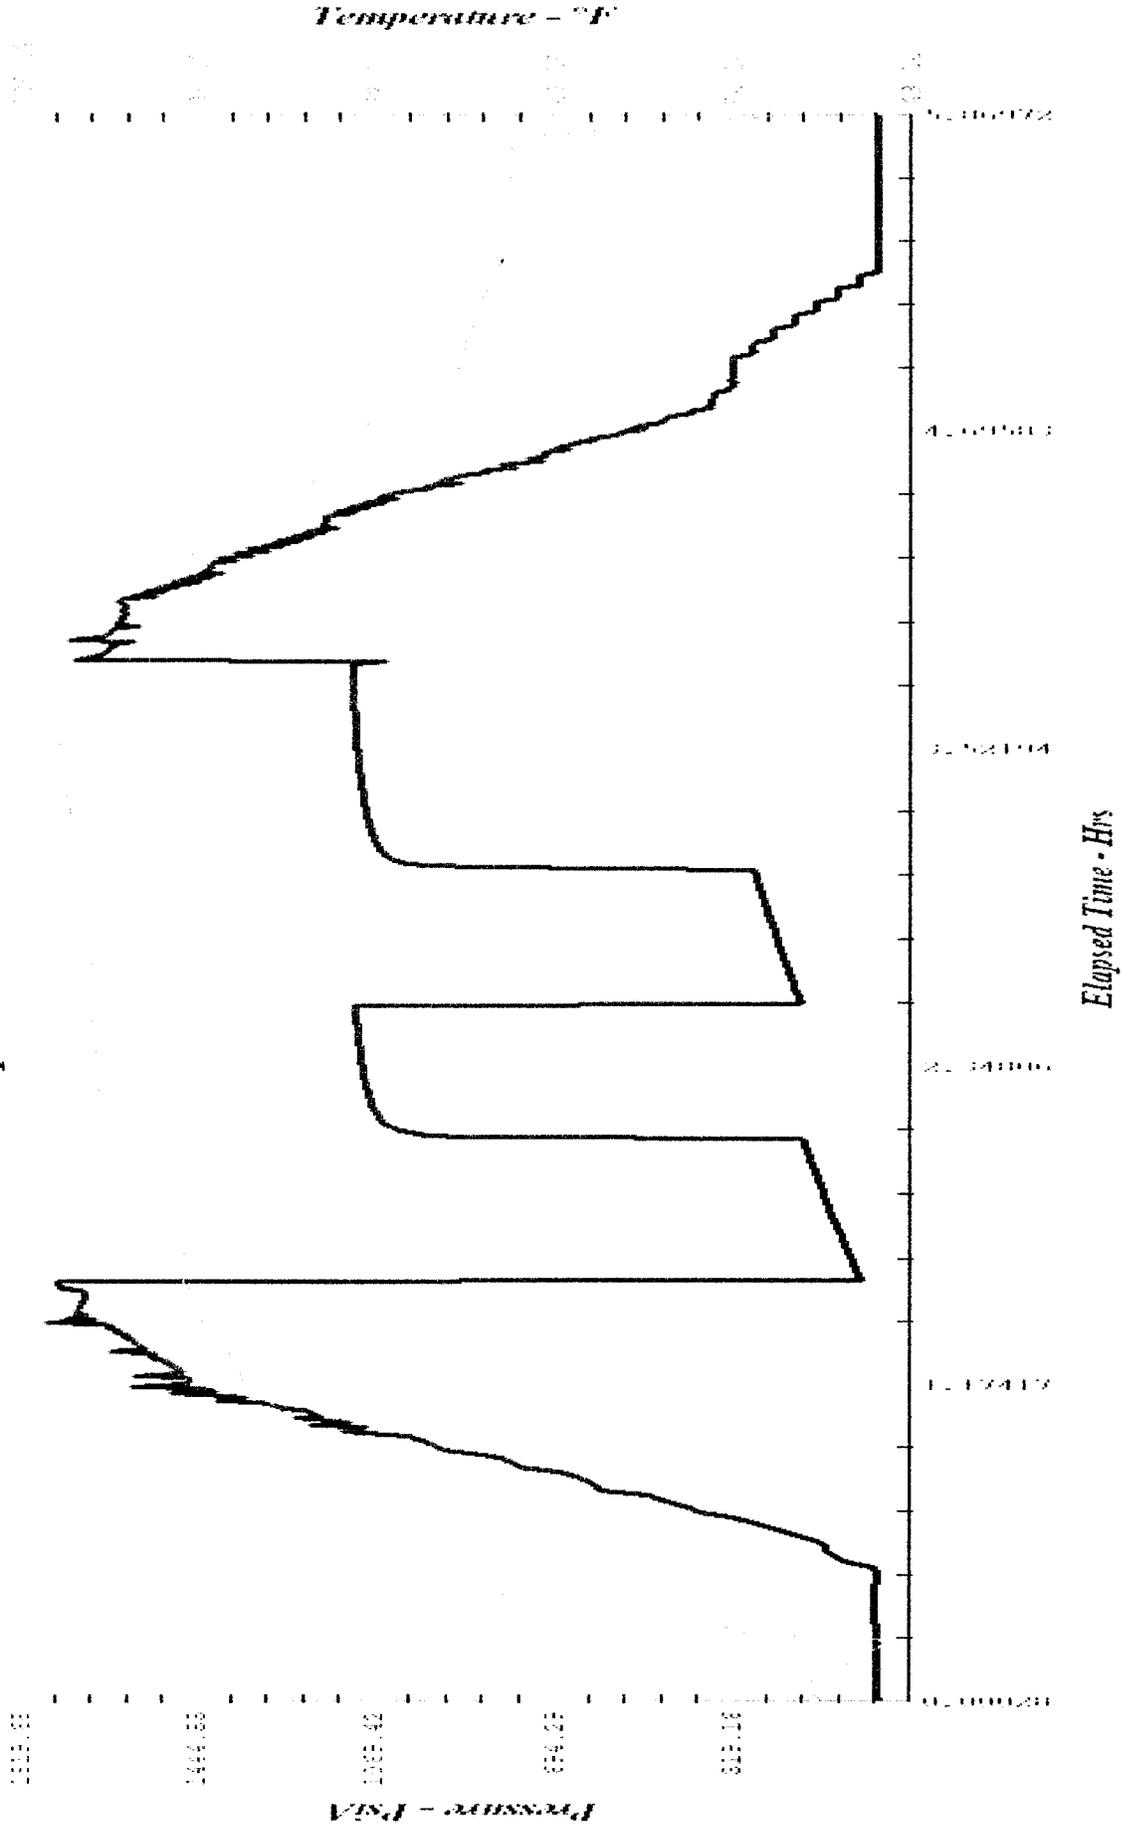

Tool serial number: 91716
Test start: 11/27/2007 08:12:55
