

ly Palomino Petroleum, Inc.  
4924 SE 84th St.  
Newton, KS 67114  
Klee R. Watchous

Lease Name Vermillion  
Lease # 1  
Legal Desc SW NE NE  
Section 6  
Township 17s  
County Ness  
Drilling Cont Southwind Drilling #1  
Job Ticket 4024  
Range 24w  
State KS

nts Times: 30 30 30 30

15-135-24643

# RAL INFORMATION

Test Date 6/5/2007  
Richard Holtz  
Conventional Bottom Hole  
Successful Test  
Packer Size 6 3/4

Gel Chem  
9.2 Viscosity 51.0  
11.2 Chlorides 2000

lar Len 0  
pe Len 0

Mississippi  
Top 4448.0 Bottom 4504.0  
Len Below 56.0 Between 0  
Depth 4504.0

Initial Flow, strong blow, BOB in 5 min. Final Flow, strong blow, BOB in 9 min.  
No blow back on shut ins.

Chokes 3/4 Hole Size 7 7/8  
Top Recorder # W1023  
Mid Recorder #  
Bott Recorder # 13564

Mileage 176 Approved By  
Standby Time 0  
Extra Equipmnt jars and safety joint  
Time on Site 9:15 PM  
Tool Picked Up 11:00 PM  
Tool Layed Dwn 6:30 AM

Elevation 2511.00 Kelley Bushings 2521.00

Start Date/Time 6/4/2007 10:29 PM  
End Date/Time 6/5/2007 6:36 AM

6-175-24w


## VERY

| Description           | Gas        | Oil         | Water  | Mud        |
|-----------------------|------------|-------------|--------|------------|
| lean oil, 36 gravity. | 0% 0ft     | 100% 720ft  | 0% 0ft | 0% 0ft     |
| issy mud cut oil      | 25% 72.5ft | 57% 165.3ft | 0% 0ft | 18% 52.2ft |
| ids 0                 |            |             |        |            |

RECEIVED  
KANSAS CORPORATION COMMISSION

AUG 27 2007

CONSERVATION DIVISION  
WICHITA, KS

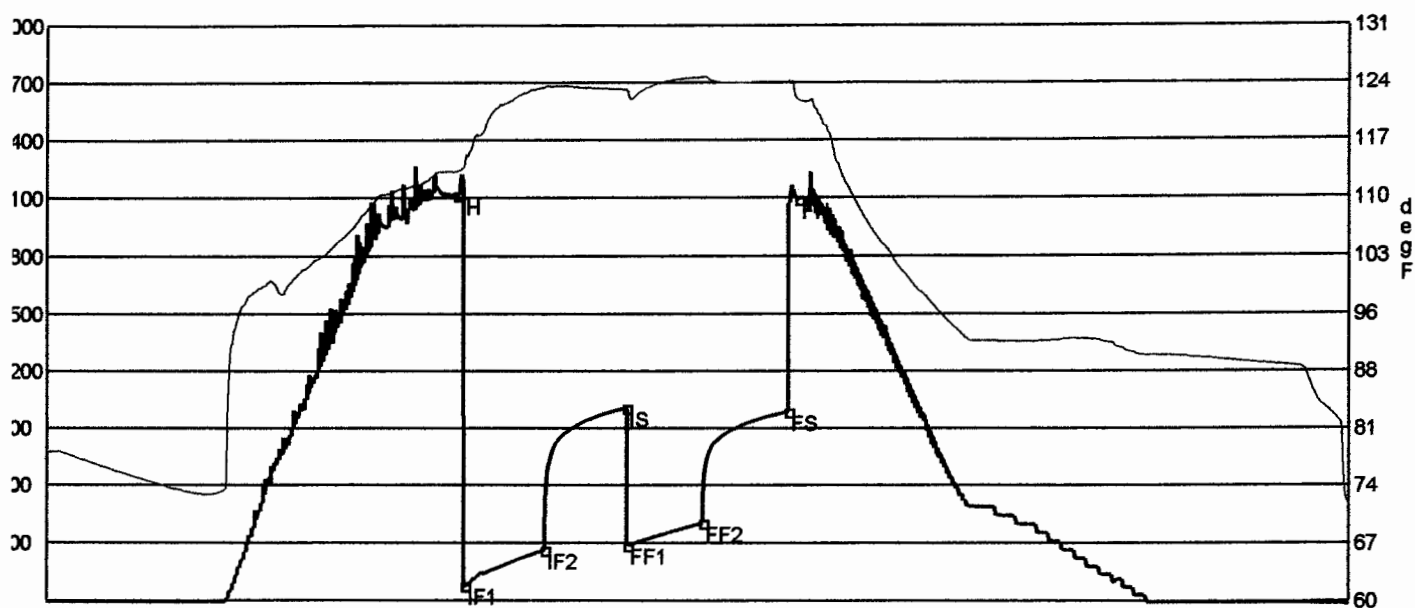

|     | Date                | Time     | Pressure | Temp    |                      |
|-----|---------------------|----------|----------|---------|----------------------|
| IH  | 6/5/2007 1:01:15 AM | 2.5375   | 2114.443 | 112.972 | Initial Hydro-static |
| IF1 | 6/5/2007 1:04:30 AM | 2.591667 | 79.083   | 114.175 | Initial Flow (1)     |
| IF2 | 6/5/2007 1:34:30 AM | 3.091667 | 264.537  | 123.371 | Initial Flow (2)     |
| IS  | 6/5/2007 2:05:00 AM | 3.6      | 1006.968 | 123.081 | Initial Shut-In      |
| FF1 | 6/5/2007 2:05:30 AM | 3.608333 | 289.574  | 122.936 | Final Flow (1)       |
| FF2 | 6/5/2007 2:33:45 AM | 4.079167 | 403.395  | 124.626 | Final Flow (2)       |
| FS  | 6/5/2007 3:05:45 AM | 4.6125   | 986.836  | 124.05  | Final Shut-In        |
| FH  | 6/5/2007 3:09:30 AM | 4.675    | 2091.477 | 121.814 | Final Hydro-static   |

## 4S FLOWS

1 Into IFP   Min Into FFP   Gas Flows   Pressure   Choke

RECEIVED  
KANSAS CORPORATION COMMISSION

AUG 27 2007

CONSERVATION DIVISION  
WICHITA, KS
