


SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

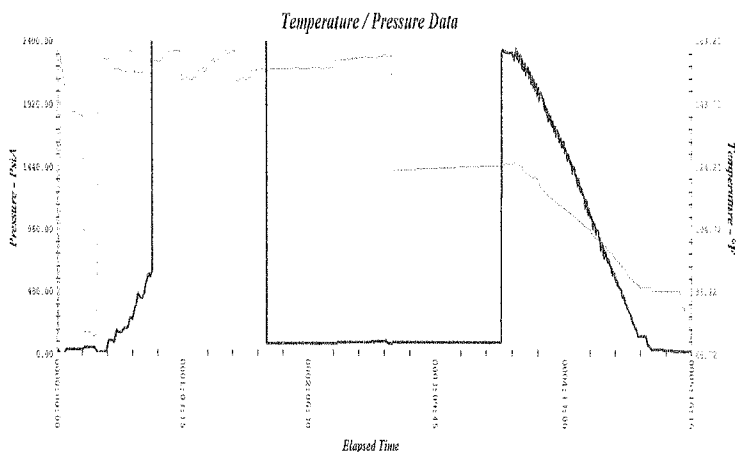

1	Initial Hydrostatic Pressure	2309
2	Initial Flow Pressure	84
3	Final Initial Flow Pressure	84
4	Initial Shut-In Pressure	99
5	Initial Final Flow Pressure	84
6	Final Flow Pressure	89
7	Final Shut-In Pressure	95
8	Final Hydrostatic Pressure	2309

Maximum Temperature 124

Tool serial number: 4163
Test start: 05/28/2008 09:44:16

GENERAL INFORMATION

COMPANY NAME RITCHIE EXPLORATION INC.	
TEST DATE 5/28/08	LEASE AND WELL NUMBER McClellen Trust # 2
SECTION-TOWN-RANGE 13-17S-31W	FORMATION TESTED JOHNSON ZONE &
STATE KANSAS	DRILL STEM TEST NUMBER 1 CHEROKEE SAND
COUNTY SCOTT	REPORT NUMBER 15284
ELEVATION GROUND LEVEL 2898	ELEVATION KELLY BUSHINGS 2893
COMPANY REPRESENTATIVE TOM FUNK	TESTING ENGINEER GENE BUDIG

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4490	TOP PACKER DEPTH 4485
TEST INTERVAL (to) 4585	BOTTOM PACKER DEPTH 4490
ANCHOR LENGTH 95	NUMBER OF PACKERS 2
TOTAL DEPTH (ft) 4585	PACKER SIZE 6 3/4
	HOLE SIZE 7 7/8

FLOW TIMES

	<i>INITIAL OPEN</i>		<i>FINAL OPEN</i>
	TOOL OPEN (from) 1:00		TOOL OPEN (from) 2:00
<i>INITIAL OPEN</i>	TOOL OPEN (to) 1:30		TOOL OPEN (to) 2:30
	DURATION (min.) 30		DURATION (min.) 30
	<i>INITIAL SHUT-IN</i>		<i>FINAL SHUT-IN</i>
	TOOL CLOSED (from) 1:30		TOOL CLOSED (from) 2:30
	TOOL CLOSED (to) 2:00		TOOL CLOSED (to) 3:00
	DURATION (min.) 30		DURATION (min.) 30

INITIAL FLOW

WEAK SURFACE BLOW FOR 15 MINUTES AND DIED

FINAL FLOW

NO BLOW

Company: RITCHIE EXPLORATION INC. Lease & Well No. McClellen Trust # 2 Test #: 1 Date: 05-28-2008 SEC.
 13 TWP. 17S RGE. 31W

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME **RITCHIE EXPLORATION INC.**
TEST DATE **5/28/08**
SECTION-TOWN-RANGE **13-17S-31W**
STATE **KANSAS**
COUNTY **SCOTT**
ELEVATION GROUND LEVEL **2898**
COMPANY REPRESENTATIVE **TOM FUNK**
LEASE AND WELL NUMBER **McClellen Trust # 2**
FORMATION TESTED **JOHNSON ZONE &**
DRILL STEM TEST NUMBER **1** **CHEROKEE SAND**
REPORT NUMBER **15284**
ELEVATION KELLY BUSHINGS **2893**
TESTING ENGINEER **GENE BUDIG**

EXTRA EQUIPMENT


JARS **NO**
SAFETY JOINT **NO**
ELECTRONIC RECORDER **YES**
CIRCULATING SUB **NO**
EXTRA PACKER (3RD) **NO**
EXTRA PACKER (4TH) **NO**
STRADDLE **NO**
HOOK WALL **NO**
SAMPLER **NO**
MILES ROUND TRIP FROM GREAT BEND
TOP RECORDER DEPTH **4582**
RECORDER NUMBER **4023**
BOTTOM RECORDER DEPTH **4583**
RECORDER NUMBER **4050**

WELL INFORMATION

DRILLING CONTRACTOR **WW DRILLING Rig # 2**
DRILL PIPE LENGTH **4351**
DRILL PIPE I.D. **3.8**
TOOL JOINT SIZE **4 1/2 X.H.**
DRILL COLLAR LENGTH **120**
DRILL COLLAR I.D. **2.25**
TOOL JOINT SIZE **4 1/2 X.H.**
CHLORIDES-PITS **2800**
CHLORIDES-DST
MUD WEIGHT #/GAL **9.6**
VISCOSITY **49**
WATER LOSS **8**

COMMENTS

Temperature / Pressure Data

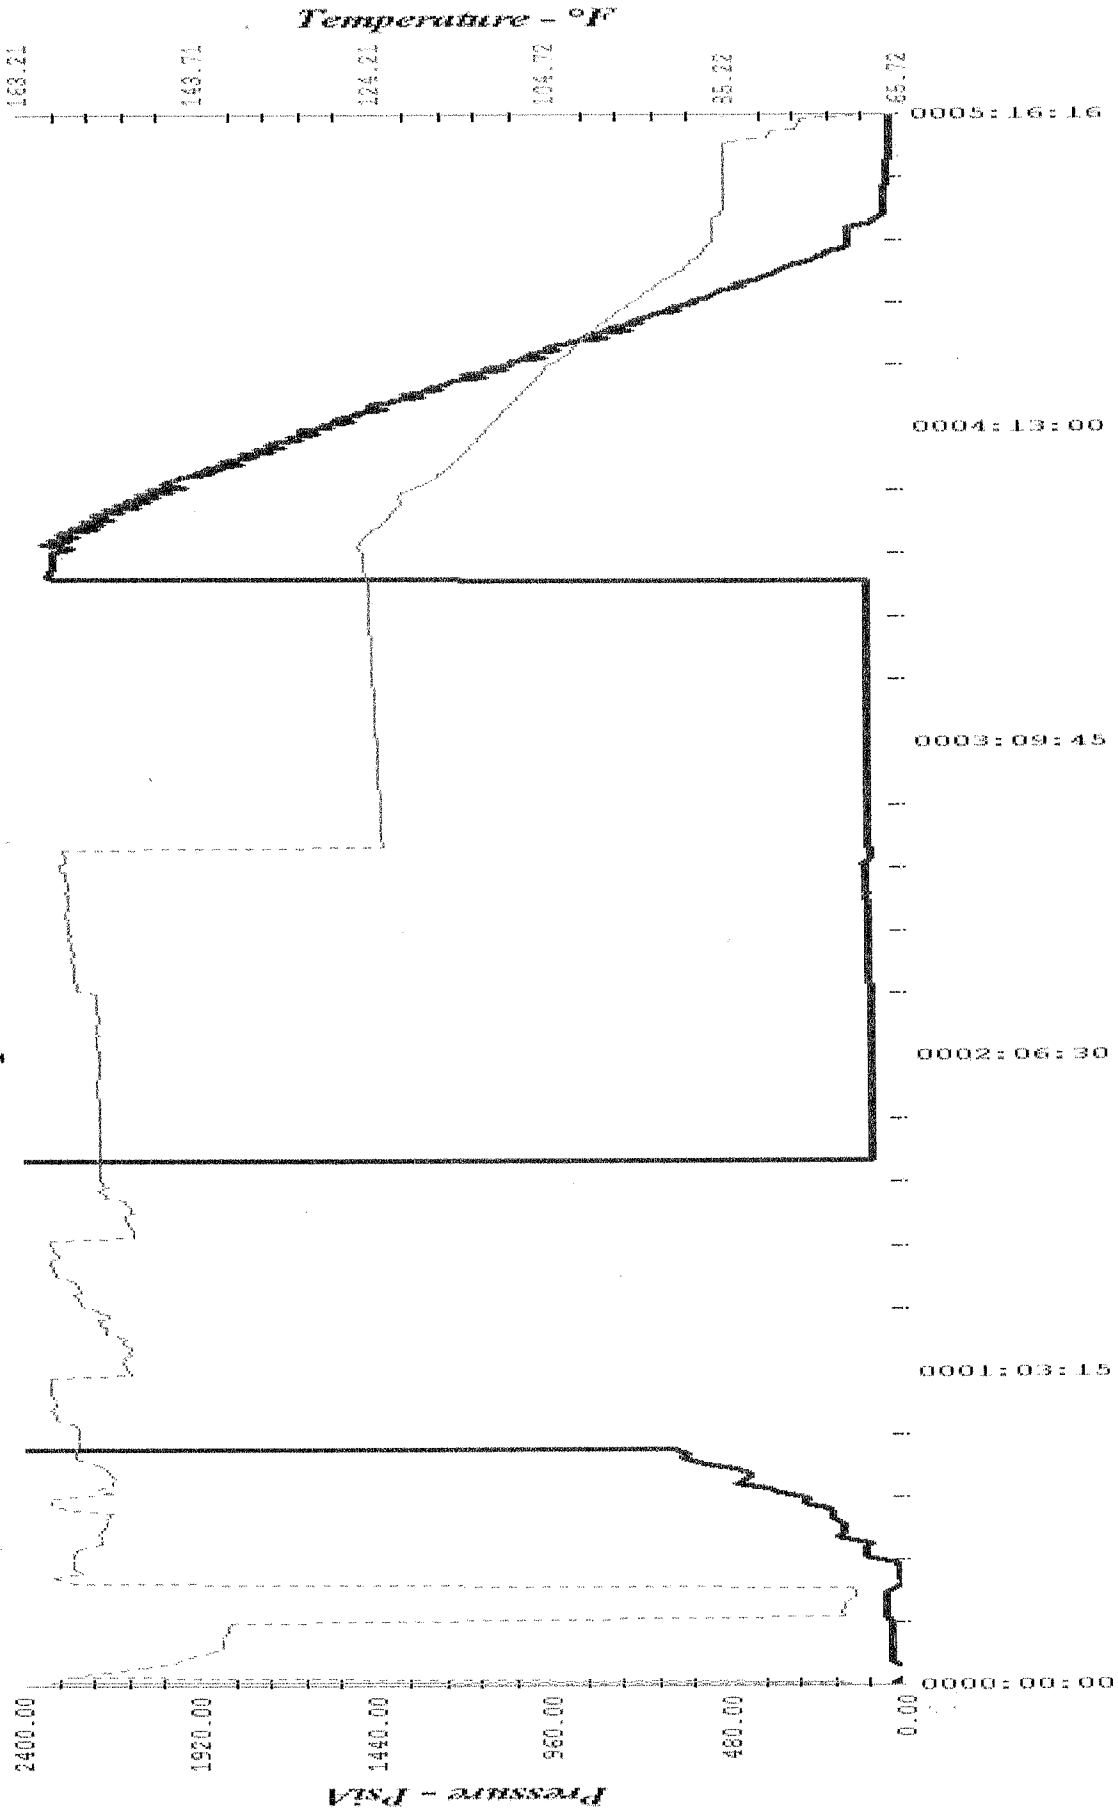

Elapsed Time

Tool serial number: 4143

Test start: 05/28/2008 07:44:26
