

**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

American Warrior Inc

P O Box 399
Garden City Ks 67846

ATTN: Cecil O'Brate

LaDonna #2-29

29-18s-21w Ness

Job Ticket: 41894

DST#: 1

Test Start: 2011.02.28 @ 16:18:00

GENERAL INFORMATION:

Formation: **Miss**

Deviated: **No** Whipstock: **ft (KB)**

Time Tool Opened: 18:23:25

Time Test Ended: 00:10:54

Test Type: **Conventional Bottom Hole**

Tester: **Ray Schwager**

Unit No: **42**

Interval: **4206.00 ft (KB) To 4215.00 ft (KB) (TVD)**

Total Depth: **4215.00 ft (KB) (TVD)**

Hole Diameter: **7.85 inches** Hole Condition: **Fair**

Reference Elevations: **2125.00 ft (KB)**

2119.00 ft (CF)

KB to GR/CF: **6.00 ft**

Serial #: 6625 **Inside**

Press@RunDepth: **226.30 psig @ 4207.00 ft (KB)**

Start Date: **2011.02.28**

End Date:

2011.03.01

Start Time: **16:18:00**

End Time:

00:10:54


Capacity: **8000.00 psig**

Last Calib.: **2011.03.01**

Time On Btm: **2011.02.28 @ 18:21:55**

Time Off Btm: **2011.02.28 @ 21:31:24**

TEST COMMENT: IFF-wk to a strg bl in 30min
ISIP-1/2"bl bk
FFP-wk to a strg bl in 25min
FSIP-surface bl bk

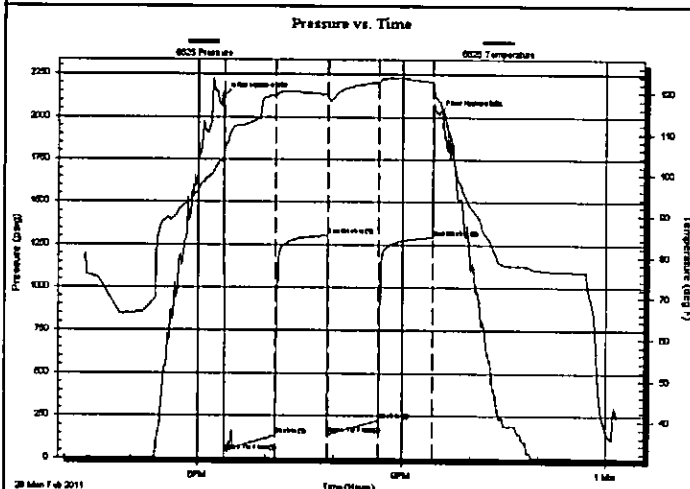

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2119.64	104.45	Initial Hydro-static
2	36.79	106.21	Open To Flow (1)
47	136.22	119.12	Shut-In(1)
92	1303.59	119.56	End Shut-In(1)
93	141.04	118.75	Open To Flow (2)
138	226.30	122.51	Shut-In(2)
185	1293.04	122.78	End Shut-In(2)
190	2020.72	118.07	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
124.00	MGO 20%G15%M65%O	0.65
455.00	CO	6.38
0.00	535'GP	0.00

Gas Rates

	Choke (Inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior Inc

LaDonna #2-29

P O Box 399
Garden City Ks 67846

29-18s-21w Ness

Job Ticket: 41894

DST#: 1

ATTN: Cecil O'Brate

Test Start: 2011.02.28 @ 16:18:00

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 51.00 sec/qt

Water Loss: 7.93 in³

Resistivity: ohm.m

Salinity: 9100.00 ppm

Filter Cake: 1.00 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

Oil API:

Water Salinity:

38 deg API

ppm

ft

bbl

psig

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
124.00	MGO 20%G15%M65%O	0.646
455.00	CO	6.382
0.00	535'GIP	0.000

Total Length: 579.00 ft

Total Volume: 7.028 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

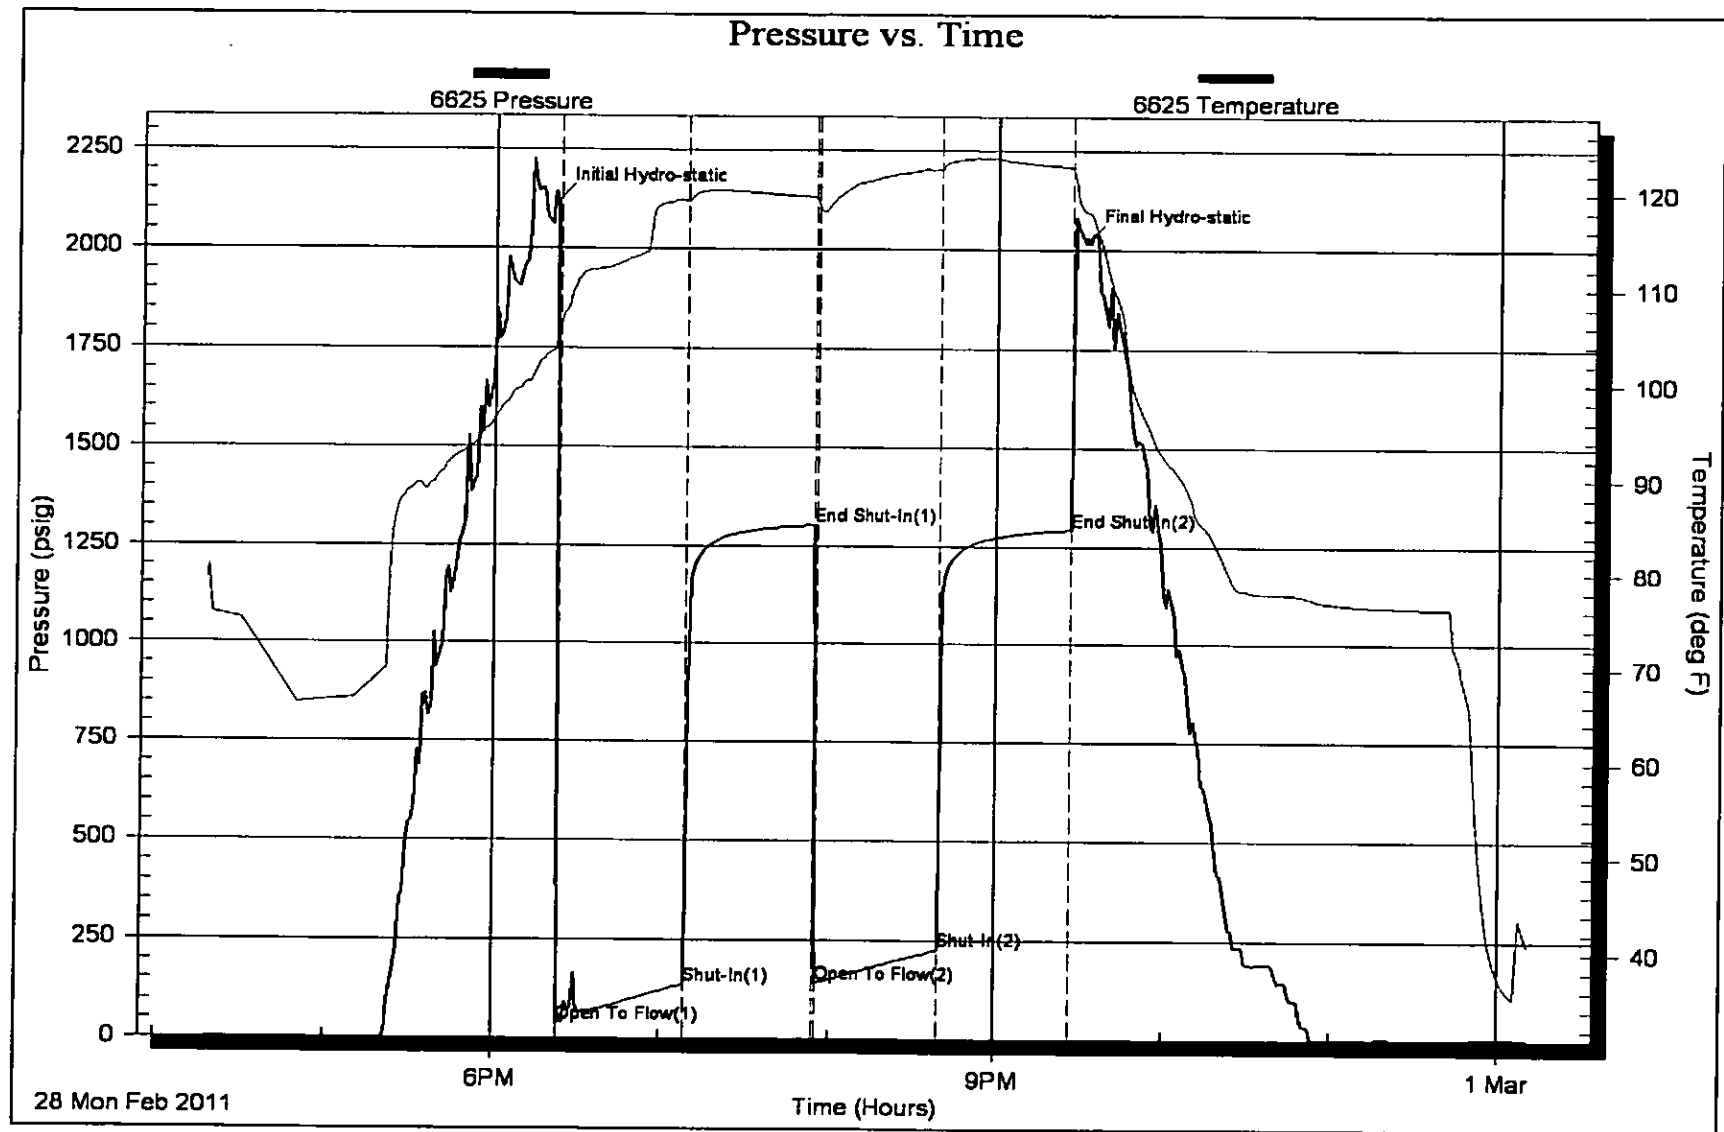



TRILOBITE TESTING INC.

P.O. Box 1733 • Hays, Kansas 67601

Test Ticket

NO. 04189415441

Well Name & No. LaDonna #2-29 Test No. 1 Date 2-28-11
Company AMERICAN WARRIOR Inc Elevation 2125 KB 2119 GL
Address P.O. Box 399 Garden City, Ks 67846
Co. Rep / Geo. JASON ALM Rig PETROMARK Rig 1
Location: Sec. 29 Twp. 18^s Rge. 21^w Co. NESS State K

Interval Tested 4206-4215 Zone Tested MISS
Anchor Length 9 Drill Pipe Run 4071 Mud Wt. 8.9
Top Packer Depth 4201 Drill Collars Run 120 Vis 51
Bottom Packer Depth 4206 Wt. Pipe Run — WL 8
Total Depth 4215 Chlorides 9100 ppm System LCM —

Blow Description TFP - WEAK TO A STRONG BLOW IN 30 MIN
TSIP - 1/2" BLOW BACK
FFP - WEAK TO A STRONG BLOW IN 25 MIN
ESIP - SURFACE BLOW BACK

Rec	Feet of	%gas	%oil	%water	%mud
<u>535</u>	<u>6TP</u>				
<u>455</u>	<u>C0</u>				
<u>124</u>	<u>M60</u>	<u>20</u>	<u>65</u>	<u>15</u>	

Rec Total 579 BHT 122 Gravity 38 API RW — @ — °F Chlorides — ppm

(A) Initial Hydrostatic 2119
(B) First Initial Flow 36
(C) First Final Flow 136
(D) Initial Shut-In 1303
(E) Second Initial Flow 141
(F) Second Final Flow 226
(G) Final Shut-In 1293
(H) Final Hydrostatic 2020

☒ Test 1225
☒ Jars 250
☒ Safety Joint 75
☐ Circ Sub
☐ Hourly Standby
☒ Mileage 100 RT 125
☐ Sampler
☐ Straddle
☐ Shale Packer
☐ Extra Packer
☐ Extra Recorder
☐ Day Standby
☐ Accessibility
Sub Total 1675

T-On Location 1530
T-Started 1618
T-Open 1840
T-Pulled 2140
T-Out 2010
Comments
☐ Ruined Shale Packer
☐ Ruined Packer
☐ Extra Copies
Sub Total 8
Total 1675
MP/DST Disc't

Initial Open 45
Initial Shut-In 45
Final Flow 45
Final Shut-In 45

Approved By JASON ALM

Our Representative RAY SCHWAGER Thank you

Trilobite Testing Inc. shall not be liable for damaged of any kind of the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test, tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.
