

DRILL STEM TEST REPORT

Prepared For: **Larson Engineering**

562 W State Rd 4
Olmitz, Ks
67564

CONFIDENTIAL
OCT 23 2009
KCC

ATTN: Steve Davis

30-18s-29w Lane, Ks

Fager #1-30

Start Date: 2009.07.07 @ 00:15:18

End Date: 2009.07.07 @ 07:10:27

Job Ticket #: 34770

DST #: 1

RECEIVED

OCT 26 2009

KCC WICHITA

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Larson Engineering

562 W State Rd 4

Olmitz, Ks

67564

ATTN: Steve Davis

Fager #1-30

30-18s-29w Lane, Ks

Job Ticket: 34770

DST#: 1

Test Start: 2009.07.07 @ 00:15:18

GENERAL INFORMATION:

Formation: H

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 03:45:43

Time Test Ended: 07:10:27

Test Type: Conventional Bottom Hole

Tester: Shane McBride

Unit No: 40

Interval: 4161.00 ft (KB) To 4188.00 ft (KB) (TVD)

Total Depth: 4188.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2844.00 ft (KB)

2834.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 6667

Inside

Press@RunDepth: 32.04 psig @ 4162.00 ft (KB)

Start Date: 2009.07.07

End Date:

2009.07.07

Start Time: 00:15:18

End Time:

06:59:27

Capacity: 7000.00 psig

Last Calib.: 2009.07.07

Time On Btm: 2009.07.07 @ 03:45:28


Time Off Btm: 2009.07.07 @ 05:20:12

TEST COMMENT: Weak blow died in 5 min.

No return

No blow

No return

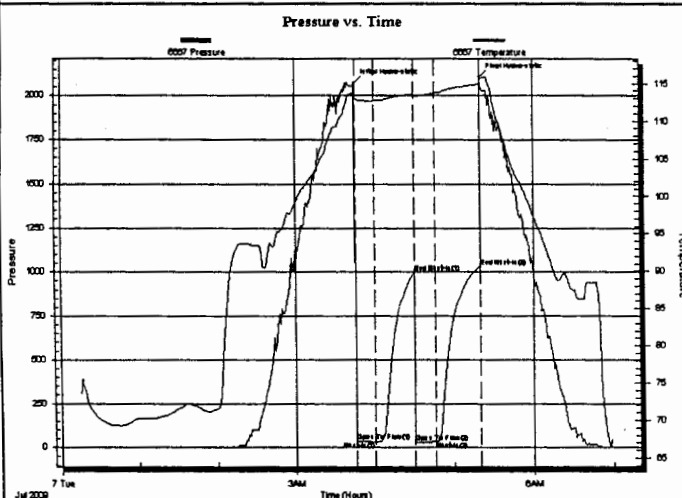

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2071.33	113.59	Initial Hydro-static
1	35.13	113.03	Open To Flow (1)
15	31.91	112.72	Shut-In(1)
45	998.33	113.64	End Shut-In(1)
45	29.04	113.10	Open To Flow (2)
60	32.04	113.70	Shut-In(2)
95	1031.73	114.94	End Shut-In(2)
95	2106.95	115.38	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
2.00	mud 100% m	0.01

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Engineering

562 W State Rd 4

Olmitz, Ks

67564

ATTN: Steve Davis

Fager #1-30

30-18s-29w Lane, Ks

Job Ticket: 34770

DST#: 1

Test Start: 2009.07.07 @ 00:15:18

Tool Information

Drill Pipe:	Length: 3984.00 ft	Diameter: 3.80 inches	Volume: 55.89 bbl	Tool Weight:	1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	25000.00 lb
Drill Collar:	Length: 186.00 ft	Diameter: 2.25 inches	Volume: 0.91 bbl	Weight to Pull Loose:	80000.00 lb
		Total Volume:	56.80 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	36.00 ft			String Weight: Initial	68000.00 lb
Depth to Top Packer:	4161.00 ft			Final	68000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	27.00 ft				
Tool Length:	54.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			4135.00	
Shut In Tool	5.00			4140.00	
Hydraulic tool	5.00			4145.00	
Jars	5.00			4150.00	
Safety Joint	2.00			4152.00	
Packer	5.00			4157.00	27.00 Bottom Of Top Packer
Packer	4.00			4161.00	
Stubb	1.00			4162.00	
Recorder	0.00	6667	Inside	4162.00	
Recorder	0.00	6771	Outside	4162.00	
Perforations	21.00			4183.00	
Bullnose	5.00			4188.00	27.00 Bottom Packers & Anchor

Total Tool Length: 54.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Engineering

Fager #1-30

562 W State Rd 4

30-18s-29w Lane, Ks

Olmritz, Ks

Job Ticket: 34770

DST#: 1

67564

ATTN: Steve Davis

Test Start: 2009.07.07 @ 00:15:18

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 52.00 sec/qt

Cushion Volume:

bbl

Water Loss: 6.76 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2800.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
2.00	mud 100% _m	0.010

Total Length: 2.00 ft

Total Volume: 0.010 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


Serial #: 6667

Inside Larson Engineering

30-18s-29w Lane, Ks


DST Test Number: 1

Pressure vs. Time

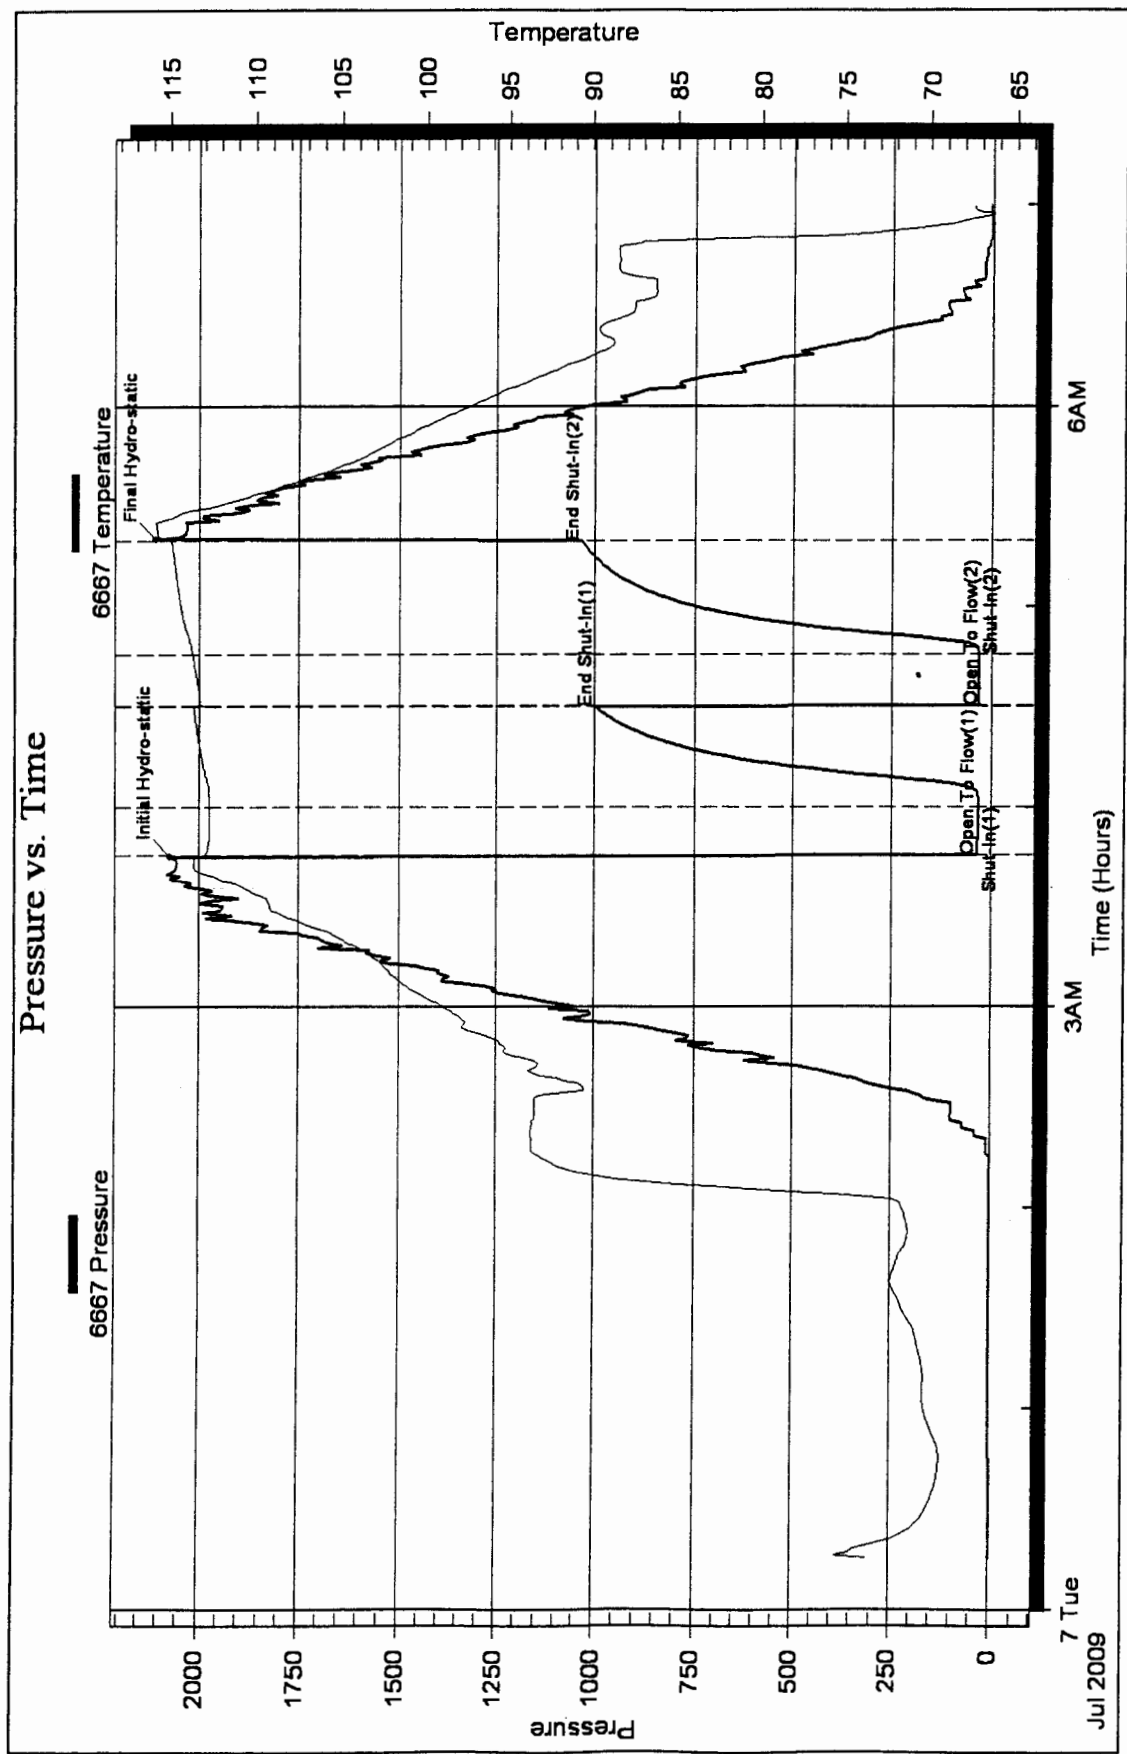

Trilobite Testing, Inc

Ref. No: 34770



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Larson Engineering**

562 W State Rd 4
Olmitz, Ks
67564

ATTN: Steve Davis

30-18s-29w Lane, Ks

Fager #1-30

Start Date: 2009.07.07 @ 19:07:12

End Date: 2009.07.08 @ 01:45:06

Job Ticket #: 34771

DST #: 2

RECEIVED


OCT 26 2009

KCC WICHITA

Trilobite Testing, Inc

PO Box 1733 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Larson Engineering

562 W State Rd 4
Olmitz, Ks
67564

ATTN: Steve Davis

Fager #1-30

30-18s-29w Lane, Ks

Job Ticket: 34771

DST#: 2

Test Start: 2009.07.07 @ 19:07:12

GENERAL INFORMATION:

Formation: I-J

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 21:02:52

Time Test Ended: 01:45:06

Interval: 4202.00 ft (KB) To 4252.00 ft (KB) (TVD)

Total Depth: 4252.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Test Type: Conventional Bottom Hole

Tester: Shane McBride

Unit No: 40

Reference Elevations: 2844.00 ft (KB)

2834.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 6667

Inside

Press@RunDepth: 96.31 psig @ 4203.00 ft (KB)

Start Date: 2009.07.07

End Date:

2009.07.08

Start Time: 19:07:12

End Time:

01:33:06


Capacity: 7000.00 psig

Last Calib.: 2009.07.08

Time On Btm: 2009.07.07 @ 21:02:37

Time Off Btm: 2009.07.07 @ 23:17:07

TEST COMMENT: Weak 1/4" in blow
No return
Surface blow in 6 min. built to 1 3/4" in
No return

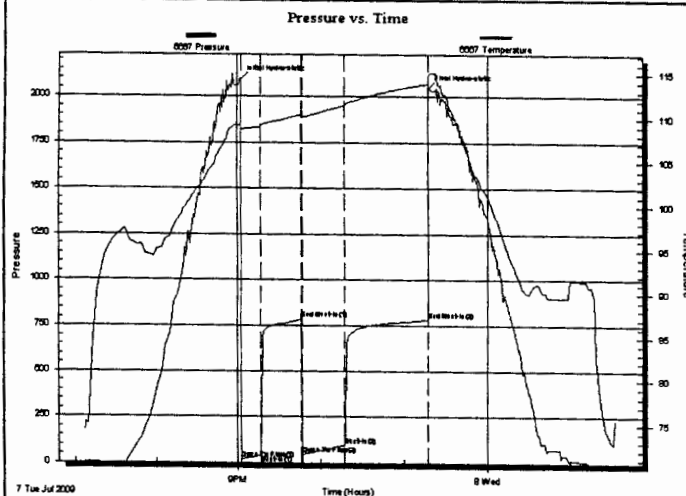

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2088.35	109.33	Initial Hydro-static
1	20.15	108.56	Open To Flow (1)
15	41.32	109.05	Shut-In (1)
44	786.54	110.42	End Shut-In (1)
45	44.69	110.06	Open To Flow (2)
75	96.31	111.45	Shut-In (2)
134	783.11	113.93	End Shut-In (2)
135	2042.36	114.66	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
120.00	mud 100% m	0.59

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Engineering

Fager #1-30

562 W State Rd 4

30-18s-29w Lane, Ks

Olmitz, Ks

Job Ticket: 34771

DST#: 2

67564

Test Start: 2009.07.07 @ 19:07:12

ATTN: Steve Davis

Tool Information

Drill Pipe:	Length: 4009.00 ft	Diameter: 3.80 inches	Volume: 56.24 bbl	Tool Weight:	1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	25000.00 lb
Drill Collar:	Length: 186.00 ft	Diameter: 2.25 inches	Volume: 0.91 bbl	Weight to Pull Loose:	85000.00 lb
		Total Volume:	57.15 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	20.00 ft			String Weight: Initial	68000.00 lb
Depth to Top Packer:	4202.00 ft			Final	68000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	50.00 ft				
Tool Length:	77.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		
Tool Comments:					

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Change Over Sub	1.00			4176.00	
Shut In Tool	5.00			4181.00	
Hydraulic tool	5.00			4186.00	
Jars	5.00			4191.00	
Safety Joint	2.00			4193.00	
Packer	5.00			4198.00	27.00 Bottom Of Top Packer
Packer	4.00			4202.00	
Stubb	1.00			4203.00	
Recorder	0.00	6667	Inside	4203.00	
Recorder	0.00	6771	Outside	4203.00	
Perforations	11.00			4214.00	
Change Over Sub	1.00			4215.00	
Drill Pipe	31.00			4246.00	
Change Over Sub	1.00			4247.00	
Bullnose	5.00			4252.00	50.00 Bottom Packers & Anchor

Total Tool Length: 77.00



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Engineering

Fager #1-30

562 W State Rd 4

30-18s-29w Lane, Ks

Olmitz, Ks

Job Ticket: 34771

DST#: 2

67564

Test Start: 2009.07.07 @ 19:07:12

ATTN: Steve Davis

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 46.00 sec/qt

Cushion Volume:

bbbl

Water Loss: 7.17 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2800.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
120.00	mud 100% _m	0.590

Total Length: 120.00 ft

Total Volume: 0.590 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


Serial #: 6667

Inside Larson Engineering

30-18s-29w Lane, Ks

DST Test Number: 2


Pressure vs. Time

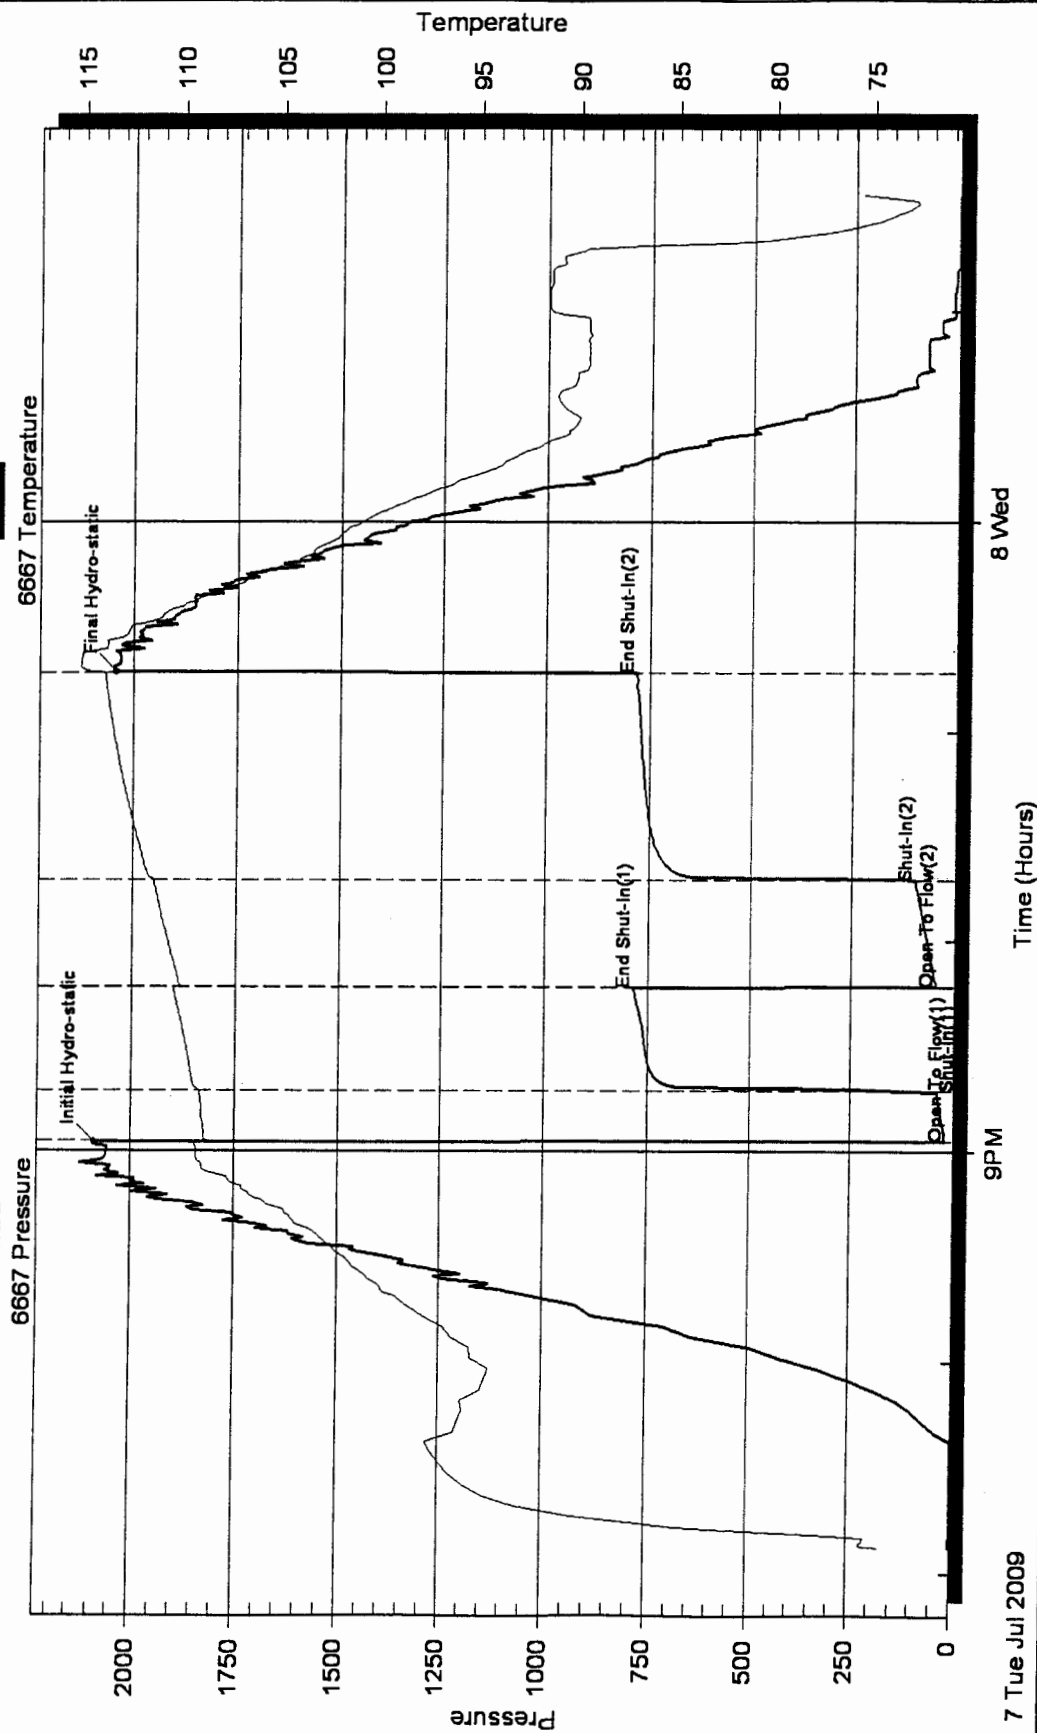

Trilobite Testing, Inc

Ref. No: 34771

Printed: 2009.07.15 @ 08:36:52 Page 5



DRILL STEM TEST REPORT

Prepared For: **Larson Engineering**

562 W State Rd 4
Olmitz, Ks
67564

ATTN: Steve Davis

30-18s-29w Lane, Ks

Fager #1-30

Start Date: 2009.07.08 @ 21:15:36

End Date: 2009.07.09 @ 02:35:36


Job Ticket #: 34772 DST #: 3

RECEIVED

OCT 26 2009

KCC WICHITA

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Larson Engineering

562 W State Rd 4
Olmitz, Ks
67564
ATTN: Steve Davis

Fager #1-30

30-18s-29w Lane, Ks

Job Ticket: 34772

DST#: 3

Test Start: 2009.07.08 @ 21:15:36

GENERAL INFORMATION:

Formation: L

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 23:11:51

Time Test Ended: 02:35:36

Test Type: Conventional Bottom Hole

Tester: Shane McBride

Unit No: 40

Interval: 4302.00 ft (KB) To 4322.00 ft (KB) (TVD)

Total Depth: 4322.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2844.00 ft (KB)

2834.00 ft (CF)

KB to GR/CF: 10.00 ft

Serial #: 6667

Inside

Press@RunDepth: 16.65 psig @ 4303.00 ft (KB)

Start Date: 2009.07.08

End Date: 2009.07.09

Capacity: 7000.00 psig

Last Calib.: 2009.07.10

Start Time: 21:15:41

End Time: 02:27:35

Time On Btm: 2009.07.08 @ 23:11:36


Time Off Btm: 2009.07.09 @ 00:45:36

TEST COMMENT: Weak blow died in 6 min.

No return

No blow

No return

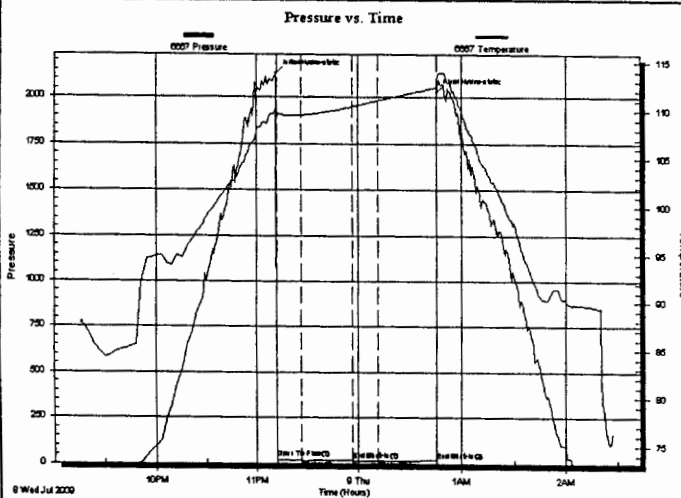

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2129.12	110.15	Initial Hydro-static
1	29.23	109.11	Open To Flow (1)
15	17.70	109.49	Shut-In (1)
45	19.71	110.38	End Shut-In (1)
45	16.77	110.39	Open To Flow (2)
60	16.65	111.00	Shut-In (2)
94	17.90	112.36	End Shut-In (2)
94	2024.91	113.25	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
1.00	mud 100% m	0.00

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Engineering

Fager #1-30

562 W State Rd 4

30-18s-29w Lane, Ks

Olmitz, Ks

Job Ticket: 34772

DST#: 3

67564

Test Start: 2009.07.08 @ 21:15:36

ATTN: Steve Davis

Tool Information

Drill Pipe:	Length: 4100.00 ft	Diameter: 3.80 inches	Volume: 57.51 bbl	Tool Weight: 1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 25000.00 lb
Drill Collar:	Length: 186.00 ft	Diameter: 2.25 inches	Volume: 0.91 bbl	Weight to Pull Loose: 85000.00 lb
		Total Volume: 58.42 bbl		Tool Chased 0.00 ft
Drill Pipe Above KB:	11.00 ft			String Weight: Initial 68000.00 lb
Depth to Top Packer:	4302.00 ft			Final 68000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	20.00 ft			
Tool Length:	47.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		
Tool Comments:				

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Change Over Sub	1.00			4276.00	
Shut In Tool	5.00			4281.00	
Hydraulic tool	5.00			4286.00	
Jars	5.00			4291.00	
Safety Joint	2.00			4293.00	
Packer	5.00			4298.00	27.00 Bottom Of Top Packer
Packer	4.00			4302.00	
Stubb	1.00			4303.00	
Recorder	0.00	6667	Inside	4303.00	
Recorder	0.00	6771	Outside	4303.00	
Perforations	14.00			4317.00	
Bullnose	5.00			4322.00	20.00 Bottom Packers & Anchor

Total Tool Length: 47.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Engineering

Fager #1-30

562 W State Rd 4

30-18s-29w Lane, Ks

Olmitz, Ks

Job Ticket: 34772

DST#: 3

67564

Test Start: 2009.07.08 @ 21:15:36

ATTN: Steve Davis

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 55.00 sec/qt

Cushion Volume:

bbl

Water Loss: 7.18 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2900.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
1.00	mud 100%m	0.005

Total Length: 1.00 ft

Total Volume: 0.005 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0


Serial #:


Laboratory Name:

Laboratory Location:

Recovery Comments:

Pressure vs. Time

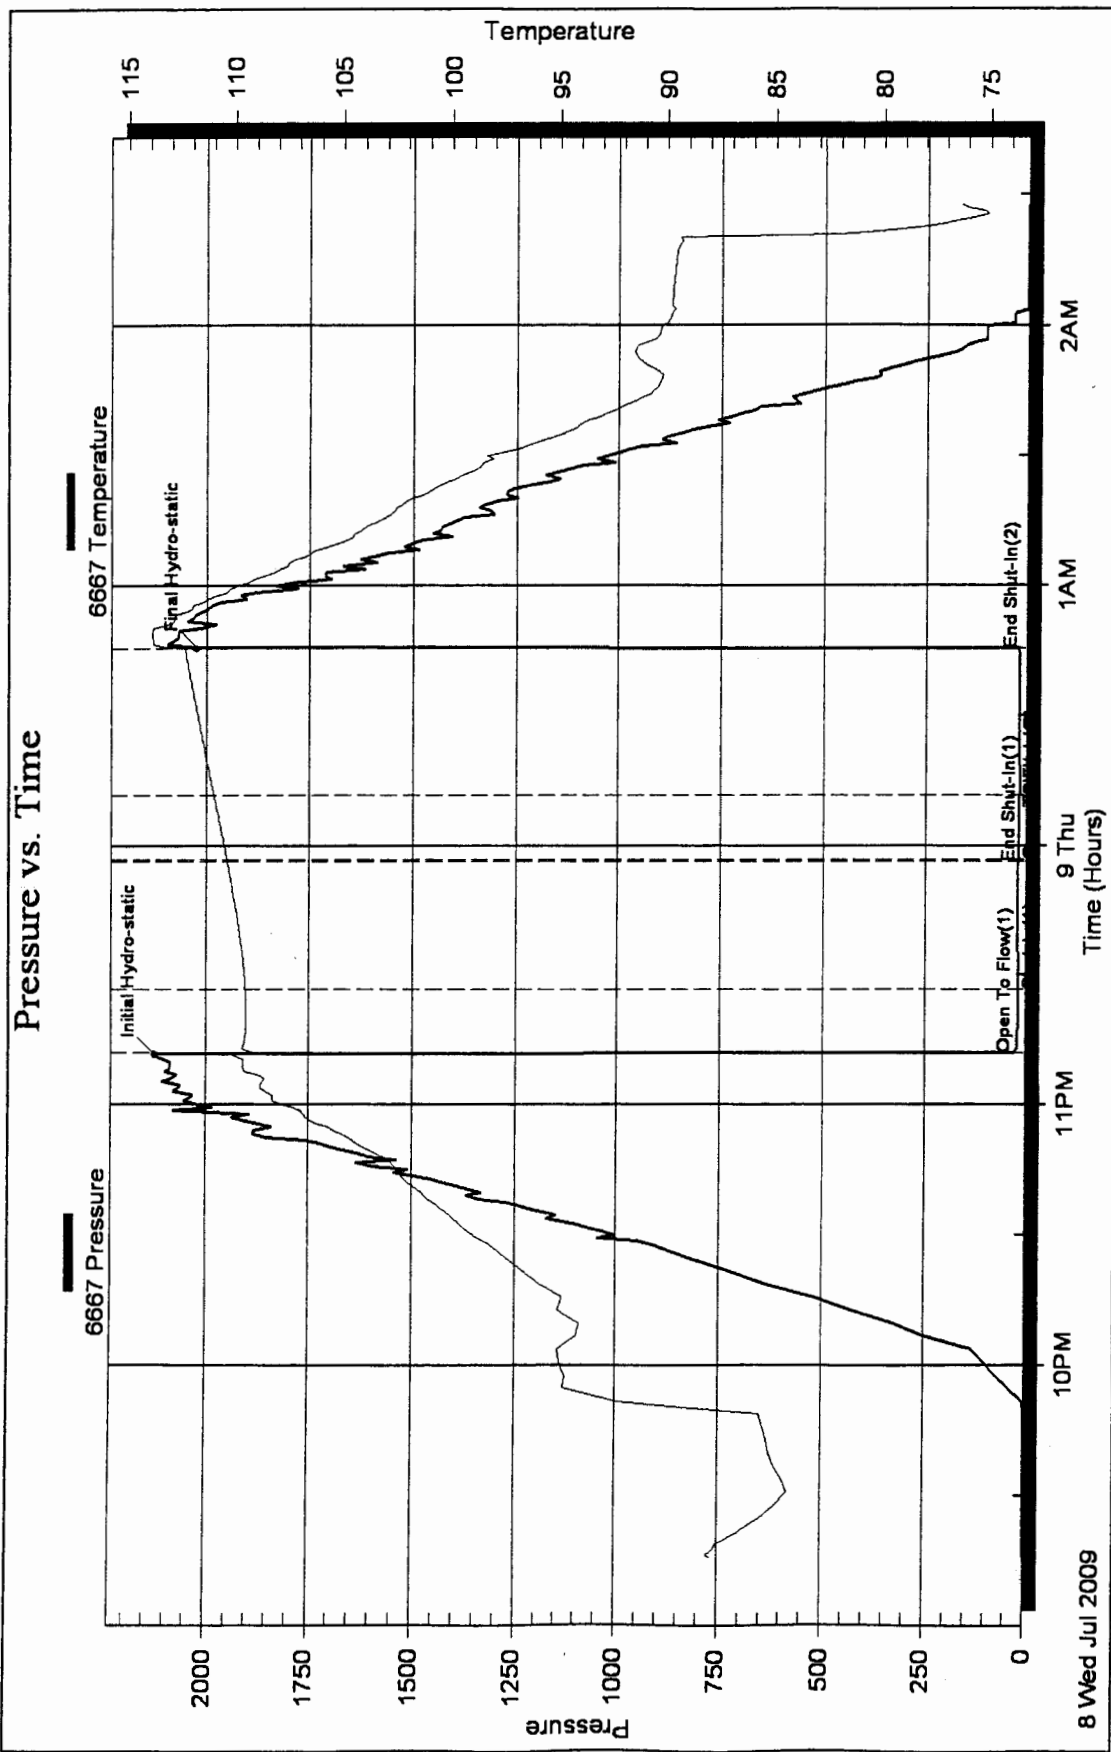



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Larson Engineering**

562 W State Rd 4
Olmitz, Ks
67564

ATTN: Steve Davis

30-18s-29w Lane, Ks

Fager #1-30

Start Date: 2009.07.10 @ 15:45:33

End Date: 2009.07.10 @ 21:55:27

Job Ticket #: 34773 DST #: 4

RECEIVED

OCT 26 2009

KCC WICHITA

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

Larson Engineering

562 W State Rd 4
Olmitz, Ks
67564
ATTN: Steve Davis

Fager #1-30

30-18s-29w Lane, Ks

Job Ticket: 34773

DST#: 4

Test Start: 2009.07.10 @ 15:45:33

GENERAL INFORMATION:

Formation: **Cherokee, Johnson**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 18:00:28

Time Test Ended: 21:55:27

Test Type: Conventional Bottom Hole

Tester: Shane McBride

Unit No: 40

Interval: **4532.00 ft (KB) To 4595.00 ft (KB) (TVD)**

Reference Elevations: 2844.00 ft (KB)

Total Depth: 4595.00 ft (KB) (TVD)

2834.00 ft (CF)

Hole Diameter: 7.88 inches Hole Condition: Fair

KB to GR/CF: 10.00 ft

Serial #: 6667

Inside

Press@RunDepth: 19.48 psig @ 4533.00 ft (KB)

Capacity: 7000.00 psig

Start Date: 2009.07.10

End Date: 2009.07.10

Last Calib.: 2009.07.10

Start Time: 15:45:33

End Time: 21:40:27

Time On Btm: 2009.07.10 @ 18:00:13


Time Off Btm: 2009.07.10 @ 19:31:13

TEST COMMENT: Weak blow died in 4 min.

No return

No blow

No return

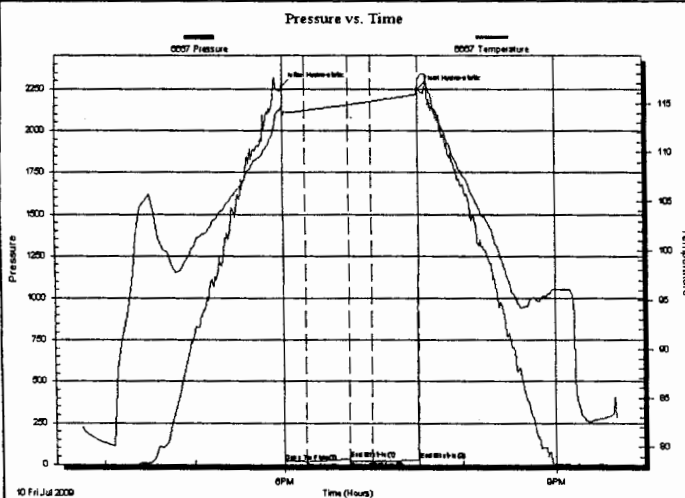

PRESSURE SUMMARY

Time (Mn.)	Pressure (psig)	Temp (deg F)	Annotation
0	2268.49	114.76	Initial Hydro-static
1	18.63	113.61	Open To Flow (1)
15	18.56	114.25	Shut-In(1)
45	34.75	114.83	End Shut-In(1)
45	20.15	114.83	Open To Flow (2)
60	19.48	115.17	Shut-In(2)
91	29.65	115.92	End Shut-In(2)
91	2250.93	117.31	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
2.00	mud 100% m	0.01

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

TOOL DIAGRAM

Larson Engineering

Fager #1-30

562 W State Rd 4
Olmitz, Ks
67564

30-18s-29w Lane, Ks

Job Ticket: 34773

DST#: 4

ATTN: Steve Davis

Test Start: 2009.07.10 @ 15:45:33

Tool Information

Drill Pipe:	Length: 4343.00 ft	Diameter: 3.80 inches	Volume: 60.92 bbl	Tool Weight:	1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	25000.00 lb
Drill Collar:	Length: 186.00 ft	Diameter: 2.25 inches	Volume: 0.91 bbl	Weight to Pull Loose:	85000.00 lb
		Total Volume:	61.83 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	24.00 ft			String Weight: Initial	70000.00 lb
Depth to Top Packer:	4532.00 ft			Final	70000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	63.00 ft				
Tool Length:	90.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Change Over Sub	1.00			4506.00	
Shut In Tool	5.00			4511.00	
Hydraulic tool	5.00			4516.00	
Jars	5.00			4521.00	
Safety Joint	2.00			4523.00	
Packer	5.00			4528.00	27.00 Bottom Of Top Packer
Packer	4.00			4532.00	
Stubb	1.00			4533.00	
Recorder	0.00	6667	Inside	4533.00	
Recorder	0.00	6771	Outside	4533.00	
Perforations	24.00			4557.00	
Change Over Sub	1.00			4558.00	
Drill Pipe	31.00			4589.00	
Change Over Sub	1.00			4590.00	
Bullnose	5.00			4595.00	63.00 Bottom Packers & Anchor

Total Tool Length: 90.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Larson Engineering

Fager #1-30

562 W State Rd 4

30-18s-29w Lane, Ks

Olmitz, Ks

Job Ticket: 34773

DST#: 4

67564

ATTN: Steve Davis

Test Start: 2009.07.10 @ 15:45:33

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 50.00 sec/qt

Cushion Volume:

bbl

Water Loss: 7.59 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 2900.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
2.00	mud 100% _m	0.010

Total Length: 2.00 ft

Total Volume: 0.010 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

