




OIL WELL CEMENTING INC.

Date 1-18-70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6918

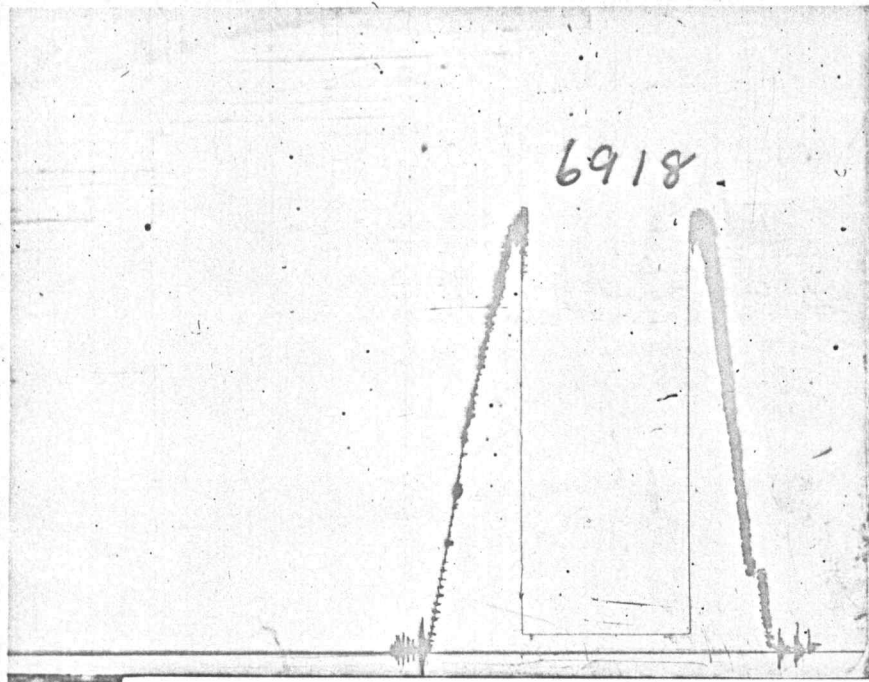

Company Ablah Contractor H-30 Drlg. Co.

Well No. 3 Lease Hill County Rice Sec. 33 Twp 18 Rng 7

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 5 1/2

Interval Tested From 3230 To 3300 Depth of Well 3300 Size Choke 5/8

Fluid Recovered In Drill Pipe Temp. Elev.

Initial Hyd. 1811 P.S.I. Final Hyd. P.S.I.

First Initial Flow Pressure 83 P.S.I. Opened Tool 3:45 PM A.M. P.M.

First Final Flow Pressure 83 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 83 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 83 P.S.I. Second Flow Pres. 30 Min.

Second Final Flow Pressure P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 83 P.S.I.

Blow Very weak decreasing blow thruout test

Recovery 10 ft. of drlg mud

Remarks

Approved By William Bradley Tester Anthony
