

TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Am Warrior
PO Box 399
Garden City, Ks
67846
ATTN: Jim Musgrove

Link 2-13

13-19-10/Rice

Job Ticket: 41783

DST#: 1

Test Start: 2011.02.19 @ 22:08:09

GENERAL INFORMATION:

Formation: LKC "D-G"

Deviated: No Whipstock:

ft (KB)

Time Tool Opened: 00:11:08

Time Test Ended: 04:26:38

Test Type: Conventional Bottom Hole

Tester: Brian Fairbank

Unit No: 41

Interval: 2972.00 ft (KB) To 3051.00 ft (KB) (TVD)

Total Depth: 3051.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition:

Reference Elevations: 1755.00 ft (KB)

1747.00 ft (CF)

KB to GR/CF: 8.00 ft

Serial #: 8372

Inside

Press@RunDepth: 76.72 psig @ 2979.00 ft (KB)

Start Date: 2011.02.19

End Date:

2011.02.20

Start Time: 22:08:09

End Time:

04:26:38

Capacity: 8000.00 psig


Last Calib.: 2011.02.20

Time On Btm: 2011.02.20 @ 00:10:08

Time Off Btm: 2011.02.20 @ 02:48:38

TEST COMMENT: IFP - BOB 10 min
ISI - no blow back
FFP - BOB 7 min
FSI - no blow back

Pressure vs. Time

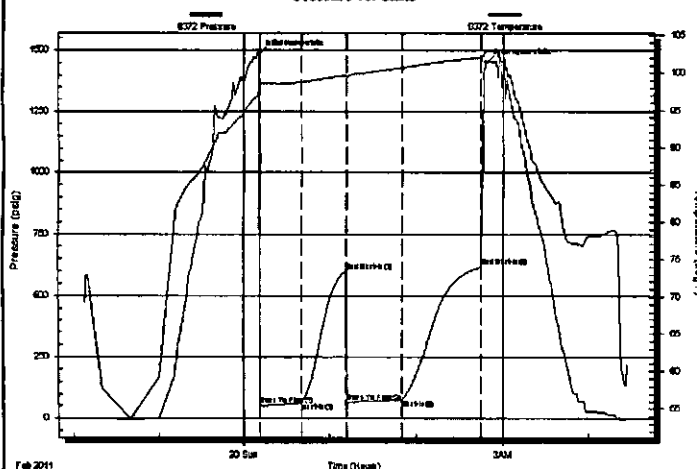

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1485.09	97.94	Initial Hydro-static
1	55.94	98.23	Open To Flow (1)
30	62.00	98.78	Shut-In(1)
61	602.65	99.69	End Shut-In(1)
62	65.91	99.58	Open To Flow (2)
100	76.72	100.67	Shut-In(2)
155	618.66	102.04	End Shut-In(2)
159	1449.66	102.85	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
70.00	MUD 100%	0.98
0.00	260' GIP	0.00


Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------

RECEIVED

MAR 29 2011

KCC WICHITA



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

Am Warrior
PO Box 399
Garden City, Ks
67846
ATTN: Jim Musgrove

Link 2-13
13-19-10/Rice
Job Ticket: 41783 DST#: 1
Test Start: 2011.02.19 @ 22:08:09

Mud and Cushion Information

Mud Type: Gel Chem
Mud Weight: 9.00 lb/gal
Viscosity: 46.00 sec/qt
Water Loss: 8.78 in³
Resistivity: ohm.m
Salinity: 3600.00 ppm
Filter Cake: inches

Cushion Type:
Cushion Length: ft
Cushion Volume: bbl
Gas Cushion Type:
Gas Cushion Pressure: psig
Oil API: deg API
Water Salinity: ppm


Recovery Information

Recovery Table

Length ft	Description	Volume bbl
70.00	MUD 100%	0.982
0.00	260' GIP	0.000

Total Length: 70.00 ft Total Volume: 0.982 bbl

Num Fluid Samples: 0 Num Gas Bombs: 0 Serial #:
Laboratory Name: Laboratory Location:
Recovery Comments:

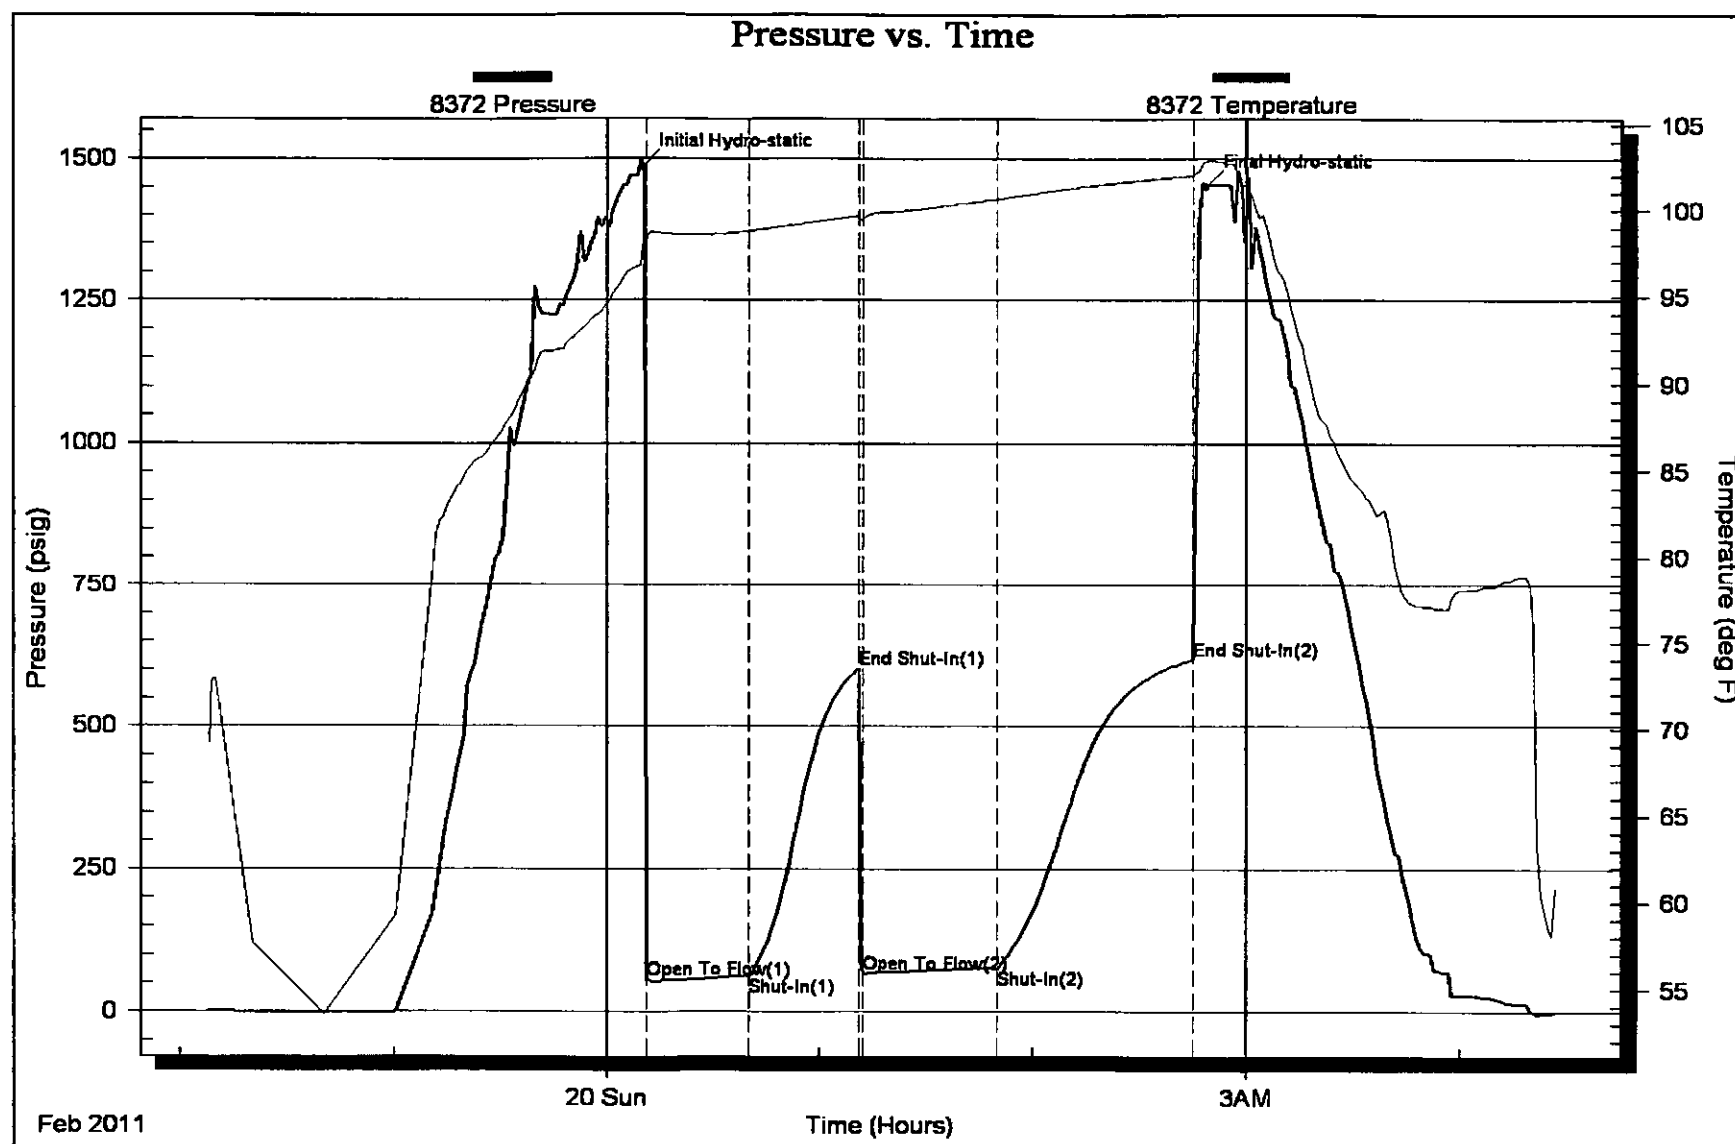



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

Am Warrior

Link 2-13

PO Box 399
Garden City, Ks
67846

ATTN: Jim Musgrove

13-19-10/Rice

Job Ticket: 41784

DST#: 2

Test Start: 2011.02.20 @ 22:04:58

GENERAL INFORMATION:

Formation: **Arbuckle**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 23:53:57

Time Test Ended: 06:41:27

Test Type: Conventional Bottom Hole

Tester: Brian Fairbank

Unit No: 41

Interval: 3215.00 ft (KB) To 3279.00 ft (KB) (TVD)

Total Depth: 3279.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition:

Reference Elevations: 1755.00 ft (KB)

1747.00 ft (CF)

KB to GR/CF: 8.00 ft

Serial #: 8372

Inside

Press@RunDepth: 699.89 psig @ 3224.00 ft (KB)

Start Date: 2011.02.20

End Date:

2011.02.21

Capacity: 8000.00 psig

Last Calib.: 2011.02.21

Start Time: 22:04:58

End Time:


06:41:27

Time On Btm: 2011.02.20 @ 23:52:57

Time Off Btm: 2011.02.21 @ 02:13:57

TEST COMMENT: IFP - BOB 1 1/2 min
ISI - 1/4" blow back
FFP - BOB 1 1/2 min
FSI - sur blow back - died 17 min

Pressure vs. Time

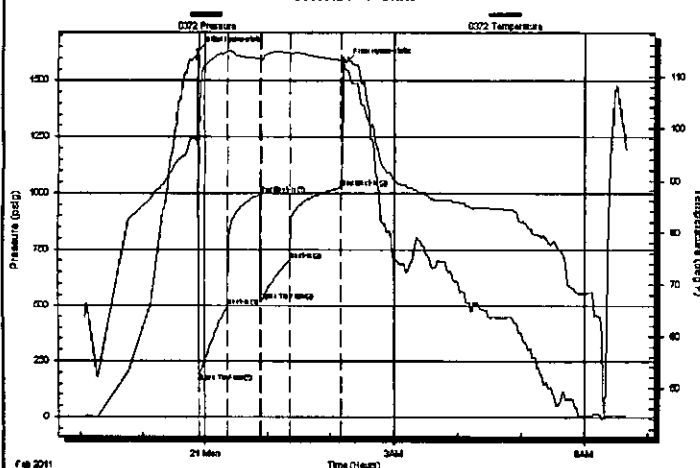

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1634.56	98.16	Initial Hydro-static
1	158.32	98.21	Open To Flow (1)
29	495.76	114.75	Shut-In(1)
60	995.47	113.45	End Shut-In(1)
60	524.01	113.19	Open To Flow (2)
89	699.89	114.57	Shut-In(2)
137	1023.73	113.05	End Shut-In(2)
141	1583.83	111.24	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
20.00	MW 90%W, 10%M	0.28
475.00	GM & WCO 30%G, 50%O, 15%W, 5%M	6.66
695.00	GOCM 40%G, 15%O, 45%M	9.75
590.00	FREE OIL 95%O, 5%M	8.28
0.00	60' GIP	0.00

Gas Rates

	Choke (Inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Am Warrior

Link 2-13

PO Box 399
Garden City, Ks
67846

13-19-10/Rice

Job Ticket: 41784

DST#: 2

ATTN: Jim Musgrove

Test Start: 2011.02.20 @ 22:04:58

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

45 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

27000 ppm

Viscosity: 49.00 sec/qt

Cushion Volume:

bbl

Water Loss: 9.58 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 4900.00 ppm

Filter Cake: inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
20.00	MW 90%W, 10%M	0.281
475.00	GM & WCO 30%G, 50%O, 15%W, 5%M	6.663
695.00	GOCM 40%G, 15%O, 45%M	9.749
590.00	FREE OIL 95%O, 5%M	8.276
0.00	60' GIP	0.000

Total Length: 1780.00 ft

Total Volume: 24.969 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

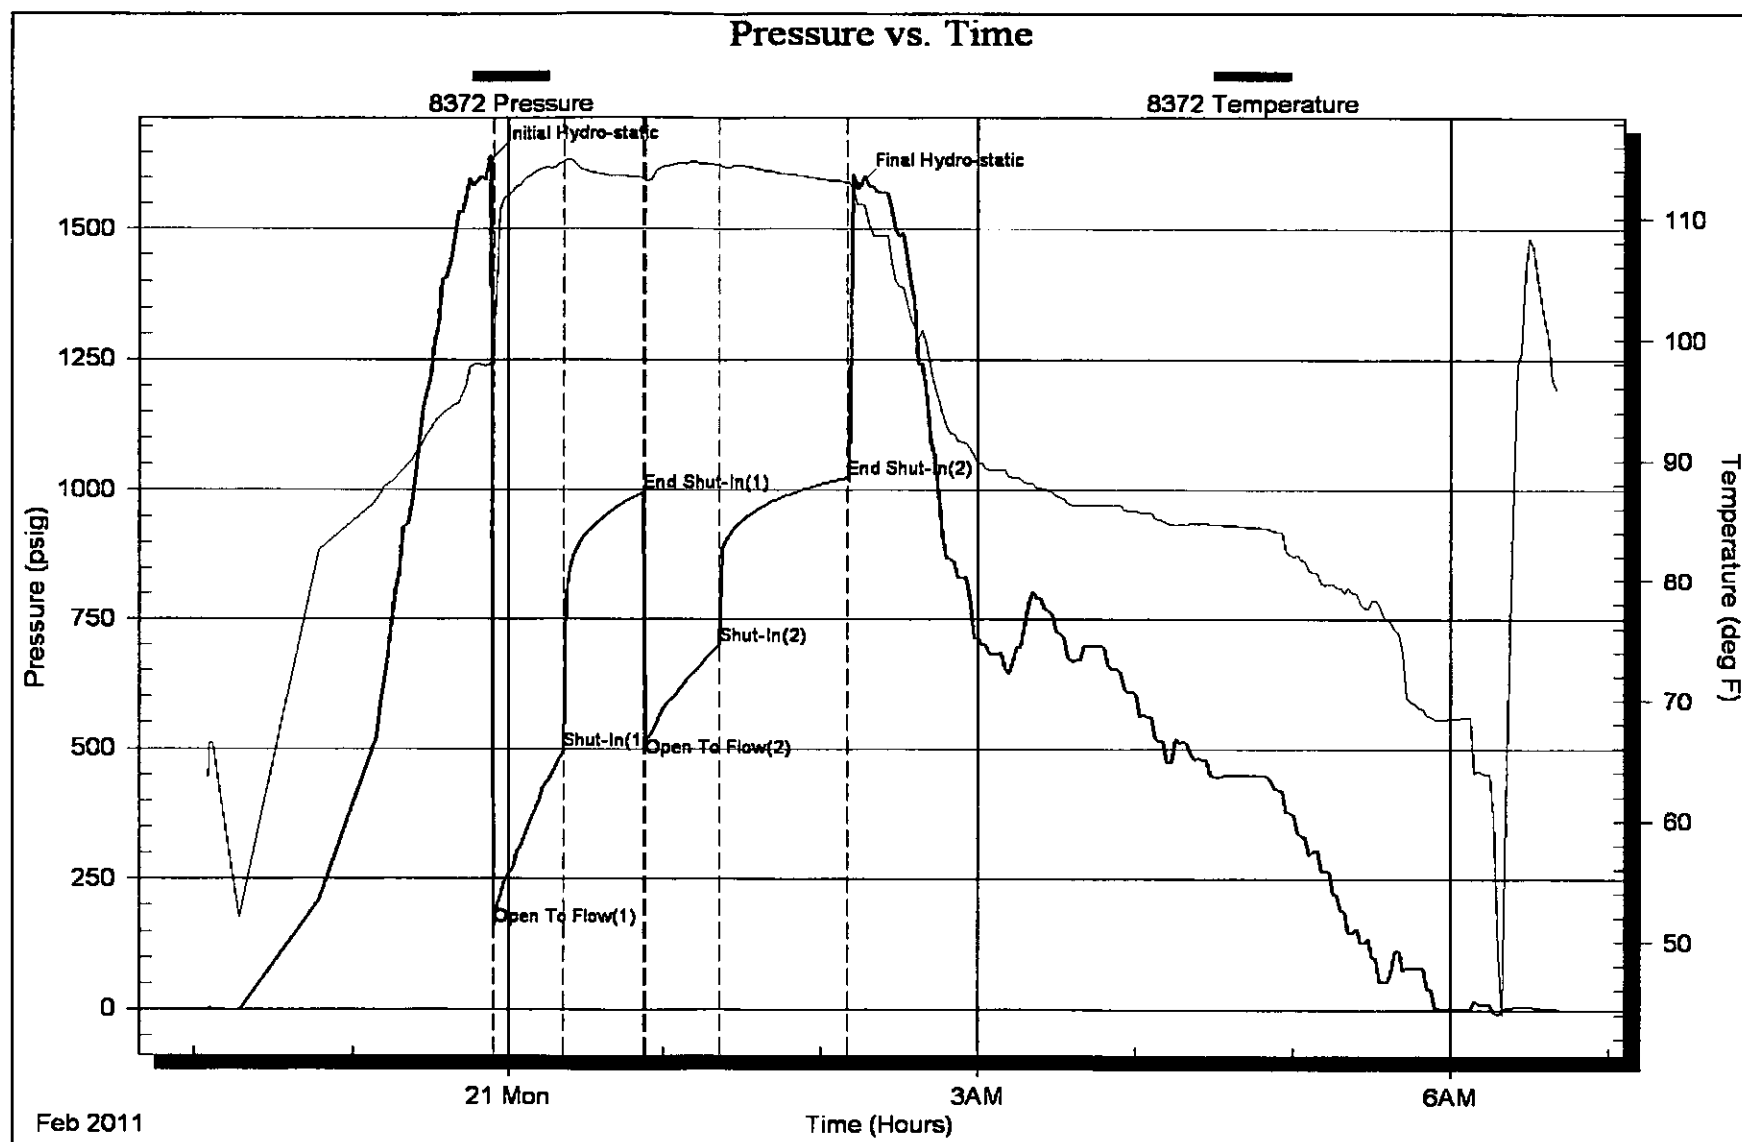



DRILL STEM TEST REPORT

Prepared For: **American Warrior Inc.**

PO Box 399
Garden City, KS 67846

ATTN: Jim Musgrove

13-19-10 Rice KS

Link 2-13

Start Date: 2011.02.19 @ 22:08:09


End Date: 2011.02.20 @ 04:26:38

Job Ticket #: 41783 DST #: 1

KCC
MAR 29 2011
CONFIDENTIAL

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620

RECEIVED
MAR 29 2011
KCC WICHITA



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

American Warrior Inc.

Link 2-13

PO Box 399
Garden City, KS 67846

13-19-10 Rice KS

Job Ticket: 41783

DST#: 1

ATTN: Jim Musgrove

Test Start: 2011.02.19 @ 22:08:09

GENERAL INFORMATION:

Formation: LKC "D-G"

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 00:11:08

Time Test Ended: 04:26:38

Test Type: Conventional Bottom Hole

Tester: Brian Fairbank

Unit No: 41

Interval: 2972.00 ft (KB) To 3051.00 ft (KB) (TVD)

Total Depth: 3051.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition:

Reference Elevations: 1755.00 ft (KB)

1747.00 ft (CF)

KB to GR/CF: 8.00 ft

Serial #: 8372

Inside

Press@RunDepth: 76.72 psig @ 2979.00 ft (KB)

Start Date: 2011.02.19

End Date:

2011.02.20

Start Time: 22:08:09

End Time:

04:26:38

Capacity: 8000.00 psig


Last Calib.: 2011.02.20

Time On Btm: 2011.02.20 @ 00:10:08

Time Off Btm: 2011.02.20 @ 02:48:38

TEST COMMENT: IFP - BOB 10 min
ISI - no blow back
FFP - BOB 7 min
FSI - no blow back

Pressure vs. Time

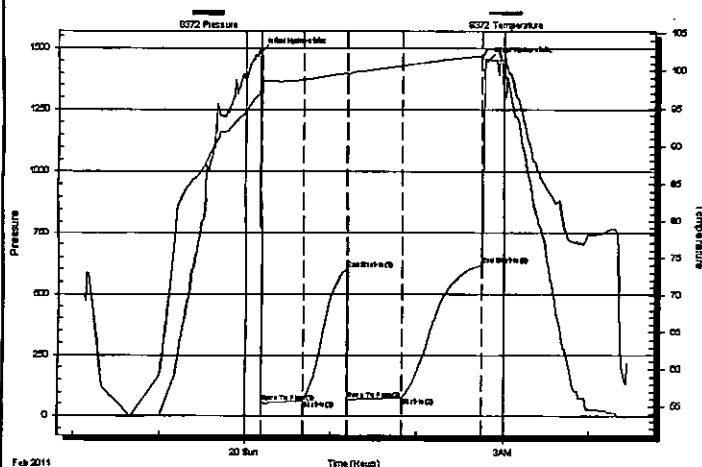

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1485.09	97.94	Initial Hydro-static
1	55.94	98.23	Open To Flow (1)
30	62.00	98.78	Shut-In(1)
61	602.65	99.69	End Shut-In(1)
62	65.91	99.58	Open To Flow (2)
100	76.72	100.67	Shut-In(2)
155	618.66	102.04	End Shut-In(2)
159	1449.66	102.85	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
70.00	MUD 100%	0.98
0.00	260' GIP	0.00

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

TOOL DIAGRAM

American Warrior Inc.

Link 2-13

PO Box 399
Garden City, KS 67846

13-19-10 Rice KS

Job Ticket: 41783

DST#: 1

ATTN: Jim Musgrove

Test Start: 2011.02.19 @ 22:08:09


Tool Information

Drill Pipe:	Length: 2983.00 ft	Diameter: 3.80 inches	Volume: 41.84 bbl	Tool Weight:	2500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	25000.00 lb
Drill Collar:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight to Pull Loose:	54000.00 lb
			Total Volume: 41.84 bbl	Tool Chased	3.00 ft
Drill Pipe Above KB:	31.00 ft			String Weight: Initial	38000.00 lb
Depth to Top Packer:	2972.00 ft			Final	40000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	79.00 ft				
Tool Length:	99.00 ft				
Number of Packers:	2	Diameter: 6.75 inches			

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Shut In Tool	5.00			2957.00	
Hydraulic tool	5.00			2962.00	
Packer	5.00			2967.00	20.00 Bottom Of Top Packer
Packer	5.00			2972.00	
Stubb	1.00			2973.00	
Perforations	5.00			2978.00	
Change Over Sub	1.00			2979.00	
Recorder	0.00	8372	Inside	2979.00	
Recorder	0.00	8365	Outside	2979.00	
Blank Spacing	63.00			3042.00	
Change Over Sub	1.00			3043.00	
Perforations	5.00			3048.00	
Bullnose	3.00			3051.00	79.00 Bottom Packers & Anchor

Total Tool Length: 99.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior Inc.

Link 2-13

PO Box 399
Garden City, KS 67846

13-19-10 Rice KS

Job Ticket: 41783

DST#: 1

ATTN: Jim Musgrove

Test Start: 2011.02.19 @ 22:08:09

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 46.00 sec/qt

Cushion Volume:

bbl

Water Loss: 8.77 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 3600.00 ppm

Filter Cake: inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
70.00	MUD 100%	0.982
0.00	260' GIP	0.000

Total Length: 70.00 ft

Total Volume: 0.982 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

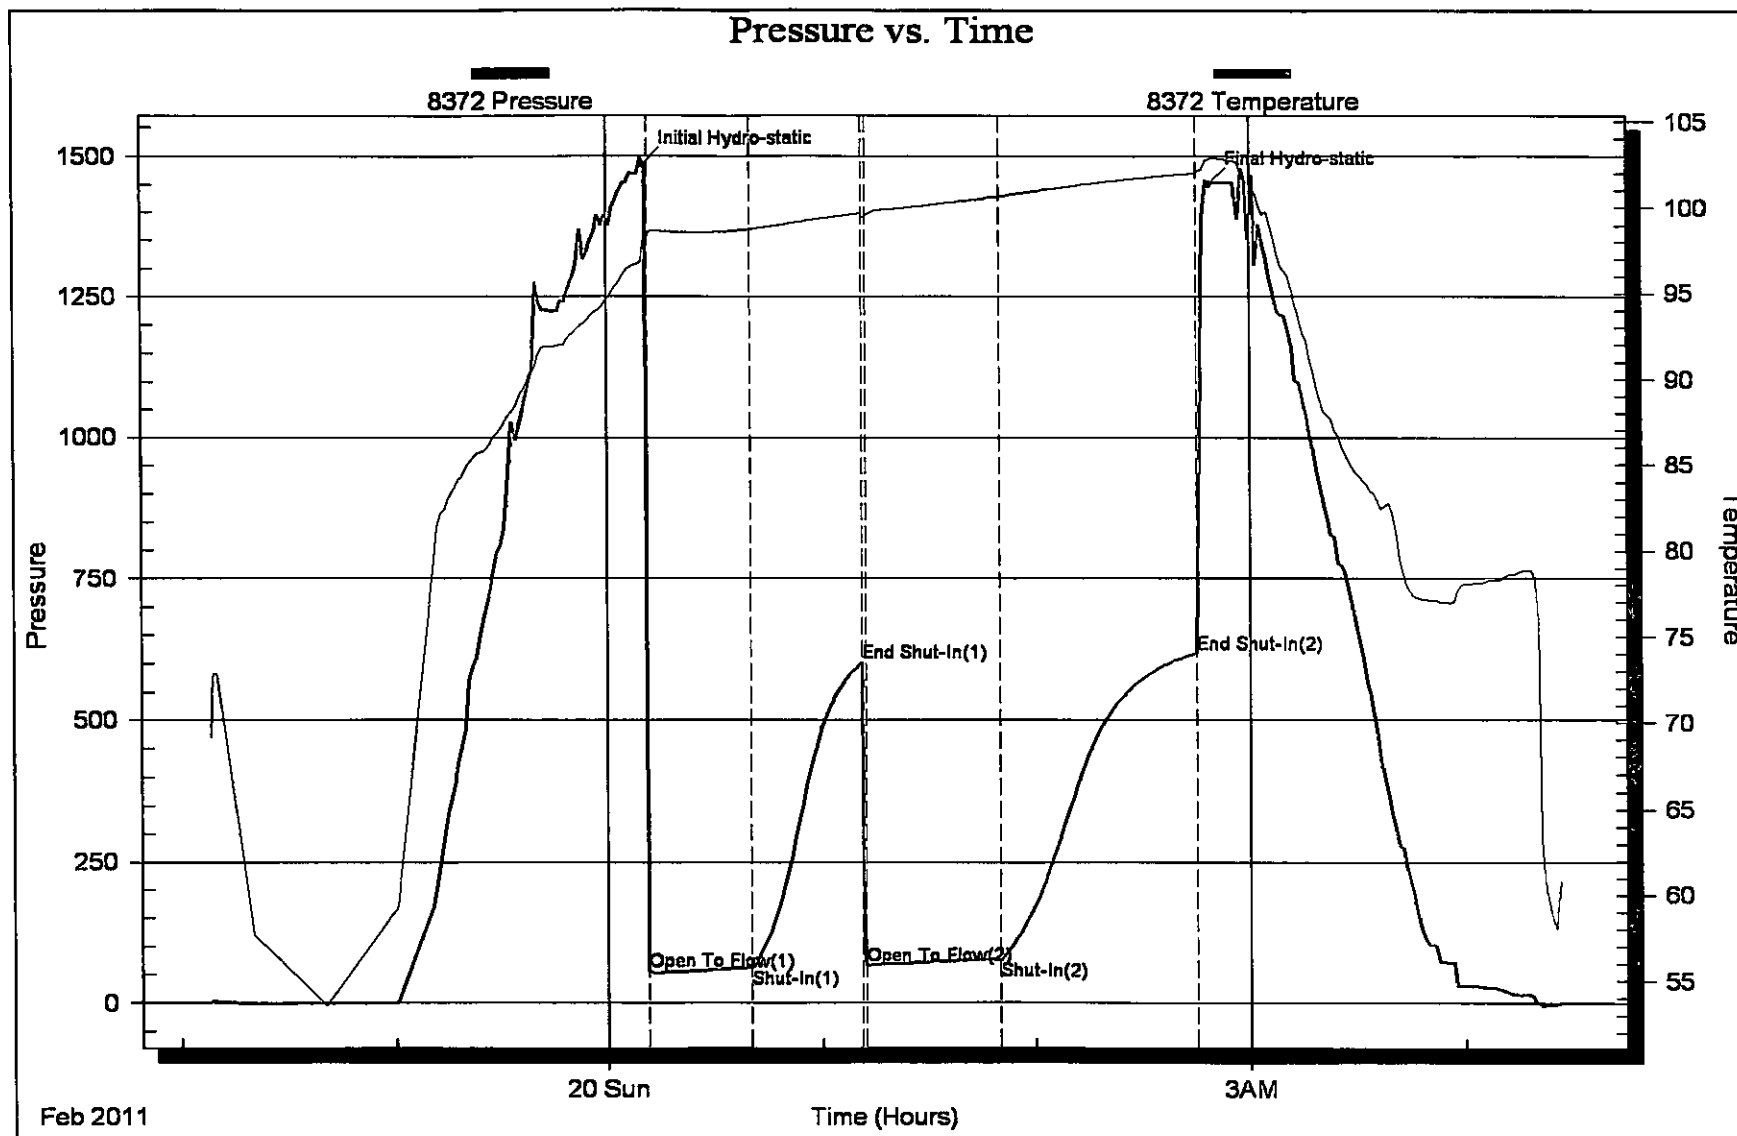



TRILOBITE TESTING INC.

P.O. Box 1733 • Hays, Kansas 67601

Test Ticket

NO. 041783 5402

Well Name & No. Link 2-13 Test No. 1 Date 2-19-11
 Company Am Warrior Elevation 1755 KB 1747 GL
 Address PO Box 399 Garden City, KS 67846
 Co. Rep / Geo. Jim McGuire Rig Duke 8
 Location: Sec. 13 Twp. 19 Rge. 10 Co. Rice State KS

Interval Tested 2972-3051 Zone Tested LKC "O-G"
 Anchor Length 79 Drill Pipe Run 2983 Mud Wt. 9.1
 Top Packer Depth 2967 Drill Collars Run — Vis 46
 Bottom Packer Depth 2972 Wt. Pipe Run — WL 8.8
 Total Depth 3051 Chlorides 3600 ppm System LCM

Blow Description IFP- BOB 10 min
ISI- no blow back
FFP- BOB 7 min
FSI- no blow back

Rec	Feet of	%gas	%oil	%water	%mud
<u>260</u>	<u>GIP</u>				
<u>70</u>	<u>mud</u>				<u>100</u>
Rec	Feet of	%gas	%oil	%water	%mud
Rec	Feet of	%gas	%oil	%water	%mud
Rec	Feet of	%gas	%oil	%water	%mud

Rec Total 70 BHT 102 Gravity 1125 API RW — @ — °F Chlorides — ppm

(A) Initial Hydrostatic 1485
 (B) First Initial Flow 56
 (C) First Final Flow 62
 (D) Initial Shut-In 603
 (E) Second Initial Flow 66
 (F) Second Final Flow 77
 (G) Final Shut-In 619
 (H) Final Hydrostatic 1450

☒ Test 1125
☐ Jars
☐ Safety Joint
☐ Circ Sub
☐ Hourly Standby 1hr 100
☒ Mileage 144 RT 180
☐ Sampler
☐ Straddle
☐ Shale Packer
☐ Extra Packer
☐ Extra Recorder
☐ Day Standby
☐ Accessibility
 Sub Total 1405


T-On Location 1818
 T-Started 2208
 T-Open 0011
 T-Pulled 0241
 T-Out 0426
 Comments
☐ Ruined Shale Packer
☐ Ruined Packer
☐ Extra Copies
 Sub Total 0
 Total 1405
 MP/DST Disc't

Initial Open 30
 Initial Shut-In 30
 Final Flow 45
 Final Shut-In 45

Approved By _____

Our Representative Brian Farber

Trilobite Testing Inc. shall not be liable for damaged of any kind of the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test, tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.



DRILL STEM TEST REPORT

Prepared For: **American Warrior Inc.**

PO Box 399
Garden City, KS 67846

ATTN: Jim Musgrove

13-19-10 Rice KS

Link 2-13

Start Date: 2011.02.20 @ 22:04:58


End Date: 2011.02.21 @ 06:41:27

Job Ticket #: 41784 DST #: 2

Trilobite Testing, Inc

PO Box 1733 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

American Warrior Inc.

PO Box 399
Garden City, KS 67846

ATTN: Jim Musgrove

Link 2-13

13-19-10 Rice KS

Job Ticket: 41784

DST#: 2

Test Start: 2011.02.20 @ 22:04:58

GENERAL INFORMATION:

Formation: **Arbuckle**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 23:53:57

Time Test Ended: 06:41:27

Test Type: Conventional Bottom Hole

Tester: Brian Fairbank

Unit No: 41

Interval: **3215.00 ft (KB) To 3279.00 ft (KB) (TVD)**

Total Depth: 3279.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition:

Reference Elevations: 1755.00 ft (KB)

1747.00 ft (CF)

KB to GR/CF: 8.00 ft

Serial #: **8372**

Inside

Press@RunDepth: 699.89 psig @ 3224.00 ft (KB)

Start Date: 2011.02.20

End Date:

2011.02.21

Start Time: 22:04:58

End Time:

06:41:27

Capacity: 8000.00 psig


Last Calib.: 2011.02.21

Time On Btm: 2011.02.20 @ 23:52:57

Time Off Btm: 2011.02.21 @ 02:13:57

TEST COMMENT: IFF - BOB 1 1/2 min
ISI - 1/4" blow back
FFP - BOB 1 1/2 min
FSI - sur blow back - died 17 min

Pressure vs. Time

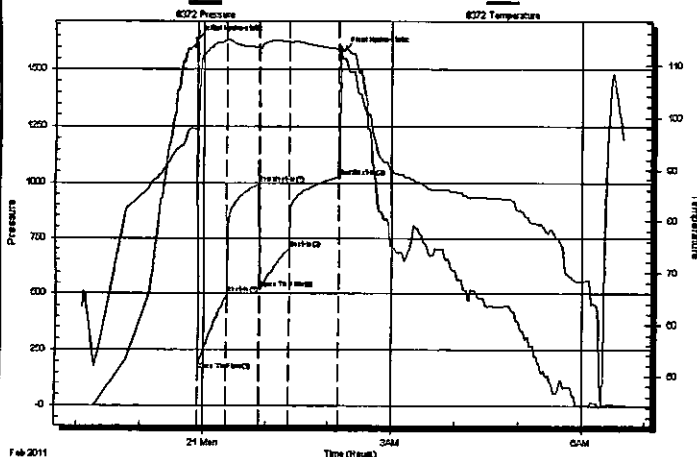

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1634.56	98.16	Initial Hydro-static
1	158.32	98.21	Open To Flow (1)
29	495.76	114.75	Shut-In (1)
60	995.47	113.45	End Shut-In (1)
60	524.01	113.19	Open To Flow (2)
89	699.89	114.57	Shut-In (2)
137	1023.73	113.05	End Shut-In (2)
141	1583.83	111.24	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
20.00	MW 90%W, 10%M	0.28
475.00	GM & WCO 30%G, 50%O, 15%W, 5%M	6.66
695.00	GOCM 40%G, 15%O, 45%M	9.75
590.00	FREE OIL 95%O, 5%M	8.28
0.00	60' GIP	0.00

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



**TRILOBITE
TESTING, INC**

DRILL STEM TEST REPORT

TOOL DIAGRAM

American Warrior Inc.

Link 2-13

PO Box 399
Garden City, KS 67846

13-19-10 Rice KS

Job Ticket: 41784

DST#: 2

ATTN: Jim Musgrove

Test Start: 2011.02.20 @ 22:04:58

Tool Information

Drill Pipe:	Length: 3202.00 ft	Diameter: 3.80 inches	Volume: 44.92 bbl	Tool Weight: 2500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 25000.00 lb
Drill Collar:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight to Pull Loose: 48000.00 lb
		Total Volume: 44.92 bbl		Tool Chased 0.00 ft
Drill Pipe Above KB:	7.00 ft			String Weight: Initial 38000.00 lb
Depth to Top Packer:	3215.00 ft			Final 45000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	64.00 ft			
Tool Length:	84.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Shut In Tool	5.00			3200.00	
Hydraulic tool	5.00			3205.00	
Packer	5.00			3210.00	20.00 Bottom Of Top Packer
Packer	5.00			3215.00	
Stubb	1.00			3216.00	
Perforations	7.00			3223.00	
Change Over Sub	1.00			3224.00	
Recorder	0.00	8372	Inside	3224.00	
Recorder	0.00	8365	Outside	3224.00	
Blank Spacing	32.00			3256.00	
Change Over Sub	1.00			3257.00	
Perforations	19.00			3276.00	
Bullnose	3.00			3279.00	64.00 Bottom Packers & Anchor

Total Tool Length: 84.00



**TRILOBITE
TESTING, INC**

DRILL STEM TEST REPORT

FLUID SUMMARY

American Warrior Inc.

Link 2-13

PO Box 399
Garden City, KS 67846

13-19-10 Rice KS

Job Ticket: 41784

DST#: 2

ATTN: Jim Musgrove

Test Start: 2011.02.20 @ 22:04:58

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

45 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

27000 ppm

Viscosity: 49.00 sec/qt

Cushion Volume:

bbl

Water Loss: 9.57 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 4900.00 ppm

Filter Cake: inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
20.00	MW 90%W, 10%M	0.281
475.00	GM & WCO 30%G, 50%O, 15%W, 5%M	6.663
695.00	GOCM 40%G, 15%O, 45%M	9.749
590.00	FREE OIL 95%O, 5%M	8.276
0.00	60' GIP	0.000

Total Length: 1780.00 ft Total Volume: 24.969 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments: RW .372 @ 49F = 27000 chlorides

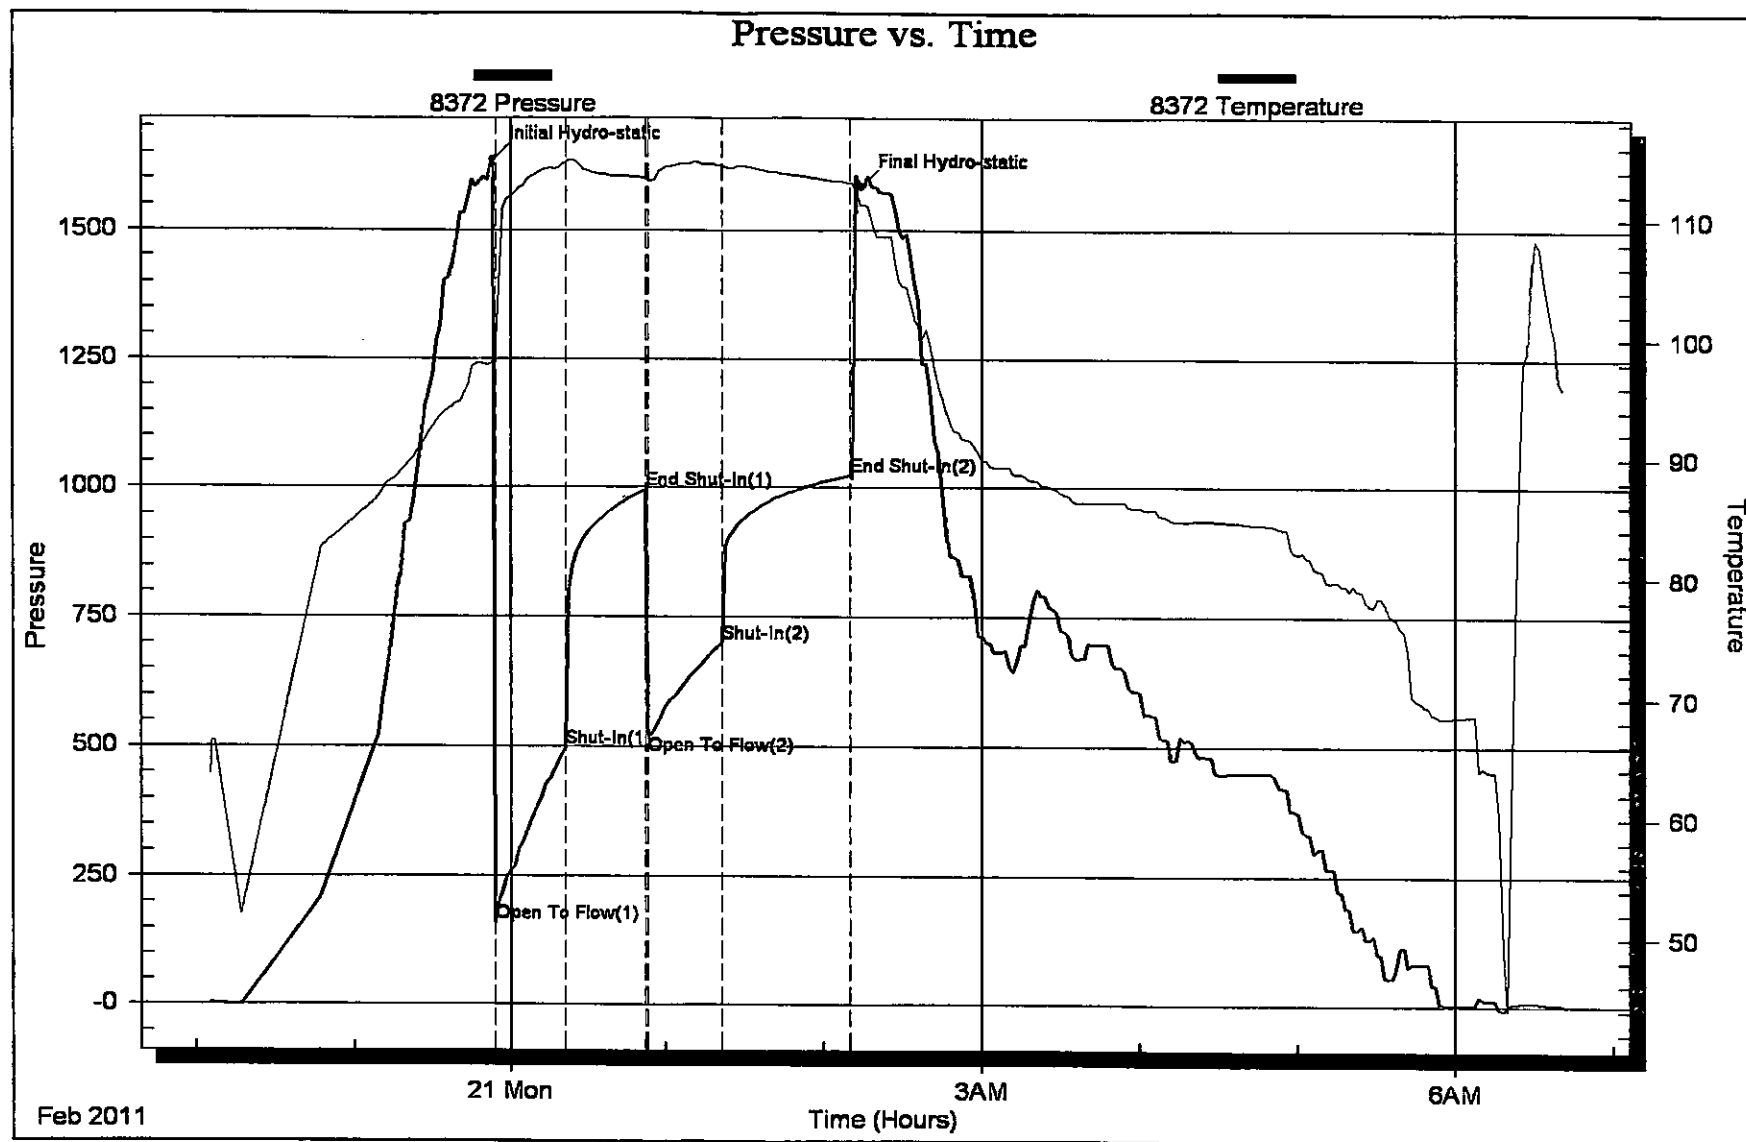



TRILOBITE TESTING INC.

P.O. Box 1733 • Hays, Kansas 67601

Test Ticket

NO. 041784

Well Name & No. Luk 2-13 Test No. 2 Date 2-20-11
 Company Am Warrior Elevation 1755 KB 1747 GL
 Address _____
 Co. Rep / Geo. Jim Musgrave Rig Duke 8
 Location: Sec. 13 Twp. 19 Rge. 10 Co. Rice State Kc

Interval Tested 3215-3279 Zone Tested ~~Arbuckle~~ Arbuckle
 Anchor Length 64 Drill Pipe Run 3202 Mud Wt. 9.2
 Top Packer Depth 3210 Drill Collars Run _____ Vis 49
 Bottom Packer Depth 3215 Wt. Pipe Run _____ WL 9.6
 Total Depth 3279 Chlorides 4900 ppm System LCM _____
 Blow Description IFFP- BOB 1 1/2 min
ISL- 1/4" blow back
FFP- BOB 1 1/2 min
FSL-

Rec	Feet of	%gas	%oil	%water	%mud
<u>60</u>	<u>GIP</u>				
<u>590</u>	<u>Free Oil</u>		<u>95%</u>		<u>5%</u>
<u>695</u>	<u>GOCM</u>	<u>40%</u>	<u>15%</u>		<u>45%</u>
<u>475</u>	<u>GMWCO</u>	<u>30%</u>	<u>50%</u>	<u>15%</u>	<u>5%</u>
<u>20</u>	<u>MW</u>		<u>90%</u>		<u>10%</u>

Rec Total 1780 BHT 113 Gravity 45 API RW .372@ 49° F Chlorides 27.000 ppm

(A) Initial Hydrostatic 1635
 (B) First Initial Flow 158
 (C) First Final Flow 496
 (D) Initial Shut-In 996
 (E) Second Initial Flow 524
 (F) Second Final Flow 700
 (G) Final Shut-In 1024
 (H) Final Hydrostatic 1584

☒ Test 1125
☐ Jars _____
☐ Safety Joint _____
☐ Circ Sub _____
☐ Hourly Standby 1/2 hr 50
☒ Mileage 144 RT 180
☐ Sampler _____
☐ Straddle _____
☐ Shale Packer _____
☐ Extra Packer _____
☐ Extra Recorder _____
☐ Day Standby _____
☐ Accessibility _____
 Sub Total 1355

T-On Location 2116
 T-Started 2204
 T-Open 2352
 T-Pulled 0207
 T-Out 0641
 Comments _____
☐ Ruined Shale Packer _____
☐ Ruined Packer _____
☐ Extra Copies _____
 Sub Total 0
 Total 1355
 MP/DST Disc't _____

Initial Open 30
 Initial Shut-In 30
 Final Flow 30
 Final Shut-In 45

Approved By _____

Our Representative

Brian Fairbank

Triobite Testing Inc. shall not be liable for damaged of any kind of the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test, tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.
