

15-009-24907

22-19s-14w

DIAMOND TESTING

P.O. Box 157

HOISINGTON, KANSAS 67544

(620) 653-7550 • (800) 542-7313

STC 21108.D221

Page 1 of 2 Pages

Company Globe Operating, Inc. Lease & Well No. Essmiller Brothers Farm No. 1
Elevation 1886KB Formation Tarkio Effective Pay -- Ft. Ticket No. J1828
Date 3-07-06 Sec. 22 Twp. 19S Range 14W County Barton State Kansas
Test Approved By Jim Musgrove Diamond Representative John C. Riedl

Formation Test No. 1 Interval Tested from 2,490 ft. to 2,600 ft. Total Depth 2,600 ft.

Packer Depth 2,485 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.

Packer Depth 2,490 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.

Depth of Selective Zone Set -- ft.

Top Recorder Depth (Inside) 2,493 ft. Recorder Number 21108 Cap. 5,000 psi

Bottom Recorder Depth (Outside) 2,597 ft. Recorder Number 11073 Cap. 4,000 psi

Below Straddle Recorder Depth -- ft. Recorder Number -- Cap. -- psi

Drilling Contractor Discovery Drilling - Rig 2 Drill Collar Length -- ft. I.D. -- in.

Mud Type Chemical Viscosity 44 Weight Pipe Length -- ft. I.D. -- in.

Weight 9.2 Water Loss 10.0 cc. Drill Pipe Length 2,470 ft. I.D. 3 1/2 in.

Chlorides 5,000 P.P.M. Test Tool Length 20 ft. Tool Size 3 1/2 - IF in.

Jars: Make Bowen Serial Number Not Run Anchor Length 110 ft. Size 4 1/2 - FH in.

Did Well Flow? No Reversed Out No Surface Choke Size 1 in. Bottom Choke Size 5/8 in.

Main Hole Size 7 7/8 in. Tool Joint Size 4 1/2 - XH in.

Blow: 1st Open: Strong blow. Off bottom of bucket in 5 mins. No blow back during shut-in.

2nd Open: Fair, 4 in., blow. No blow back during shut-in.

Recovered 230 ft. of water cut mud = 3.266000 bbls. (Grind out: 30%-water; 70%-mud)

Recovered 930 ft. of gassy water = 13.206000 bbls. (Grind out: 10%-gas; 90%-water) Chlorides: 70,000 Ppm

Recovered 1,160 ft. of TOTAL FLUID = 16.472000

Recovered -- ft. of --

Recovered -- ft. of --

Remarks --

Time Set Packer(s) 2:05 ~~PM~~ ^{A.M.} Time Started Off Bottom 4:05 ~~PM~~ ^{A.M.} Maximum Temperature 87°

Initial Hydrostatic Pressure (A) 1158 P.S.I.

Initial Flow Period Minutes 30 (B) 88 P.S.I. to (C) 430 P.S.I.

Initial Closed In Period Minutes 30 (D) 871 P.S.I.

Final Flow Period Minutes 30 (E) 428 P.S.I. to (F) 596 P.S.I.

Final Closed In Period Minutes 30 (G) 876 P.S.I.

Final Hydrostatic Pressure (H) 1143 P.S.I.

GENERAL INFORMATION

Client Information:

Company: GLOBE OPERATING INC

Contact: RICHARD STALCUP

Phone: Fax: e-mail:

Site Information:

Contact: JIM MUSGROVE

Phone: Fax: e-mail:

Well Information:

Name: ESSMILLER BROS FARM #1

Operator: GLOBE OPERATING INC

Location-Downhole: DST #1 2490 TO 2600

Location-Surface: S22/29S/14W BARTON COUNTY

Test Information:

Company: DIAMOND TESTING INC

Representative: JOHN RIEDL

Supervisor: JIM MUSGROVE

Test Type: CONVENTIONAL

Job Number: D221

Test Unit: 2

Start Date: 2006/03/06

Start Time: 11:51:00

End Date: 2006/03/07

End Time: 17:00:00

Report Date: 2006/03/07

Prepared By: JOHN RIEDL

Remarks:

Qualified By: JIM MUSGROVE

RECOVERY: 230' WCM (30% WATER 70% MUD)


930' GASSY WATER (10% GAS 90% WATER) CHLORIDES 70,000 PPM


TOTAL FLUID REC. 1160'

ESSMILLER BROS FARM #1
 Formation: TARKIO
 Job Number: D221

GLOBE OPERATING INC
 DST #1 2490 TO 2600
 Start Test Date: 2006/03/06
 Final Test Date: 2006/03/07


ESSMILLER BROS FARM #1

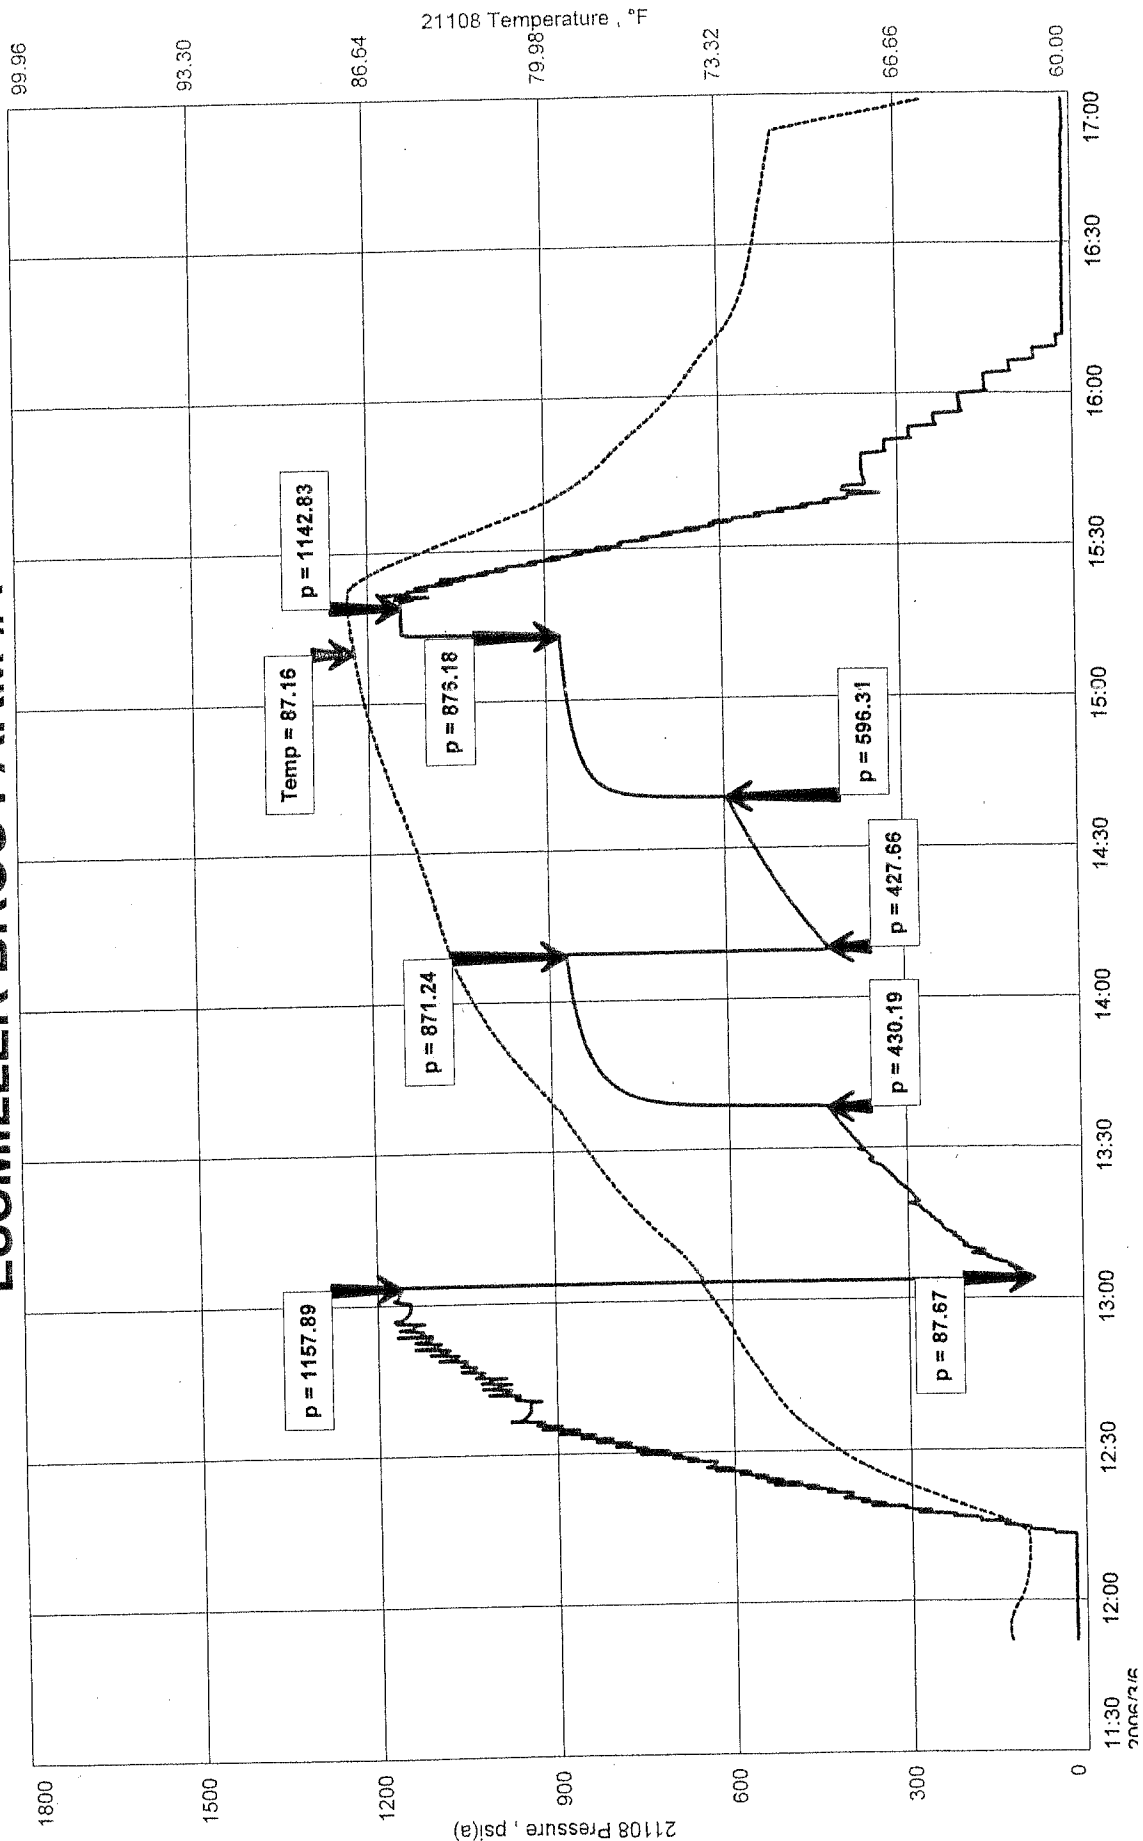

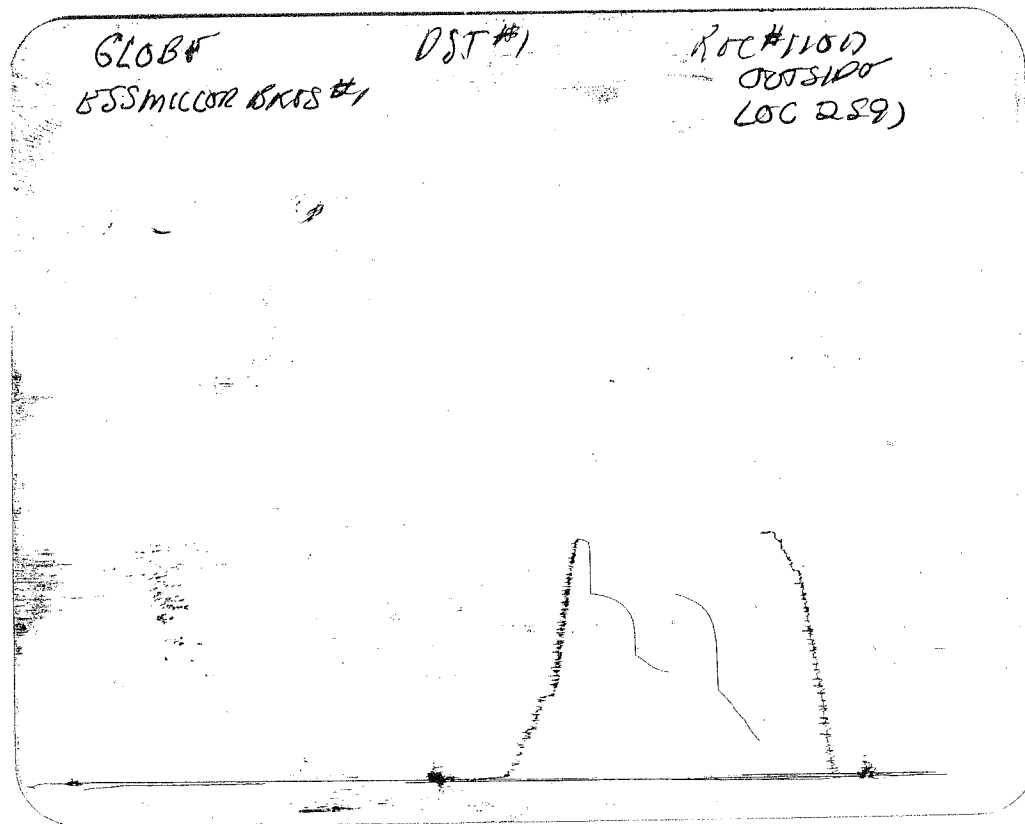

This is an actual photograph of recorder chart.

POINT	PRESSURE		Elec.
	Field Reading	Office Reading	
(A) Initial Hydrostatic Mud	1158	1158	PSI
(B) First Initial Flow Pressure.....	88	88	PSI
(C) First Final Flow Pressure	430	430	PSI
(D) Initial Closed-in Pressure	871	871	PSI
(E) Second Initial Flow Pressure.....	428	428	PSI
(F) Second Final Flow Pressure.....	596	596	PSI
(G) Final Closed-in Pressure.....	876	876	PSI
(H) Final Hydrostatic Mud.....	1143	1143	PSI



DIAMOND TESTING

P.O. Box 157

HOISINGTON, KANSAS 67544

(620) 653-7550 • (800) 542-7313

STC 21108.D222

Page 1 of 2 Pages

Company Globe Operating, Inc. Lease & Well No. Essmiller Brothers Farm No. 1
Elevation 1886KB Formation Lansing/Kansas City "A"-"F" Effective Pay -- Ft. Ticket No. J1829
Date 3-08-06 Sec. 22 Twp. 19S Range 14W County Barton State Kansas
Test Approved By Jim Musgrove Diamond Representative John C. Riedl

Formation Test No. 2 Interval Tested from 3,204 ft. to 3,272 ft. Total Depth 3,272 ft.

Packer Depth 3,199 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.

Packer Depth 3,204 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.

Depth of Selective Zone Set -- ft.

Top Recorder Depth (Inside) 3,207 ft. Recorder Number 21108 Cap. 5,000 psi

Bottom Recorder Depth (Outside) 3,269 ft. Recorder Number 11073 Cap. 4,000 psi

Below Straddle Recorder Depth -- ft. Recorder Number -- Cap. -- psi

Drilling Contractor Discovery Drilling - Rig 2 Drill Collar Length -- ft. I.D. -- in.

Mud Type Chemical Viscosity 47 Weight Pipe Length -- ft. I.D. -- in.

Weight 9.1 Water Loss 11.8 cc. Drill Pipe Length 3,184 ft. I.D. 3 1/2 in.

Chlorides 8,000 P.P.M. Test Tool Length 20 ft. Tool Size 3 1/2 - IF in.

Jars: Make Bowen Serial Number Not Run Anchor Length 68 ft. Size 4 1/2 - FH in.

Did Well Flow? No Reversed Out No Surface Choke Size 1 in. Bottom Choke Size 5/8 in.

Main Hole Size 7 7/8 in. Tool Joint Size 4 1/2 - XH in.

Blow: 1st Open: Strong blow. Off bottom of bucket in 5 mins. No blow back during shut-in.
2nd Open: Strong blow. Off bottom of bucket immediately. Decreasing to 6 ins. Gas to surface in 55 mins.
Too small to measure. No blow back during shut-in.

Recovered 10 ft. of gas cut mud = .142000 bbls. (Grind out: 10%-gas; 90%-mud)

Recovered -- ft. of --

Recovered -- ft. of --

Recovered -- ft. of --

Recovered -- ft. of --

Remarks Gas burned.

Time Set Packer(s) 6:18 AM P.M. Time Started Off Bottom 9:18 AM P.M. Maximum Temperature 99°

Initial Hydrostatic Pressure (A) 1528 P.S.I.

Initial Flow Period Minutes 30 (B) 36 P.S.I. to (C) 38 P.S.I.

Initial Closed In Period Minutes 45 (D) 894 P.S.I.

Final Flow Period Minutes 45 (E) 31 P.S.I. to (F) 32 P.S.I.

Final Closed In Period Minutes 60 (G) 765 P.S.I.

Final Hydrostatic Pressure (H) 1511 P.S.I.

GENERAL INFORMATION

Client Information:

Company: GLOBE OPERATING INC

Contact: RICHARD STALCUP

Phone: Fax: e-mail:

Site Information:

Contact: JIM MUSGROVE

Phone: Fax: e-mail:

Well Information:

Name: ESSMILLER BROS #1

Operator: GLOBE OPERATING INC

Location-Downhole: DST #2 3204 TO 3272

Location-Surface: S22/19S/14W BARTON COUNTY

Test Information:

Company: DIAMOND TESTING INC

Representative: JOHN RIEDL

Supervisor: JIM MUSGROVE

Test Type: CONVENTIONAL

Job Number: D222

Test Unit: 2

Start Date: 2006/03/08

Start Time: 17:26:00

End Date: 2006/03/08

End Time: 22:35:00

Report Date: 2006/03/08

Prepared By: JOHN RIEDL

Remarks:

Qualified By: JIM MUSGROVE


RECOVERY: 10' GCM (10%GAS 90%MUD)


GTS 55 MINUTES 2ND FLOW TSTM GAS BURNED

ESSMILLER BROS #1
 Formation: LKC "A-F"
 Job Number: D222

ESSMILLER BROS #1


GLOBE OPERATING INC
 DST #2 3204 TO 3272
 Start Test Date: 2006/03/08
 Final Test Date: 2006/03/08

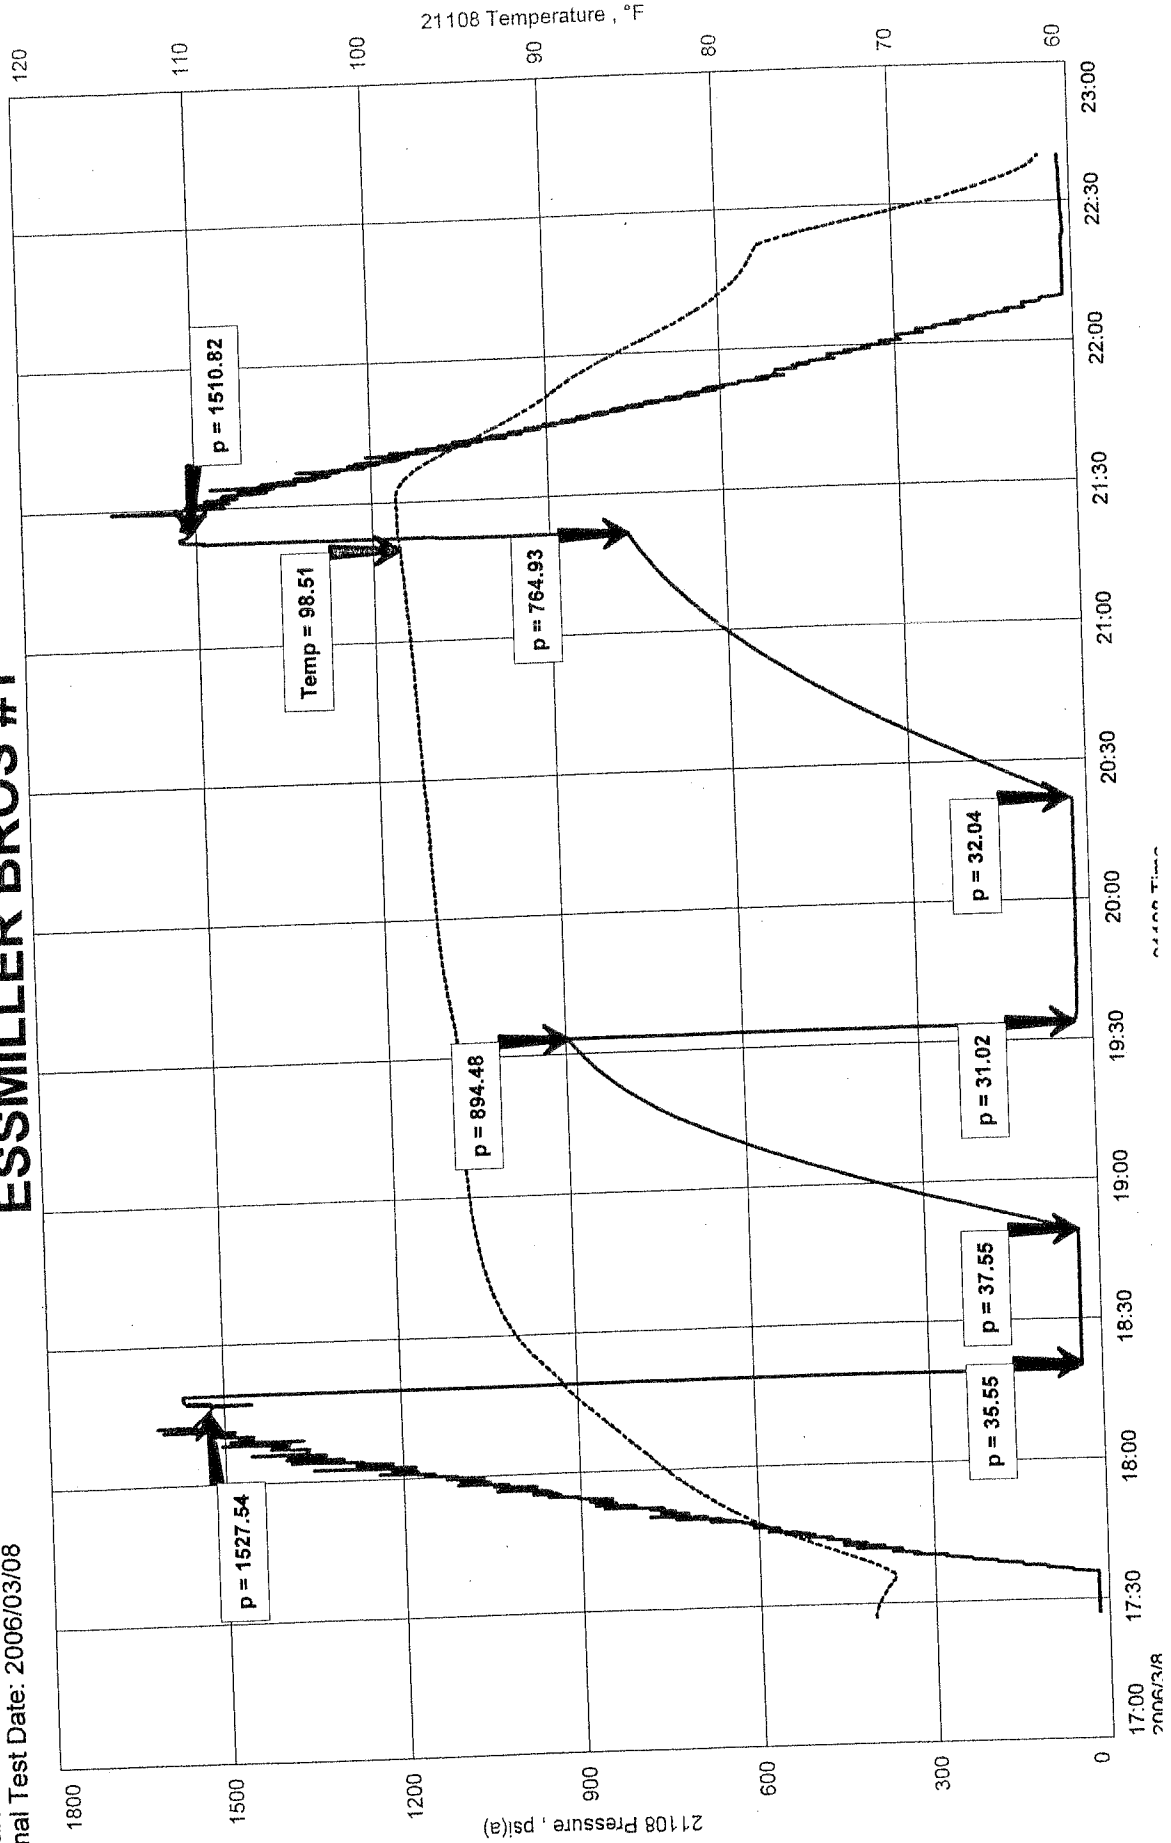

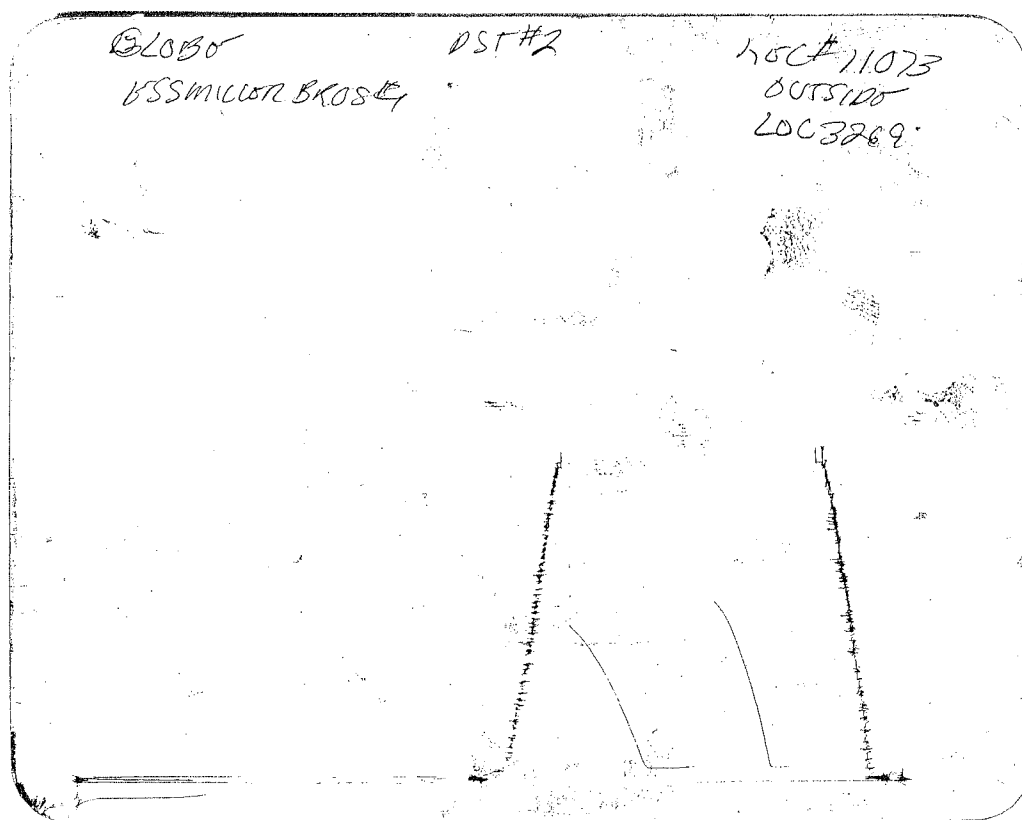

This is an actual photograph of recorder chart.

POINT	PRESSURE		Elec.
	Field Reading	Office Reading	
(A) Initial Hydrostatic Mud	1528	1528	PSI
(B) First Initial Flow Pressure.....	36	36	PSI
(C) First Final Flow Pressure	38	38	PSI
(D) Initial Closed-in Pressure	894	894	PSI
(E) Second Initial Flow Pressure	31	31	PSI
(F) Second Final Flow Pressure.....	32	32	PSI
(G) Final Closed-in Pressure.....	765	765	PSI
(H) Final Hydrostatic Mud	1511	1511	PSI



DIAMOND TESTING

P.O. Box 157

HOISINGTON, KANSAS 67544


(620) 653-7550 • (800) 542-7313

STC 21108.D223

Page 1 of 3 Pages

Company Globe Operating, Inc. Lease & Well No. Essmiller Brothers Farm No. 1
Elevation 1886KB Formation Lansing/Kansas City "H" & "I" Effective Pay -- Ft. Ticket No. J1830
Date 3-09-06 Sec. 22 Twp. 19S Range 14W County Barton State Kansas
Test Approved By Jim Musgrove Diamond Representative John C. Riedl
Formation Test No. 3 Interval Tested from 3,325 ft. to 3,390 ft. Total Depth 3,390 ft.
Packer Depth 3,320 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.
Packer Depth 3,325 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.
Depth of Selective Zone Set -- ft.
Top Recorder Depth (Inside) 3,328 ft. Recorder Number 21108 Cap. 5,000 psi
Bottom Recorder Depth (Outside) 3,387 ft. Recorder Number 11073 Cap. 4,000 psi
Below Straddle Recorder Depth -- ft. Recorder Number -- Cap. -- psi
Drilling Contractor Discovery Drilling - Rig 2 Drill Collar Length -- ft. I.D. -- in.
Mud Type Chemical Viscosity 44 Weight Pipe Length -- ft. I.D. -- in.
Weight 9.3 Water Loss 9.6 cc. Drill Pipe Length 3,305 ft. I.D. 3 1/2 in.
Chlorides 5,000 P.P.M. Test Tool Length 20 ft. Tool Size 3 1/2 - IF in.
Jars: Make Bowen Serial Number Not Run Anchor Length 65 ft. Size 4 1/2 - FH in.
Did Well Flow? No Reversed Out No Surface Choke Size 1 in. Bottom Choke Size 5/8 in.
Main Hole Size 7 7/8 in. Tool Joint Size 4 1/2 - XH in.
Blow: 1st Open: Strong blow. Off bottom of bucket in 30 secs. Gas to surface in 3 mins. No blow back during shut-in.
2nd Open: Strong blow. Gas to surface throughout. (SEE GAS VOLUME REPORT)
Recovered 50 ft. of very slightly oil cut gassy mud = .710000 bbls. (Grind out: 2%-oil; 10%-gas; 88%-mud)
Recovered 120 ft. of heavy oil & gas cut mud = 1.704000 bbls. (Grind out: 25%-gas; 25%-oil; 50%-mud) Chlorides: 5,000 Ppm
Recovered 170 ft. of TOTAL FLUID = 2.414000 bbls.
Recovered -- ft. of --
Recovered -- ft. of --
Remarks Gas sample taken. Gas burned.

Time Set Packer(s) 12:20 XXM. P.M. Time Started Off Bottom 3:20 XXM. P.M. Maximum Temperature 102°
Initial Hydrostatic Pressure (A) 1621 P.S.I.
Initial Flow Period Minutes 30 (B) 135 P.S.I. to (C) 129 P.S.I.
Initial Closed In Period Minutes 45 (D) 988 P.S.I.
Final Flow Period Minutes 45 (E) 123 P.S.I. to (F) 120 P.S.I.
Final Closed In Period Minutes 60 (G) 901 P.S.I.
Final Hydrostatic Pressure (H) 1595 P.S.I.



DIAMOND TESTING

P.O. Box 157

HOISINGTON, KANSAS 67544

(620) 653-7550 • (800) 542-7313

Page 2 of 3 Pages

GAS VOLUME REPORT

Company Globe Operating, Inc. Lease & Well No. Essmiller Brothers Farm No. 1
Date 3-9-06 Sec. 22 Twp. 19 S Rge. 14 W Location SE NE NW County Barton State KS
Drilling Contractor Discovery Drilling - Rig 2 Formation Lansing/Kansas City "H" & "I" DST No. 3
Remarks: 1st Open: Gas to surface in 3 mins. Sample taken. Gas did burn.

INITIAL FLOW

Open Tool: 12:20 p.m.

Time O'Clock	Orifice Size	Gauge	MCF/D
12:30 p.m.	1 in.	7.5 psi	400,000
12:40 p.m.	1 in.	7.5 psi	400,000
12:50 p.m.	1 in.	7.5 psi	400,000

FINAL FLOW


Open Tool: 1:35 p.m.


Time O'Clock	Orifice Size	Gauge	MCF/D
1:40 p.m.	1 in.	7.5 psi	400,000
1:50 p.m.	1 in.	7.5 psi	400,000
2:00 p.m.	1 in.	7.5 psi	400,000
2:10 p.m.	1 in.	7.0 psi	385,000
2:20 p.m.	1 in.	6.5 psi	369,000

ESSMILLER BROS #1 DST#3
Formation: LKC "H+I"
Job Number: D223

GLOBE OPERATING INC
DST #3 3325 TO 3390
Start Test Date: 2006/03/09
Final Test Date: 2006/03/09


ESSMILLER BROS #1 DST#3

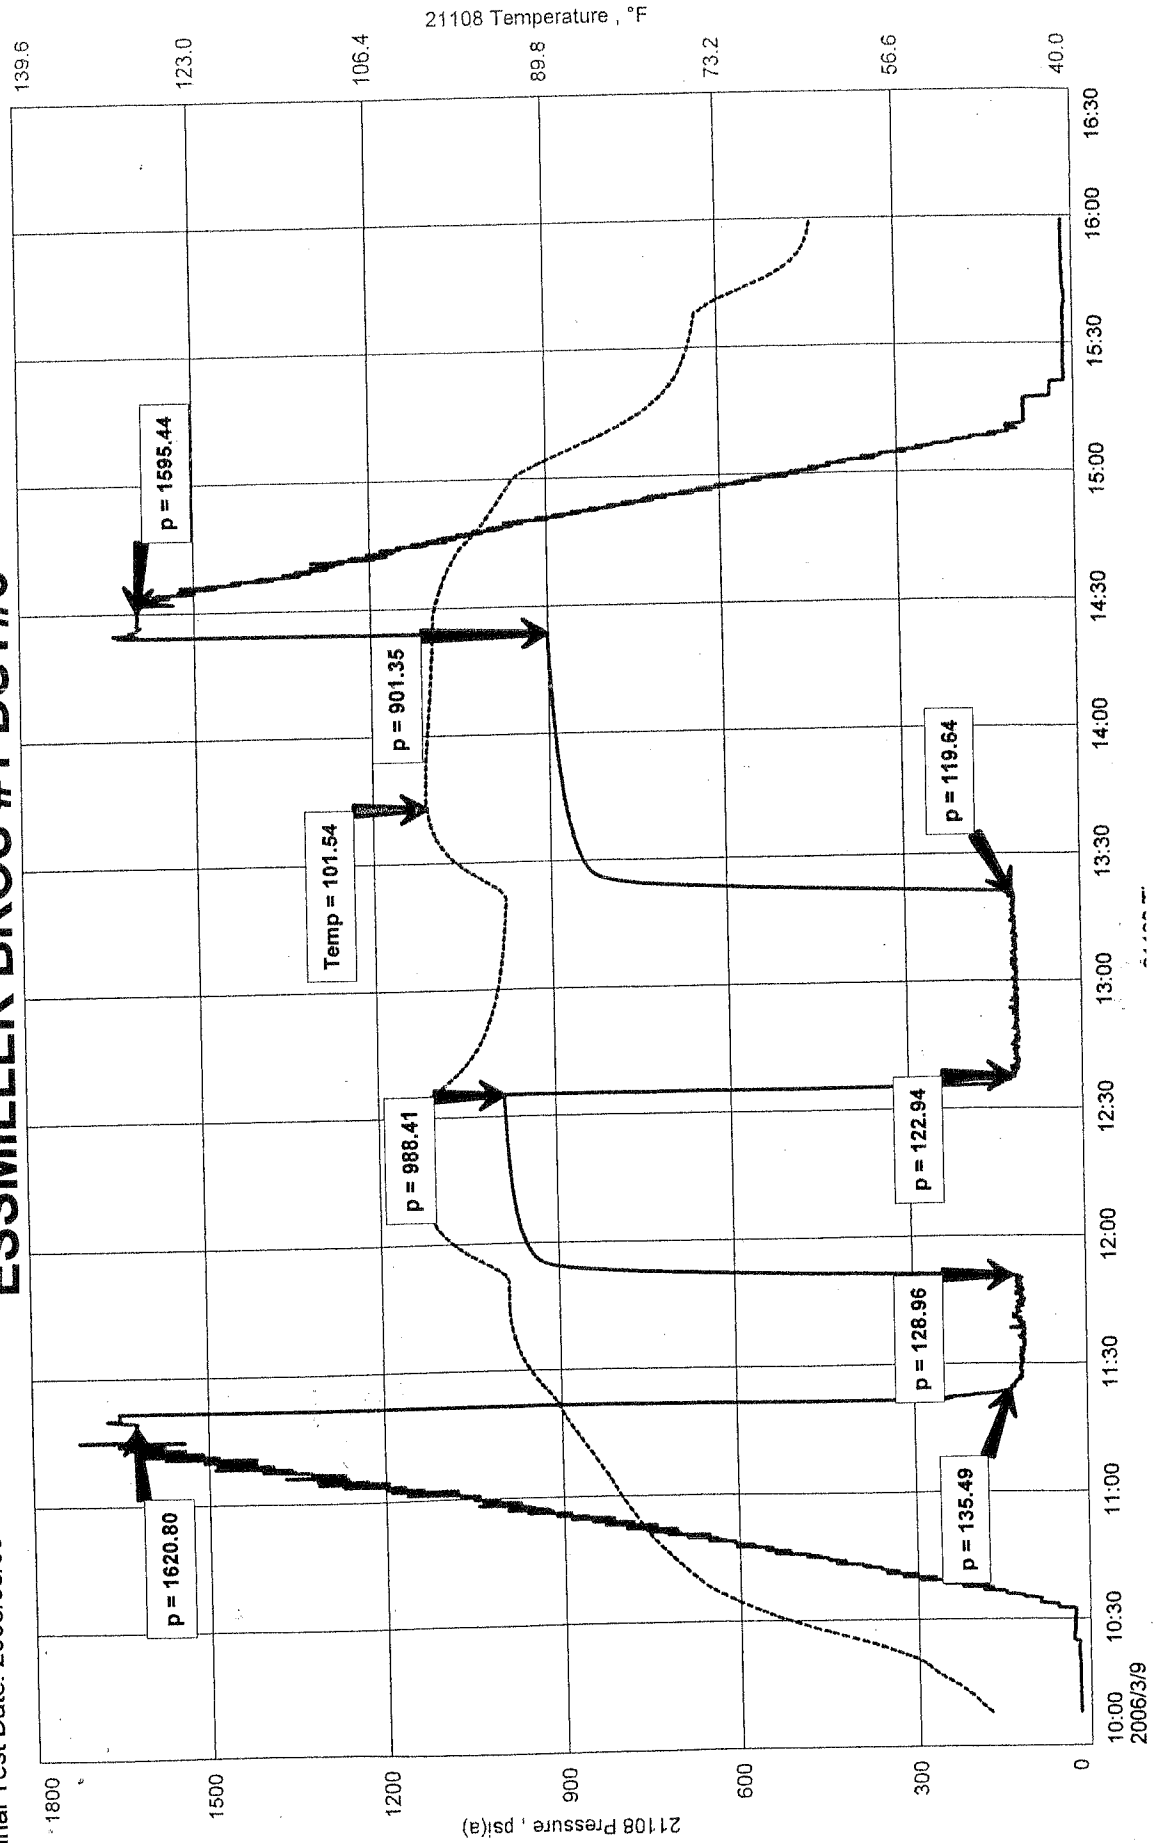

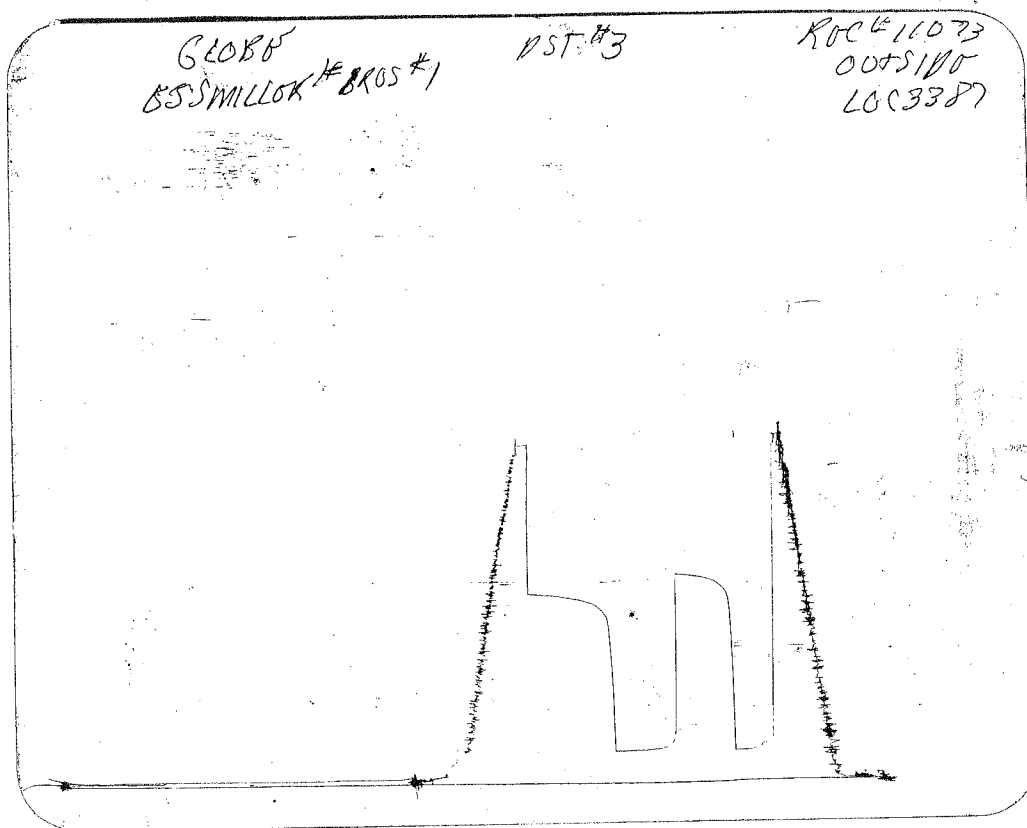

This is an actual photograph of recorder chart.

POINT	PRESSURE Elec.	
	Field Reading	Office Reading
(A) Initial Hydrostatic Mud	1621	1621
(B) First Initial Flow Pressure.....	135	135
(C) First Final Flow Pressure	129	129
(D) Initial Closed-in Pressure	988	988
(E) Second Initial Flow Pressure.....	123	123
(F) Second Final Flow Pressure.....	120	120
(G) Final Closed-in Pressure.....	901	901
(H) Final Hydrostatic Mud	1595	1595



DIAMOND TESTING

P.O. Box 157

HOISINGTON, KANSAS 67544

(620) 653-7550 • (800) 542-7313

STC 21108.D224

Page 1 of 2 Pages

Company Globe Operating, Inc. Lease & Well No. Essmiller Brothers Farm No. 1
Elevation 1886KB Formation Lansing/Kansas City "K" - "L" Effective Pay -- Ft. Ticket No. J1831
Date 3-10-06 Sec. 22 Twp. 19S Range 14W County Barton State Kansas
Test Approved By Jim Musgrove Diamond Representative John C. Riedl
Formation Test No. 4 Interval Tested from 3,381 ft. to 3,426 ft. Total Depth 3,426 ft.
Packer Depth 3,376 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.
Packer Depth 3,381 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.
Depth of Selective Zone Set -- ft.
Top Recorder Depth (Inside) 3,384 ft. Recorder Number 21108 Cap. 5,000 psi
Bottom Recorder Depth (Outside) 3,423 ft. Recorder Number 11073 Cap. 4,000 psi
Below Straddle Recorder Depth -- ft. Recorder Number -- Cap. -- psi
Drilling Contractor Discovery Drilling - Rig 2 Drill Collar Length -- ft. I.D. -- in.
Mud Type Chemical Viscosity 44 Weight Pipe Length -- ft. I.D. -- in.
Weight 9.3 Water Loss 9.6 cc. Drill Pipe Length 3,361 ft. I.D. 3 1/2 in.
Chlorides 5,000 P.P.M. Test Tool Length 20 ft. Tool Size 3 1/2 - IF in.
Jars: Make Bowen Serial Number Not Run Anchor Length 45 ft. Size 4 1/2 - FH in.
Did Well Flow? No Reversed Out No Surface Choke Size 1 in. Bottom Choke Size 5/8 in.
Main Hole Size 7 7/8 in. Tool Joint Size 4 1/2 - XH in.

Blow: 1st Open: Weak blow. Dead in 2 mins.
2nd Open: No blow. Flushed tool & received short surge.

Recovered 5 ft. of drilling mud = .071000 bbls.

Recovered -- ft. of --

Recovered -- ft. of --

Recovered -- ft. of --

Recovered -- ft. of --

Remarks --

Time Set Packer(s) 2:00 ~~P.M.~~ A.M. Time Started Off Bottom 3:20 ~~P.M.~~ A.M. Maximum Temperature 90°
Initial Hydrostatic Pressure (A) 1633 P.S.I.
Initial Flow Period Minutes 20 (B) 31 P.S.I. to (C) 32 P.S.I.
Initial Closed In Period Minutes 20 (D) 293 P.S.I.
Final Flow Period Minutes 20 (E) 30 P.S.I. to (F) 33 P.S.I.
Final Closed In Period Minutes 20 (G) 211 P.S.I.
Final Hydrostatic Pressure (H) 1620 P.S.I.

GENERAL INFORMATION

Client Information:

Company: GLOBE OPERATING INC

Contact: RICHARD STALCUP

Phone: Fax: e-mail:

Site Information:

Contact: JIM MUSGROVE

Phone: Fax: e-mail:

Well Information:

Name: ESSMILLER BROS #1

Operator: GLOBE OPERATING INC

Location-Downhole: DST #4 3381 TO 3426

Location-Surface: S22/17S/14W BARTON COUNTY

Test Information:

Company: DIAMOND TESTING

Representative: JOHN RIEDL

Supervisor: JIM MUSGROVE

Test Type: CONVENTIONAL

Job Number: D224

Test Unit: 2

Start Date: 2006/03/10

Start Time: 00:40:00

End Date: 2006/03/10

End Time: 04:45:00

Report Date: 2006/03/10


Prepared By: JOHN RIEDL


Remarks:

Qualified By: JIM MUSGROVE

RECOVERY: 5' DRILLING MUD


ESSMILLER BROS #1

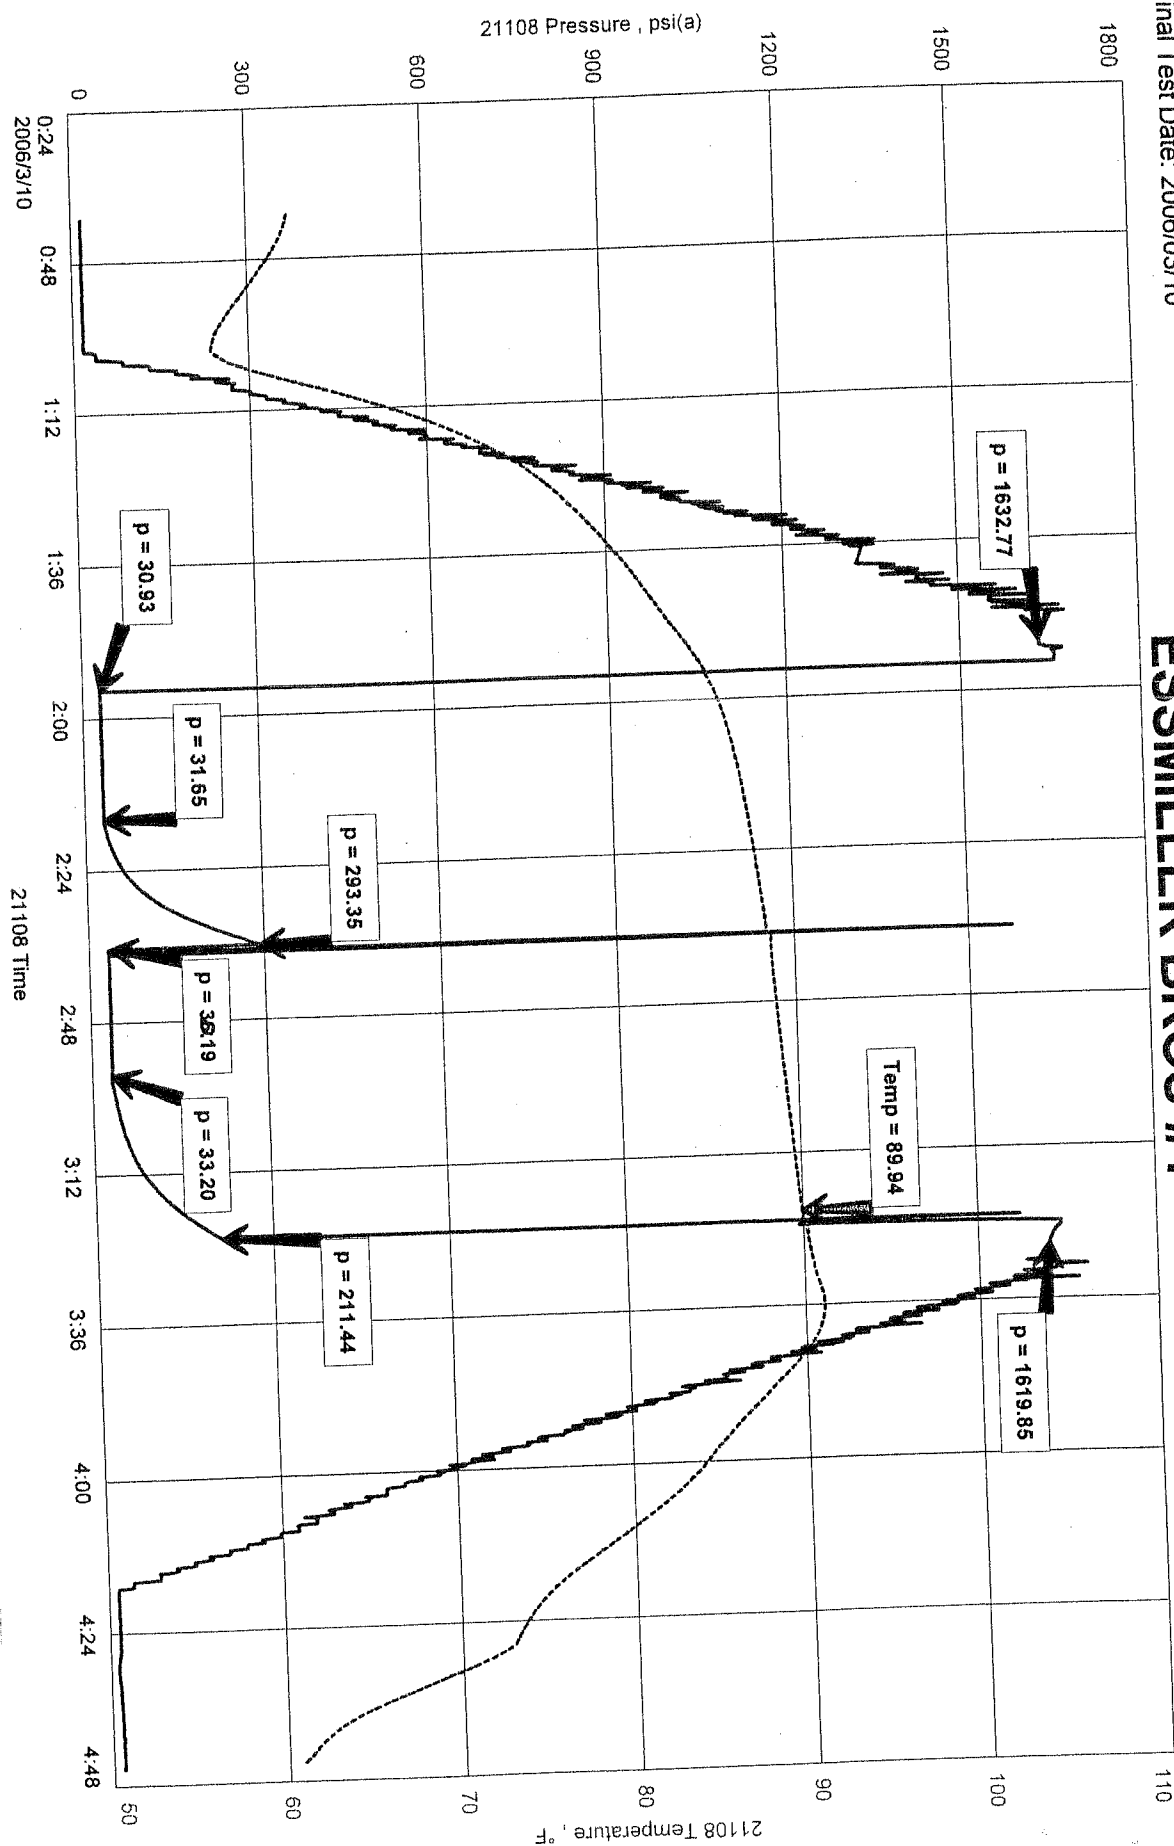

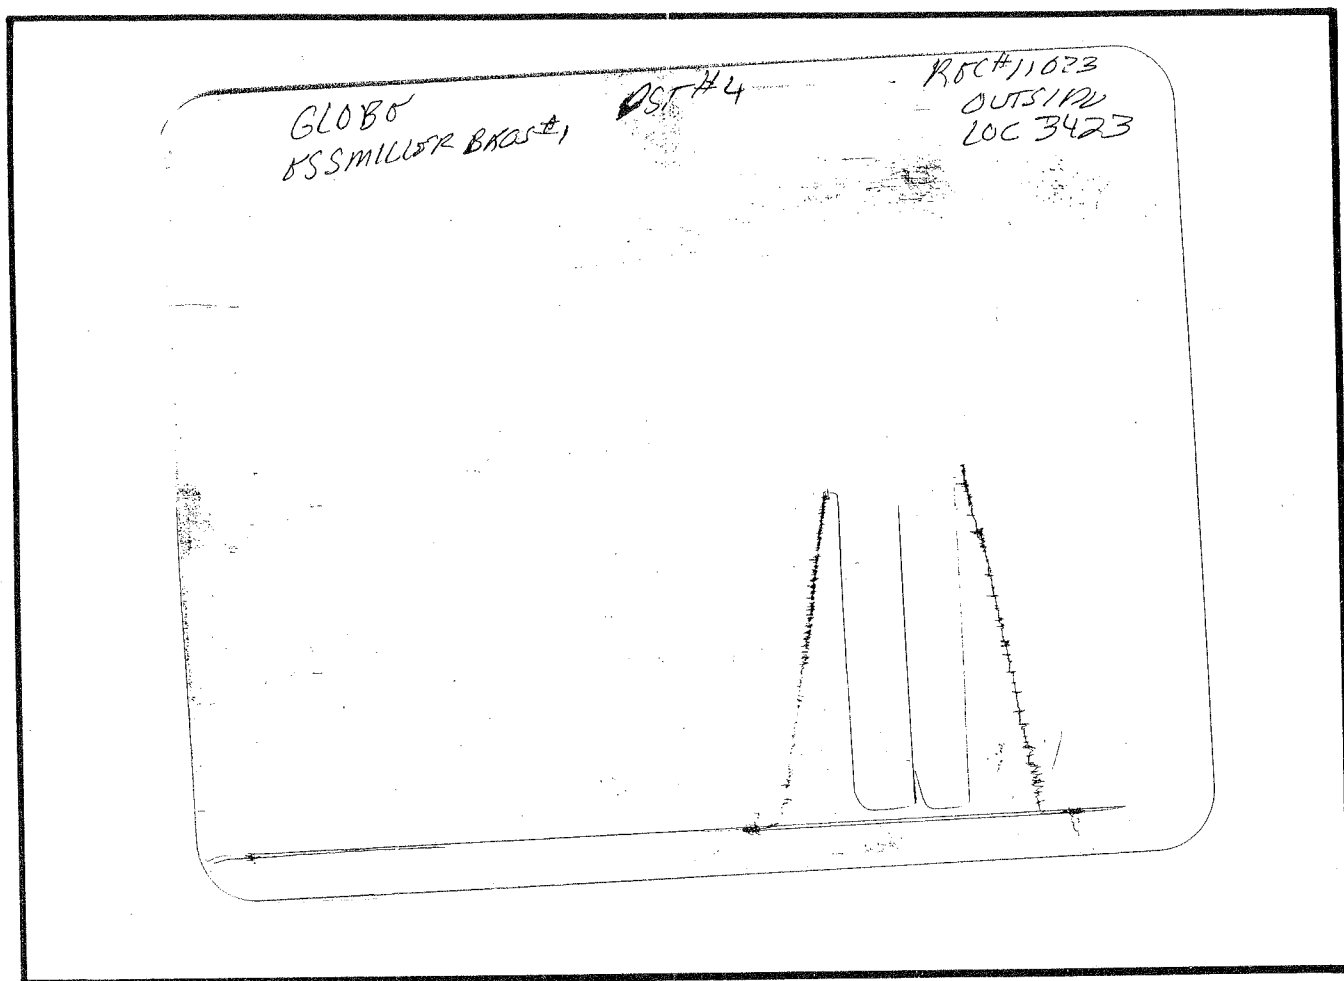

This is an actual photograph of recorder chart.

POINT	PRESSURE		Elec.
	Field Reading	Office Reading	
(A) Initial Hydrostatic Mud	1633	1633	PSI
(B) First Initial Flow Pressure	31	31	PSI
(C) First Final Flow Pressure	32	32	PSI
(D) Initial Closed-in Pressure	293	293	PSI
(E) Second Initial Flow Pressure	30	30	PSI
(F) Second Final Flow Pressure	33	33	PSI
(G) Final Closed-in Pressure	211	211	PSI
(H) Final Hydrostatic Mud	1620	1620	PSI



DIAMOND TESTING

P.O. Box 157

HOISINGTON, KANSAS 67544

(620) 653-7550 • (800) 542-7313

STC 21108.D225

Page 1 of 2 Pages

Company Globe Operating, Inc. Lease & Well No. Essmiller Brothers Farm No. 1
Elevation 1886KB Formation Conglomerate/Arbuckle Effective Pay -- Ft. Ticket No. J1832
Date 3-10-06 Sec. 22 Twp. 19S Range 14W County Barton State Kansas
Test Approved By Jim Musgrove Diamond Representative John C. Riedl
Formation Test No. 5 Interval Tested from 3,425 ft. to 3,511 ft. Total Depth 3,511 ft.
Packer Depth 3,420 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.
Packer Depth 3,425 ft. Size 6 3/4 in. Packer Depth -- ft. Size -- in.
Depth of Selective Zone Set -- ft.
Top Recorder Depth (Inside) 3,428 ft. Recorder Number 21108 Cap. 5,000 psi
Bottom Recorder Depth (Outside) 3,508 ft. Recorder Number 11073 Cap. 4,000 psi
Below Straddle Recorder Depth -- ft. Recorder Number -- Cap. -- psi
Drilling Contractor Discovery Drilling - Rig 2 Drill Collar Length -- ft. I.D. -- in.
Mud Type Chemical Viscosity 45 Weight Pipe Length -- ft. I.D. -- in.
Weight 9.1 Water Loss 11.0 cc. Drill Pipe Length 3,405 ft. I.D. 3 1/2 in.
Chlorides 5,000 P.P.M. Test Tool Length 20 ft. Tool Size 3 1/2 - IF in.
Jars: Make Bowen Serial Number Not Run Anchor Length 86 ft. Size 4 1/2 - FH in.
Did Well Flow? No Reversed Out No Surface Choke Size 1 in. Bottom Choke Size 5/8 in.
Main Hole Size 7 7/8 in. Tool Joint Size 4 1/2 - XH in.

Blow: 1st Open: Weak blow. Dead in 2 mins.
2nd Open: No blow. Flushed tool & received a weak surge.

Recovered 15 ft. of drilling mud = .213000 bbls.

Recovered -- ft. of --

Recovered -- ft. of --

Recovered -- ft. of --

Recovered -- ft. of --

Remarks --

Time Set Packer(s) 6:50 ~~AM~~ P.M. Time Started Off Bottom 8:50 ~~AM~~ P.M. Maximum Temperature 94°

Initial Hydrostatic Pressure (A) 1663 P.S.I.

Initial Flow Period Minutes 30 (B) 33 P.S.I. to (C) 34 P.S.I.

Initial Closed In Period Minutes 30 (D) 53 P.S.I.

Final Flow Period Minutes 30 (E) 35 P.S.I. to (F) 39 P.S.I.

Final Closed In Period Minutes 30 (G) 47 P.S.I.

Final Hydrostatic Pressure (H) 1645 P.S.I.

GENERAL INFORMATION

Client Information:

Company: GLOBE OPERATING INC
Contact: RICHARD STALCUP
Phone: Fax: e-mail:

Site Information:

Contact: JIM MUSGROVE
Phone: Fax: e-mail:

Well Information:

Name: ESSMILLER BROS #1
Operator: GLOBE OPERATING INC
Location-Downhole: DST #5 3425 TO 3511
Location-Surface: S22/17S/14W BARTON COUNTY

Test Information:

Company:	DIAMOND TESTING	
Representative:	JOHN RIEDL	
Supervisor:	JIM MUSGROVE	
Test Type:	CONVENTIONAL	Job Number: JIM D225
Test Unit:	2	
Start Date:	2006/03/10	Start Time: 17:30:00
End Date:	2006/03/10	End Time: 22:00:00
Report Date:	2006/03/10	Prepared By: JOHN RIEDL
		Qualified By: JIM MUSGROVE

Remarks:

RECOVERY:15' DRILLING MUD

GLOBE OPERATING INC
 DST #5 3425 TO 3511
 Start Test Date: 2006/03/10
 Final Test Date: 2006/03/10

ESSMILLER BROS #1

ESSMILLER BROS #1
 Formation: CONG/ARB
 Job Number: JIM D225

