

P.O. Box 138, Great Bend, Kansas 67530

Company Gilbert Stewart Operating L.L.C.
Address 1801 Broadway #450 Denver CO 80202
Lease & # DDIC #7 Sec. 22 Twp 20 Rng 12
Date 2-27-2007 County Barton Elevation 1822 G.L. 1828 K.B.
Drilling Contractor Excel Drilling Rig #10
Drill Pipe Length 3055 I.D. of Drill Pipe 3.5 Tool Joint Size 4 1/2"
Drill Collar Length 600 I.D. of Drill Collars 2.25 Tool Joint Size 4 1/2" XH
Mud Weight 9.1 Viscosity 48 Filtrate 7.6 Chlorides-Pits _____ DST _____
Top Packer Depth 3130 Bottom Packer Depth 3135 Number of Packers 2
Tested From 3135 to 3232 Total Depth 3232 Anchor Length 97
Test # 1 Formation Tested Lansing A-F Hole Size 7 7/8
Initial Blow weak Bludging Blow Bottom Bucket in 15 min
Final Blow weak Bludging Blow Bottom Bucket in 13 min Blow back on the 1st Shut-in YES

Initial Opening	50 P.S.I. to 65	P.S.I.	from	3:45 A	m to	4:15 A	m	30	minutes
Initial Shut-in	885	P.S.I.	from	4:15	m to	4:15	m	60	minutes
Final Opening	64 P.S.I. to 84	P.S.I.	from	5:15	m to	6:15	m	60	minutes
Final Shut-in	885	P.S.I.	from	6:15	m to	7:45	m	90	minutes

Total Feet Recovered 85 Recovery Chlorides — Rw. — ohms @ — Degrees
Gravity of oil — Corrected Gas to Surface in — minutes into the —
Max. Gas Gauged — MCF/day See Gas Flow Report Was a gas sample taken —
Comments —

Extra Equipment-Jars	_____	Safety Joint	_____	Circulating Sub	_____	Straddle	_____
Electronic Recorder No.	71784	Depth	3228	Extra Packer (3rd)	_____	Hook Wall	_____
Bottom Recorder No	4337	Depth	3229	Extra Packer (4th)	_____	Sampler	_____
Tool Operator	DAVID Nichols			Approved By	_____		

Ticket No. 15105


SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: GILBERT STEWART OPERATING
 Lease & Well No. DDK#7
 Test #: 1
 Date: 2-27-07
 SEC. 22
 TWP. 20
 RGE. 12

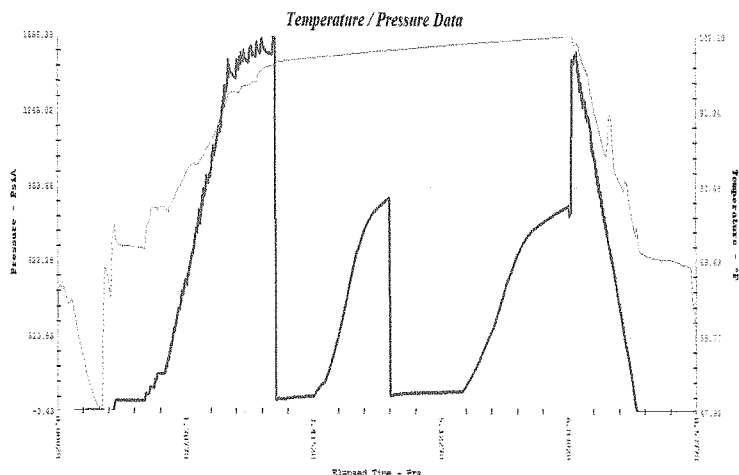

1	Initial Hydrostatic Pressure	1548
2	Initial Flow Pressure	50
3	Final Initial Flow Pressure	65
4	Initial Shut-In Pressure	885
5	Initial Final Flow Pressure	64
6	Final Flow Pressure	84
7	Final Shut-In Pressure	885
8	Final Hydrostatic Pressure	1492

Maximum Temperature 102

GENERAL INFORMATION

COMPANY NAME GILBERT STEWART OPERATING

TEST DATE 2/27/07

SECTION-TOWN-RANGE 22-20-12

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1822

COMPANY REPRESENTATIVE CLAYTON

LEASE AND WELL NUMBER DDK#7

FORMATION TESTED LANSING A-F

DRILL STEM TEST NUMBER 1

REPORT NUMBER ####

ELEVATION KELLY BUSHINGS 1828

TESTING ENGINEER DAVID NICHOLS

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3135

TEST INTERVAL (to) 3232

ANCHOR LENGTH 97

TOTAL DEPTH (ft) 3232

TOP PACKER DEPTH 3130

BOTTOM PACKER DEPTH 3135

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 3:45

TOOL OPEN (to) 4:15

DURATION (min.) 30

INITIAL SHUT-IN

TOOL CLOSED (from) 4:15

TOOL CLOSED (to) 5:15

DURATION (min.) 60

FINAL OPEN

TOOL OPEN (from) 5:15

TOOL OPEN (to) 6:15

DURATION (min.) 60

FINAL SHUT-IN

TOOL CLOSED (from) 6:15

TOOL CLOSED (to) 7:45

DURATION (min.) 90

INITIAL FLOW

WEAK BUILDING BLOW BUILT TO BOTTOM OF BUCKET IN 15 MIN

FINAL FLOW

WEAK BUILDING BLOW BUILT TO BOTTOM OF BUCKET IN 13 MIN

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GILBERT STEWART OPERATING	LEASE AND WELL NUMBER	DDK#7
TEST DATE	2/27/07	FORMATION TESTED	LANSING A-F
SECTION-TOWN-RANGE	22-20-12	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	15105
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1828
ELEVATION GROUND LEVEL	1822	TESTING ENGINEER	DAVID NICHOLS
COMPANY REPRESENTATIVE	CLAYTON		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	NO	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	30 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	3228	BOTTOM RECORDER DEPTH	3229
RECORDER NUMBER	4023	RECORDER NUMBER	3088

WELL INFORMATION

DRILLING CONTRACTOR	EXCEL#10	DRILL COLLAR LENGTH	60
DRILL PIPE LENGTH	3055	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		


COMMENTS

Recovery Sample Description

Great Bend, Kansas 67530

[illegible]

Temperature / Pressure Data

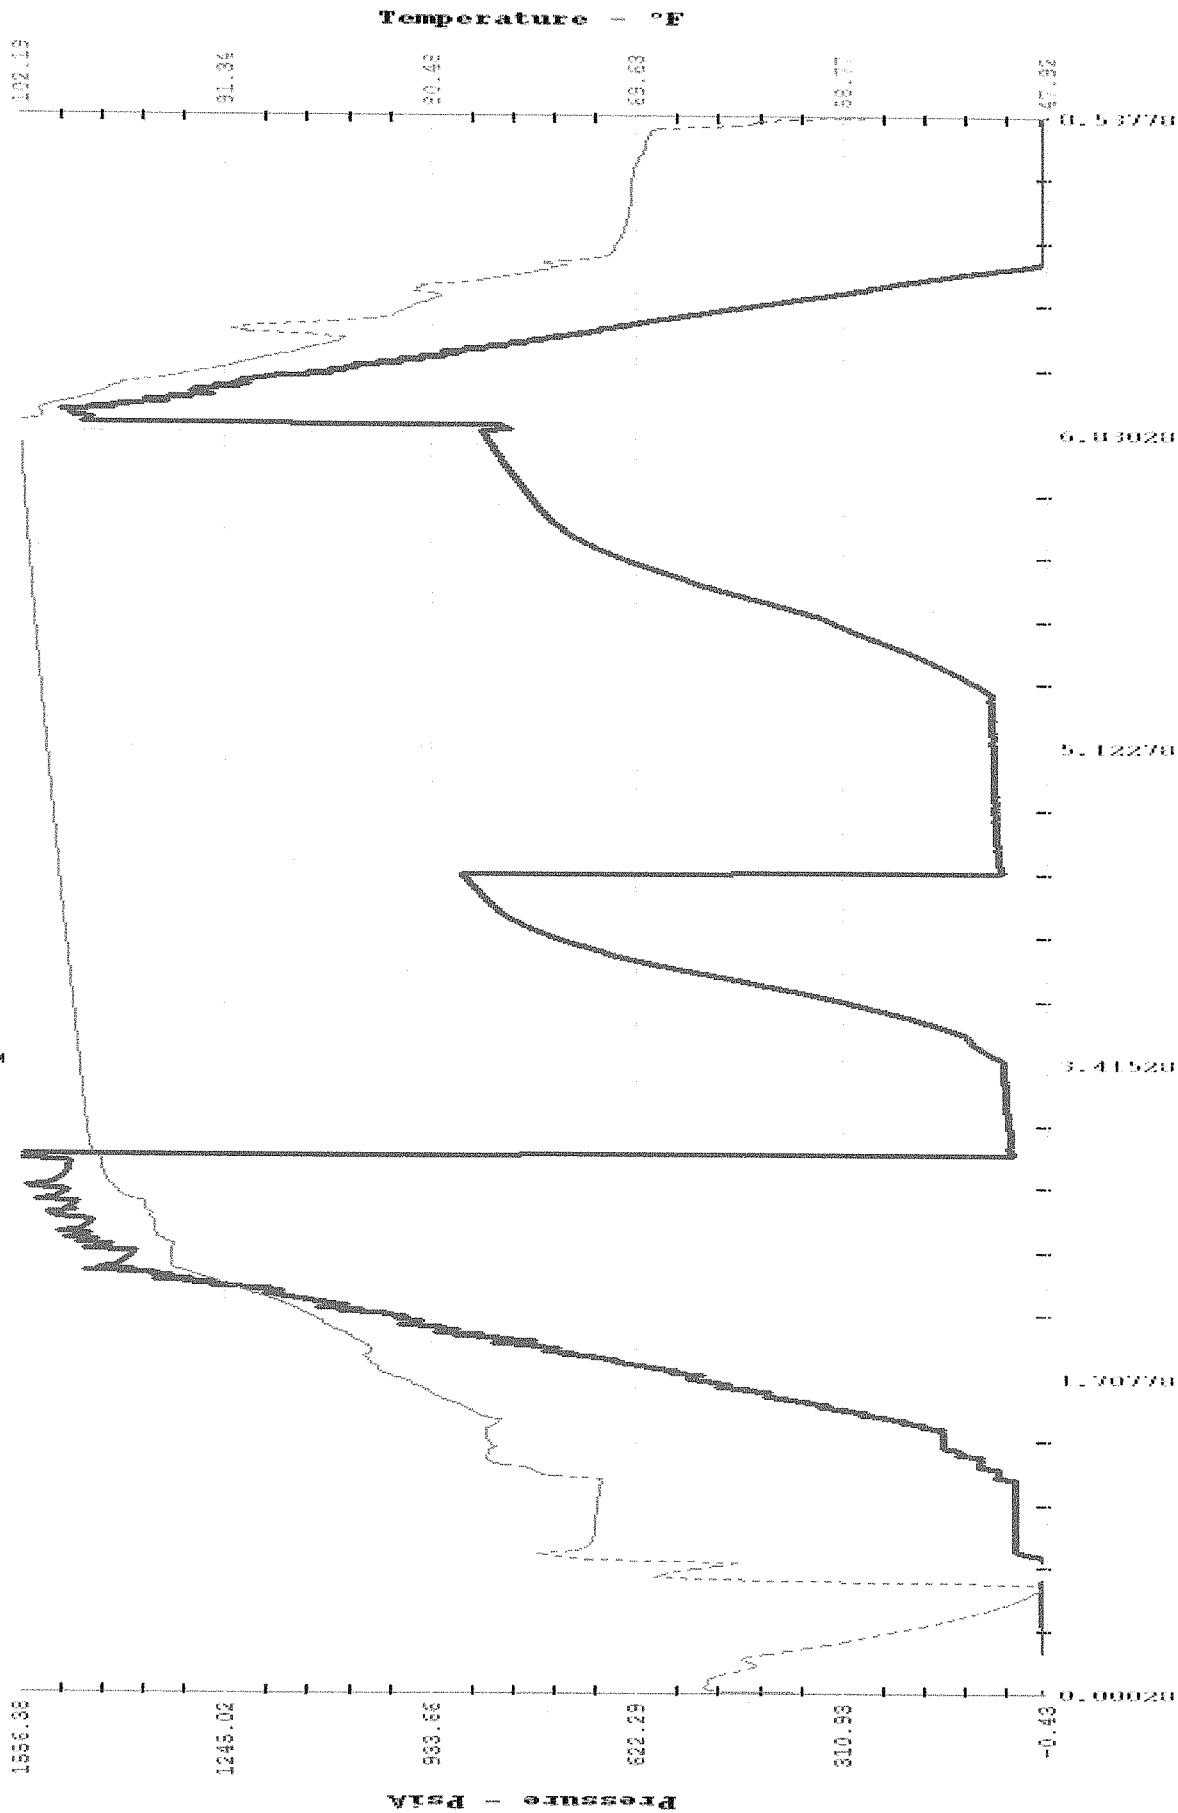

Superior Testers Enterprises L.L.C.

P.O. Box 138, Great Bend, Kansas 67530

(800) 792-6902

Company Gilbert Stewart operating L.L.C.
 Address 1801 Broadway #450 Denver Co 80202
 Lease & # DDK #7 Sec. 22 Twp 20 Rng 12
 Date 2-28-2007 County Barton Elevation 1822 G.L. 1828 K.B.
 Drilling Contractor Excell Rig #10
 Drill Pipe Length 3180 I.D. of Drill Pipe 3 Tool Joint Size 4 IF
 Drill Collar Length 60 I.D. of Drill Collars 2.25 Tool Joint Size 4 1/2 x H
 Mud Weight 9.1 Viscosity 44 Filtrate 10 Chlorides-Pits 7,700 DST
 Top Packer Depth 3200 Bottom Packer Depth 3200 Number of Packers 2
 Tested From 3200 to 3329 Total Depth 3329 Anchor Length 63
 Test # 2 Formation Tested Lansing H-I-J Hole Size 7 7/8
 Initial Blow good Blow Bottom Bucket in 4min

Final Blow good Blow Bottom Bucket in 3min Blow back on the 1st Shut-in YES

Initial Hydrostatic 1640 P.S.I. Final Hydrostatic 1590 Blow back on the 2nd Shut-in YES
 P.S.I. Maximum Temp. 105 F

Initial Opening <u>38</u> P.S.I. to <u>97</u>	P.S.I. from <u>10:20</u> m to <u>10:50</u> m	<u>30</u> minutes
Initial Shut-in <u>952</u>	P.S.I. from <u>10:50</u> m to <u>11:50</u> m	<u>60</u> minutes
Final Opening <u>113</u> P.S.I. to <u>154</u>	P.S.I. from <u>11:50</u> m to <u>12:50</u> m	<u>60</u> minutes
Final Shut-in <u>949</u>	P.S.I. from <u>12:50</u> m to <u>2:20</u> m	<u>90</u> minutes

Feet	Recovery Description	% Gas	% Oil	% Mud	% Water
10	Mud			100	
60	Mud cut oil + gas	30	20	50	
60	oil + Mud cut gas with a trace of water	20	40	25	5
60	oil + gas trace of mud	40	50	10	
60	oil + gas trace of mud	40	50	10	
60	oil + water + gas + Mud	35	10	35	20

Total Feet Recovered _____ Recovery Chlorides _____ Rw. _____ ohms @ _____ Degrees
 Gravity of oil _____ Corrected Gas to Surface in _____ minutes into the _____
 Max. Gas Gauged _____ MCF/day See Gas Flow Report Was a gas sample taken _____
 Comments _____

Extra Equipment-Jars _____ Safety Joint _____ Circulating Sub _____ Straddle _____
 Electronic Recorder No. 91834 Depth 3325 Extra Packer (3rd) _____ Hook Wall _____
 Bottom Recorder No. 4337 Depth 3320 Extra Packer (4th) _____ Sampler _____
 Tool Operator DAVID Nichols Approved By _____

Ticket No. 15106

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902


DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

RG. 12

Company: GILBERT STEWART OPERATING Lease & Well No. DDK#7 Test #: 2 Date: 2-28-07 SEC. 22 TWP. 20

Temperature / Pressure Data

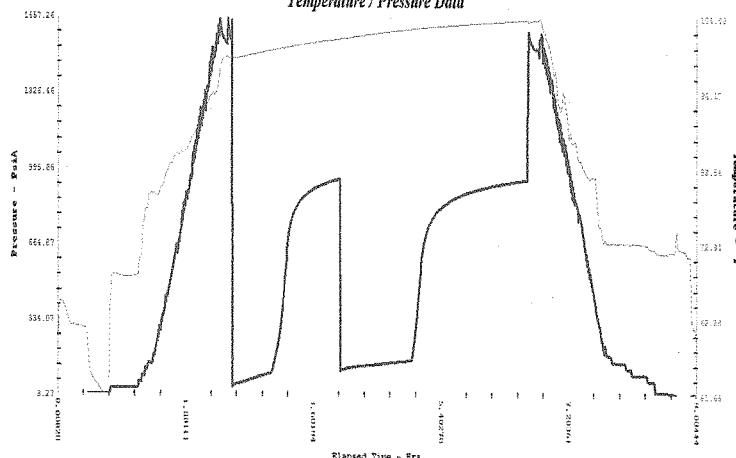

1	Initial Hydrostatic Pressure	1640
2	Initial Flow Pressure	38
3	Final Initial Flow Pressure	97
4	Initial Shut-In Pressure	952
5	Initial Final Flow Pressure	113
6	Final Flow Pressure	154
7	Final Shut-In Pressure	949
8	Final Hydrostatic Pressure	1596

Maximum Temperature 105

GENERAL INFORMATION

COMPANY NAME GILBERT STEWART OPERATING

TEST DATE 2/28/07

SECTION-TOWN-RANGE 22-20-12

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1822

COMPANY REPRESENTATIVE CLAYTON

LEASE AND WELL NUMBER DDK#7

FORMATION TESTED LANSING H-I-J

DRILL STEM TEST NUMBER 2

REPORT NUMBER #####

ELEVATION KELLY BUSHINGS 1828

TESTING ENGINEER DAVID NICHOLS

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3266

TEST INTERVAL (to) 3329

ANCHOR LENGTH 63

TOTAL DEPTH (ft) 3329

TOP PACKER DEPTH 3261

BOTTOM PACKER DEPTH 3266

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 10:20

TOOL OPEN (to) 10:50

DURATION (min.) 30

INITIAL SHUT-IN

TOOL CLOSED (from) 10:50

TOOL CLOSED (to) 11:50

DURATION (min.) 60

FINAL OPEN

TOOL OPEN (from) 11:50

TOOL OPEN (to) 12:50

DURATION (min.) 60

FINAL SHUT-IN

TOOL CLOSED (from) 12:50

TOOL CLOSED (to) 2:20

DURATION (min.) 90

INITIAL FLOW

GOOD BLOW BOTTOM OF BUCKET IN 4 MIN

FINAL FLOW

GOOD BLOW BOTTOM OF BUCKET IN 3 MIN

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GILBERT STEWART OPERATING	LEASE AND WELL NUMBER	DDK#7
TEST DATE	2/28/07	FORMATION TESTED	LANSING H-I-J
SECTION-TOWN-RANGE	22-20-12	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	15106
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1828
ELEVATION GROUND LEVEL	1822	TESTING ENGINEER	DAVID NICHOLS
COMPANY REPRESENTATIVE	CLAYTON		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	NO	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	30 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3325	BOTTOM RECORDER DEPTH	3326
RECORDER NUMBER	4023	RECORDER NUMBER	3088


WELL INFORMATION

DRILLING CONTRACTOR	EXCELL#10	DRILL COLLAR LENGTH	60
DRILL PIPE LENGTH	3186	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS

[illegible]

Temperature / Pressure Data

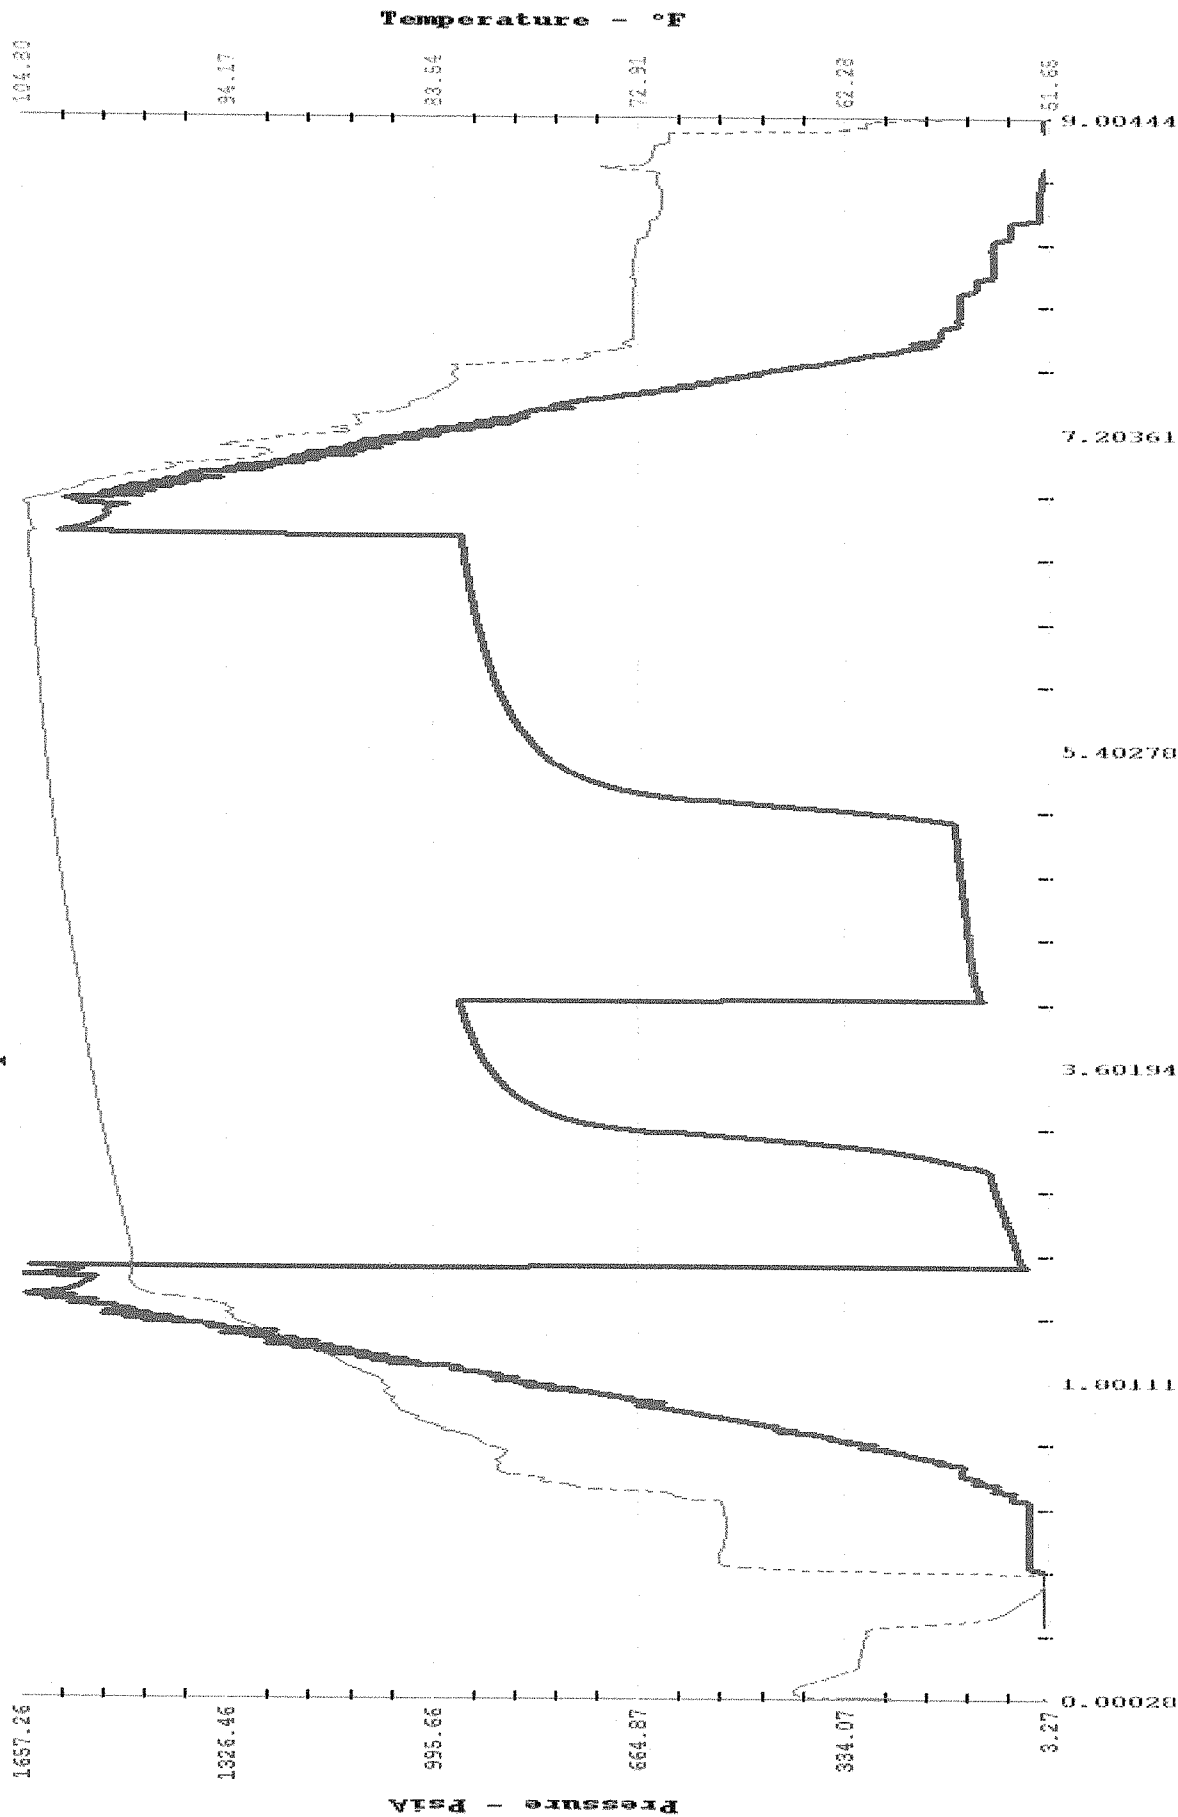

Elapsed Time - Hrs

GILBERT STEWART OPERATING 22-20-12 DDK#7 2-28-07 DST#2 LANSING H-I-J

(800) 792-6902

Ticket No. 15107

SUPERIOR TESTERS ENTERPRISES L.L.C.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: GILBERT-STEWART OPERATING LLC
 Lease & Well No. DDK #7
 Test #: 3
 Date: 2-28-07
 SEC. 22
 TWP. 20S RGE. 12W

Temperature / Pressure Data

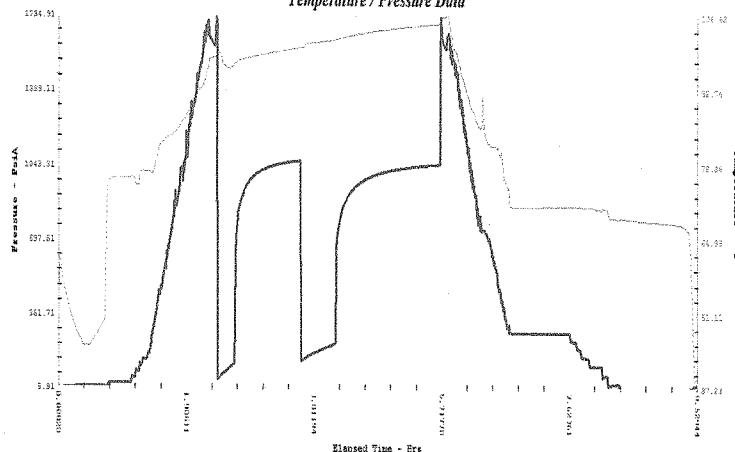

1	Initial Hydrostatic Pressure	1727
2	Initial Flow Pressure	45
3	Final Initial Flow Pressure	119
4	Initial Shut-In Pressure	1065
5	Initial Final Flow Pressure	130
6	Final Flow Pressure	214
7	Final Shut-In Pressure	1049
8	Final Hydrostatic Pressure	1504

Maximum Temperature 106

GENERAL INFORMATION

COMPANY NAME GILBERT-STEWART OPERATING LLC

TEST DATE 2/28/07

LEASE AND WELL NUMBER DDK #7

SECTION-TOWN-RANGE 22-20S-12W

FORMATION TESTED LANSING "L"- ARBUCK

STATE KANSAS

DRILL STEM TEST NUMBER 3

COUNTY BARTON

REPORT NUMBER 15107

ELEVATION GROUND LEVEL 1822

ELEVATION KELLY BUSHINGS 1828

COMPANY REPRESENTATIVE CLAYTON CAMOZZI TESTING ENGINEER GENE BUDIG

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3358

TOP PACKER DEPTH 3353

TEST INTERVAL (to) 3418

BOTTOM PACKER DEPTH 3358

ANCHOR LENGTH 60

NUMBER OF PACKERS 2

TOTAL DEPTH (ft) 3418

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 9:03P

TOOL OPEN (from) 10:18

INITIAL OPEN TOOL OPEN (to) 9:18

FINAL OPEN TOOL OPEN (to) 10:48

DURATION (min.) 15

DURATION (min.) 30

TOOL CLOSED (from) 9:18

TOOL CLOSED (from) 10:48

INITIAL SHUT-IN TOOL CLOSED (to) 10:18

FINAL SHUT-IN TOOL CLOSED (to) 12:18

DURATION (min.) 60

DURATION (min.) 90

INITIAL FLOW

FAIR BULING BLOW BUILT TO BOTTOM OF 5 GALLON BUCKET IN 6 MINUTES
BLOW BACK

FINAL FLOW

FAIR BULING BLOW BUILT TO BOTTOM OF 5 GALLON BUCKET IN 7 MINUTES
BLOW BACK

Feet of Recovery	RESISTIVITY	AT	DEGREES	CHLORIDES				
	RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER	
1) 305	OIL			5	95			
2) 180	OIL CUT MUD				25	75		
3)								
4)								
5)								

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GILBERT-STEWART OPERATING LLC	LEASE AND WELL NUMBER	DDK #7
TEST DATE	2/28/07	FORMATION TESTED	LANSING "L"- ARBUCKLE
SECTION-TOWN-RANGE	22-20S-12W	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	15107
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1828
ELEVATION GROUND LEVEL	1822	TESTING ENGINEER	FRANK ZAMARRIPA
COMPANY REPRESENTATIVE	CLAYTON CAMOZZI		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	30 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3414	BOTTOM RECORDER DEPTH	3415
RECORDER NUMBER	91986	RECORDER NUMBER	4337

WELL INFORMATION

DRILLING CONTRACTOR	EXELL RIG #10	DRILL COLLAR LENGTH	60
DRILL PIPE LENGTH	3128	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 I.F.		
WEIGHT PIPE LENGTH	210	MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	64
TOOL JOINT SIZE	4 1/2 I.F.	WATER LOSS	9.2
		CHLORIDES-PITS	8000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

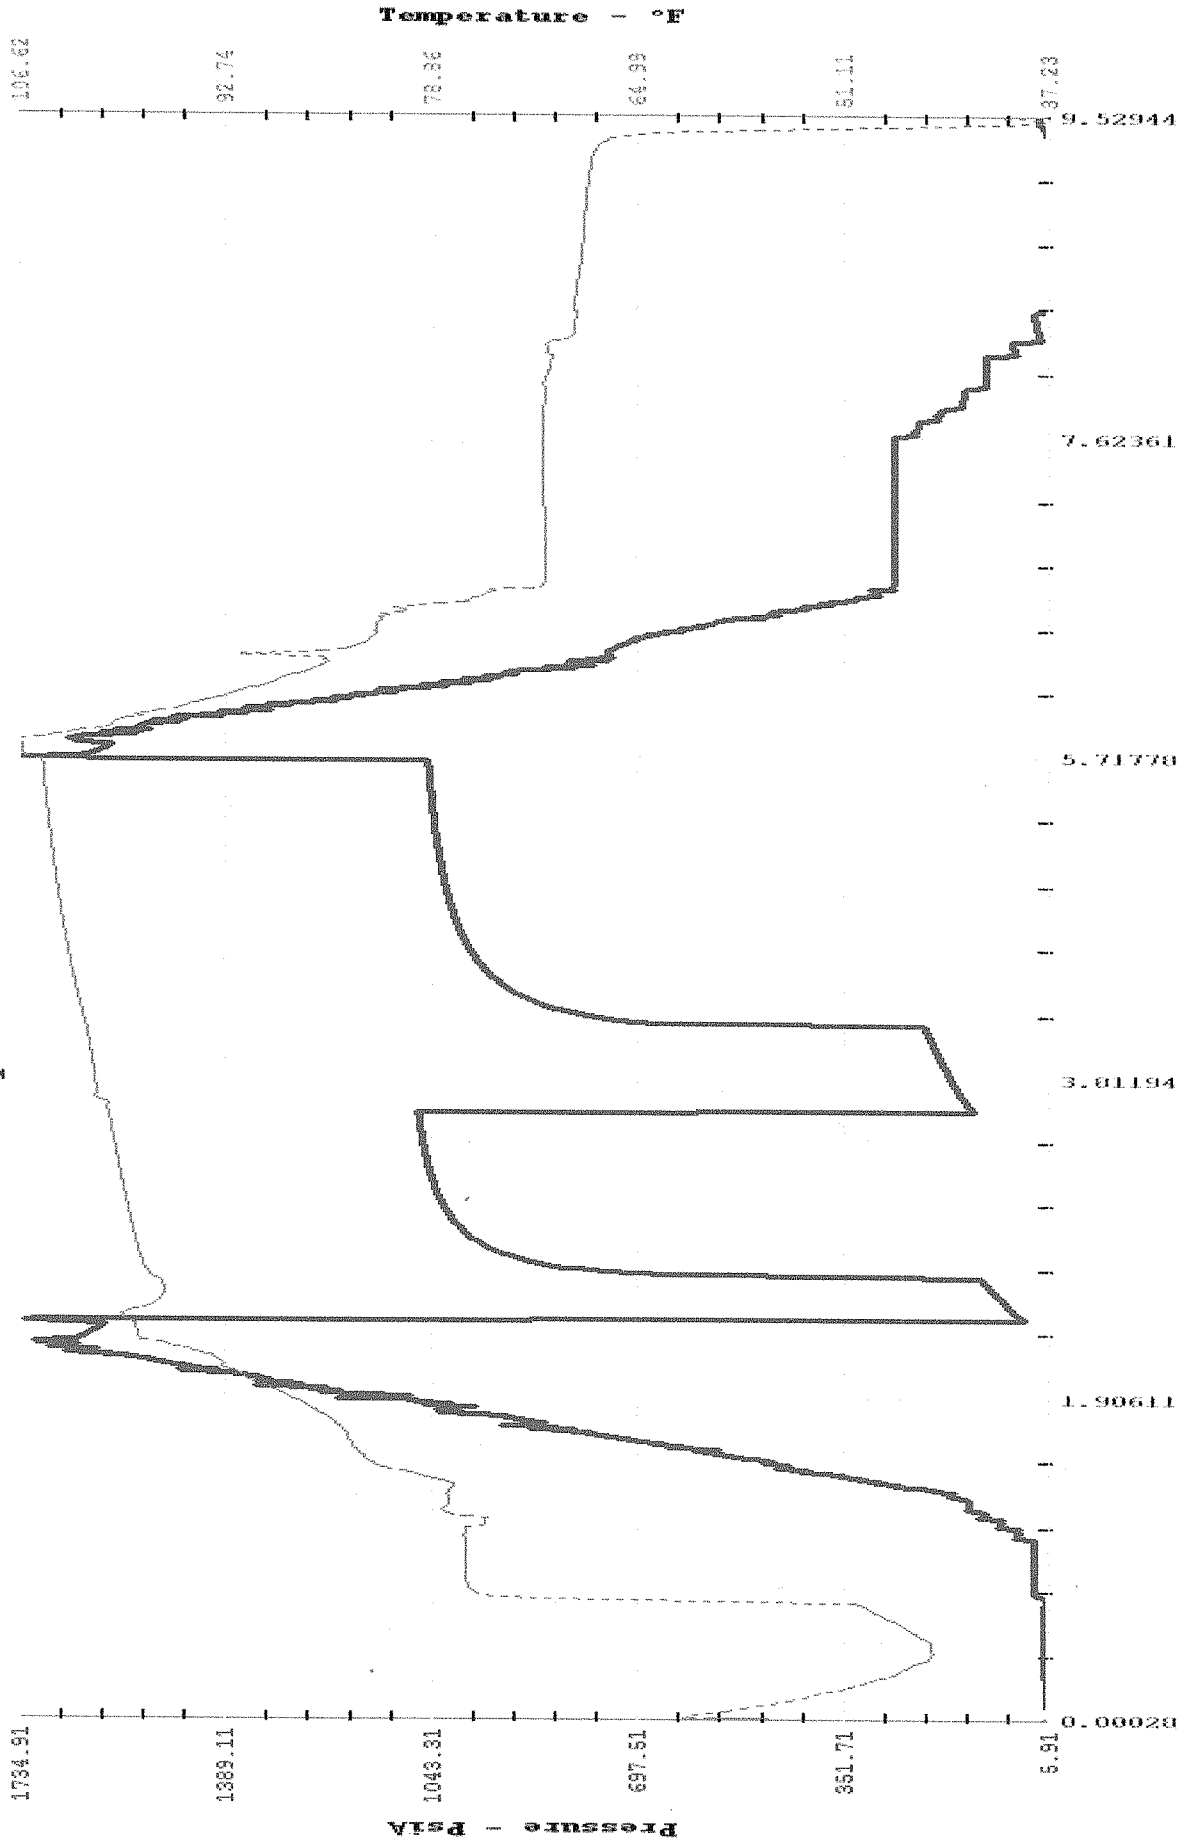

(800) 792-6902

Initial Opening	83	P.S.I. to	590	P.S.I.	from	1:47 p m	to	2:17 p m	30	minutes	
Initial Shut-in	979	P.S.I.			from	2:17 p m	to	3:17 p m	60	minutes	
Final Opening	607	P.S.I. to	848	P.S.I.	from	3:17	m to	4:17	m	60	minutes
Final Shut-in	978	P.S.I.			from	4:17	m to	5:47	m	90	minutes

[illegible]

Extra Equipment-Jars	<u>NO</u>	Safety Joint	<u>NO</u>	Circulating Sub	<u>YES</u>	Straddle	<u>NO</u>
Electronic Recorder No.	<u>91984</u>	Depth	<u>3428</u>	Extra Packer (3rd)	<u>NO</u>	Hook Wall	<u>NO</u>
Bottom Recorder No	<u>4337</u>	Depth	<u>3429</u>	Extra Packer (4th)	<u>NO</u>	Sampler	<u>NO</u>
Tool Operator	<u>Frank Zornick</u>			Approved By			

Ticket No. 15108


SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: GILBERT-STEWART OPERATING LLC Lease & Well No. DDK #7 Test #: 4 Date: 3-1-07 SEC. 22 TWP. 20S RGE. 12W

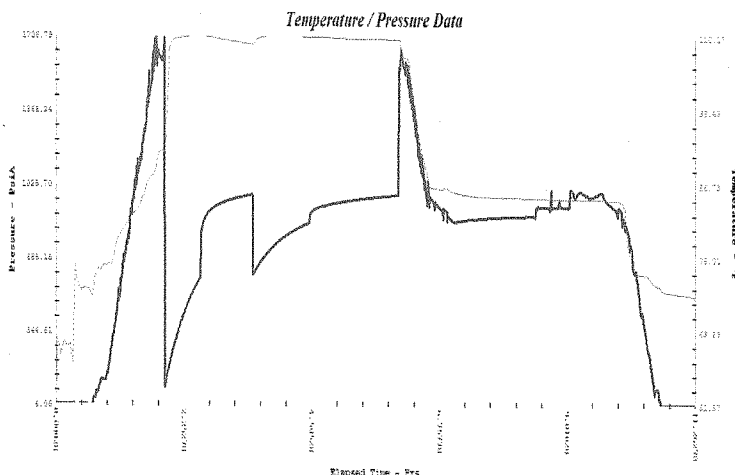

- | | | |
|---|------------------------------|------|
| 1 | Initial Hydrostatic Pressure | 1699 |
| 2 | Initial Flow Pressure | 83 |
| 3 | Final Initial Flow Pressure | 590 |
| 4 | Initial Shut-In Pressure | 979 |
| 5 | Initial Final Flow Pressure | 607 |
| 6 | Final Flow Pressure | 848 |
| 7 | Final Shut-In Pressure | 978 |
| 8 | Final Hydrostatic Pressure | 1556 |

Maximum Temperature 110

GENERAL INFORMATION

COMPANY NAME GILBERT-STEWART OPERATING LLC

TEST DATE 3/1/07

SECTION-TOWN-RANGE 22-20S-12W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1822

COMPANY REPRESENTATIVE CLAYTON

LEASE AND WELL NUMBER DDK #7

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 4

REPORT NUMBER 15108

ELEVATION KELLY BUSHINGS 1828

TESTING ENGINEER FRANK ZAMARRIPA

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3419

TEST INTERVAL (to) 3432

ANCHOR LENGTH 13

TOTAL DEPTH (ft) 3432

TOP PACKER DEPTH 3414

BOTTOM PACKER DEPTH 3419

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 1:47P

INITIAL OPEN

TOOL OPEN (to) 2:17

FINAL OPEN

TOOL OPEN (from) 3:17

TOOL OPEN (to) 4:17

DURATION (min.) 30

DURATION (min.) 60

TOOL CLOSED (from) 2:17

INITIAL SHUT-IN

TOOL CLOSED (to) 3:17

FINAL SHUT-IN

TOOL CLOSED (from) 4:17

TOOL CLOSED (to) 5:47

DURATION (min.) 60

DURATION (min.) 90

INITIAL FLOW

STRONG BLOW TO BOTTOM OF 5 GALLON BUCKET IN 1 MINUTE
BLOW BACK

FINAL FLOW

STRONG BLOW TO BOTTOM OF 5 GALLON BUCKET IN 2 MINUTE
BLOW BACK DIED OFF AFTER 20 MINUTES

Feet of Recovery	RESISTIVITY AT DEGREES CHLORIDES			
	RECOVERY DESCRIPTION			
		% GAS	% OIL	% MUD
1) 1800	OIL		100	
2) 60	OIL CUT MUD		15	85
3) 60	SLIGHT OIL CUT WATER		5	95
4)				
5)				

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GILBERT-STEWART OPERATING LLC	LEASE AND WELL NUMBER	DDK #7
TEST DATE	3/1/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	22-20S-12W	DRILL STEM TEST NUMBER	4
STATE	KANSAS	REPORT NUMBER	15108
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1828
ELEVATION GROUND LEVEL	1822	TESTING ENGINEER	FRANK ZAMARRIPA
COMPANY REPRESENTATIVE	CLAYTON		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	30 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3428	BOTTOM RECORDER DEPTH	3429
RECORDER NUMBER	91986	RECORDER NUMBER	4337

WELL INFORMATION

DRILLING CONTRACTOR	EXCELL RIG #10	DRILL COLLAR LENGTH	60
DRILL PIPE LENGTH	3129	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 I.F		
WEIGHT PIPE LENGTH	210	MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	72
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	9.6
		CHLORIDES-PITS	9500
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

