

F.G. Holl Co.

Barnes Trust 2-29

29-20s-14w

15-009-25010

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

1400 KB

Date 1-4-07 Location 29-20-14w Elevation 1899 County BartonCompany F.G. Holl Company LLC Number of Copies 5Charts Mailed to 9431 E Central Suite #100 Wichita K 67206Drilling Contractor Duke Drilling Rig #8Length Drill Pipe 3284 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 x 4

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars 225 Tool Joint Size 4 1/2 x 4Top Packer Depth 3301 Bottom Packer Depth 3306 Number of Packers 2 Packer Size 6 3/4TESTED FROM 3306 TO 3369 ANCHOR LENGTH 63 TOTAL DEPTH 3369 Hole Size 7 7/8LEASE & WELL NO. Barnes Trust 2-29 FORMATION TESTED Simpson sand TEST NO. 1Mud Weight 9.3 Viscosity 62 Water Loss 9.2 Chlorides - Pits 55000 D.S.T. _____Maximum Temp. 103 °F Initial Hydrostatic Pressure (A) 1646 P.S.I. Final Hydrostatic Pressure (H) 1627 P.S.I.Tool Open I.F.P. from 5:56 A m to 6:11 A m 15 minTool Closed I.C.I.P. from 6:11 A m to 6:41 A m 30 minTool Open F.F.P. from 6:41 A m to 7:26 A m 45 minTool Closed F.C.I.P. from 7:26 A m to 8:56 A m 90 minInitial Blow Weak Blow Built 3 1/2 inches in 15 minFinal Blow Weak Blow Built 3 1/2 inches in 45 minTotal Feet Recovered 62 feet Total Gravity of Oil _____ Corrected _____62 Feet of Drilling mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint yes Extra Packer _____ Straddle _____ Hook Wall _____Top Recorder No. 4423 Clock No. Electronic Depth 3365 Cir. Sub _____ Sampler _____Bottom Recorder No. 3088 Clock No. 47441 Depth 3366 Insurance _____

Price of Job _____

Tool Operator Jeff Schute

Approved By _____

No 14329


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

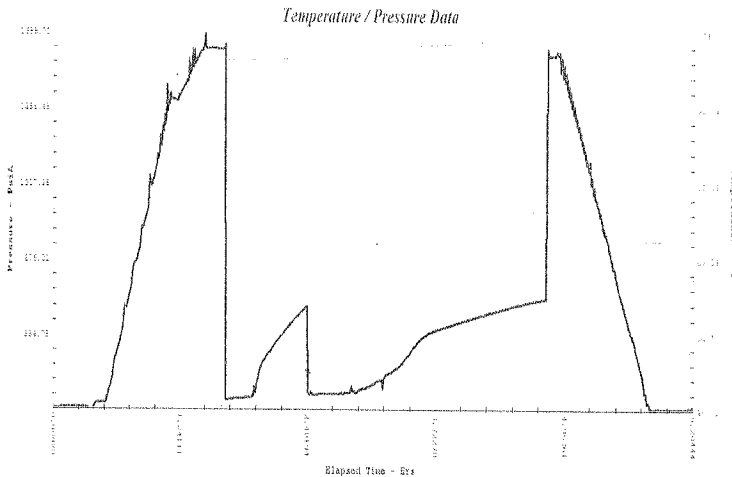

1	Initial Hydrostatic Pressure	1646
2	Initial Flow Pressure	37
3	Final Initial Flow Pressure	51
4	Initial Shut-In Pressure	465
5	Initial Final Flow Pressure	64
6	Final Flow Pressure	71
7	Final Shut-In Pressure	497
8	Final Hydrostatic Pressure	1627

Maximum Temperature 103

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/4/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE A

LEASE AND WELL NUMBER BARNES TRUST #2-29

FORMATION TESTED SIMPSON SAND

DRILL STEM TEST NUMBER 1

REPORT NUMBER 14329

ELEVATION KELLY BUSHINGS 1906

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3306

TEST INTERVAL (to) 3369

ANCHOR LENGTH 63

TOTAL DEPTH (ft) 3369

TOP PACKER DEPTH 3301

BOTTOM PACKER DEPTH 3306

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:56A

TOOL OPEN (from) 6:41

INITIAL OPEN TOOL OPEN (to) 6:11

FINAL OPEN TOOL OPEN (to) 7:26

DURATION (min.) 15

DURATION (min.) 45

TOOL CLOSED (from) 6:11

TOOL CLOSED (from) 7:26

INITIAL SHUT-IN TOOL CLOSED (to) 6:41

FINAL SHUT-IN TOOL CLOSED (to) 8:56A

DURATION (min.) 30

DURATION (min.) 90

INITIAL FLOW WEAK BLOW BUILT 3 1/2 INCHS IN 15 MIN

FINAL FLOW WEAK BLOW BUILT 3 1/2 INCHES IN 45 MIN

Feet of	RESISTIVITY	AT	DEGREES	CHLORIDES				
Recovery	RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER	
1) 62	DRILLING MUD							
2)								
3)								
4)								
5)								

Company: F.G HOLL COMPANY L.L.C
TWP. 20 RGE. 14
Lease & Well No. BARNES TRUST #2-29 Test #: 1 Date: 1-4-07 SEC. 29

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/4/07	FORMATION TESTED	SIMPSON SAND
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	14329
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1906
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENEA		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
20	MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3365	BOTTOM RECORDER DEPTH	3366
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG # 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3284	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.3
WEIGHT PIPE I.D.	2.25	VISCOSITY	62
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	9.2
		CHLORIDES-PITS	5,500
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

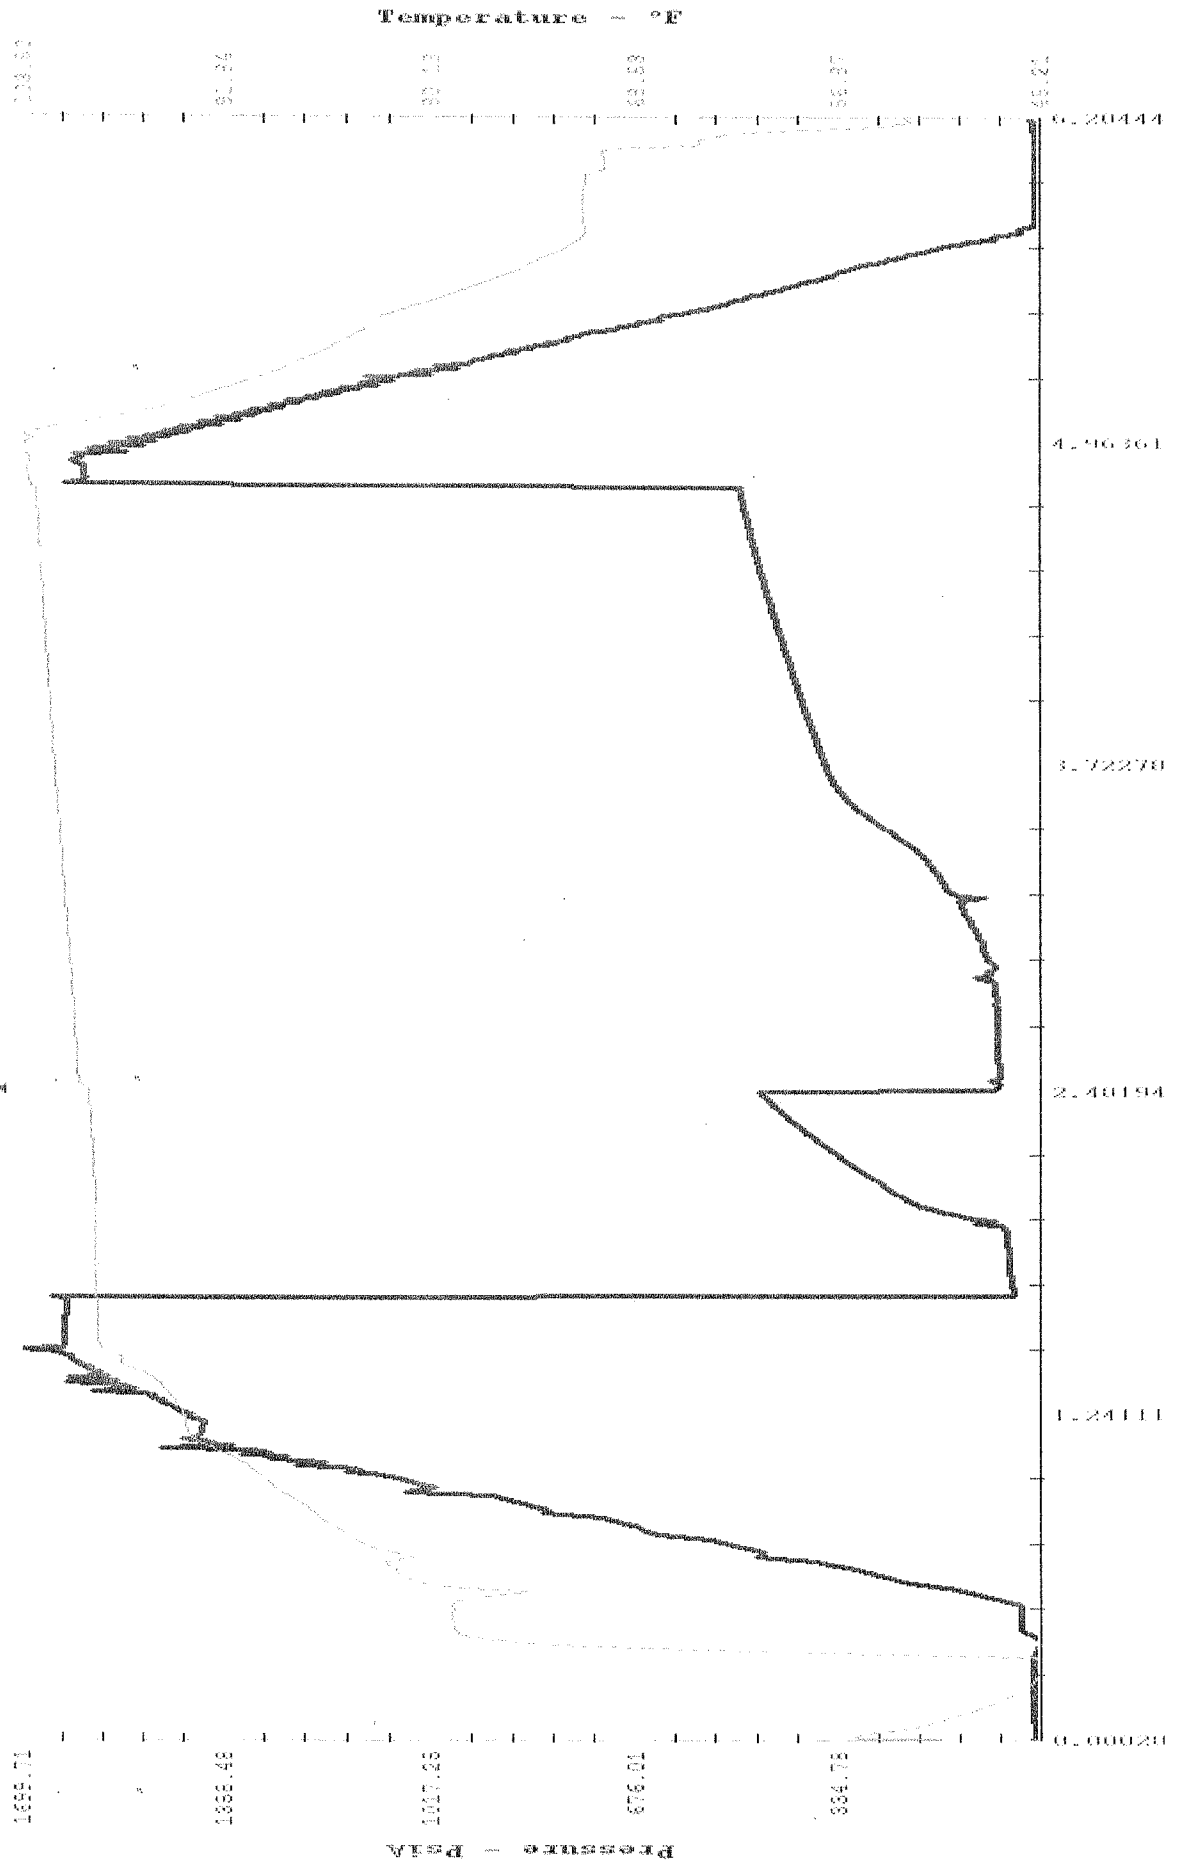

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-4-07 Location 29-20-14W Elevation 1899 County Barton
Company F.G. Holl Company L.L.C. Number of Copies 5
Charts Mailed to 9431 E Central Suite #100 Wichita KS 67206
Drilling Contractor Duke Drilling Rig #8
Length Drill Pipe 3348 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 x 11
Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____
Length Drill Collars _____ I.D. Drill Collars 205 Tool Joint Size 4 1/2 x 11
Top Packer Depth 3364 Bottom Packer Depth 3369 Number of Packers 2 Packer Size 6 3/4
TESTED FROM 3369 TO 3389 ANCHOR LENGTH 20 TOTAL DEPTH 3389 Hole Size 7 7/8
LEASE & WELL NO. Barnes Trust 2-29 FORMATION TESTED Lansing F-15 TEST NO. 2
Mud Weight 9.3 Viscosity 47 Water Loss 6.4 Chlorides - Pits 6500 D.S.T. 80,000
Maximum Temp. 111 °F Initial Hydrostatic Pressure (A) 1632 P.S.I. Final Hydrostatic Pressure (H) 1512 P.S.I.

Tool Open I.F.P. from 6:10 p.m. to 6:25 p.m. 15 min
Tool Closed I.C.I.P. from 6:25 p.m. to 6:55 p.m. 30 min
Tool Open F.F.P. from 6:55 p.m. to 7:40 p.m. 45 min
Tool Closed F.C.I.P. from 7:40 p.m. to 8:10 p.m. 90 min

from [B] <u>13</u>	P.S.I. to [C] <u>21</u>	P.S.I.
[D] <u>1075</u>		P.S.I.
from [E] <u>21</u>	P.S.I. to [F] <u>40</u>	P.S.I.
[G] <u>1074</u>		P.S.I.

Initial Blow Weak Blow Built 2 inches in 15 min

Final Blow Weak Blow Built 4 inches in 45 min

Total Feet Recovered _____ Gravity of Oil _____ Corrected _____
61 Feet of water cut mud _____ % Gas _____ % Oil 15 % Mud 85 % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars _____ Safety Joint Yes Extra Packer _____ Straddle _____ Hook Wall _____
Top Recorder No. 4023 Clock No. Election Depth 3385 Cir. Sub _____ Sampler _____
Bottom Recorder No. 3098 Clock No. 47441 Depth 3386 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14330

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT


GREAT BEND, KANSAS 67530

TWP. 20 RGE. 14

Company: F.G HOLL COMPANY L.L.C

Lease & Well No. BARNES TRUST 2-29 Test #: 2 Date: 1-4-07 SEC. 29

Temperature / Pressure Data

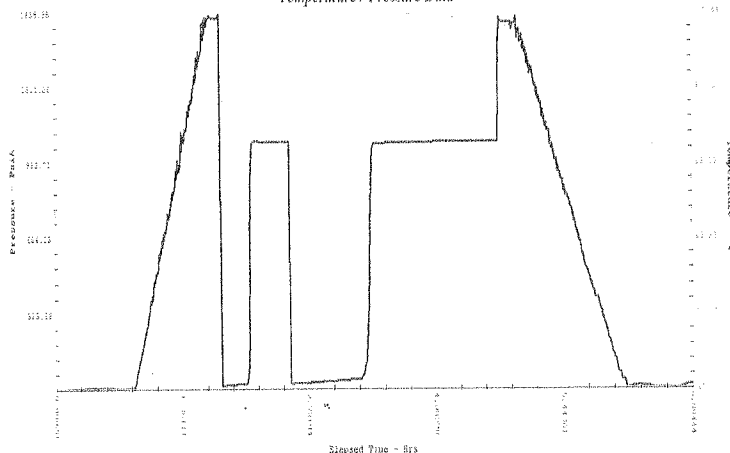

1	Initial Hydrostatic Pressure	1632
2	Initial Flow Pressure	13
3	Final Initial Flow Pressure	21
4	Initial Shut-In Pressure	1075
5	Initial Final Flow Pressure	21
6	Final Flow Pressure	40
7	Final Shut-In Pressure	1074
8	Final Hydrostatic Pressure	1512

Maximum Temperature 111

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/4/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE

LEASE AND WELL NUMBER BARNES TRUST 2-29

FORMATION TESTED LANSING E-F

DRILL STEM TEST NUMBER 2

REPORT NUMBER 14330

ELEVATION KELLY BUSHINGS 1906

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3369

TEST INTERVAL (to) 3389

ANCHOR LENGTH 20

TOTAL DEPTH (ft) 3389

TOP PACKER DEPTH 3364

BOTTOM PACKER DEPTH 3369

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 6:10P

INITIAL OPEN TOOL OPEN (to) 6:25

DURATION (min.) 15

TOOL OPEN (from) 6:55

FINAL OPEN TOOL OPEN (to) 7:40

DURATION (min.) 45

TOOL CLOSED (from) 6:25

INITIAL SHUT-IN TOOL CLOSED (to) 6:55

DURATION (min.) 30

TOOL CLOSED (from) 7:40

FINAL SHUT-IN TOOL CLOSED (to) 9:10

DURATION (min.) 90

INITIAL FLOW

WEAK BLOW BUILT 2 INCHS IN 15 MIN

FINAL FLOW

WEAK BLOW BUILT 4 INCHS INTO BUCKET IN 45 MIN

Feet of Recovery		RESISTIVITY	AT	DEGREES	CHLORIDES			
		RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER
1)	61	WATER CUT MUD					15	85
2)								
3)								
4)								
5)								

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST 2-29
TEST DATE	1/4/07	FORMATION TESTED	LANSING E-F
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	14330
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1906
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	20 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3385	BOTTOM RECORDER DEPTH	3386
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3348	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.3
WEIGHT PIPE I.D.	2.25	VISCOSITY	47
TOOL JOINT SIZE*	4 1/2 X.H.	WATER LOSS	6.4
		CHLORIDES-PITS	6,500
		CHLORIDES-DST	80,000

COMMENTS

Temperature / Pressure Data

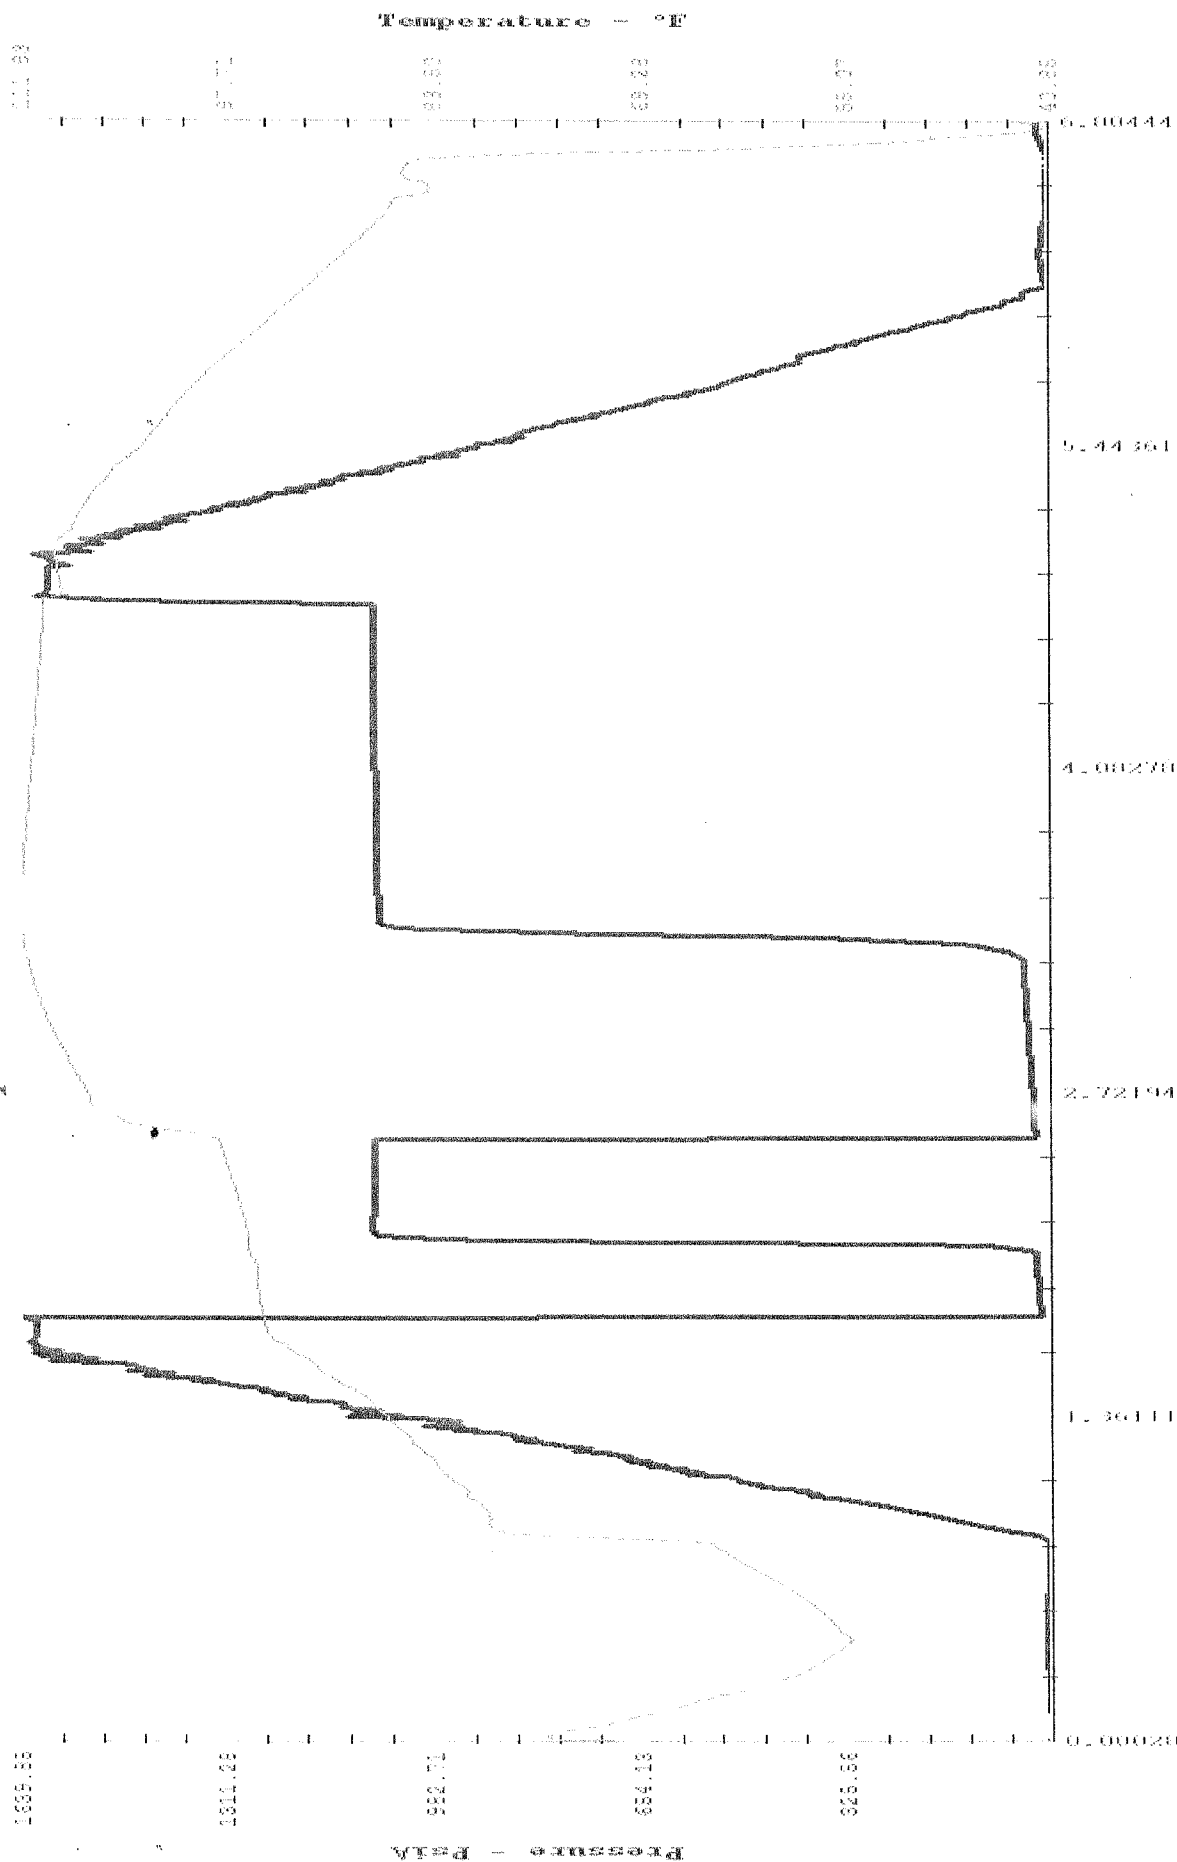

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-5-07 Location 29-20-14W Elevation 1907 KB County Barton
Company F.6 Holl Company LLC Number of Copies 5
Charts Mailed to 9431 E Central Suite #100 Wichita KS 67206
Drilling Contractor Duke Drilling Rig #8
Length Drill Pipe 3469 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 HH
Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____
Length Drill Collars _____ I.D. Drill Collars 225 Tool Joint Size 4 1/2 HH
Top Packer Depth 3485 Bottom Packer Depth 3490 Number of Packers 2 Packer Size 6 3/4
TESTED FROM 3490 TO 3502 ANCHOR LENGTH 12 TOTAL DEPTH 3502 Hole Size 7 7/8
LEASE & WELL NO. Barnes Frust 2-29 FORMATION TESTED Lansing K zone TEST NO. 3
Mud Weight 9.3 Viscosity 47 Water Loss 6.4 Chlorides - Pits 6.50 D.S.T. 84,000
Maximum Temp. 109 °F Initial Hydrostatic Pressure (A) 1702 P.S.I. Final Hydrostatic Pressure (H) 1695 P.S.I.

Tool Open I.F.P. from 2:17 pm to 2:32 pm 75 min
Tool Closed I.C.I.P. from 2:32 pm to 3:02 pm 30 min
Tool Open F.F.P. from 3:02 pm to 3:32 pm 30 min
Tool Closed F.C.I.P. from 3:32 pm to 4:32 pm 60 min

from [B] <u>11</u>	P.S.I. to [C] <u>32</u>	P.S.I.
[D] <u>1091</u>		P.S.I.
from [E] <u>39</u>	P.S.I. to [F] <u>73</u>	P.S.I.
[G] <u>1088</u>		P.S.I.

Initial Blow Fair Blow Built 6 1/2 inches in 15 min

Final Blow Fair Blow Built 7 inches in 30 min

Total Feet Recovered 125 Gravity of Oil _____ Corrected _____
60 Feet of mud cut water % Gas _____ % Oil 5 % Mud 95 % Water
65 Feet of mud cut water % Gas _____ % Oil 10 % Mud 90 % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars _____ Safety Joint yes Extra Packer _____ Straddle _____ Hook Wall _____
Top Recorder No. 4023 Clock No. Electronic Depth _____ Cir. Sub _____ Sampler _____
Bottom Recorder No. 3088 Clock No. 47441 Depth _____ Insurance _____

Price of Job _____
Tool Operator Jim Beale
Approved By _____
No 14331


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

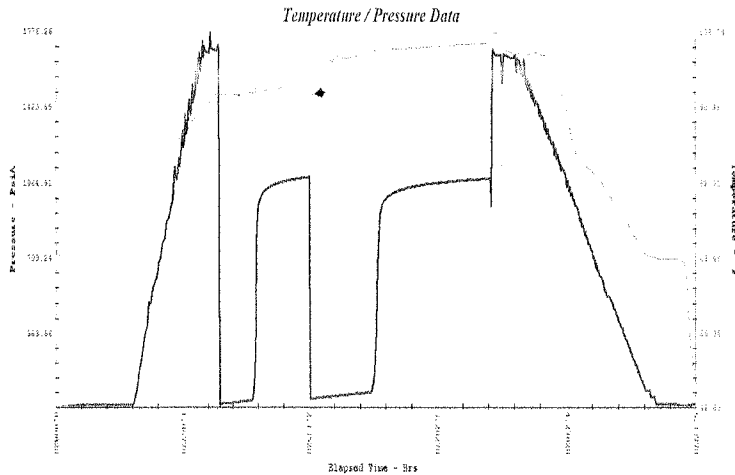

1	Initial Hydrostatic Pressure	1702
2	Initial Flow Pressure	11
3	Final Initial Flow Pressure	32
4	Initial Shut-In Pressure	1091
5	Initial Final Flow Pressure	39
6	Final Flow Pressure	73
7	Final Shut-In Pressure	1085
8	Final Hydrostatic Pressure	1695

Maximum Temperature 109

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/5/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE

LEASE AND WELL NUMBER BARNES TRUST #2-29

FORMATION TESTED LANSING K ZONE

DRILL STEM TEST NUMBER 3

REPORT NUMBER 14331

ELEVATION KELLY BUSHINGS 1907

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3490

TEST INTERVAL (to) 3502

ANCHOR LENGTH 12

TOTAL DEPTH (ft) 3502

TOP PACKER DEPTH 3485

BOTTOM PACKER DEPTH 3490

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 2:17P

INITIAL OPEN TOOL OPEN (to) 2:32

DURATION (min.) 15

TOOL CLOSED (from) 2:32

INITIAL SHUT-IN TOOL CLOSED (to) 3:02

DURATION (min.) 30

TOOL OPEN (from) 3:02

FINAL OPEN TOOL OPEN (to) 3:32

DURATION (min.) 30

TOOL CLOSED (from) 3:32

FINAL SHUT-IN TOOL CLOSED (to) 4:32

DURATION (min.) 60

INITIAL FLOW FAIR BLOW BUILT 6 1/2 INCHES IN 15 MIN

FINAL FLOW FAIR BLOW BUILT 7 INCHES IN 30 MIN

Feet of Recovery		RESISTIVITY	AT	DEGREES	CHLORIDES			
		RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER
1)	60	MUD CUT WATER					5	95
2)	65	MUD CUT WATER					10	90
3)								
4)								
5)								

Company: F.G HOLL COMPANY L.L.C
 TWP. 20 RGE. 14
 Lease & Well No. BARNES TRUST #2-29 Test #: 3 Date: 1-5-07 SEC. 29

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/5/07	FORMATION TESTED	LANSING K ZONE
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	14331
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1907
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	20 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	3499	BOTTOM RECORDER DEPTH	3500
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG # 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3469	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.3
WEIGHT PIPE I.D.	2.25	VISCOSITY	47
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	6.4
		CHLORIDES-PITS	6,500
		CHLORIDES-DST	84,000

COMMENTS

Temperature / Pressure Data

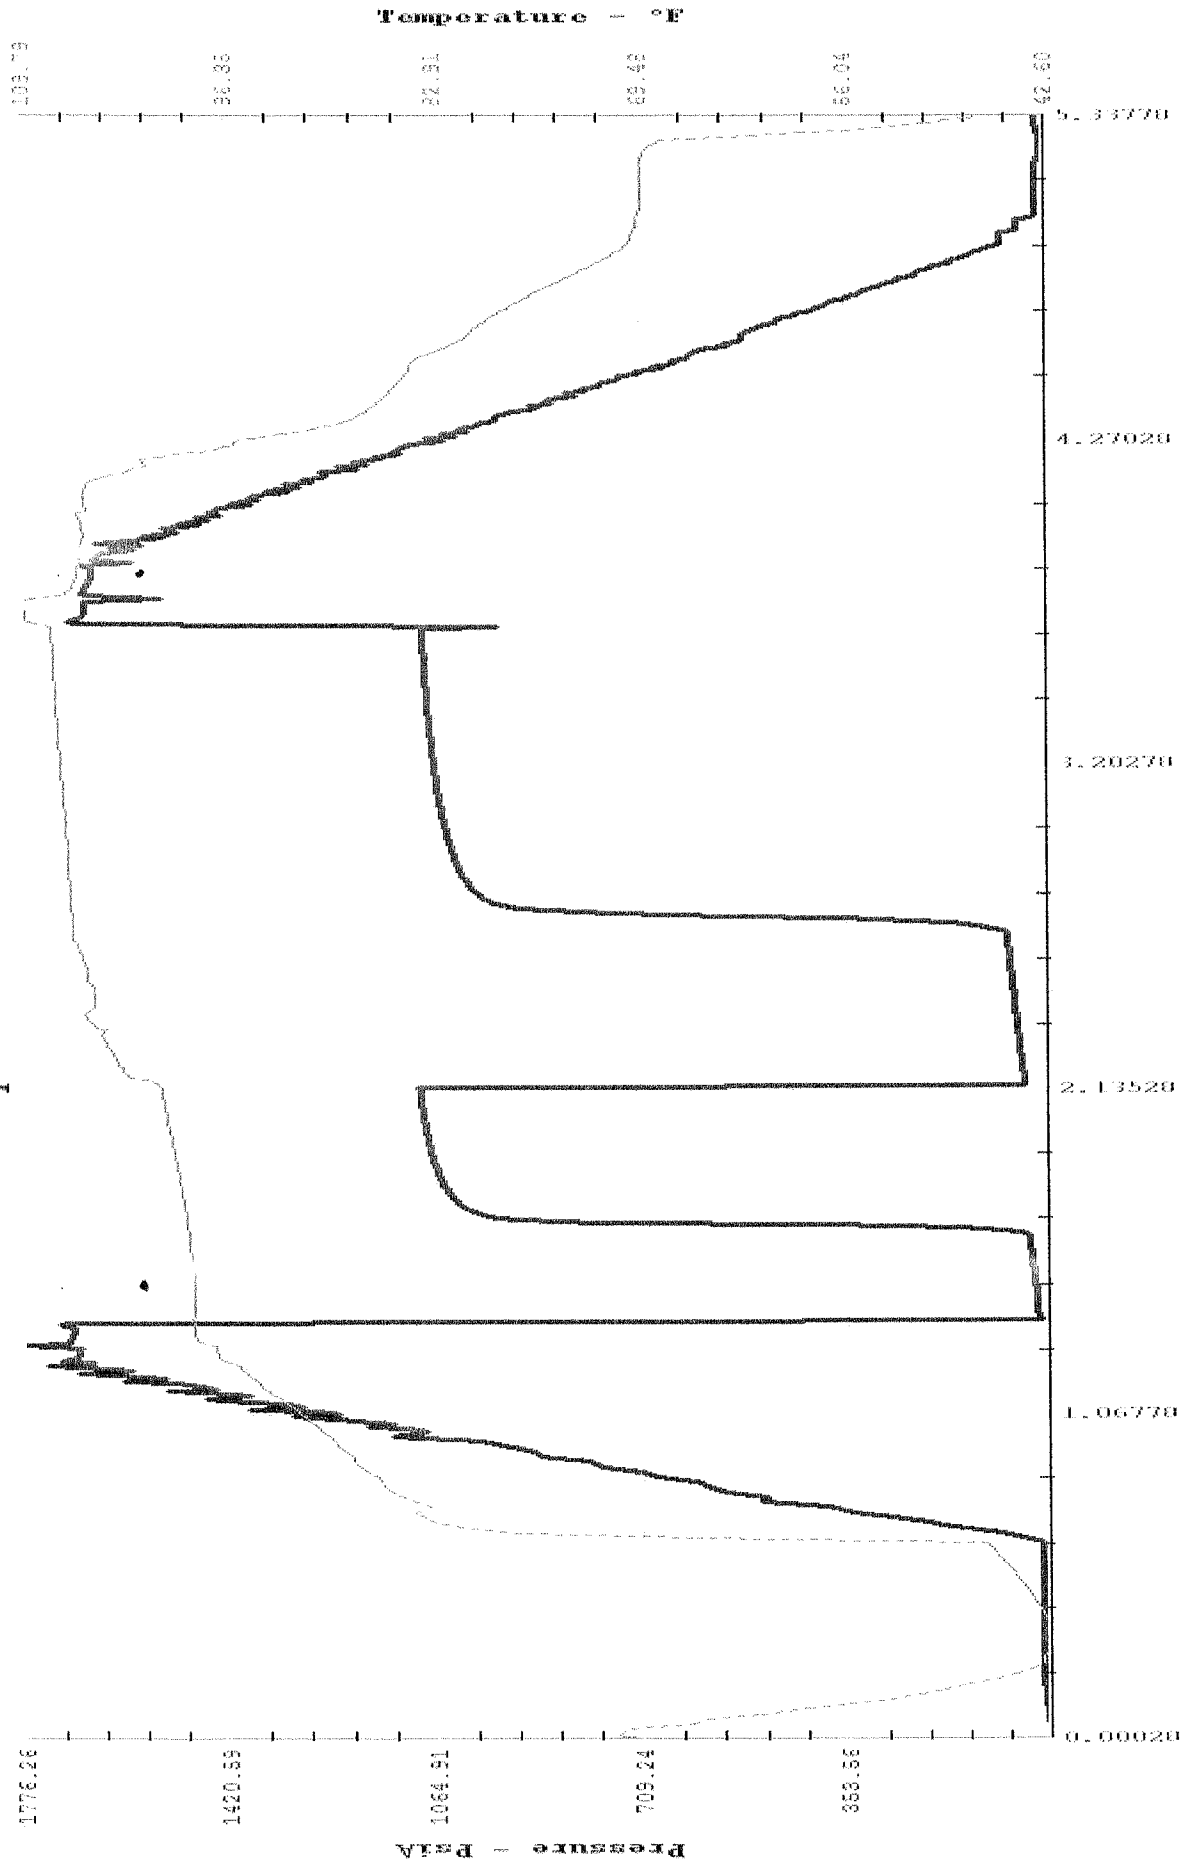

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-6-07 Location 29-20-14W Elevation 1899 County Barton

Company F.G. Holl Company LLC Number of Copies 5

Charts Mailed to 9431 E Central Suite #100 Wichita KS 67206

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 3579 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 xH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 xH

Top Packer Depth 3595 Bottom Packer Depth 3600 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3600 TO 3608 ANCHOR LENGTH 8 TOTAL DEPTH 3608 Hole Size 7 7/8

LEASE & WELL NO. Barnes + Rust #2-29 FORMATION TESTED Arduckle TEST NO. 4

Mud Weight 92 Viscosity 52 Water Loss 8.8 Chlorides - Pits 4700 D.S.T. _____

Maximum Temp. _____ °F Initial Hydrostatic Pressure (A) 1912 P.S.I. Final Hydrostatic Pressure (H) 1796 P.S.I.

Tool Open I.F.P. from 9:17 Am to 9:32 Am 15 min

Tool Closed I.C.I.P. from 9:32 Am to 10:02 Am 30 min

Tool Open F.F.P. from 10:02 Am to 10:32 Am 30 min

Tool Closed F.C.I.P. from 10:32 Am to 11:32 Am 60 min

Initial Blow Strong Blow Bottom of Bucket in 8 min

Final Blow Fair Blow Built Sinks in 30 min

Total Feet Recovered 5 Drilling mud Gravity of Oil _____ Corrected

5 Feet of Drilling mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 3604 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 3605 Insurance _____

Price of Job _____

Tool Operator _____

Approved By _____

No. 14332

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

1	Initial Hydrostatic Pressure	1912
2	Initial Flow Pressure	11
3	Final Initial Flow Pressure	23
4	Initial Shut-In Pressure	70
5	Initial Final Flow Pressure	11
6	Final Flow Pressure	11
7	Final Shut-In Pressure	542
8	Final Hydrostatic Pressure	1796

Maximum Temperature

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/6/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE

LEASE AND WELL NUMBER BARNES TRUST #2-29

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 4

REPORT NUMBER 14332

ELEVATION KELLY BUSHINGS 1907

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3600

TEST INTERVAL (to) 3608

ANCHOR LENGTH 8

TOTAL DEPTH (ft) 3608

TOP PACKER DEPTH 3595

BOTTOM PACKER DEPTH 3600

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 9:17A

INITIAL OPEN

TOOL OPEN (to) 9:32

FINAL OPEN

TOOL OPEN (from) 10:02

TOOL OPEN (to) 10:32

DURATION (min.) 15

DURATION (min.) 30

TOOL CLOSED (from) 9:32

INITIAL SHUT-IN

TOOL CLOSED (to) 10:02

FINAL SHUT-IN

TOOL CLOSED (from) 10:32

TOOL CLOSED (to) 11:32A

DURATION (min.) 30

DURATION (min.) 60

INITIAL FLOW

STRONG BLOW BOTTOM OF BUCKRT IN 8 MIN

FINAL FLOW

FAIR BLOW BUILT 5 INCHS IN 30 MIN

Feet of Recovery		RESISTIVITY	AT	DEGREES	CHLORIDES			
		RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER
1)	5	DRILLING MUD						
2)								
3)								
4)								
5)								

Company: F.G HOLL COMPANY L.L.C
 TWP. 20 RGE. 14
 Lease & Well No. BARNES TRUST #2-29 Test #: 4 Date: 1-06-07 SEC. 29

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/6/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	4
STATE	KANSAS	REPORT NUMBER	14332
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1907
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	20 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND		
TOP RECORDER DEPTH	3604	BOTTOM RECORDER DEPTH	3605
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG # 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3579	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	52
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	4,700
		CHLORIDES-DST	

COMMENTS

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-6-07 Location 29-20-14W Elevation 1899 County Barton

Company F.O. Hall Company LLC Number of Copies 5

Charts Mailed to 9431 E Central Suite #100 Wichita KS 67206

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 3579 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 3603 Bottom Packer Depth 3608 Number of Packers _____ Packer Size 6 3/4

TESTED FROM 3608 TO 3618 ANCHOR LENGTH 10 TOTAL DEPTH 3618 Hole Size 7 7/8

LEASE & WELL NO. Barnes Tract 2-29 FORMATION TESTED Arbuckle TEST NO. 5

Mud Weight 9.2 Viscosity 52 Water Loss 8.8 Chlorides - Pits 4,700 D.S.T. _____

Maximum Temp. 110 °F Initial Hydrostatic Pressure (A) 1749 P.S.I. Final Hydrostatic Pressure (H) 1660 P.S.I.

Tool Open I.F.P. from 7:50 pm to 7:55 pm 5 min

Tool Closed I.C.I.P. from 7:55 pm to 8:55 pm 60 min

Tool Open F.F.P. from 8:55 pm to 9:25 pm 30 min

Tool Closed F.C.I.P. from 9:25 pm to 10:25 pm 60 min

Initial Blow Strong Blow Bottom of Bucket in 1 1/2 min

Final Blow Fair Blow Bottom of Bucket in 12 min

Total Feet Recovered 50 Drilling mud Gravity of Oil _____ Corrected

50 Feet of Drilling mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks Slight plugging cleaned up 2nd open

Extra Equipment - Jars _____ Safety Joint Yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 3614 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 3615 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14333

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G HOLL COMPANY L.L.C
 TWP. 20 RGE. 14
 Lease & Well No. BARNES TRUST #2-29 Test #: 5 Date: 1-6-07 SEC. 29

Temperature / Pressure Data

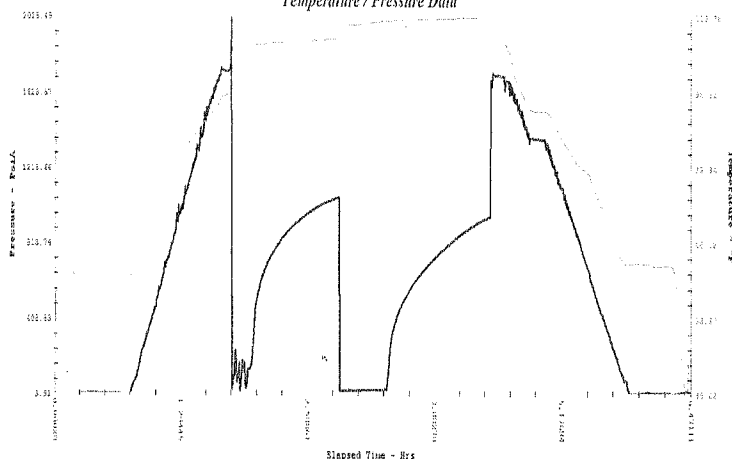

1	Initial Hydrostatic Pressure	1749
2	Initial Flow Pressure	30
3	Final Initial Flow Pressure	58
4	Initial Shut-In Pressure	1060
5	Initial Final Flow Pressure	23
6	Final Flow Pressure	29
7	Final Shut-In Pressure	958
8	Final Hydrostatic Pressure	1660

Maximum Temperature 110

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/6/07

LEASE AND WELL NUMBER BARNES TRUST #2-29

SECTION-TOWN-RANGE 29-20-14W

FORMATION TESTED ARBUCKLE

STATE KANSAS

DRILL STEM TEST NUMBER 5

COUNTY BARTON

REPORT NUMBER 14333

ELEVATION GROUND LEVEL 1899

ELEVATION KELLY BUSHINGS 1907

COMPANY REPRESENTATIVE RENE

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3608

TOP PACKER DEPTH 3603

TEST INTERVAL (to) 3618

BOTTOM PACKER DEPTH 3608

ANCHOR LENGTH 10

NUMBER OF PACKERS 2

TOTAL DEPTH (ft) 3618

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 7:50P

TOOL OPEN (from) 8:55

INITIAL OPEN TOOL OPEN (to) 7:55

FINAL OPEN TOOL OPEN (to) 9:25

DURATION (min.) 5

DURATION (min.) 30

TOOL CLOSED (from) 7:55

TOOL CLOSED (from) 9:25

INITIAL SHUT-IN TOOL CLOSED (to) 8:55

FINAL SHUT-IN TOOL CLOSED (to) 10:25P

DURATION (min.) 60

DURATION (min.) 60

INITIAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 1 1/2 MIN

FINAL FLOW

FAIR BLOW BOTTOM OF BUCKET IN 12 MIN

Feet of Recovery		RESISTIVITY	AT	DEGREES	CHLORIDES			
		RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER
1)	50	DRILLING MUD						
2)								
3)								
4)								
5)								

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/6/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	5
STATE	KANSAS	REPORT NUMBER	14333
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1907
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	20 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3614	BOTTOM RECORDER DEPTH	3615
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG # 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3579	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	52
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	4,700
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

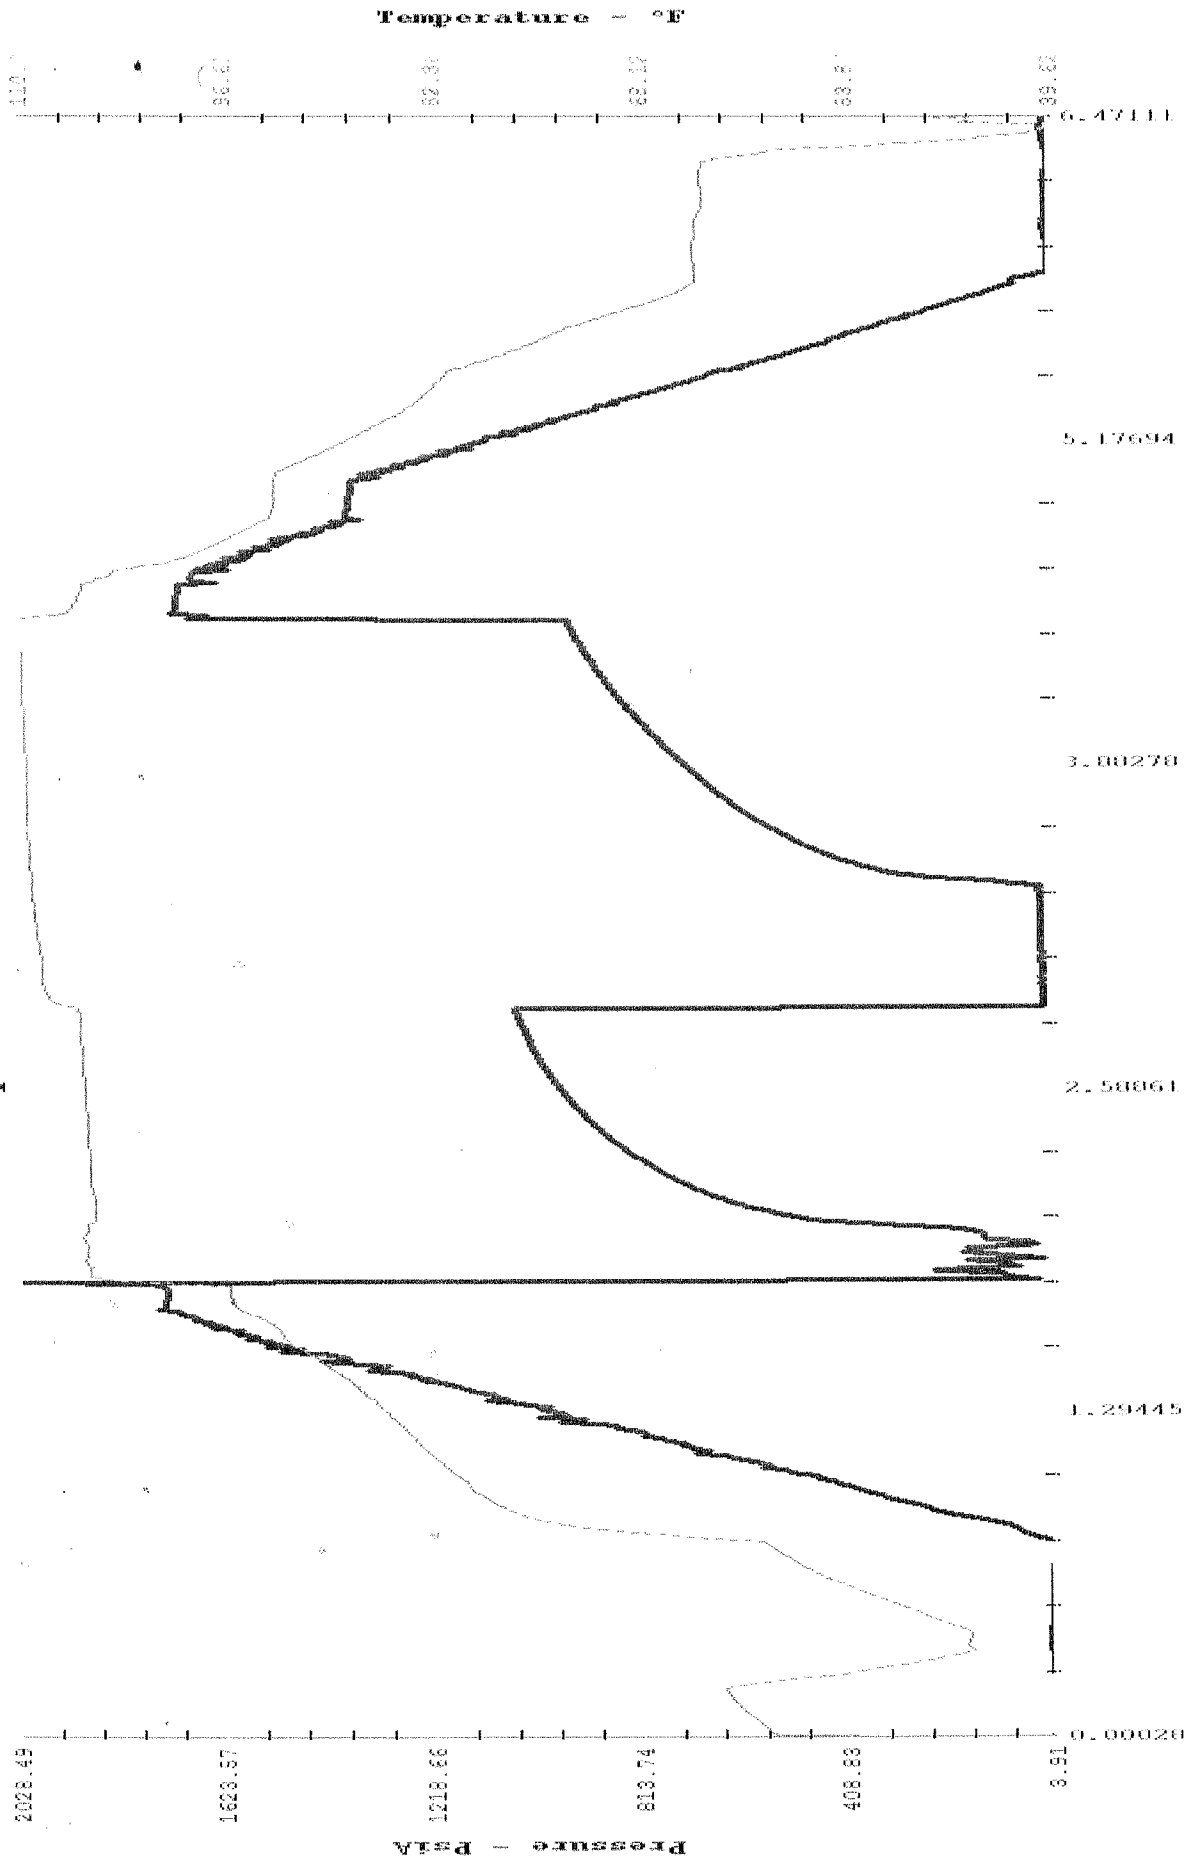

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

1907KB

Date 1-7-06 Location 29-20-14W Elevation 1899 County Barton

Company F. & Hall Company LLC Number of Copies 5

Charts Mailed to 9431 E Central suite #100 Wichita KS 67206

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 3579 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 3613 Bottom Packer Depth 3618 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3618 TO 3628 ANCHOR LENGTH 10 TOTAL DEPTH 3628 Hole Size 7 1/8

LEASE & WELL NO. Barnes Trust #2-29 FORMATION TESTED Airbuckle TEST NO. 6

Mud Weight 9.2 Viscosity 60 Water Loss 8.8 Chlorides - Pits 4200 D.S.T. _____

Maximum Temp. 104 °F Initial Hydrostatic Pressure (A) 1759 P.S.I. Final Hydrostatic Pressure (H) 1752 P.S.I.

Tool Open I.F.P. from 8:51 m to 9:06 m 15 min

Tool Closed I.C.I.P. from 9:06 m to 9:36 m 30 min

Tool Open F.F.P. from 9:36 m to 10:06 m 30 min

Tool Closed F.C.I.P. from 10:06 m to 11:06 m 60 min

Initial Blow Strong Blow Bottom of Bucket in 5 min

Final Blow Fair Blow Bottom of Bucket in 16 min

Total Feet Recovered 35 feet Drilling mud Gravity of Oil _____ Corrected _____

35 Feet of Drilling mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronic Depth 3624 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 3625 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14334


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

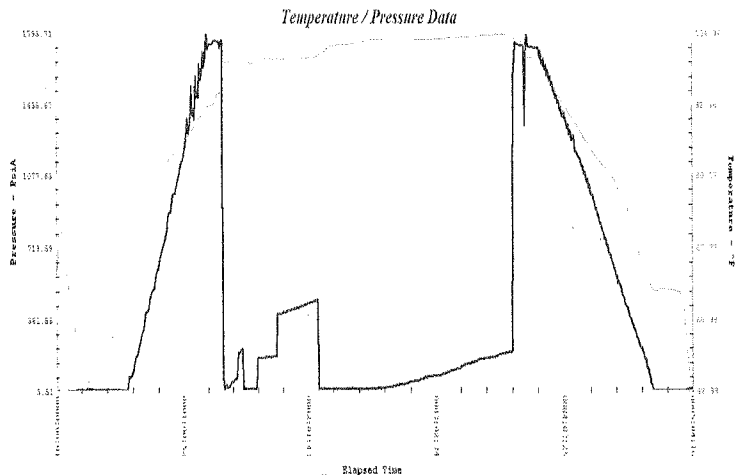

1	Initial Hydrostatic Pressure	1759
2	Initial Flow Pressure	73
3	Final Initial Flow Pressure	178
4	Initial Shut-In Pressure	459
5	Initial Final Flow Pressure	16
6	Final Flow Pressure	19
7	Final Shut-In Pressure	204
8	Final Hydrostatic Pressure	1752

Maximum Temperature 104

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/7/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE

LEASE AND WELL NUMBER BARNES TRUST #2-29

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 6

REPORT NUMBER 14334

ELEVATION KELLY BUSHINGS 1907

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3618

TEST INTERVAL (to) 3628

ANCHOR LENGTH 10

TOTAL DEPTH (ft) 3628

TOP PACKER DEPTH 3613

BOTTOM PACKER DEPTH 3618

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 8:51A

INITIAL OPEN

TOOL OPEN (to) 9:06

FINAL OPEN

TOOL OPEN (from) 9:36

TOOL OPEN (to) 10:06

DURATION (min.) 15

DURATION (min.) 30

TOOL CLOSED (from) 9:06

INITIAL SHUT-IN

TOOL CLOSED (to) 9:36

FINAL SHUT-IN

TOOL CLOSED (from) 10:06

TOOL CLOSED (to) 11:06A

DURATION (min.) 30

DURATION (min.) 60

INITIAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 5 MIN

FINAL FLOW

FAIR BLOW BOTTOM OF BUCKET IN 16 MIN

Feet of Recovery	RESISTIVITY	AT	DEGREES	CHLORIDES			
	RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER
1) 35	DRILLING MUD						
2)							
3)							
4)							
5)							

TWP. 20 RGE. 14

Company: F.G HOLL COMPANY L.L.C

Lease & Well No. BARNES TRUST #2-29 Test #: 6 Date: 1-7-07 SEC. 29

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/7/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	6
STATE	KANSAS	REPORT NUMBER	14334
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1907
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	20 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3624	BOTTOM RECORDER DEPTH	3625
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3579	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	60
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	4,000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

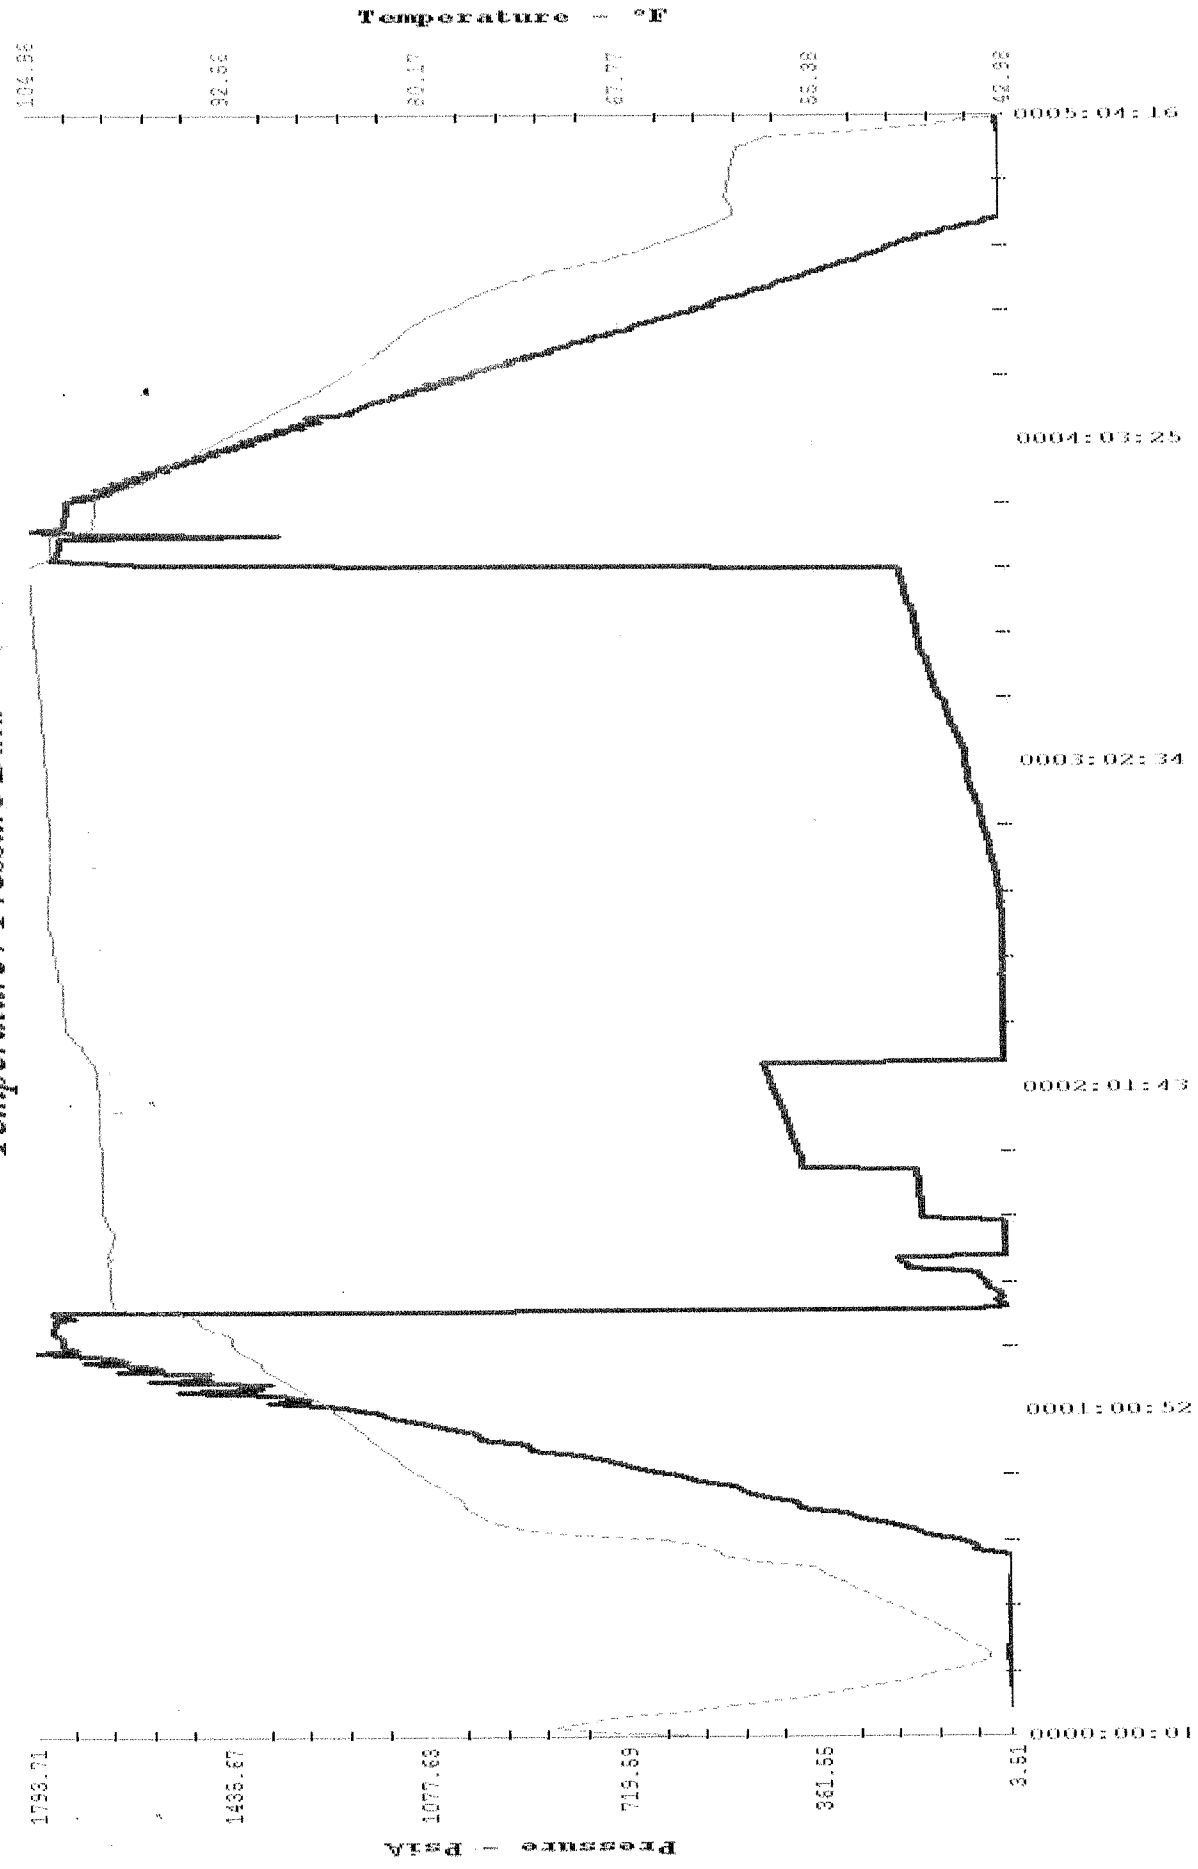

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

1907 KB

Date 1-8-06 Location 29-20-14W Elevation 1899 County Barton

Company F. G. Hall Company LLC Number of Copies 5

Charts Mailed to 9431 E Central Suite #100 Wichita KS 67206

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 3579 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 3615 Bottom Packer Depth 3620 Number of Packers _____ Packer Size 6 3/4

TESTED FROM 3620 TO 3638 ANCHOR LENGTH 18 TOTAL DEPTH 3638 Hole Size 7 7/8

LEASE & WELL NO. Barnes Trust #2-29 FORMATION TESTED Arbuckle TEST NO. 7

Mud Weight 9.0 Viscosity 54 Water Loss 8.8 Chlorides - Pits 5500 D.S.T. _____

Maximum Temp. 106 °F Initial Hydrostatic Pressure (A) 1785 P.S.I. Final Hydrostatic Pressure (H) 1720 P.S.I.

Tool Open I.F.P. from 12:15 A m to 12:30 A m 15 min

Tool Closed I.C.I.P. from 12:30 A m to 1:00 A m 30 min

Tool Open F.F.P. from 1:00 A m to 1:45 A m 45 min

Tool Closed F.C.I.P. from 1:45 A m to 3:15 A m 90 min

Initial Blow Strong Blow Bottom of Bucket in 3min

Final Blow Strong Blow Bottom of Bucket in 3min

Total Feet Recovered 65 feet Gravity of Oil _____ Corrected _____

65 Feet of Slightly oil cut mud % Gas 15 % Oil 85 % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint yes Extra Packer x Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronia Depth 3634 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 3635 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14335

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G HOLL COMPANY L.L.C
 TWP. 20 RGE. 14
 Lease & Well No. BARNES TRUST #2-29 Test #: 7 Date: 1-8-07 SEC. 29

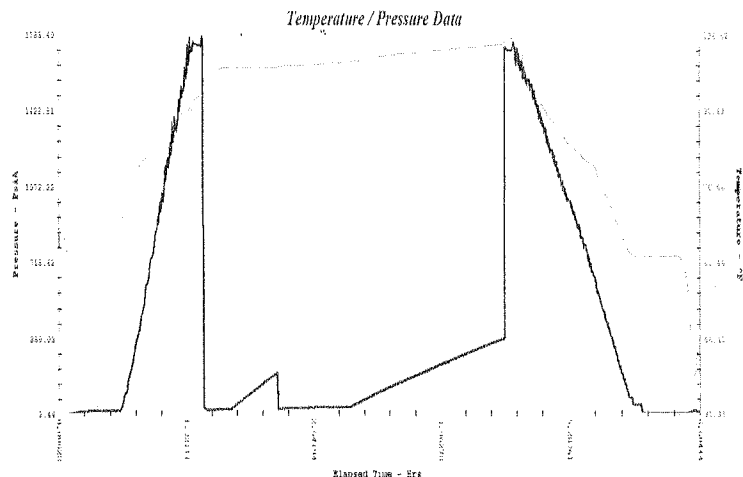

1	Initial Hydrostatic Pressure	1785
2	Initial Flow Pressure	24
3	Final Initial Flow Pressure	28
4	Initial Shut-In Pressure	197
5	Initial Final Flow Pressure	29
6	Final Flow Pressure	36
7	Final Shut-In Pressure	362
8	Final Hydrostatic Pressure	1720

Maximum Temperature 106

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/8/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE

LEASE AND WELL NUMBER BARNES TRUST #2-29

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 7

REPORT NUMBER 14335

ELEVATION KELLY BUSHINGS 1907

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3620

TEST INTERVAL (to) 3638

ANCHOR LENGTH 18

TOTAL DEPTH (ft) 3638

TOP PACKER DEPTH 3615

BOTTOM PACKER DEPTH 3620

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 12:15A

INITIAL OPEN TOOL OPEN (to) 12:30

DURATION (min.) 15

TOOL CLOSED (from) 12:30

INITIAL SHUT-IN TOOL CLOSED (to) 1:00

DURATION (min.) 30

TOOL OPEN (from) 1:00

FINAL OPEN TOOL OPEN (to) 1:45

DURATION (min.) 45

TOOL CLOSED (from) 1:45

FINAL SHUT-IN TOOL CLOSED (to) 3:15A

DURATION (min.) 90

INITIAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 3 MIN

FINAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 3 MIN

Feet of Recovery	RESISTIVITY	AT	DEGREES	CHLORIDES				
	RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER	
1) 65	SLIGHTLEY OIL CUT MUD				15	85		
2)								
3)								
4)								
5)								

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/8/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	7
STATE	KANSAS	REPORT NUMBER	14335
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1907
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	20 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	3634	BOTTOM RECORDER DEPTH	3635
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3579	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9
WEIGHT PIPE I.D.	2.25	VISCOSITY	54
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	5,500
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

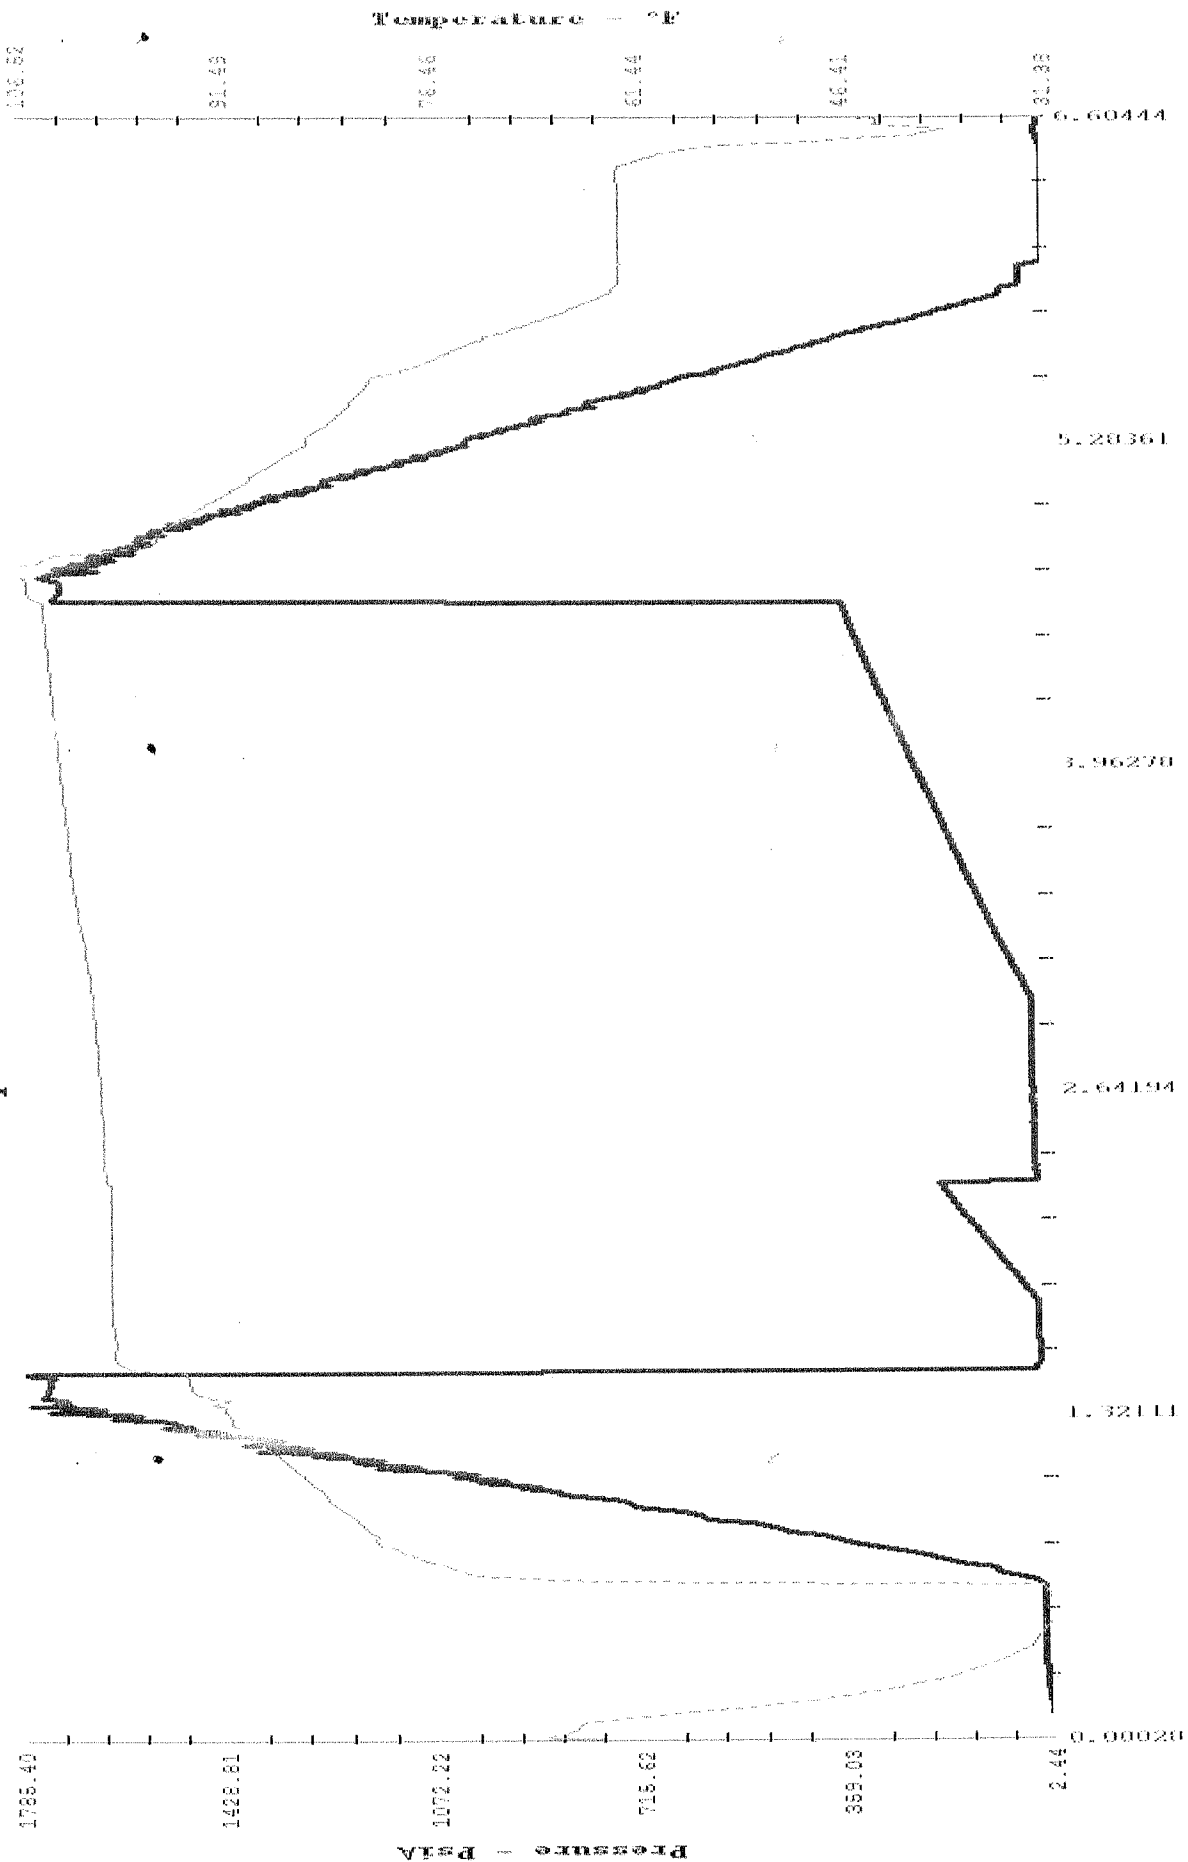

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

1907

Date 1-8-06 Location 29-20-14W Elevation 1899 County Barton

Company F.6 Hall Company LLC Number of Copies 5

Charts Mailed to 9431 E Central Suite #100 Wichita KS 67206

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 3579 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 3634 Bottom Packer Depth 3639 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3639 TO 3649 ANCHOR LENGTH 10 TOTAL DEPTH 3649 Hole Size 7 7/8

LEASE & WELL NO. Barnes Trst #229 FORMATION TESTED Airbuckle TEST NO. 8

Mud Weight 9.1 Viscosity 58 Water Loss 8.8 Chlorides - Pits \$100 D.S.T. _____

Maximum Temp. 105 °F Initial Hydrostatic Pressure (A) 1792 P.S.I. Final Hydrostatic Pressure (H) 1722 P.S.I.

Tool Open I.F.P. from 2:04 p m to 2:34 p m 30 min

Tool Closed I.C.I.P. from 2:34 p m to 3:34 p m 60 min

Tool Open F.F.P. from 3:34 p m to 4:19 p m 45 min

Tool Closed F.C.I.P. from 4:19 p m to 5:49 p m 90 min

Initial Blow Fair Blow Built 1 1/2 off Bottom of Bucket in 30 min

Final Blow Fair Blow Built 2 1/2 inches off bottom of Bucket in 45 min

Total Feet Recovered 50 feet Gravity of Oil _____ Corrected _____

50 Feet of Slightly oil cut mud % Gas 10 % Oil 90 % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint Yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronia Depth 3645 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 4744 Depth 3646 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14336


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

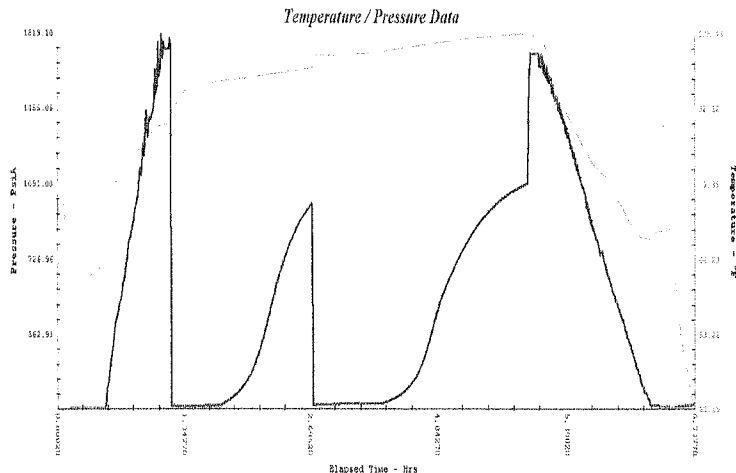

1	Initial Hydrostatic Pressure	1792
2	Initial Flow Pressure	12
3	Final Initial Flow Pressure	13
4	Initial Shut-In Pressure	994
5	Initial Final Flow Pressure	14
6	Final Flow Pressure	26
7	Final Shut-In Pressure	1092
8	Final Hydrostatic Pressure	1722

Maximum Temperature 105

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/8/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE

LEASE AND WELL NUMBER BARNES TRUST #2-29

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 8

REPORT NUMBER 14336

ELEVATION KELLY BUSHINGS 1907

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3639

TEST INTERVAL (to) 3649

ANCHOR LENGTH 10

TOTAL DEPTH (ft) 3649

TOP PACKER DEPTH 3634

BOTTOM PACKER DEPTH 3639

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 2:04P

INITIAL OPEN TOOL OPEN (to) 2:34

DURATION (min.) 30

TOOL CLOSED (from) 2:34

INITIAL SHUT-IN TOOL CLOSED (to) 3:34

DURATION (min.) 60

TOOL OPEN (from) 3:34

FINAL OPEN TOOL OPEN (to) 4:19

DURATION (min.) 45

TOOL CLOSED (from) 4:19

FINAL SHUT-IN TOOL CLOSED (to) 5:49

DURATION (min.) 90

INITIAL FLOW

FAIR BLOW BUILT 1 1/2 INCHS OFF BOTTOM OF BUCKET IN 30 MIN

FINAL FLOW

FAIR BLOW BUILT 2 1/2 INCHS OFF BOTTOM OF BUCKET IN 45 MIN

Feet of Recovery	RESISTIVITY	AT	DEGREES	CHLORIDES				
	RECOVERY DESCRIPTION			% GAS	% OIL	% MUD	% WATER	
1) 50	SLIGHTLEY OIL CUT MUD				10	90		
2)								
3)								
4)								
5)								

Company: F.G HOLL COMPANY L.L.C
TWP. 20 RGE. 14
Lease & Well No. BARNES TRUST #2-29 Test #: 8 Date: 1-8-07 SEC. 29

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/8/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	8
STATE	KANSAS	REPORT NUMBER	14336
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1907
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	20 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	3646	BOTTOM RECORDER DEPTH	3647
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3579	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	58
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	5,100
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

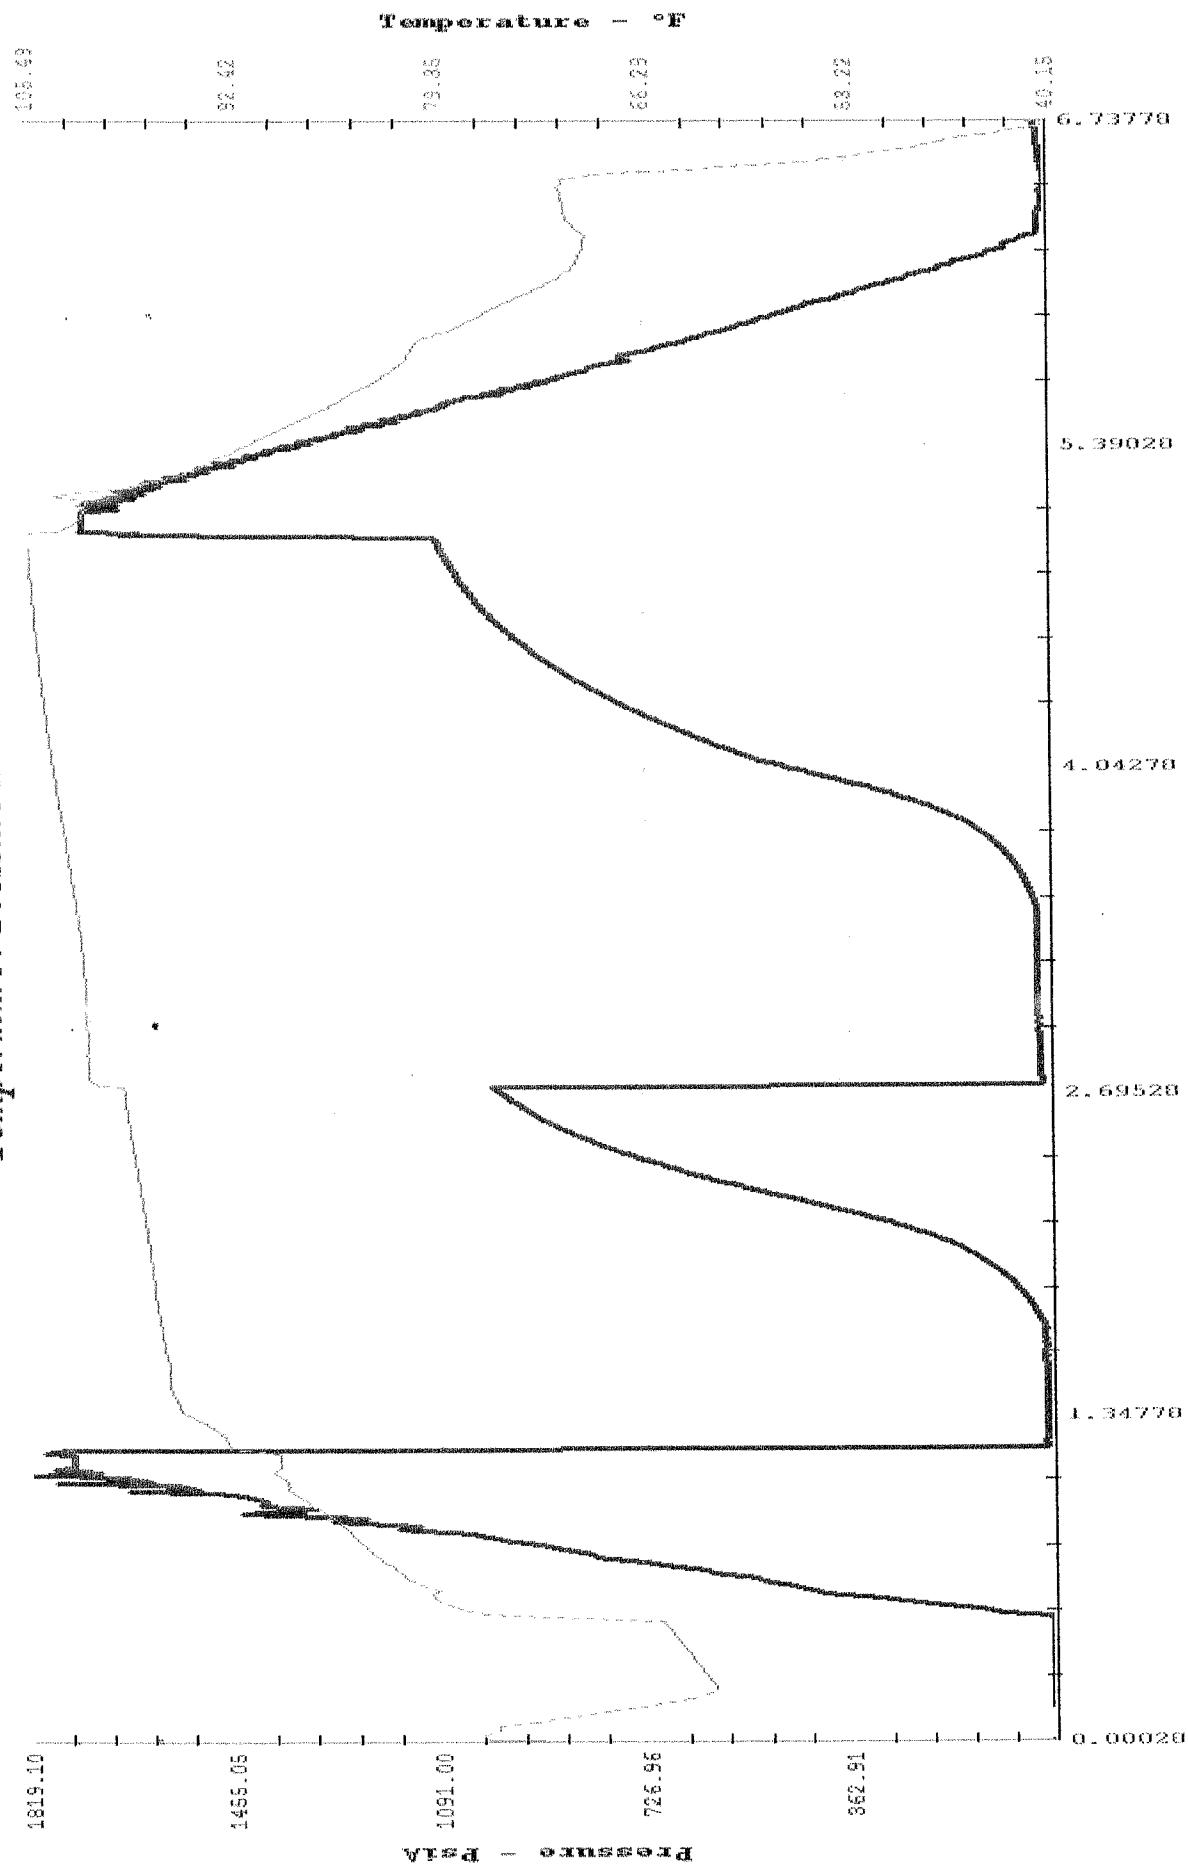

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-9-07 Location 29-20-14W Elevation 1899 County Barton

Company F.O. Hall Company LLC Number of Copies 5

Charts Mailed to 9431 E Central Suite #100

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 3628 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 3644 Bottom Packer Depth 3649 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3649 TO 3659 ANCHOR LENGTH 10 TOTAL DEPTH 3659 Hole Size 7 7/8

LEASE & WELL NO. Barnes Trust #2-29 FORMATION TESTED Arkville TEST NO. 9

Mud Weight 9.1 Viscosity 58 Water Loss 8.8 Chlorides - Pits 5100 D.S.T. 39,000

Maximum Temp. 114 °F Initial Hydrostatic Pressure (A) 1866 P.S.I. Final Hydrostatic Pressure (H) 1745 P.S.I.

Tool Open I.F.P. from 5:12 m to 5:27 a m 15 min

Tool Closed I.C.I.P. from 5:27 a m to 6:27 a m 60 min

Tool Open F.F.P. from 6:27 a m to 6:57 a m 30 min

Tool Closed F.C.I.P. from 6:57 a m to 7:57 a m 60 min

Initial Blow Fair Blow Bu. It 2 in. off Bottom of Bucket in 15 m

Final Blow Fair Blow Bu. It Bottom of Bucket in 23 m

Total Feet Recovered 150 Gravity of Oil _____ Corrected _____

30 Feet of mud cut water % Gas _____ % Oil 70 % Mud 30 % Water

60 Feet of mud cut water % Gas _____ % Oil 50 % Mud 50 % Water

60 Feet of mud cut water % Gas _____ % Oil 10 % Mud 90 % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of Chlorides 30,000 % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars _____ Safety Joint yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Election ca Depth 3655 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3068 Clock No. 47441 Depth 3656 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14337

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT


GREAT BEND, KANSAS 67530

TWP. 20 RGE. 14

Company: F.G HOLL COMPANY L.L.C

Lease & Well No. BARNES TRUST #2-29 Test #: 9 Date: 1-9-07 SEC. 29

Temperature / Pressure Data

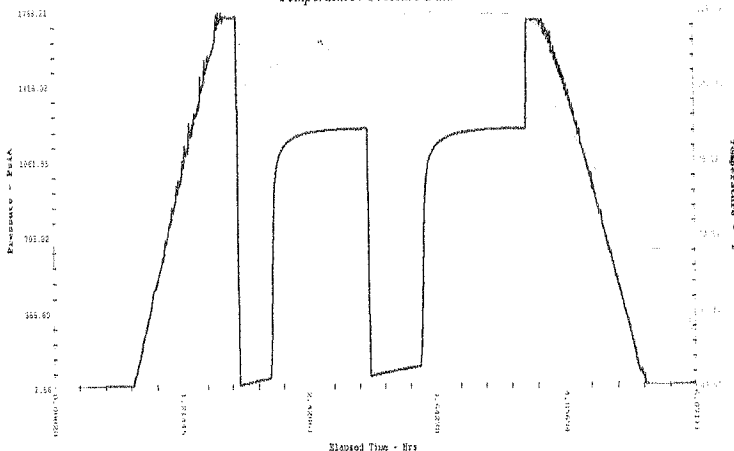

1	Initial Hydrostatic Pressure	1745
2	Initial Flow Pressure	15
3	Final Initial Flow Pressure	47
4	Initial Shut-In Pressure	1216
5	Initial Final Flow Pressure	50
6	Final Flow Pressure	102
7	Final Shut-In Pressure	1216
8	Final Hydrostatic Pressure	1726

Maximum Temperature 114

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/9/07

SECTION-TOWN-RANGE 29-20-14W

STATE KANSAS

COUNTY BARTON

ELEVATION GROUND LEVEL 1899

COMPANY REPRESENTATIVE RENE

LEASE AND WELL NUMBER BARNES TRUST #2-29

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 9

REPORT NUMBER 14337

ELEVATION KELLY BUSHINGS 1907

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3649

TEST INTERVAL (to) 3659

ANCHOR LENGTH 10

TOTAL DEPTH (ft) 3659

TOP PACKER DEPTH 3644

BOTTOM PACKER DEPTH 3649

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:12A

INITIAL OPEN

TOOL OPEN (to) 5:27

FINAL OPEN

DURATION (min.) 15

TOOL OPEN (from) 6:27

TOOL OPEN (to) 6:57

DURATION (min.) 30

TOOL CLOSED (from) 5:27

INITIAL SHUT-IN TOOL CLOSED (to) 6:27

DURATION (min.) 60

TOOL CLOSED (from) 6:57

FINAL SHUT-IN TOOL CLOSED (to) 7:57A

DURATION (min.) 60

INITIAL FLOW

FAIR BLOW BUILT 2 INCHS OFF BOTTOM OF BUCKET IN 15 MIN

FINAL FLOW

FAIR BLOW BOTTOM OF BUCKET IN 23 MIN

Feet of Recovery	RESISTIVITY AT DEGREES		CHLORIDES			
	RECOVERY DESCRIPTION		% GAS	% OIL	% MUD	% WATER
1) 30	mud cut water				70	30
2) 60	mud cut water				50	50
3) 60	mud cut water				10	90
4)						
5)	30,000 CHLORIDES					

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	BARNES TRUST #2-29
TEST DATE	1/9/07	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	29-20-14W	DRILL STEM TEST NUMBER	9
STATE	KANSAS	REPORT NUMBER	14337
COUNTY	BARTON	ELEVATION KELLY BUSHINGS	1907
ELEVATION GROUND LEVEL	1899	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	RENE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	20 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3655	BOTTOM RECORDER DEPTH	3656
RECORDER NUMBER	91971	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3628	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	58
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	5,100
		CHLORIDES-DST	30,000

COMMENTS

Temperature / Pressure Data

