

F.G. Hall Co.
Apley Trust 1-30

30-21s-15w
15-145-21534

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 12-28-05 Location 30-21-15 Elevation 1961 County Pawnee
Company F.G. Hall Company LLC Number of Copies 5
Charts Mailed to 943/E Central St #100 Wichita KS 67206
Drilling Contractor Duke Drilling Company Rig #8
Length Drill Pipe 1907 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH
Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____
Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____
Top Packer Depth 1887 Bottom Packer Depth 1892 Number of Packers 2 Packer Size 6 3/4
TESTED FROM 1892 TO 1960 ANCHOR LENGTH 68 TOTAL DEPTH 1960 Hole Size 7 7/8
LEASE & WELL NO. Apley Trust 1-30 FORMATION TESTED Harrington TEST NO. 1
Mud Weight 8.6 Viscosity 42 Water Loss 8.0 Chlorides - Pits 8200 D.S.T. 23,000
Maximum Temp. 78 °F Initial Hydrostatic Pressure (A) 936 P.S.I. Final Hydrostatic Pressure (H) 850 P.S.I.

Tool Open I.F.P. from 5:08 p.m. to 5:14 p.m. 6 min
Tool Closed I.C.I.P. from 5:14 p.m. to 5:44 p.m. 30 min
Tool Open F.F.P. from 5:44 p.m. to 6:29 p.m. 45 min
Tool Closed F.C.I.P. from 6:29 p.m. to 7:59 p.m. 90 min

from [B] <u>56</u> P.S.I. to [C] <u>59</u> P.S.I.
[D] <u>567</u> P.S.I.
from [E] <u>100</u> P.S.I. to [F] <u>104</u> P.S.I.
[G] <u>562</u> P.S.I.

Initial Blow Fair Blow Bottom Bracket in 6 min

Final Blow Strong Blow Bottom Bracket in 1 min

Total Feet Recovered 170 feet Total Gravity of Oil _____ Corrector _____

50 Feet of Mud cut water % Gas _____ % Oil 90 % Mud 10 % Water

120 Feet of Mud cut water % Gas _____ % Oil 95 % Mud 5 % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars yes Safety Joint yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronics Depth 1956 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3068 Clock No. 47441 Depth 1957 Insurance _____

Price of Job _____

Tool Operator Paul Baker

Approved By _____

No. 14700


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

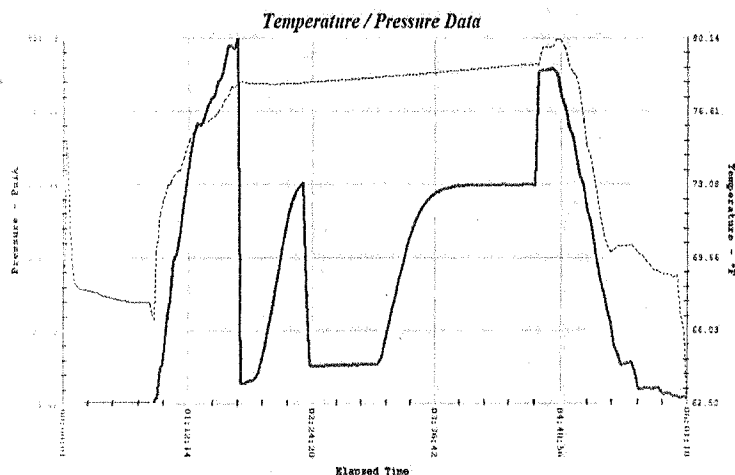

1	Initial Hydrostatic Pressure	936
2	Initial Flow Pressure	56
3	Final Initial Flow Pressure	59
4	Initial Shut-In Pressure	567
5	Initial Final Flow Pressure	100
6	Final Flow Pressure	104
7	Final Shut-In Pressure	562
8	Final Hydrostatic Pressure	850

Maximum Temperature 78

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 12/28/05

SECTION-TOWN-RANGE 30-21-15

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REA

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED HERRINGTON

DRILL STEM TEST NUMBER 1

REPORT NUMBER 14700

ELEVATION KELLY BUSHINGS 1969

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 1892

TEST INTERVAL (to) 1960

ANCHOR LENGTH 68

TOTAL DEPTH (ft) 1960

TOP PACKER DEPTH 1887

BOTTOM PACKER DEPTH 1892

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:08P

INITIAL OPEN

TOOL OPEN (to) 5:14

FINAL OPEN

TOOL OPEN (from) 5:44

TOOL OPEN (to) 6:29

DURATION (min.) 6

DURATION (min.) 45

TOOL CLOSED (from) 5:14

INITIAL SHUT-IN

TOOL CLOSED (to) 5:44

FINAL SHUT-IN

TOOL CLOSED (from) 6:29

TOOL CLOSED (to) 7:59P

DURATION (min.) 30

DURATION (min.) 90

INITIAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 6 MIN

FINAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 1 MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 50	MUD CUT WATER			90	10
2) 120	MUD CUT WATER			95	5
3)					
4)					
5)					
6)					

Company: F.G HOLL COMPANY L.L.C
TWP. 21 RGE. 15W

Lease & Well No. APLEY TRUSY 1-30


Test #: 1

Date: 12-28-05

SEC. 30

GREAT BEND, KANSAS 67530 (800) 792-6902

Temperature / Pressure Data

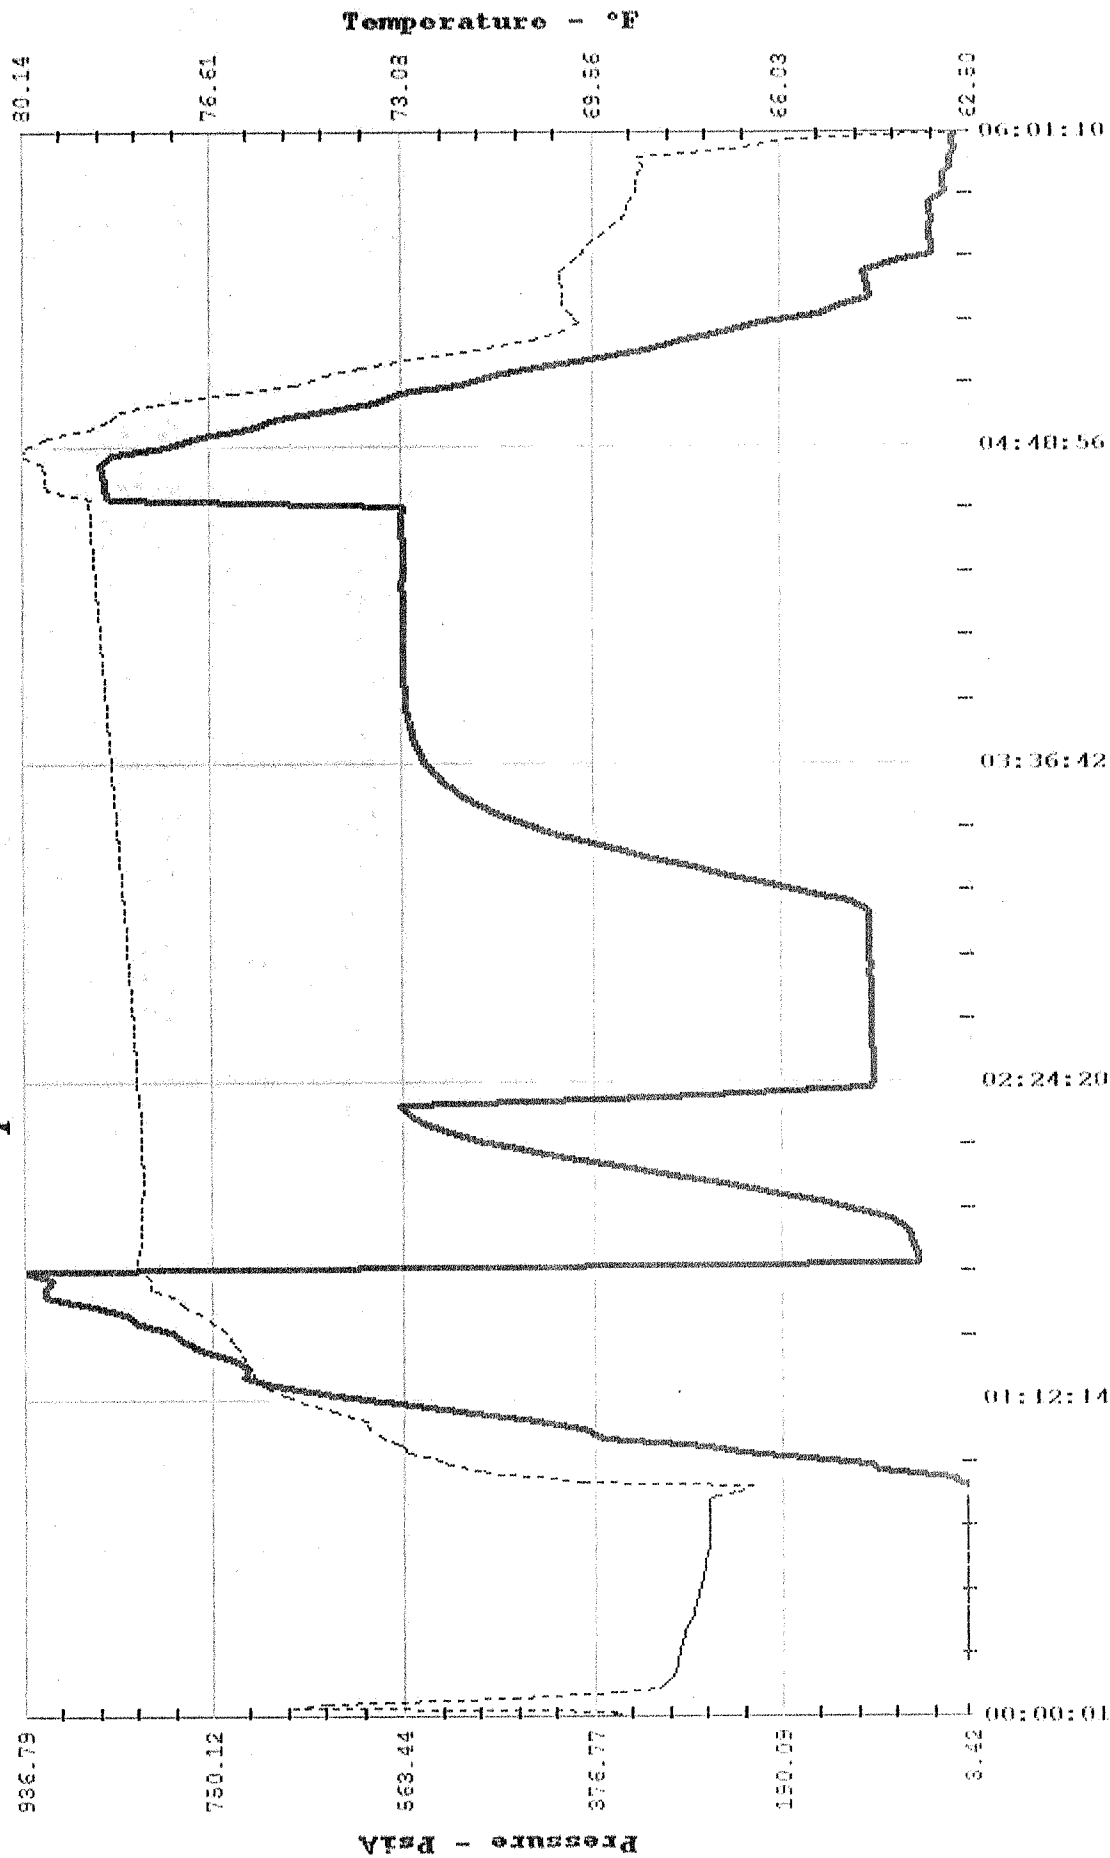

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

1969 KLB

Date 12-30-2005 Location 30-21^S-15^W Elevation 1961 County RAWNEE

Company F.G. Hall Company L.L.C. Number of Copies 5

Charts Mailed to 9431 East Central Suite 100 Wichita Kansas 67206-2543

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 2217 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2" X 14

Length Weight Pipe NONE I.D. Weight Pipe NONE Tool Joint Size NONE

Length Drill Collars NONE I.D. Drill Collars NONE Tool Joint Size NONE

Top Packer Depth 2238 Bottom Packer Depth 2243 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 2243 TO 2361 ANCHOR LENGTH 118 TOTAL DEPTH 2361 Hole Size 7 7/8

LEASE & WELL NO. APLEY TRUST #130 FORMATION TESTED BADER TEST NO. 2

Mud Weight 8.8 Viscosity 43 Water Loss 6.8 Chlorides - Pits 25000 D.S.T. 50,000

Maximum Temp. _____ °F Initial Hydrostatic Pressure (A) _____ P.S.I. Final Hydrostatic Pressure (H) _____ P.S.I.

Tool Open I.F.P. from 5:47 m to 5:52 m 5 min

Tool Closed I.C.I.P. from 5:52 m to 6:52 m 60 min

Tool Open F.F.P. from 6:52 m to 7:37 m 45 min

Tool Closed F.C.I.P. from 7:37 m to 9:09 m 90 min

Initial Blow OPEN 9:10 m to 9:13 m 3 min

Final Blow CLOSED 9:22 to 9:52 30

Total Feet Recovered 1st open Straddle Blow 2nd open Straddle Blow Gravity of Oil _____ Corrected

60 Feet of Gas cut watery mud % Gas 0 % Oil 70 % Mud 30 % Water

180 Feet of Gas cut watery mud 11 % Gas 0 % Oil 29 % Mud 10 % Water

120 Feet of Gas cut watery mud 5 % Gas 0 % Oil 75 % Mud 20 % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars YES Safety Joint YES Extra Packer NONE Straddle NONE Hook Wall NONE

Top Recorder No. 2308 Clock No. 9198 Depth 2356 Cir. Sub NONE Sampler NONE

Bottom Recorder No. 2359 Clock No. 4744 Depth 2359 Insurance NONE

Price of Job _____

Tool Operator Jared School

Approved By _____

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


Nº 14501

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

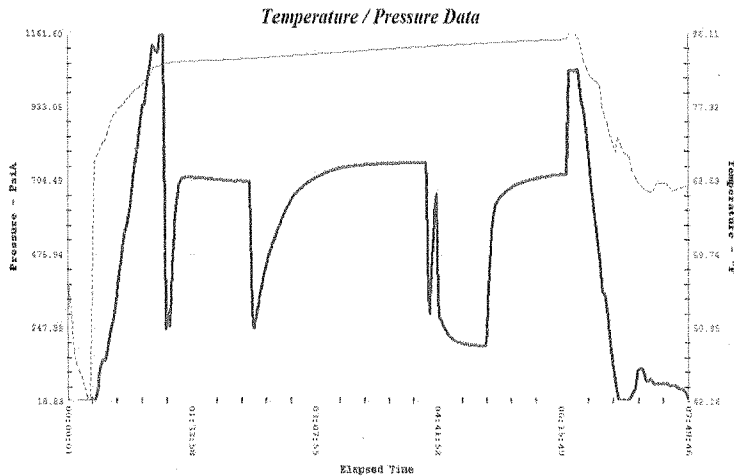

1	Initial Hydrostatic Pressure	1161
2	Initial Flow Pressure	242
3	Final Initial Flow Pressure	297
4	Initial Shut-In Pressure	703
5	Initial Final Flow Pressure	264
6	Final Flow Pressure	190
7	Final Shut-In Pressure	725
8	Final Hydrostatic Pressure	1048

Maximum Temperature 86

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 12/30/05

SECTION-TOWN-RANGE 30-21-15

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REA

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED HERRINGTON *BADGE*

DRILL STEM TEST NUMBER 2

REPORT NUMBER

ELEVATION KELLY BUSHINGS

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 2243

TEST INTERVAL (to) 2361

ANCHOR LENGTH 118

TOTAL DEPTH (ft) 2361

TOP PACKER DEPTH 2238

BOTTOM PACKER DEPTH 2243

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:47A

INITIAL OPEN TOOL OPEN (to) 5:52

DURATION (min.) 5

TOOL OPEN (from) 6:52 #2 9:10 OPEN

TOOL OPEN (to) 7:37 9:13 CLOSE

DURATION (min.) 45

TOOL CLOSED (from) 5:52

INITIAL SHUT-IN TOOL CLOSED (to) 6:52

DURATION (min.) 60

TOOL CLOSED (from) 7:37 9:22 OPEN

TOOL CLOSED (to) 9:07 9:52 CLOSE

DURATION (min.) 90 10:52 PULL

INITIAL FLOW

STRONG BLOW BOTTOM BUCKET IN 1 MIN

FINAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 1 MIN HOSE PLUGGED OPEN TOOL BACK UP AND HAD GAS TO SURFACE

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 60	GAS CUT MUDDY WATER			70	30
2) 180	GAS CUT MUDDY WATER	11		79	10
3) 120	GAS CUT MUDDY WATER	5		75	20
4)					
5)					
6)					

Company: F.G HOLL COMPANY L.L.C

TWP. 21 RGE. 15

Lease & Well No. APLEY TRUST 1-30 Test #: 2 Date: 12-30-05 SEC. 30

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST 1-30
TEST DATE	12/30/05	FORMATION TESTED	HERRINGTON
SECTION-TOWN-RANGE	30-21-15	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	
ELEVATION GROUND LEVEL	1961	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REA		

EXTRA EQUIPMENT

JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	40 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	2358	BOTTOM RECORDER DEPTH	2359
RECORDER NUMBER	91981	RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLINGRIG 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	2217	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	8.8
WEIGHT PIPE I.D.	2.25	VISCOSITY	43
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	6.8
		CHLORIDES-PITS	25,000
		CHLORIDES-DST	50,000

COMMENTS

RESISTIVITY .2

Temperature / Pressure Data

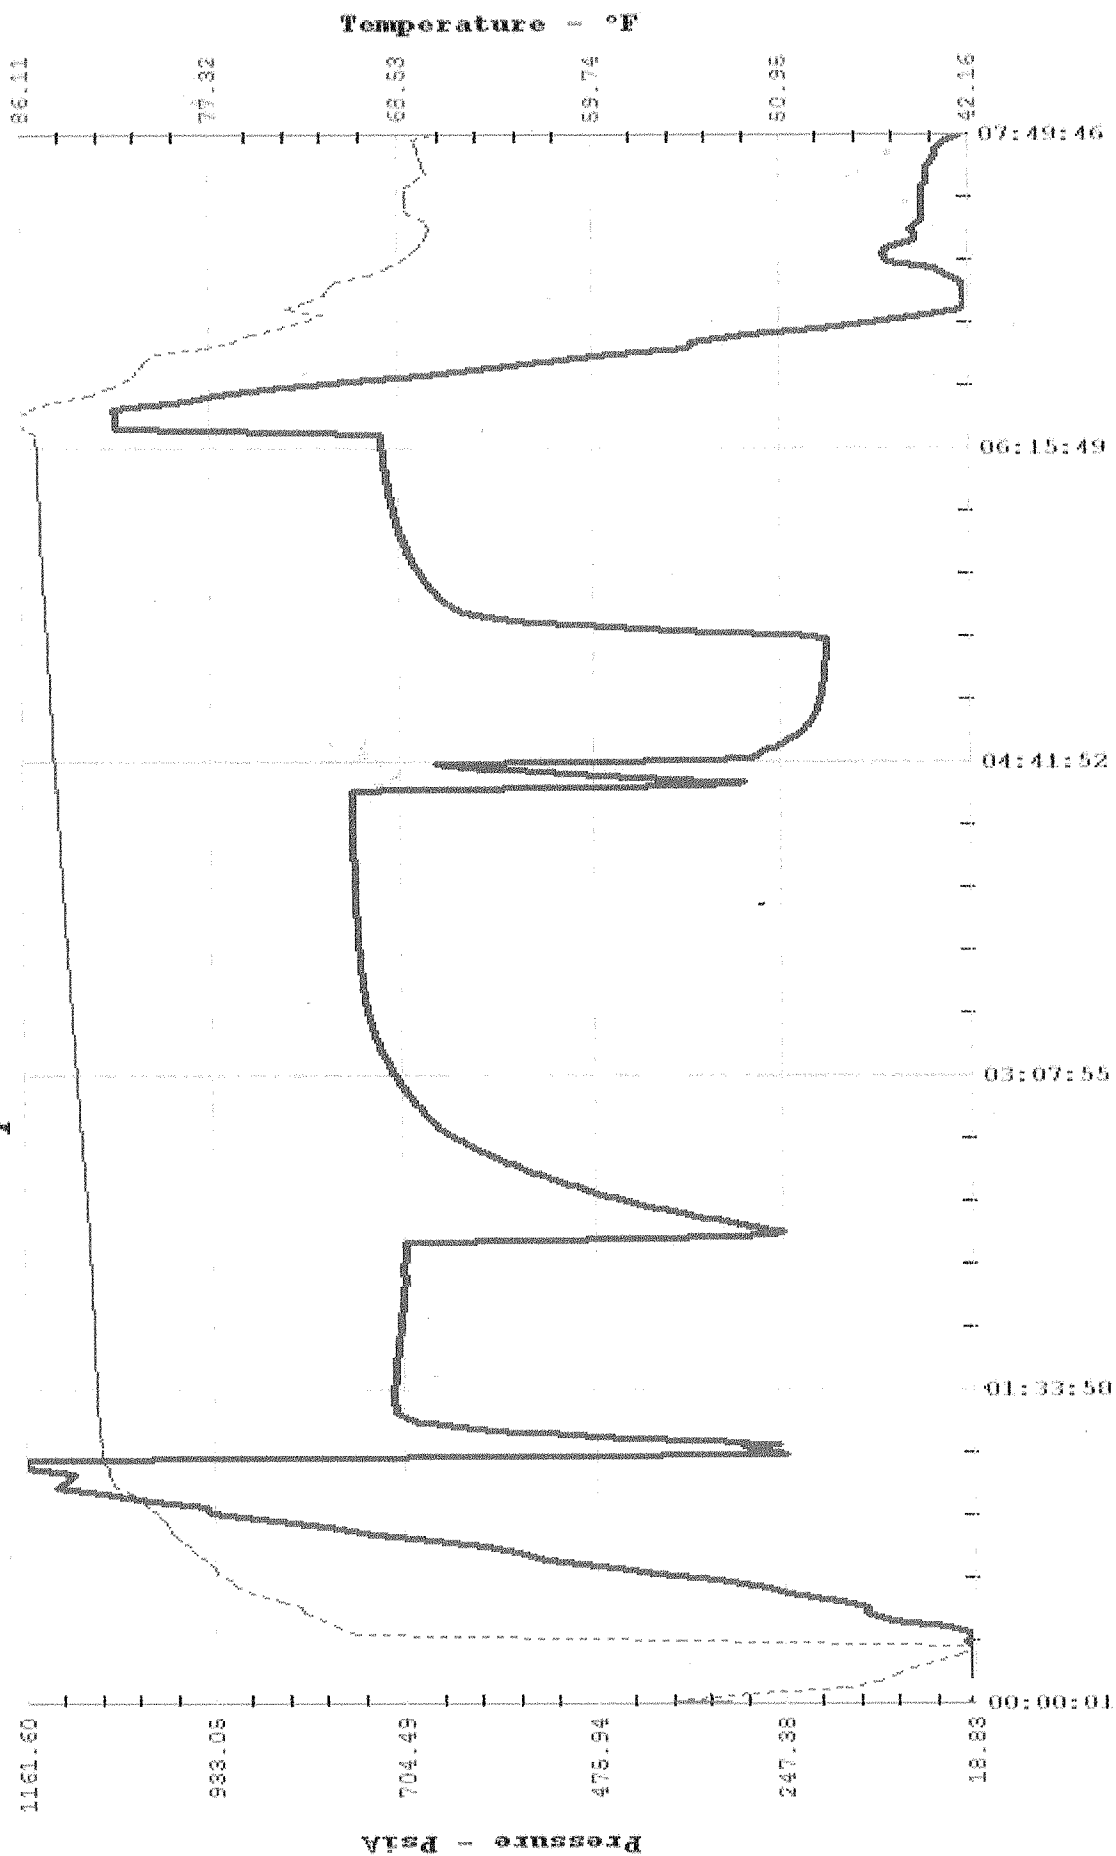

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 12-30-05 Location 30-21-15 Elevation 1961 County Pawnee

Company F.G. Holl Company LLC Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Drake Drilling #8

Length Drill Pipe 2390 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 X 1 1/4

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 2411 Bottom Packer Depth 2416 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 2416 TO 2458 ANCHOR LENGTH 42 TOTAL DEPTH 2458 Hole Size 7 1/8

LEASE & WELL NO. API-First 1-30 FORMATION TESTED Neva TEST NO. 3

Mud Weight 8.8 Viscosity 43 Water Loss 6.8 Chlorides - Pits 25,000 D.S.T. 43,000

Maximum Temp. 87 °F Initial Hydrostatic Pressure (A) 1213 P.S.I. Final Hydrostatic Pressure (H) 1178 P.S.I.

Tool Open I.F.P. from 12:10 A to 12:15 A 5 min

Tool Closed I.C.I.P. from 12:15 A to 12:45 A 30 min

Tool Open F.F.P. from 12:45 A to 12:50 A 5 min

Tool Closed F.C.I.P. from 12:50 A to 1:20 A 30 min

Initial Blow Weak Surface Blow Died off in 1 min

Final Blow Weak Surface Blow Died off

Total Feet Recovered 20 Drilling mrd Gravity of Oil _____ Corrected

20 Feet of Drilling mrd % Gas _____ % Oil 70 % Mud 30 % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks Resistivity 2

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 2454 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 2455 Insurance _____

Price of Job _____

Tool Operator Gap Smith

Approved By _____

NO 14526

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902


DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G HOLL COMPANY L.L.C
TWP. 21 RGE. 15

Lease & Well No. APLEY TRUST 1-30

Test #: 3 Date: 12-30-05 SEC. 30

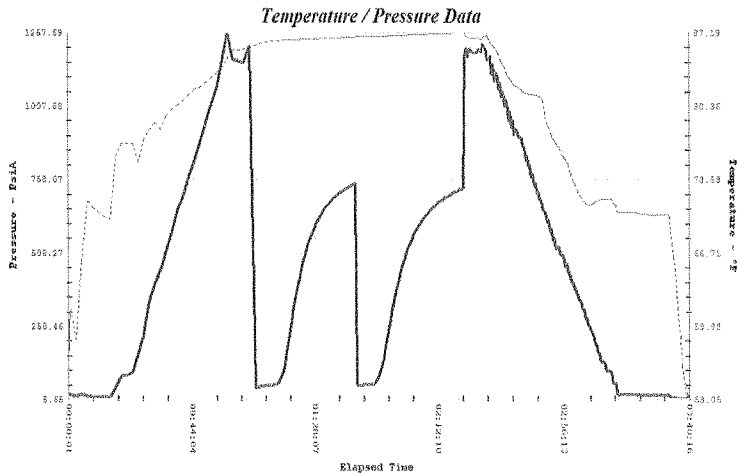

1	Initial Hydrostatic Pressure	1213
2	Initial Flow Pressure	47
3	Final Initial Flow Pressure	57
4	Initial Shut-In Pressure	742
5	Initial Final Flow Pressure	57
6	Final Flow Pressure	61
7	Final Shut-In Pressure	726
8	Final Hydrostatic Pressure	1178

Maximum Temperature 87

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 12/30/05

SECTION-TOWN-RANGE 30-21-15

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED NEVA

DRILL STEM TEST NUMBER 3

REPORT NUMBER 14526

ELEVATION KELLY BUSHINGS 1969

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 2416

TEST INTERVAL (to) 2458

ANCHOR LENGTH 42

TOTAL DEPTH (ft) 2458

TOP PACKER DEPTH 2411

BOTTOM PACKER DEPTH 2416

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 12:10A

INITIAL OPEN TOOL OPEN (to) 12:15

DURATION (min.) 5

FINAL OPEN

TOOL OPEN (from) 12:45A

TOOL OPEN (to) 12:50

DURATION (min.) 5

TOOL CLOSED (from) 12:15

INITIAL SHUT-IN TOOL CLOSED (to) 12:45

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 12:50

TOOL CLOSED (to) 1:20

DURATION (min.) 30

INITIAL FLOW

WEAK SURFACE BLOW DIED OFF AFTER 1 MIN

FINAL FLOW

WEAK SURFACE DIED OFF

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 20	MUDDY WATER			70	30
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	E.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST 1-30
TEST DATE	12/30/05	FORMATION TESTED	NEVA
SECTION-TOWN-RANGE	30-21-15	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	14526
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	1969
ELEVATION GROUND LEVEL	1961	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	40 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	2454	BOTTOM RECORDER DEPTH	2455
RECORDER NUMBER	91981	RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING COMPANY RIG 8		
DRILL PIPE LENGTH	2390	DRILL COLLAR LENGTH	
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	8.8
WEIGHT PIPE I.D.	2.25	VISCOSITY	43
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	6.8
		CHLORIDES-PITS	25,000
		CHLORIDES-DST	43,000

COMMENTS

Resistivity - 2

Temperature / Pressure Data

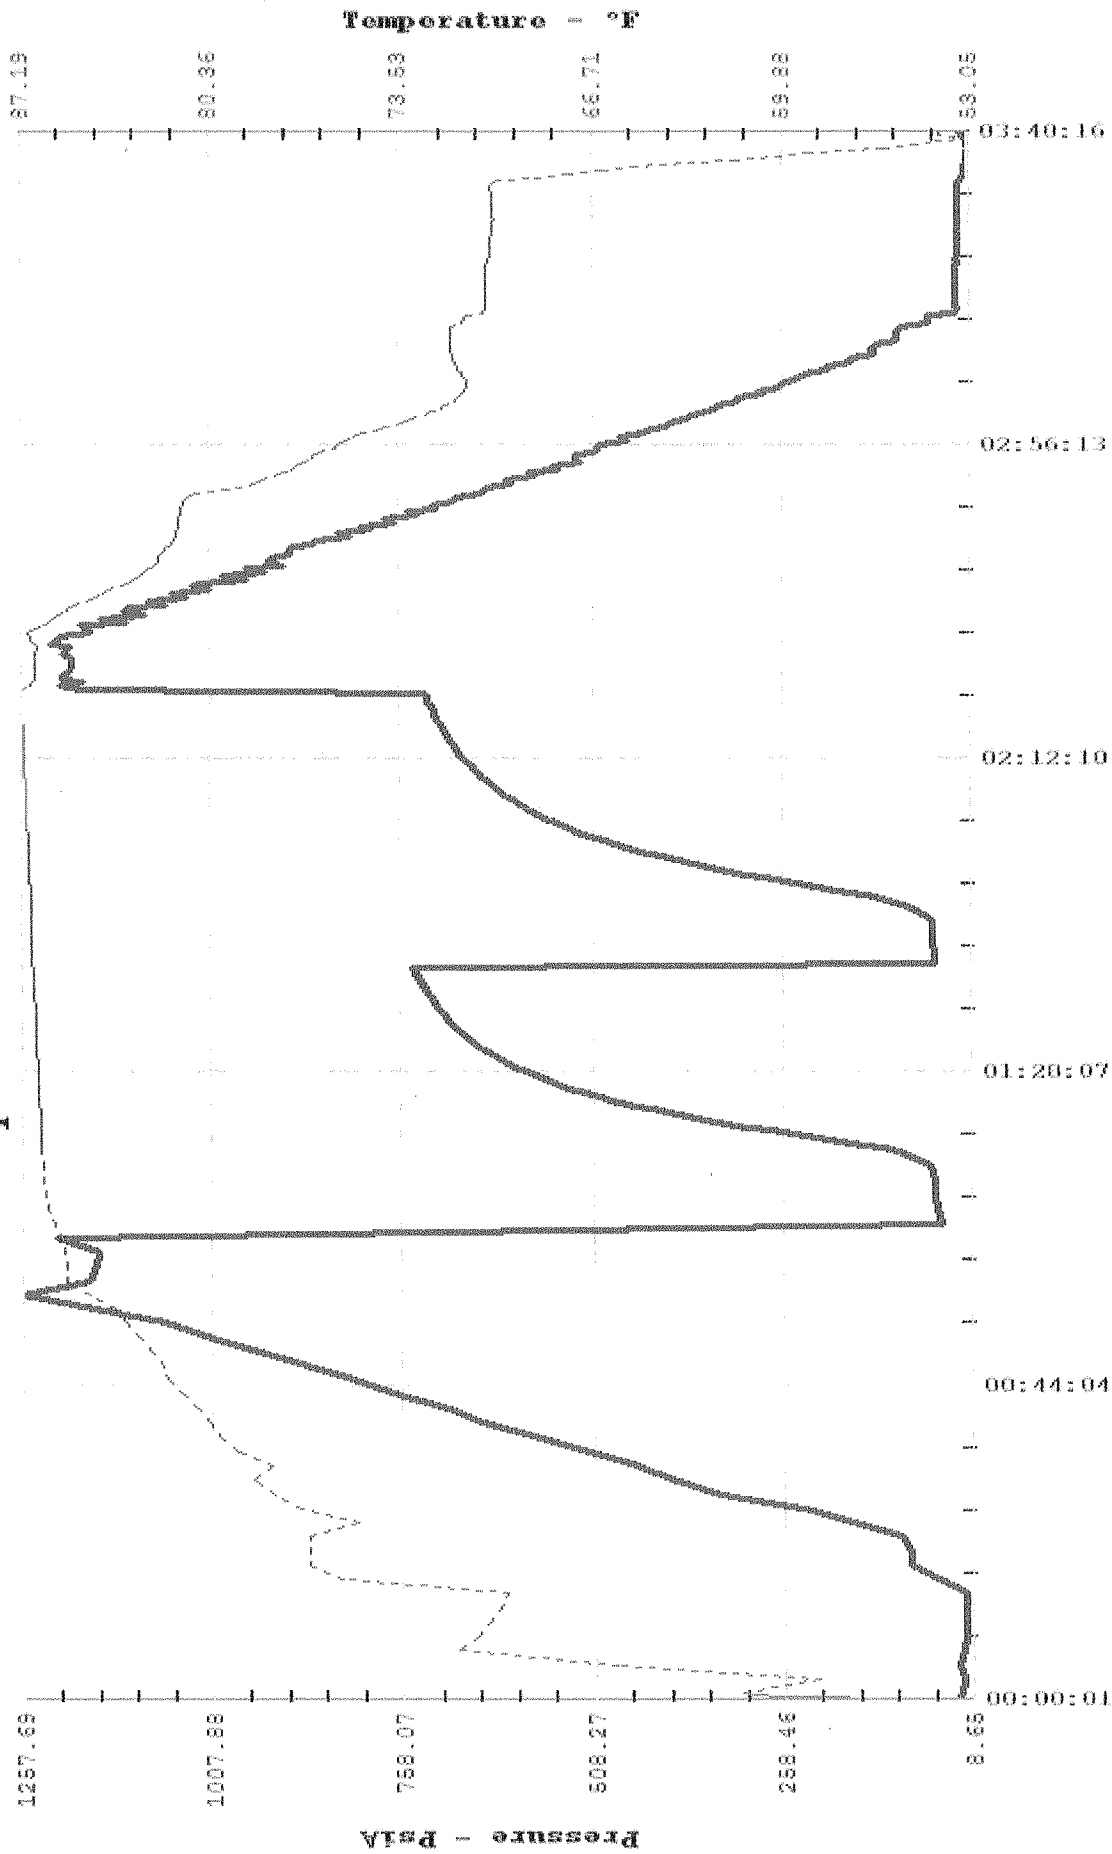

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 12-31-05 Location 30-21-15 Elevation 1961 County Pawnee

Company F.O. Hell Company L.C.C. Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Duke Drilling Rig #8

Length Drill Pipe 2506 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe NONE I.D. Weight Pipe NONE Tool Joint Size NONE

Length Drill Collars NONE I.D. Drill Collars NONE Tool Joint Size NONE

Top Packer Depth 2527 Bottom Packer Depth 2532 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 2532 TO 2596 ANCHOR LENGTH 64 TOTAL DEPTH 2596 Hole Size 7 7/8

LEASE & WELL NO. APLEY Trust 1-30 FORMATION TESTED four Acres TEST NO. 4

Mud Weight 8.8 Viscosity 44 Water Loss 8.8 Chlorides - Pits 23000 D.S.T.

Maximum Temp. 81 °F Initial Hydrostatic Pressure (A) 1187 P.S.I. Final Hydrostatic Pressure (H) 1183 P.S.I.

Tool Open I.F.P. from 5:30 p.m. to 5:45 p.m. 15 min

Tool Closed I.C.I.P. from 5:45 p.m. to 6:15 p.m. 30 min

Tool Open F.F.P. from 6:15 p.m. to 6:45 p.m. 30 min

Tool Closed F.C.I.P. from 6:45 p.m. to 7:15 p.m. 30 min

Initial Blow weak Blow 7 inches into Bucket in 10 m 5 min Plus

Final Blow weak building blow built to 10 inches into the water

Total Feet Recovered _____ Gravity of Oil _____ Corrected

<u>100</u> Feet of <u>Drilling Mud</u>	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water
Feet of	% Gas	% Oil	% Mud	% Water

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronic Depth 2592 Cir. Sub NONE Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 2593 Insurance NONE

Price of Job _____

Tool Operator Jared School

Approved By _____

No 14527

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G HOLL COMPANY L.L.C
TWP. 21 RGE. 15

Lease & Well No. APLEY TRUST 1-30 Test #: 4 Date: 12-31-05 SEC. 30

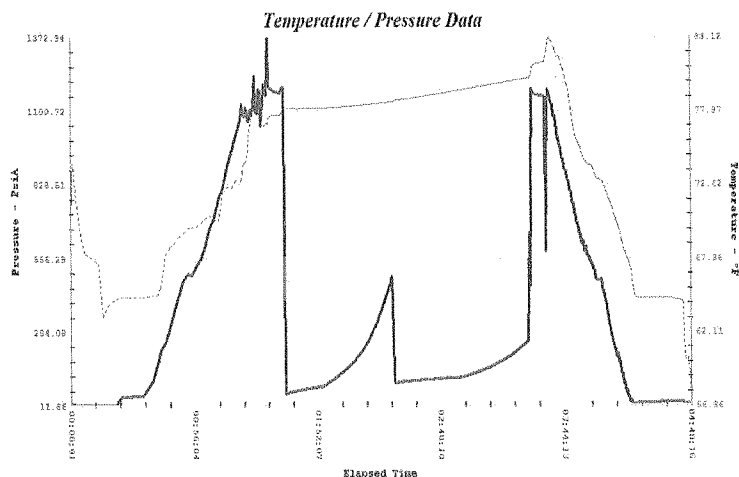

1	Initial Hydrostatic Pressure	1187
2	Initial Flow Pressure	55
3	Final Initial Flow Pressure	81
4	Initial Shut-In Pressure	488
5	Initial Final Flow Pressure	97
6	Final Flow Pressure	119
7	Final Shut-In Pressure	250
8	Final Hydrostatic Pressure	1183

Maximum Temperature 81

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 12/31/05

SECTION-TOWN-RANGE 30-21S-15W

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED FOUR ACRES

DRILL STEM TEST NUMBER 4

REPORT NUMBER 14527

ELEVATION KELLY BUSHINGS 1969

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 2532

TEST INTERVAL (to) 2596

ANCHOR LENGTH 64

TOTAL DEPTH (ft) 2596

TOP PACKER DEPTH 2527

BOTTOM PACKER DEPTH 2532

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:30

INITIAL OPEN TOOL OPEN (to) 5:45

DURATION (min.) 15

FINAL OPEN

TOOL OPEN (from) 6:15

TOOL OPEN (to) 6:45

DURATION (min.) 30

TOOL CLOSED (from) 5:45

INITIAL SHUT-IN TOOL CLOSED (to) 6:15

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 6:45

TOOL CLOSED (to) 7:15

DURATION (min.) 30

INITIAL FLOW

WEAK BUILDING BLOW BUILT TO 7 INCHES INTO THE BUCKET

FINAL FLOW

WEAK BUILDING BLOW BUILT TO 10 INCHES INTO THE WATER

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 100	DRILLING MUD				
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST 1-30
TEST DATE	12/31/05	FORMATION TESTED	FOUR ACRES
SECTION-TOWN-RANGE	30-21S-15W	DRILL STEM TEST NUMBER	4
STATE	KANSAS	REPORT NUMBER	14527
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	1969
ELEVATION GROUND LEVEL	1961	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT


JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	40 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	2592	BOTTOM RECORDER DEPTH	2593
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	2506	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	8.8
WEIGHT PIPE I.D.	2.25	VISCOSITY	44
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	23,000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

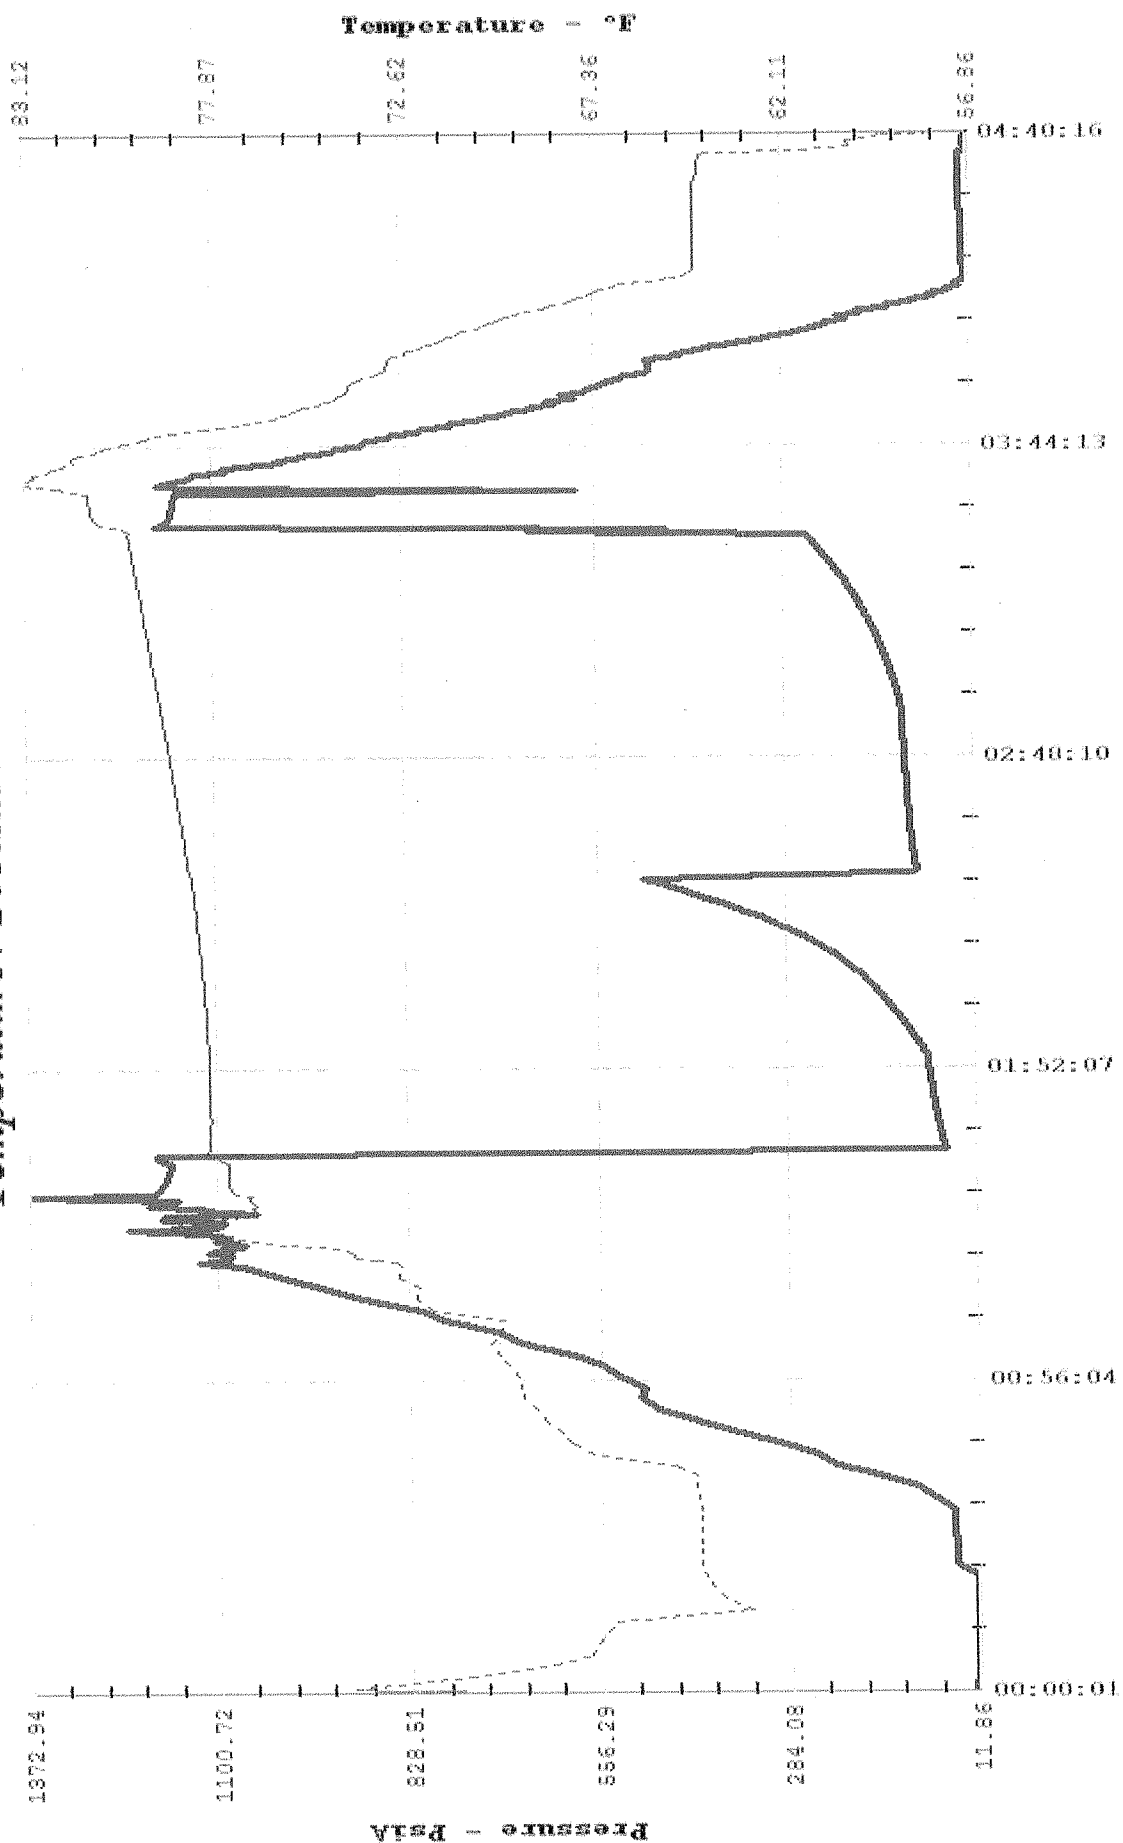

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-3-06 Location 30-21-15 Elevation 1961 County Pawnee

Company FGHoll Company LLC Number of Copies 6

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Duke Drilling Rig 8

Length Drill Pipe 3447 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 3468 Bottom Packer Depth 3473 Number of Packers _____ Packer Size 6 3/4

TESTED FROM 3473 TO 3535 ANCHOR LENGTH 62 TOTAL DEPTH 3535 Hole Size 7 1/8

LEASE & WELL NO. APLEY Trust 1-30 FORMATION TESTED KC TEST NO. #5

Mud Weight 9.2 Viscosity 62 Water Loss 8.8 Chlorides - Pits 6,800 D.S.T. 7,000

Maximum Temp. 90 °F Initial Hydrostatic Pressure (A) 1775 P.S.I. Final Hydrostatic Pressure (H) 1665 P.S.I.

Tool Open I.F.P. from 5:32 A.m. to 5:47 A.m. 15 min

Tool Closed I.C.I.P. from 5:47 A.m. to 6:17 A.m. 30 min

Tool Open F.F.P. from 6:17 A.m. to 6:32 A.m. 15 min

Tool Closed F.C.I.P. from 6:32 A.m. to 7:02 A.m. 30 min

Initial Blow Weak Surface Blow 1 1/2 inch into Bucket in 15 min

Final Blow Weak Surface Blow 1 inch into Bucket in 15 min

Total Feet Recovered 50 feet Drilling Mud Gravity of Oil _____ Corrected

50 Feet of Drilling Mud % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks Resistivity 1

Extra Equipment - Jars yes Safety Joint yes Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 3531 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 4794 Depth 3532 Insurance _____

Price of Job _____

Tool Operator Inf 8dd

Approved By _____

No 14528

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G HOLL COMPANY L.L.C
TWP. 21 RGE. 15

Lease & Well No. APLEY TRUST 1-30
Test #: 5 Date: 1-3-06 SEC. 30

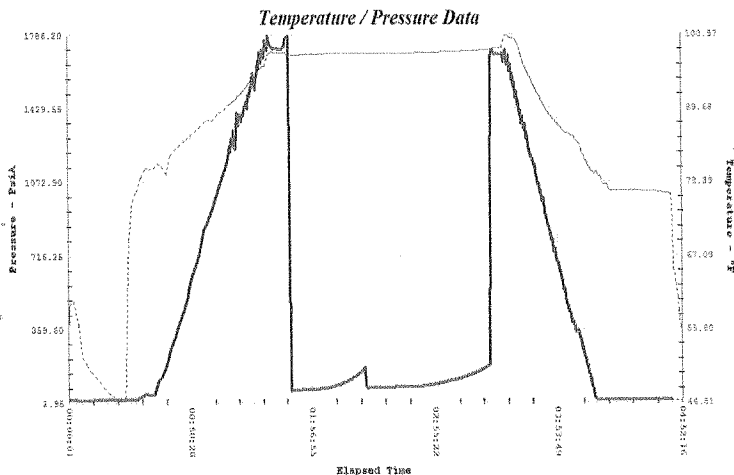

1	Initial Hydrostatic Pressure	1775
2	Initial Flow Pressure	61
3	Final Initial Flow Pressure	65
4	Initial Shut-In Pressure	173
5	Initial Final Flow Pressure	74
6	Final Flow Pressure	78
7	Final Shut-In Pressure	185
8	Final Hydrostatic Pressure	1665

Maximum Temperature 100

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/3/06

SECTION-TOWN-RANGE 30-21-15

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED

DRILL STEM TEST NUMBER 5

REPORT NUMBER 14528

ELEVATION KELLY BUSHINGS 1969

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3473

TEST INTERVAL (to) 3535

ANCHOR LENGTH 62

TOTAL DEPTH (ft) 3535

TOP PACKER DEPTH 3468

BOTTOM PACKER DEPTH 3473

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:32A

INITIAL OPEN TOOL OPEN (to) 5:47A

DURATION (min.) 15

TOOL OPEN (from) 6:17

FINAL OPEN TOOL OPEN (to) 6:32

DURATION (min.) 15

TOOL CLOSED (from) 5:47

INITIAL SHUT-IN TOOL CLOSED (to) 6:17

DURATION (min.) 30

TOOL CLOSED (from) 6:32

FINAL SHUT-IN TOOL CLOSED (to) 7:02

DURATION (min.) 30

INITIAL FLOW

WEAK SURFACE BLOW 1 1/2 INCHES INTO BUCKET

FINAL FLOW

WEAK SURFACE BLOW 1 INCH INTO BUCKET IN 15 MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 50	DRILLING MUD				
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST1-30
TEST DATE	1/3/06	FORMATION TESTED	KANSAS CITY A-D
SECTION-TOWN-RANGE	30-21-15	DRILL STEM TEST NUMBER	5
STATE	KANSAS	REPORT NUMBER	14528
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	1969
ELEVATION GROUND LEVEL	1961	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	40 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND		
TOP RECORDER DEPTH	3531	BOTTOM RECORDER DEPTH	3532
RECORDER NUMBER	91981	RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3447	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	62
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	6,800
		CHLORIDES-DST	7,000

COMMENTS

RESISTIVITY 1

Temperature / Pressure Data

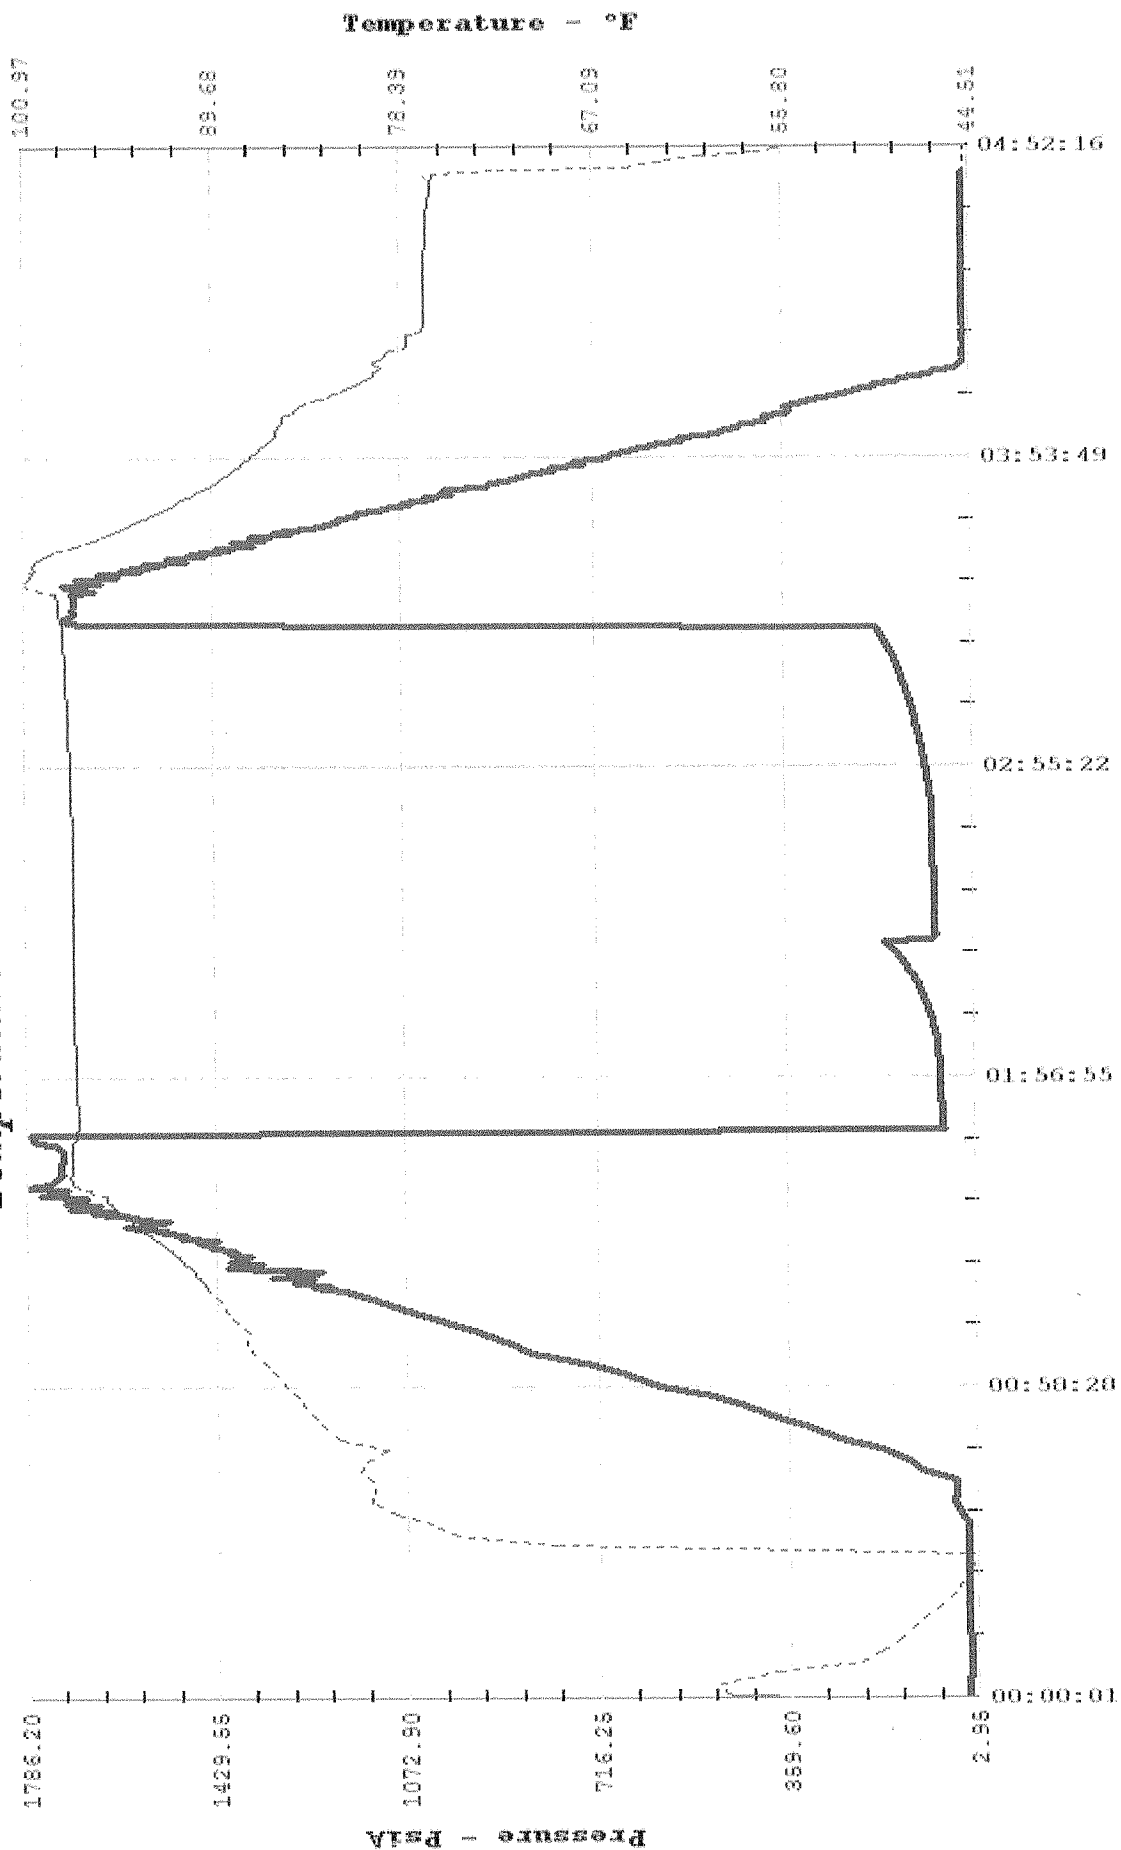

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-3-06 Location 30-21-15 Elevation 1961 County Pawnee

Company F.G. Hall Company L.L.C. Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Duke Drilling Company Rig 8

Length Drill Pipe 3591 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 x H

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 3605 Bottom Packer Depth 3610 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3610 TO 3634 ANCHOR LENGTH 24 TOTAL DEPTH 3634 Hole Size 7 7/8

LEASE & WELL NO. APley trust 1-30 FORMATION TESTED (TD) Kargocdy TEST NO. 6

Mud Weight 9.4 Viscosity 61 Water Loss 8.0 Chlorides - Pits 6,700 D.S.T. _____

Maximum Temp. 104 °F Initial Hydrostatic Pressure (A) 1810 P.S.I. Final Hydrostatic Pressure (H) 1712 P.S.I.

Tool Open I.F.P. from 10:46 p.m. to 11:01 p.m. 15 min

Tool Closed I.C.I.P. from 11:01 p.m. to 11:31 p.m. 30 min

Tool Open F.F.P. from 11:31 p.m. to 12:01 a.m. 30 min

Tool Closed F.C.I.P. from 12:01 a.m. to 1:01 a.m. 60 min

Initial Blow Weak Blow 4 inches into Bucket in 15 min.

Final Blow Fair Blow Bottom Bucket in 4 min then died off

Total Feet Recovered 60 Total Oil cut mud Gravity of Oil _____ Corrected _____

60 Feet of Oil cut mud % Gas 25 % Oil 75 % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 3630 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 3631 Insurance _____

Price of Job _____

Tool Operator Paul Schur

Approved By _____

No 14529


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

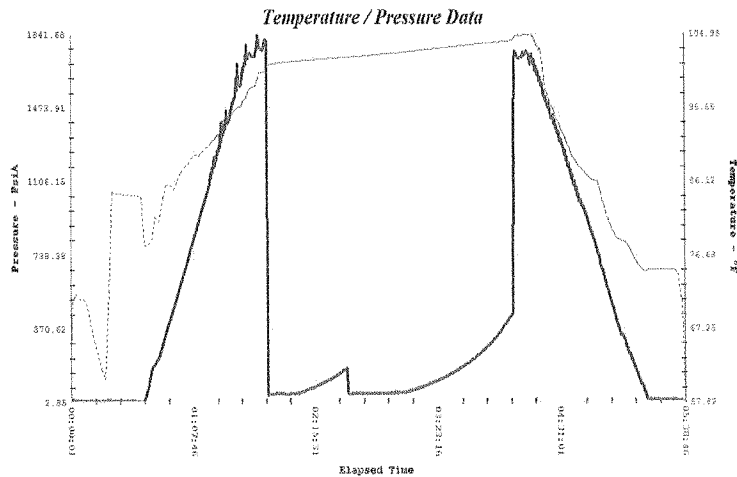

- | | | |
|---|------------------------------|------|
| 1 | Initial Hydrostatic Pressure | 1810 |
| 2 | Initial Flow Pressure | 40 |
| 3 | Final Initial Flow Pressure | 47 |
| 4 | Initial Shut-In Pressure | 172 |
| 5 | Initial Final Flow Pressure | 44 |
| 6 | Final Flow Pressure | 49 |
| 7 | Final Shut-In Pressure | 449 |
| 8 | Final Hydrostatic Pressure | 1712 |

Maximum Temperature 104

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/3/06

SECTION-TOWN-RANGE 30-21-15

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED I KANSAS CITY

DRILL STEM TEST NUMBER 6

REPORT NUMBER 14529

ELEVATION KELLY BUSHINGS 1960

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3610

TEST INTERVAL (to) 3634

ANCHOR LENGTH 24

TOTAL DEPTH (ft) 3634

TOP PACKER DEPTH 3605

BOTTOM PACKER DEPTH 3610

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 10:46P

INITIAL OPEN TOOL OPEN (to) 11:01P

DURATION (min.) 15

FINAL OPEN

TOOL OPEN (from) 11:31P

TOOL OPEN (to) 12:01A

DURATION (min.) 30

TOOL CLOSED (from) 11:01P

INITIAL SHUT-IN TOOL CLOSED (to) 11:31P

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 12:01A

TOOL CLOSED (to) 12:31A

DURATION (min.) 60

INITIAL FLOW

WEAK BLOW 4ICHS INTO BUCKET IN 15 MIN

FINAL FLOW

FAIR BLOW BOTTOM OF BUCKET IN 4 MIN BUT THEN DIED OFF

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 60	OIL CUT MUD		25	75	
2)					
3)					
4)					
5)					
6)					

Company: F.G HOLL COMPANY L.L.C

TWP. 21 RGE. 15

Lease & Well No. APLEY TRUST 1-30

Test #: 6

Date: 1-3-06

SEC. 30

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST 1-30
TEST DATE	1/3/06	FORMATION TESTED	I KANSAS CITY
SECTION-TOWN-RANGE	30-21-15	DRILL STEM TEST NUMBER	6
STATE	KANSAS	REPORT NUMBER	14529
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	1960
ELEVATION GROUND LEVEL	1961	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	40 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3630	BOTTOM RECORDER DEPTH	3631
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG 8	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3591	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	61
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8
		CHLORIDES-PITS	6,700
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

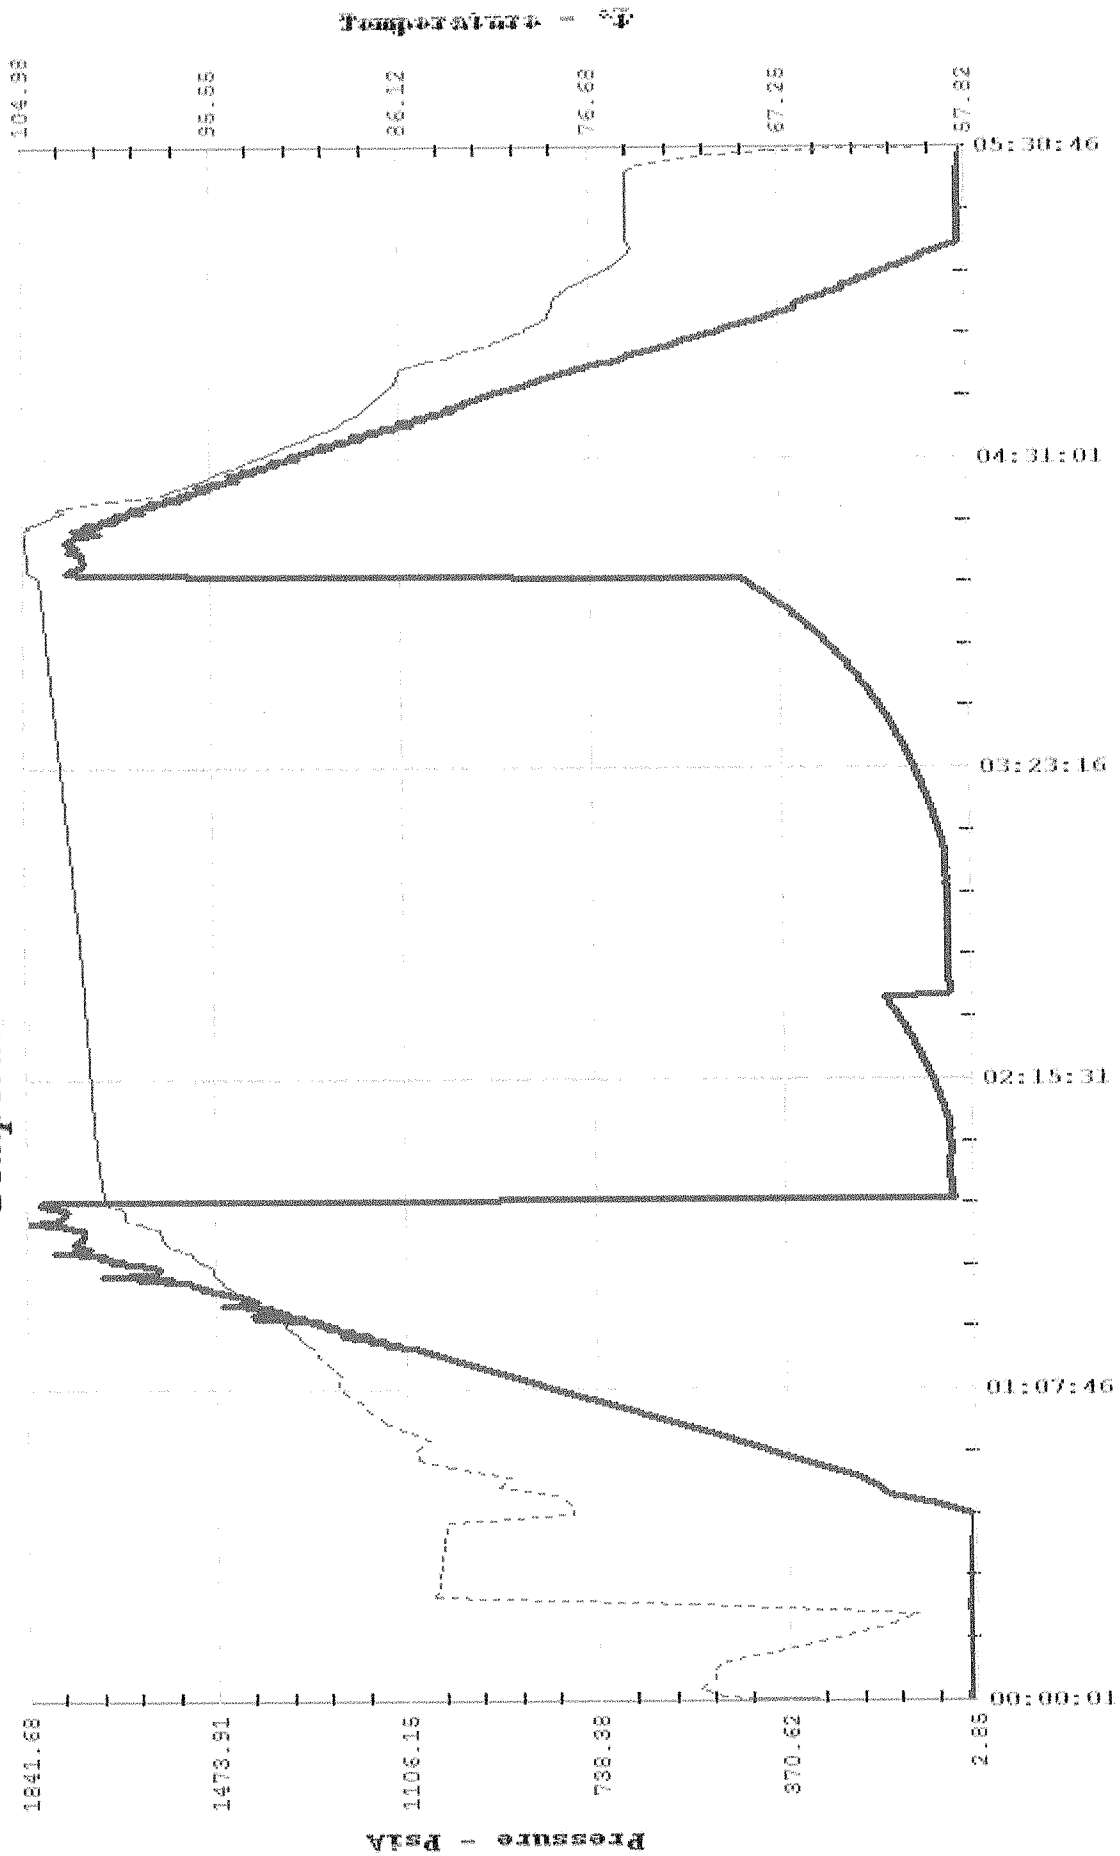

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-4-06 Location 30-21-15 Elevation 1961 County Pawnee

Company F.G. Hall Company, L.L.C. Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Duke Drilling Company Rig #8

Length Drill Pipe 3683 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 3697 Bottom Packer Depth 3702 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3702 TO 3828 ANCHOR LENGTH 126 TOTAL DEPTH 3828 Hole Size 7 7/8

LEASE & WELL NO. APLEY Trust 1-30 FORMATION TESTED Konkr/Viola TEST NO. 7

Mud Weight 92 Viscosity 98 Water Loss 88 Chlorides - Pits 7,500 D.S.T. _____

Maximum Temp. _____ °F Initial Hydrostatic Pressure (A) 1926 P.S.I. Final Hydrostatic Pressure (H) 1781 P.S.I.

Tool Open I.F.P. from 10:03 p.m. to 10:08 p.m. 5 min

Tool Closed I.C.I.P. from 10:08 p.m. to 10:38 p.m. 30 min

Tool Open F.F.P. from 10:38 p.m. to 11:30 p.m. 52 min

Tool Closed F.C.I.P. from 11:30 p.m. to 1:00 a.m. 90 min

Initial Blow Strong Blow Bottom of Bucket in 1 min Gas to Surface

Final Blow Gas to Surface Does Light.

Total Feet Recovered No fluid Gravity of Oil _____ Corrected _____

0 Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks Gas to Surface Does light. Gas sample was taken

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 3824 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 3825 Insurance _____

Price of Job _____

Tool Operator Jeff D. [Signature]

Approved By _____

No 14530

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

1(800)792-6902

GREAT BEND, KANSAS 67530


TWP. 21 RGE. 15

Company: F.G.HOLL COMPANY L.L.C

Lease & Well No. APLEY TRUST 1-30

Test #: 7 Date: 1-4-06 SEC. 30

Temperature / Pressure Data

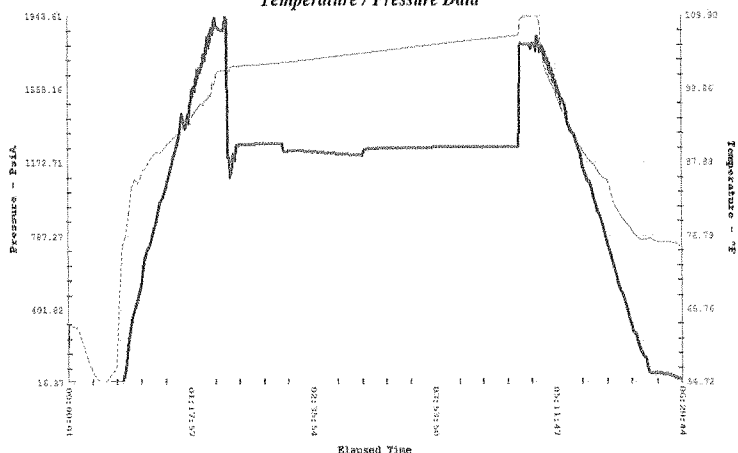

1	Initial Hydrostatic Pressure	1926
2	Initial Flow Pressure	1197
3	Final Initial Flow Pressure	1185
4	Initial Shut-In Pressure	1273
5	Initial Final Flow Pressure	1229
6	Final Flow Pressure	1209
7	Final Shut-In Pressure	1255
8	Final Hydrostatic Pressure	1781

Maximum Temperature 109

GENERAL INFORMATION

COMPANY NAME F.G.HOLL COMPANY L.L.C

TEST DATE 1/4/06

SECTION-TOWN-RANGE 42298

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED CONGRAMA, VIOLA

DRILL STEM TEST NUMBER 7

REPORT NUMBER 14530

ELEVATION KELLY BUSHINGS 1969

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3702

TEST INTERVAL (to) 3828

ANCHOR LENGTH 126

TOTAL DEPTH (ft) 3828

TOP PACKER DEPTH 3697

BOTTOM PACKER DEPTH 3702

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 10:03P

INITIAL OPEN TOOL OPEN (to) 10:08

DURATION (min.) 5

FINAL OPEN

TOOL OPEN (from) 10:38

TOOL OPEN (to) 11:30

DURATION (min.) 52

TOOL CLOSED (from) 10:08

INITIAL SHUT-IN TOOL CLOSED (to) 10:38

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 11:30

TOOL CLOSED (to) 1:00A

DURATION (min.) 90

INITIAL FLOW

STRONG BLOW BOTTOM OF BUCKET IN 1 MIN GAS TO SURFACE

FINAL FLOW

GAS TO SURFACE SEE GAS CHART

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1)					
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.GHOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST 1-30
TEST DATE	1/4/06	FORMATION TESTED	CONGRAMA, VIOLA
SECTION-TOWN-RANGE	10/21/2015	DRILL STEM TEST NUMBER	7
STATE	KANSAS	REPORT NUMBER	14530
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	1969
ELEVATION GROUND LEVEL	1961	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	40 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3824	BOTTOM RECORDER DEPTH	3825
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING COMPANY RIG 8		
DRILL PIPE LENGTH	3683	DRILL COLLAR LENGTH	
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	48
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	88
		CHLORIDES-PITS	7,500
		CHLORIDES-DST	

COMMENTS

GAS TO SURFACE ON THE FIRST OPEN

SUPERIOR TESTERS ENTERPRISES INC.

GREAT BEND, KANSAS

GAS FLOW RATE

(800) 792-6902

#

STATE..... KANSAS

Test Date 1/0/1900

COUNTY..... PAWNEE

Sec Town Range #####

FIELD.....

Report Number 14530

Initial Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)

Final Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)
TOLL OPEN 10:38	10:58	10		86		1 1/2	5901.000
	11:08	10		82		1 1/2	5662.000
	11:18	10		82		1 1/2	5662.000
	11:28	10		82		1 1/2	5662.000
GAS SAMPLE WAS TAKEN							

Temperature / Pressure Data



Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-5-06 Location 30-21-15 Elevation 1961 County Pawnee

Company F.G. Hall Company L.L.C. Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Duke Drilling Company Rig 8

Length Drill Pipe 3849 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 3863 Bottom Packer Depth 3868 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3868 TO 3884 ANCHOR LENGTH 16 TOTAL DEPTH 3884 Hole Size 7 7/8

LEASE & WELL NO. APLEY Trust 1-30 FORMATION TESTED Arbuckle TEST NO. 8

Mud Weight 9.1 Viscosity 57 Water Loss 8.8 Chlorides - Pits 6,500 D.S.T. _____

Maximum Temp. 106 °F Initial Hydrostatic Pressure (A) 1970 P.S.I. Final Hydrostatic Pressure (H) 1902 P.S.I.

Tool Open I.F.P. from 2:15 p.m. to 2:20 p.m. 5 min

Tool Closed I.C.I.P. from 2:20 p.m. to 2:50 p.m. 30 min

Tool Open F.F.P. from 2:50 p.m. to 3:50 p.m. 60 min

Tool Closed F.C.I.P. from 3:50 p.m. to 5:20 p.m. 90 min

Initial Blow Strong Blow Bottom of Bucket in 1 min Gas to Surface

Final Blow Gas to Surface Gas does light

Total Feet Recovered 0 Gravity of Oil _____ Corrected _____

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks Gas to Surface First Blm Does light

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electronica Depth 3880 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47941 Depth 3881 Insurance _____

Price of Job _____

Tool Operator Gar Bohm

Approved By _____

No. 14531


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

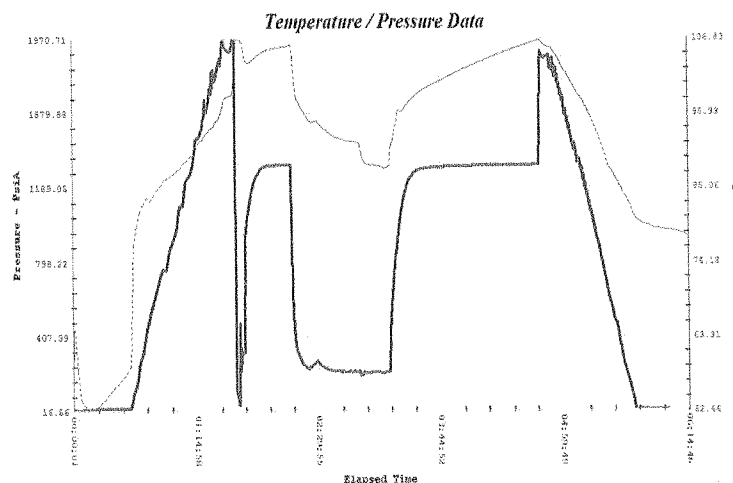

1	Initial Hydrostatic Pressure	1970
2	Initial Flow Pressure	145
3	Final Initial Flow Pressure	321
4	Initial Shut-In Pressure	1309
5	Initial Final Flow Pressure	239
6	Final Flow Pressure	219
7	Final Shut-In Pressure	1307
8	Final Hydrostatic Pressure	1902

Maximum Temperature 106

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C

TEST DATE 1/5/06

SECTION-TOWN-RANGE 30-21-15

STATE KANSAS

COUNTY PAWNEE

ELEVATION GROUND LEVEL 1961

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER APLEY TRUST 1-30

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 8

REPORT NUMBER 14531

ELEVATION KELLY BUSHINGS 1969

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3868

TEST INTERVAL (to) 3884

ANCHOR LENGTH 16

TOTAL DEPTH (ft) 3884

TOP PACKER DEPTH 3863

BOTTOM PACKER DEPTH 3868

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 2:15P

INITIAL OPEN

TOOL OPEN (to) 2:20P

FINAL OPEN

DURATION (min.) 5

TOOL OPEN (from) 2:50P

TOOL OPEN (to) 3:50P

DURATION (min.) 60

TOOL CLOSED (from) 2:20P

INITIAL SHUT-IN TOOL CLOSED (to) 2:50P

DURATION (min.) 30

TOOL CLOSED (from) 3:50P

FINAL SHUT-IN TOOL CLOSED (to) 5:20P

DURATION (min.) 90

INITIAL FLOW

STRONG BLOW BOTTO OF BUCKET IN 1 MIN

GAS TO SUFACE

FINAL FLOW

GAS TO SURFACE GAS DOES LIGHT

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1)					
2)					
3)					
4)					
5)					
6)					

Company: F.G HOLL COPANY L.L.C
21 RGE. 15

Lease & Well No. APLEY TRUST 1-30 Test #: 8 Date: 1-5-06 SEC. 30 TWP.

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST 1-30
TEST DATE	1/5/06	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	30-21-15	DRILL STEM TEST NUMBER	8
STATE	KANSAS	REPORT NUMBER	14531
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	1969
ELEVATION GROUND LEVEL	1961	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	40 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3880	BOTTOM RECORDER DEPTH	3881
RECORDER NUMBER	91981	RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING COMPANY RIG 8		
DRILL PIPE LENGTH	3849	DRILL COLLAR LENGTH	
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.7
WEIGHT PIPE I.D.	2.25	VISCOSITY	57
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	6,500
		CHLORIDES-DST	

COMMENTS

GAS TO SURFACE IN FIRST OPEN GAS DOES LIGHT

Temperature / Pressure Data

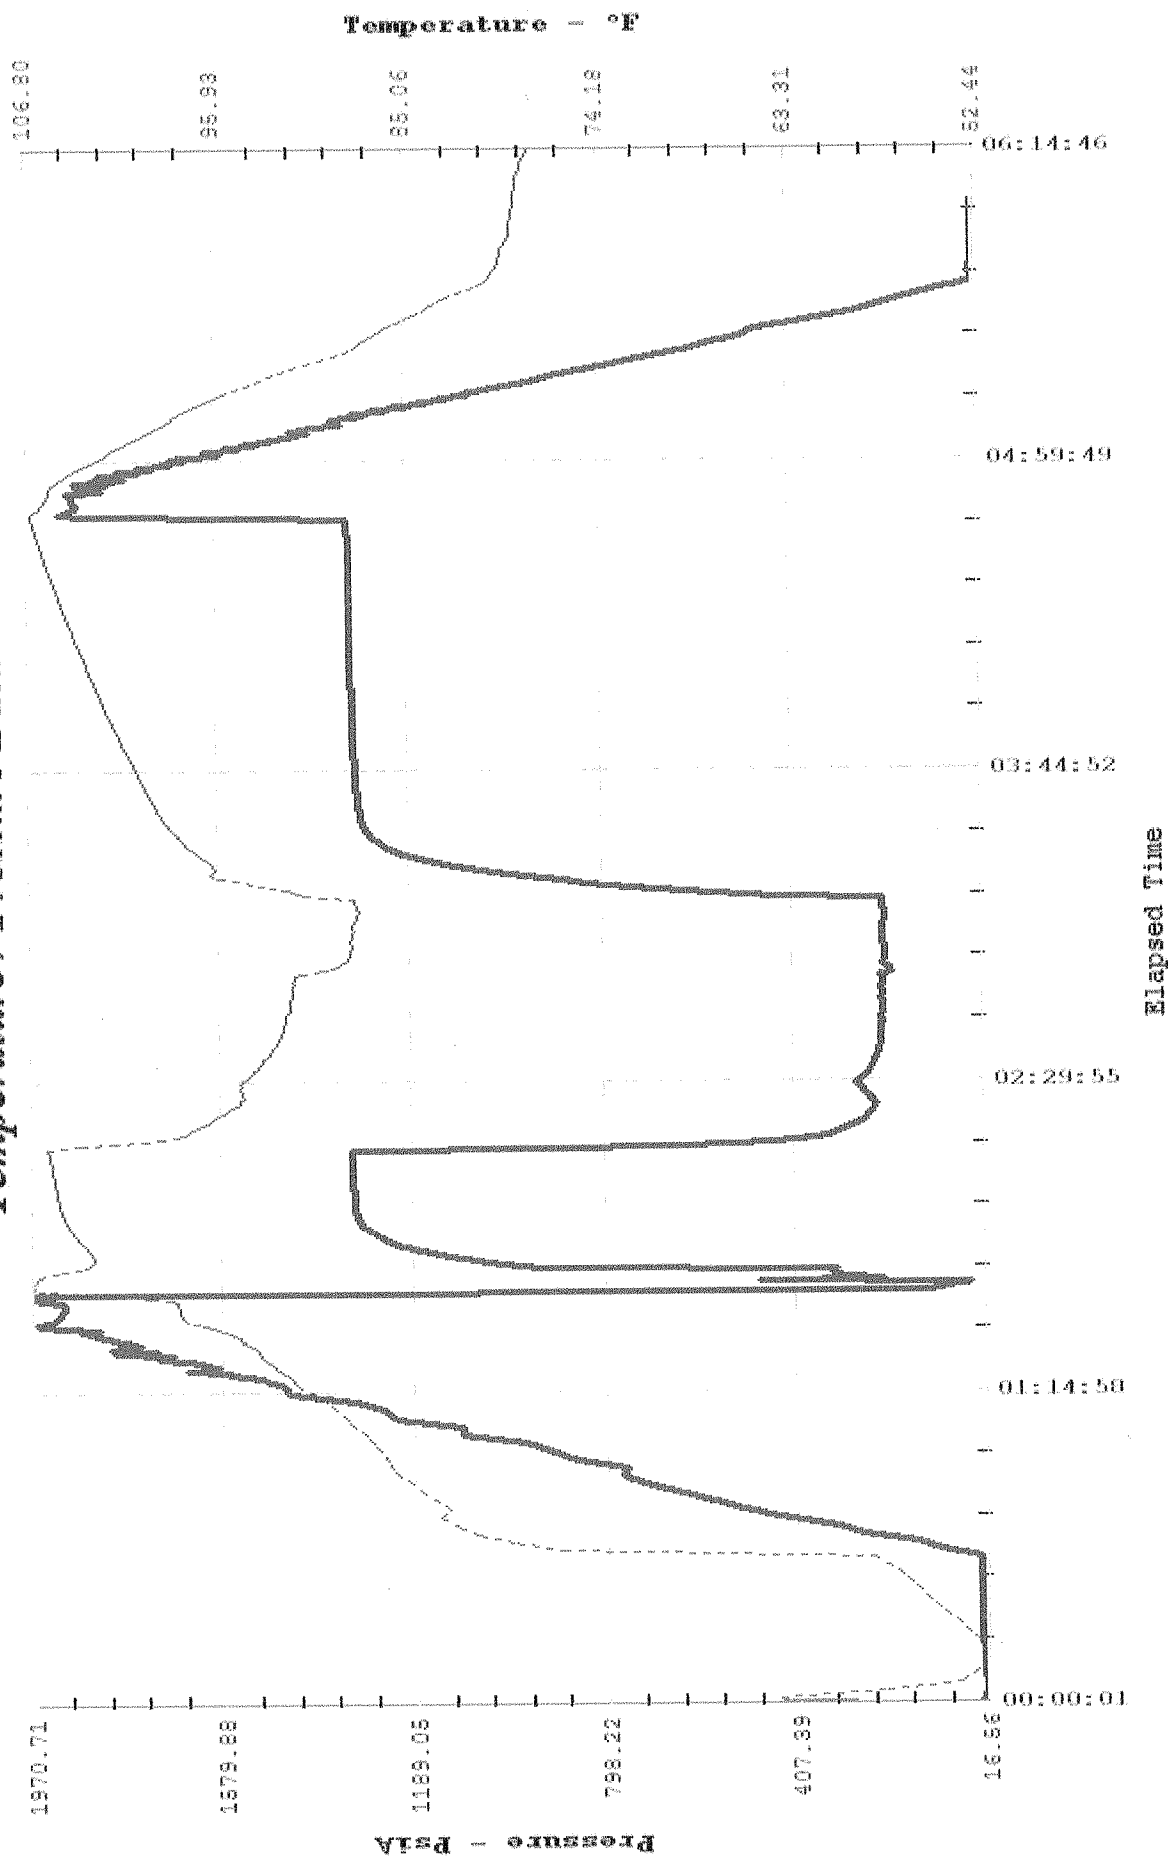

Superior Testers Enterprises, Inc.

R.R. 3, Box 296B, Great Bend, Kansas 67530

(316) 792-6902

Date 1-6-06 Location 30-21-15 Elevation 1961 County Pawnee

Company F.G. Hall Company L.C.C. Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Duke Drilling Company R.D. 8

Length Drill Pipe 3865 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 3879 Bottom Packer Depth 3884 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3884 TO 3927 ANCHOR LENGTH 23 TOTAL DEPTH 3907 Hole Size 7 7/8

LEASE & WELL NO. APLEY TRUST 1-30 FORMATION TESTED Arbuckle TEST NO. 9

Mud Weight 9.8 Viscosity 57 Water Loss 8.8 Chlorides - Ppt 6500 D.S.T. 60,000

Maximum Temp. 118 °F Initial Hydrostatic Pressure (A) 2002 P.S.I. Final Hydrostatic Pressure (H) 1911 P.S.I.

Tool Open I.F.P. from 437 A.M. to 4:42 A.M. 5 min

Tool Closed I.C.I.P. from 4:42 A.M. to 5:12 A.M. 30 min

Tool Open F.P.P. from 5:12 A.M. to 5:42 A.M. 30 min

Tool Closed F.C.I.P. from 5:42 A.M. to 6:42 A.M. 60 min

Initial Blow Strong Blow Bottom Broken in Train Gas to Surface

Final Blow Gas to Surface Fluid to Surface

Total Feet Recovered 1200 Fluid to Surface 1200 Fluid to Surface

Feet of Gas Oil Gravity 43 % Gas 100 % Oil _____ % Mud _____ % Water _____

Feet of Gas Water _____ % Gas _____ % Oil _____ % Mud 100 % Water _____

Feet of Gas Water _____ % Gas _____ % Oil _____ % Mud 100 % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks Gas to Surface first open Gas light 15' 20' open Fluid to Surface in 8 min. Gas Oil column 5800' Gravity 43

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4025 Clock No. Electron Depth 3903 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 4744 Depth 3904 Insurance _____

Price of Job _____ Tool Operator Jim Bohn

Approved By _____

No. 14532


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property of personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

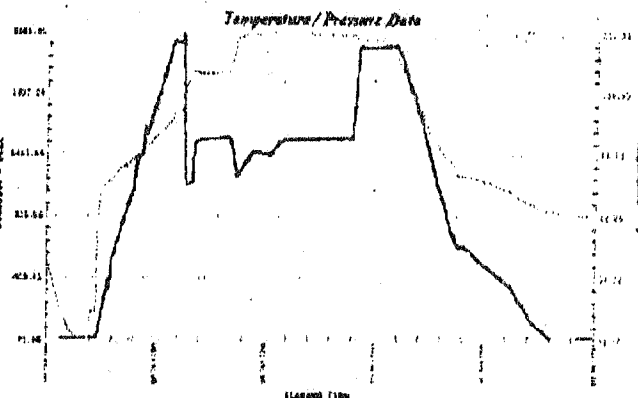

1	Initial Hydrostatic Pressure	2002
2	Initial Flow Pressure	1038
3	Final Initial Flow Pressure	1035
4	Initial Shut-In Pressure	1317
5	Initial Final Flow Pressure	1070
6	Final Flow Pressure	1207
7	Final Shut-In Pressure	1314
8	Final Hydrostatic Pressure	1911

Maximum Temperature 118

GENERAL INFORMATION

COMPANY NAME F.G HOLL COMPANY L.L.C
 TEST DATE 1/6/06
 SECTION-TOWN-RANGE 30-21-15
 STATE KANSAS
 COUNTY PAWNEE
 ELEVATION GROUND LEVEL 1961
 COMPANY REPRESENTATIVE BILL REE
 LEASE AND WELL NUMBER APLEY TRUST 1-30
 FORMATION TESTED ARBUCKLE
 DRILL STEM TEST NUMBER 9
 REPORT NUMBER 14532
 ELEVATION KELLY BUSHINGS 1969
 TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3884
 TEST INTERVAL (to) 3907
 ANCHOR LENGTH 23
 TOTAL DEPTH (M) 3907
 TOP PACKER DEPTH 3879
 BOTTOM PACKER DEPTH 3884
 NUMBER OF PACKERS 2
 PACKER SIZE 6 3/4
 HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 4:37A
 INITIAL OPEN TOOL OPEN (to) 4:42A
 DURATION (min.) 5
 FINAL OPEN TOOL OPEN (from) 5:12
 TOOL OPEN (to) 5:42
 DURATION (min.) 30
 TOOL CLOSED (from) 4:42A
 INITIAL SHUT-IN TOOL CLOSED (to) 5:12
 DURATION (min.) 30
 FINAL SHUT-IN TOOL CLOSED (from) 5:42
 TOOL CLOSED (to) 6:42
 DURATION (min.) 60

INITIAL FLOW

STROG BLOW BOTTOM OF BUCKET IN 1 MIN GAS TO SURFACE

FINAL FLOW

GAS TO SURFACE FLUID TO SURFACE IN 10 MI 8 MIN

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 120	GASSY OIL		100		
2) 540	GASSY WATER				100
3) 540	GASSY WATER				100
4)					
5)					
6)	1200 TOTAL				

Company: F.G HOLL COMPANY L.L.C
 TWP. 21 RGE. 15

Lease & Well No. APLEY TRUST 1-30

Test #: 9 Date: 1-6-06 SEC. 30

SUPERIOR TESTERS ENTERPRISES INC.**DRILL STEM TEST REPORT****GREAT BEND, KANSAS 67530 (800)792-6902****GENERAL INFORMATION**

COMPANY NAME	F.G HOLL COMPANY L.L.C	LEASE AND WELL NUMBER	APLEY TRUST 1-30
TEST DATE	1/8/08	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	30-21-16	DRILL STEM TEST NUMBER	9
STATE	KANSAS	REPORT NUMBER	14632
COUNTY	PAWNEE	ELEVATION KELLY BUSHINGS	1969
ELEVATION GROUND LEVEL	1981	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (BRD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	40 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	3803	BOTTOM RECORDER DEPTH	3904
RECORDER NUMBER	91981	RECORDER NUMBER	5483

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING COMPANY RIG 8		
DRILL PIPE LENGTH	3869	DRILL COLLAR LENGTH	
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH		MUD WEIGHT W/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	67
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	6,900
		CHLORIDES-DST	60,000

COMMENTS

GRVITY 43 RESISTIVITY .15

Temperature / Pressure Data

