

(800) 792-6902

[illegible]

15211


TR-154 No. 15211

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

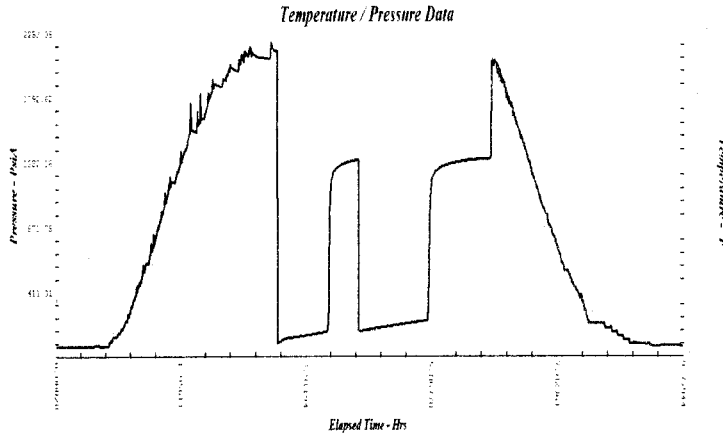

1	Initial Hydrostatic Pressure	2122
2	Initial Flow Pressure	40
3	Final Initial Flow Pressure	123
4	Initial Shut-In Pressure	1346
5	Initial Final Flow Pressure	128
6	Final Flow Pressure	206
7	Final Shut-In Pressure	1356
8	Final Hydrostatic Pressure	2014

Maximum Temperature 118

GENERAL INFORMATION

COMPANY NAME HARTMAN OIL CO. INC.	
TEST DATE 10/19/07	LEASE AND WELL NUMBER ANTRIM #6
SECTION-TOWN-RANGE 18-21S-22W	FORMATION TESTED MISSISSIPPI
STATE KANSAS	DRILL STEM TEST NUMBER 2
COUNTY HODGEMAN	REPORT NUMBER 15211
ELEVATION GROUND LEVEL 2280	ELEVATION KELLY BUSHINGS 2290
COMPANY REPRESENTATIVE JIM MUSGROVE	TESTING ENGINEER KEVIN WEBSTER

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4381	TOP PACKER DEPTH 4376
TEST INTERVAL (to) 4390	BOTTOM PACKER DEPTH 4381
ANCHOR LENGTH 9	NUMBER OF PACKERS 2
TOTAL DEPTH (ft) 4390	PACKER SIZE 6 3/4
	HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN		FINAL OPEN	
TOOL OPEN (from) 4:30		TOOL OPEN (from) 6:00	
TOOL OPEN (to) 5:15		TOOL OPEN (to) 6:45	
DURATION (min.) 45		DURATION (min.) 45	
INITIAL SHUT-IN		FINAL SHUT-IN	
TOOL CLOSED (from) 5:15		TOOL CLOSED (from) 6:45	
TOOL CLOSED (to) 6:00		TOOL CLOSED (to) 7:45	
DURATION (min.) 45		DURATION (min.) 60	

INITIAL FLOW WEAK SURFACE BLOW BUILT TO BOTTOM OF BUCKET IN 21 MINUTES

FINAL FLOW WEAK SURFACE BLOW BUILT TO BOTTOM OF BUCKET IN 15 MINUTES

Company: HARTMAN OIL CO. INC. Lease & Well No. ANTRIM #6 Test #: 2 Date: 10/19/07 SEC. 18 TWP.
 21S RGE. 22W

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	HARTMAN OIL CO. INC.	LEASE AND WELL NUMBER	ANTRIM #6
TEST DATE	10/19/07	FORMATION TESTED	MISSISSIPPI
SECTION-TOWN-RANGE	18-21S-22W	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	15211
COUNTY	HODGEMAN	ELEVATION KELLY BUSHINGS	2290
ELEVATION GROUND LEVEL	2280	TESTING ENGINEER	KEVIN WEBSTER
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	152 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	4386	BOTTOM RECORDER DEPTH	4387
RECORDER NUMBER	4023	RECORDER NUMBER	3088

WELL INFORMATION

DRILLING CONTRACTOR	H 2 #2	DRILL COLLAR LENGTH	123
DRILL PIPE LENGTH	4243	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS

Recovery Sample Description

Great Bend, Kansas 67530

Drill Pipe	I.D.	Feet		Recovery Description For Drill Pipe	Gas	Oil	Mud	Water	Total bbls.
4 1/2	3.82	404	CLEAN GASSY OIL		10%	90%			5.7368
		1116	GAS IN THE PIPE						15.8472
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
Drill Collars	I.D.			Recovery Description For Drill Collars	0.5737	5.1631	0.0000	0.0000	
	2.25	62	MUD CUT OIL			50%	50%		0.3038
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
Total Recovery	1582	Feet		Total bbls. Recovered From Drill Pipe	0.5737	5.1631	0.0000	0.0000	Total
				Total bbls. Recovered From Drill Collars	0.0000	0.1519	0.1519	0.0000	bbls
				Total bbls Recovered	0.5737	5.3150	0.1519	0.0000	21.8878
					Gas	Oil	Mud	Water	
				Gravity of Oil Corrected	34			Degrees	
MUD WEIGHT #/GAL	9.2			Resistivity		ohms @			
VISCOSITY	45			Recovery Chlorides		ppm			
WATER LOSS	11.2			Pit Chlorides	10000	ppm			
				4 1/2 inch Drill Pipe 3.83 I.D. Drill Collars 2.25 I.D					
				HARTMAN OIL CO. INC.	ANTRIM #6	18-21S-22W	10/19/07	DST#2 MISSISSIPPI	

Temperature / Pressure Data



Tool serial number: 4143
 Test start: 10/20/2007 01:01:03

Superior Testers Enterprises L.L.C.

P.O. Box 138, Great Bend, Kansas 67530

(800) 792-6902

Company Hartman Oil Co. Inc.
Address 12950 E 13th Street Wichita, KS 67230
Lease & # Antline #6 Sec. 18 Twp 21S Rng 22W
Date 10-18-2007 County Hogman Elevation 2280 G.L. 2290 K.B.
Drilling Contractor H2 #2
Drill Pipe Length 4181 I.D. of Drill Pipe 7.8 Tool Joint Size 4.5
Drill Collar Length 123 I.D. of Drill Collars 2.5 Tool Joint Size 4.5
Mud Weight 9.9 Viscosity 42 Filtrate 10.4 Chlorides-Pits 5700 DST
Top Packer Depth 4295 Bottom Packer Depth 4300 Number of Packers 2
Tested From 4300 to 4326 Total Depth 4326 Anchor Length 26'
Test # 1 Formation Tested Fort Scott Hole Size 7 7/8
Initial Blow Fair blow built to 4"

Final Blow head blow built to 3" Blow back on the 1st Shut-in NO

Initial Hydrostatic 2101 P.S.I. Final Hydrostatic 2049 P.S.I. Maximum Temp. 120 F

Initial Opening	P.S.I. to	P.S.I. from	Time	Minutes
<u>47</u>	<u>105</u>	<u>2:10 pm</u>	<u>2:40 pm</u>	<u>30</u>
<u>1147</u>		<u>2:40 pm</u>	<u>3:25 pm</u>	<u>45</u>
<u>108</u>	<u>131</u>	<u>3:25 pm</u>	<u>4:10 pm</u>	<u>45</u>
<u>1114</u>		<u>4:10 pm</u>	<u>5:10 pm</u>	<u>60</u>

Feet	Recovery Description	% Gas	% Oil	% Mud	% Water
120	Muddy water			45	55
60	slightly muddy water slightly muddy water			15	85

Total Feet Recovered 180 Recovery Chlorides 770,000 Rw. 186 ohms @ 56 Degrees

Gravity of oil Corrected Gas to Surface in minutes into the

Max. Gas Gauged MCF/day See Gas Flow Report Was a gas sample taken NO

Comments

Extra Equipment-Jars 91986 Safety Joint 4322 Circulating Sub Straddle
Electronic Recorder No. 4337 Depth 4323 Extra Packer (3rd) Hook Wall
Bottom Recorder No. 4337 Depth 4323 Extra Packer (4th) Sampler
Tool Operator Joe Approved By


Ticket No 15210

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

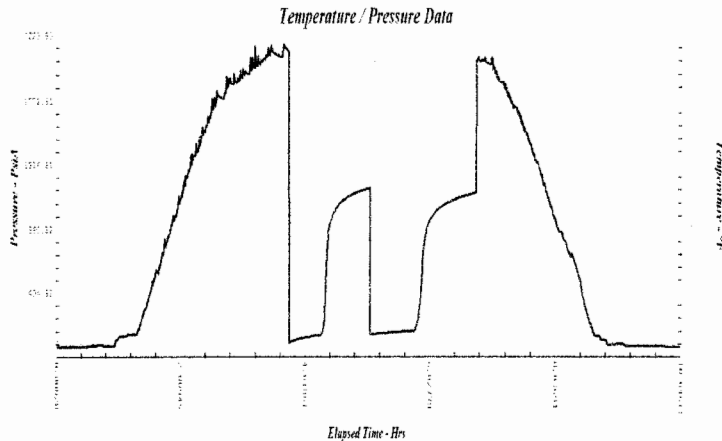

1	Initial Hydrostatic Pressure	2101
2	Initial Flow Pressure	47
3	Final Initial Flow Pressure	105
4	Initial Shut-In Pressure	1147
5	Initial Final Flow Pressure	108
6	Final Flow Pressure	131
7	Final Shut-In Pressure	1114
8	Final Hydrostatic Pressure	2049

Maximum Temperature 120

GENERAL INFORMATION

COMPANY NAME	 HARTMAN OIL CO. INC.	LEASE AND WELL NUMBER	 ANTRIM #6
TEST DATE	 10/18/07	FORMATION TESTED	 FORT SCOTT
SECTION-TOWN-RANGE	 18-21S-22W	DRILL STEM TEST NUMBER	 1
STATE	 KANSAS	REPORT NUMBER	 15210
COUNTY	 HODGEMAN	ELEVATION KELLY BUSHINGS	 2290
ELEVATION GROUND LEVEL	 2280	TESTING ENGINEER	 KEVIN WEBSTER
COMPANY REPRESENTATIVE	 JIM MUSGROVE		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	 4300	TOP PACKER DEPTH	 4295
TEST INTERVAL (to)	 4326	BOTTOM PACKER DEPTH	 4300
ANCHOR LENGTH	 26	NUMBER OF PACKERS	 2
TOTAL DEPTH (ft)	 4326	PACKER SIZE	 6 3/4
		HOLE SIZE	 7 7/8

FLOW TIMES

INITIAL OPEN	FINAL OPEN
TOOL OPEN (from) 2:10	TOOL OPEN (from) 3:25
TOOL OPEN (to) 2:40	TOOL OPEN (to) 4:10
DURATION (min.) 30	DURATION (min.) 45
INITIAL SHUT-IN	FINAL SHUT-IN
TOOL CLOSED (from) 2:40	TOOL CLOSED (from) 4:10
TOOL CLOSED (to) 3:25	TOOL CLOSED (to) 5:10
DURATION (min.) 45	DURATION (min.) 60

INITIAL FLOW FAIR BLOW BUILT TO 4"

FINAL FLOW WEAK BLOW BUILT TO 3"

Company: HARTMAN OIL CO. INC. Lease & Well No. ANTRIM #6 Test #: 1 Date: 10/18/07 SEC. 18 TWP.
21S RGE. 22W

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	HARTMAN OIL CO. INC.	LEASE AND WELL NUMBER	ANTRIM #6
TEST DATE	10/18/07	FORMATION TESTED	FORT SCOTT
SECTION-TOWN-RANGE	18-21S-22W	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	15210
COUNTY	HODGEMAN	ELEVATION KELLY BUSHINGS	2290
ELEVATION GROUND LEVEL	2280	TESTING ENGINEER	KEVIN WEBSTER
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	152 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	4322	BOTTOM RECORDER DEPTH	4323
RECORDER NUMBER	4023	RECORDER NUMBER	3088

WELL INFORMATION

DRILLING CONTRACTOR	H 2 #2	DRILL COLLAR LENGTH	123
DRILL PIPE LENGTH	4181	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		


COMMENTS

Recovery Sample Description

Great Bend, Kansas 67530

Drill Pipe	I.D.	Feet	Recovery Description For Drill Pipe		Gas	Oil	Mud	Water	Total bbls.
4 1/2	3.82	60	MUDDY WATER				45%	55%	0.8520
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
Drill Collars	I.D.		Recovery Description For Drill Collars		0.0000	0.0000	0.3834	0.4686	0.0000
	2.25	0	MUDDY WATER				45%	55%	0.0000
		60	SLIGHTLY MUD CUT WATER				15%	85%	0.2940
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
									0.0000
Total Recovery	120	Feet	Total bbls. Recovered From Drill Pipe		0.0000	0.0000	0.3834	0.4686	Total
			Total bbls. Recovered From Drill Collars		0.0000	0.0000	0.0441	0.2499	bbls
			Total bbls Recovered		0.0000	0.0000	0.4275	0.7185	1.1460
				Gravity of Oil Corrected					
MUD WEIGHT #/GAL	9.0		Resistivity	.18		ohms @	S _C	Degrees	
VISCOSITY	42		Recovery Chlorides	350000		ppm			
WATER LOSS	10.4		Pit Chlorides	5700		ppm			
				4 1/2 inch Drill Pipe 3.83 I.D. Drill Collars 2.25 I.D					
HARTMAN OIL CO. INC.	ANTRIM #6	10/18/07	18-2IS-22W	DST# 1 FORT SCOTT					

Temperature / Pressure Data

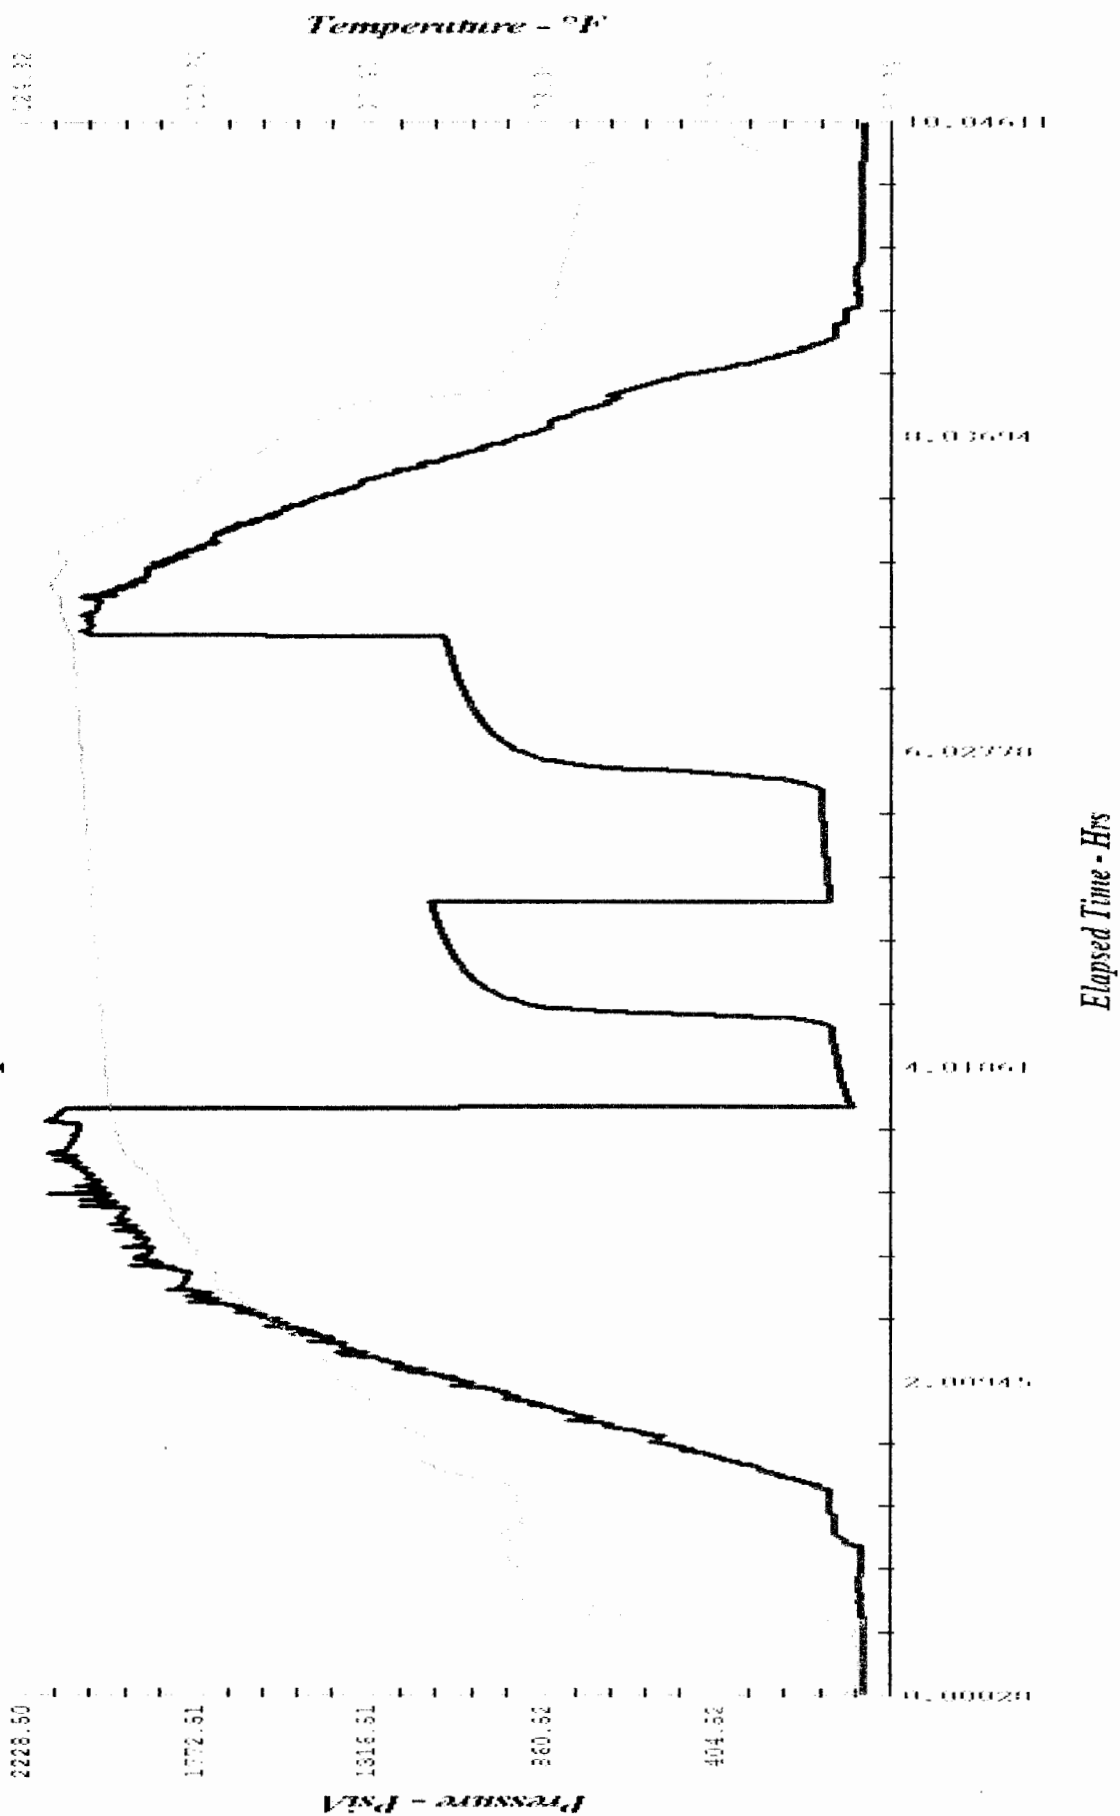


Tool serial number: 4143
 Test start: 10/18/2007 22:37:23

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

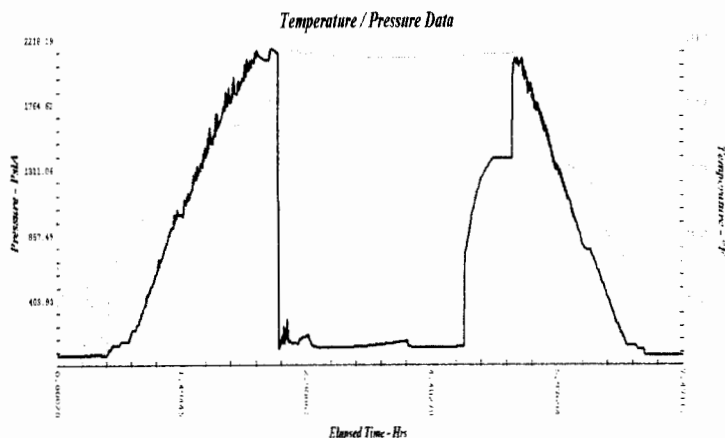

1	Initial Hydrostatic Pressure	2120
2	Initial Flow Pressure	68
3	Final Initial Flow Pressure	74
4	Initial Shut-In Pressure	117
5	Initial Final Flow Pressure	79
6	Final Flow Pressure	78
7	Final Shut-In Pressure	1384
8	Final Hydrostatic Pressure	2039

Maximum Temperature 120

GENERAL INFORMATION

COMPANY NAME	 HARTMAN OIL CO. INC.	LEASE AND WELL NUMBER	 ANTRIM #6
TEST DATE	 10/20/07	FORMATION TESTED	 MISSISSIPPI
SECTION-TOWN-RANGE	 18-21S-22W	DRILL STEM TEST NUMBER	 3
STATE	 KANSAS	REPORT NUMBER	 15212
COUNTY	 HODGEMAN	ELEVATION KELLY BUSHINGS	 2290
ELEVATION GROUND LEVEL	 2280	TESTING ENGINEER	 KEVIN WEBSTER
COMPANY REPRESENTATIVE	 JIM MUSGROVE		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	 4390	TOP PACKER DEPTH	 4385
TEST INTERVAL (to)	 4398	BOTTOM PACKER DEPTH	 4390
ANCHOR LENGTH	 8	NUMBER OF PACKERS	 2
TOTAL DEPTH (ft)	 4398	PACKER SIZE	 6 3/4
		HOLE SIZE	 7 7/8

FLOW TIMES

INITIAL OPEN		FINAL OPEN	
TOOL OPEN (from)	 11:10	TOOL OPEN (from)	 12:40
TOOL OPEN (to)	 11:55	TOOL OPEN (to)	 1:10
DURATION (min.)	 45	DURATION (min.)	 30
INITIAL SHUT-IN		FINAL SHUT-IN	
TOOL CLOSED (from)	 11:55	TOOL CLOSED (from)	 1:10
TOOL CLOSED (to)	 12:40	TOOL CLOSED (to)	 1:55
DURATION (min.)	 45	DURATION (min.)	 45

INITIAL FLOW

WEAK SURFACE BLOW BUILT TO 1 1/2" FLUSHED TOOL

FINAL FLOW

NO BLOW FLUSHED TOOL STILL NO BLOW

Company: HARTMAN OIL CO. INC. Lease & Well No. ANTRIM #6 Test #: 3 Date: 10/20/07 SEC. 18 TWP.
21S RGE. 22W

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	HARTMAN OIL CO. INC.	LEASE AND WELL NUMBER	ANTRIM #6
TEST DATE	10/20/07	FORMATION TESTED	MISSISSIPPI
SECTION-TOWN-RANGE	18-21S-22W	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	15212
COUNTY	HODGEMAN	ELEVATION KELLY BUSHINGS	2290
ELEVATION GROUND LEVEL	2280	TESTING ENGINEER	KEVIN WEBSTER
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	152 MILES ROUND TRIP FROM		GREAT BEND
TOP RECORDER DEPTH	4394	BOTTOM RECORDER DEPTH	4395
RECORDER NUMBER	4023	RECORDER NUMBER	3088

WELL INFORMATION

DRILLING CONTRACTOR	H 2 #2	DRILL COLLAR LENGTH	123
DRILL PIPE LENGTH	4243	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		


COMMENTS

Recovery Sample Description

Great Bend, Kansas 67530

[illegible]

Temperature / Pressure Data

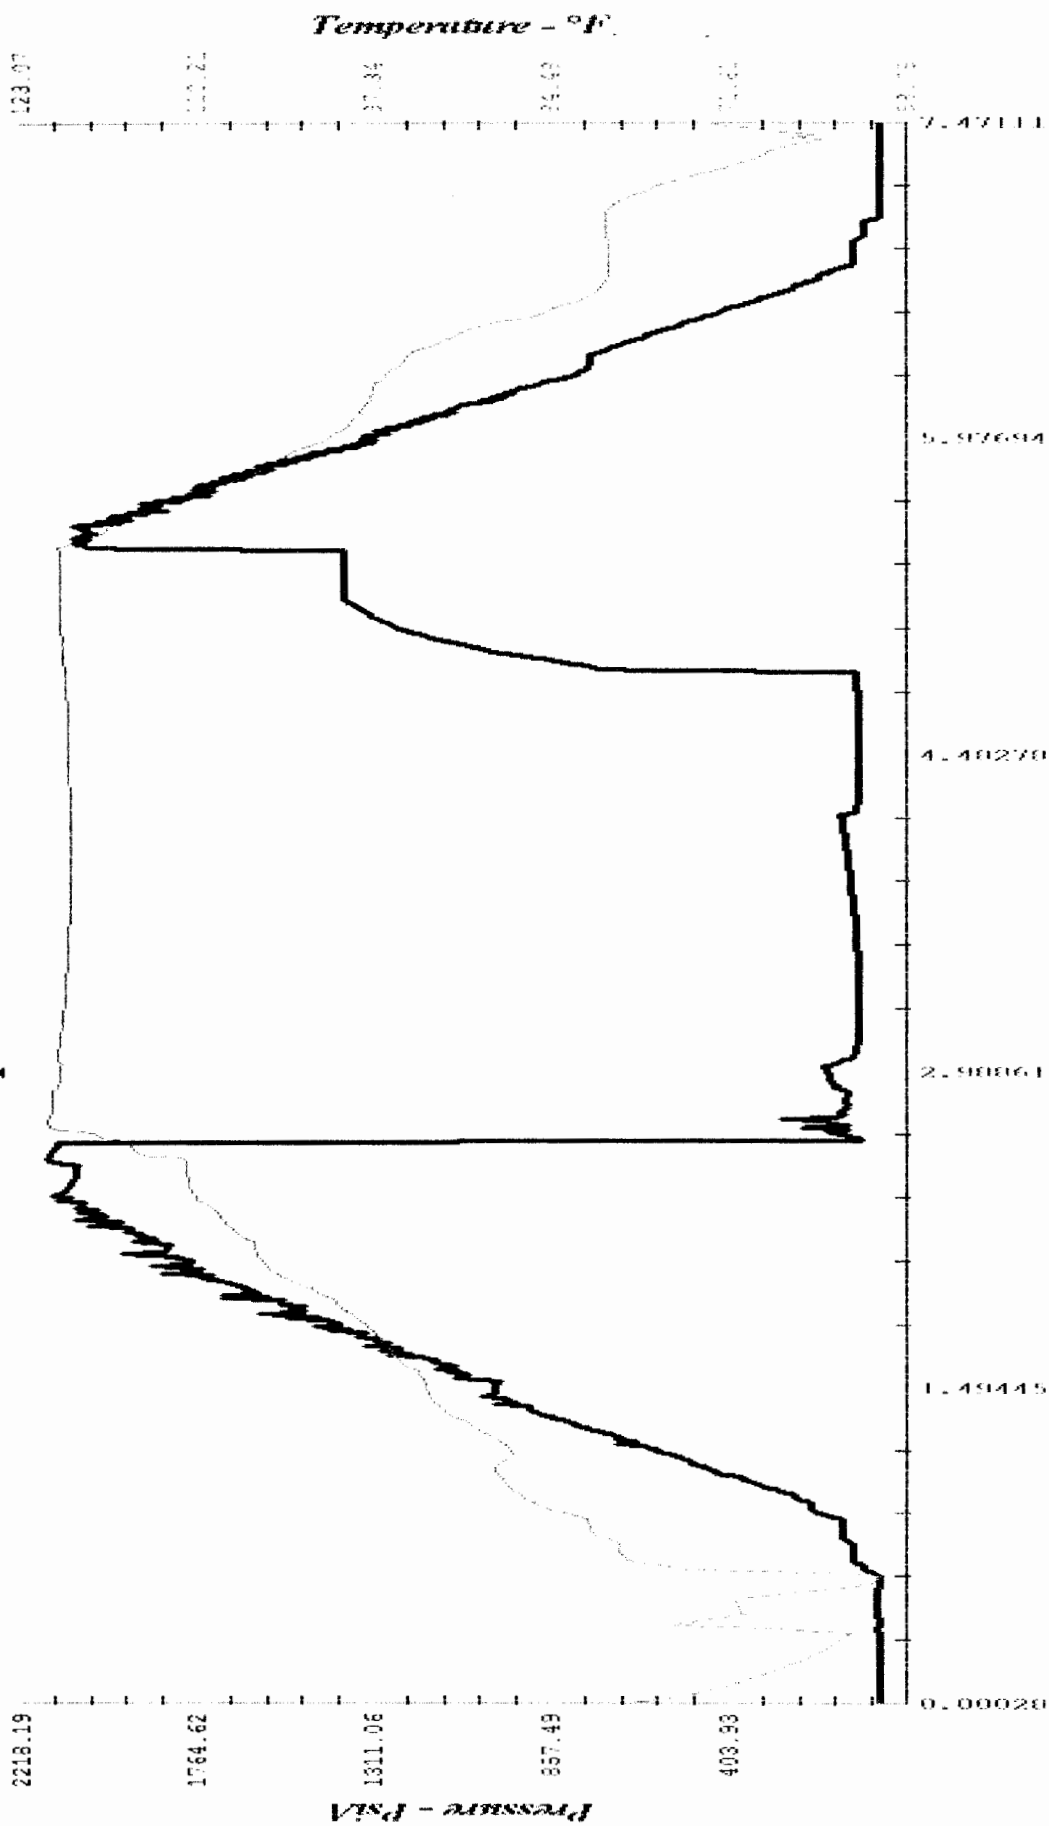

Tool serial number: 4143

Test start: 10/20/2007 18:02:20

(800) 792-6902

Initial Opening	268 P.S.I. to 1034 P.S.I.	from 6:00 Am to 6:30 Am	30 minutes
Initial Shut-in	138 P.S.I. to 1374 P.S.I.	from 6:30 Am to 7:15 Am	45 minutes
Final Opening	1046 P.S.I. to 1374 P.S.I.	from 7:15 Am to 8:00 Am	45 minutes
Final Shut-in	1395 P.S.I. to 1374 P.S.I.	from 8:00 Am to 9:00 Am	60 minutes

[illegible]

Total Feet Recovered 3934 Recovery Chlorides 220,900 Rv. .32 ohms @ 62 Degrees
Gravity of oil _____ Corrected Gas to Surface in _____ minutes into the _____
Max. Gas Gauged _____ MCF/day See Gas Flow Report Was a gas sample taken _____
Comments Runners' 1 packer

Extra Equipment-Jars _____	Safety Joint _____	Circulating Sub _____	Straddle _____
Electronic Recorder No. <u>91986</u>	Depth <u>4404</u>	Extra Packer (3rd) _____	Hook Wall _____
Bottom Recorder No. <u>4327</u>	Depth <u>4405</u>	Extra Packer (4th) _____	Sampler _____
Tool Operator <u>1</u>		Approved By _____	


Ticket No. 15213

SUPERIOR TESTERS ENTERPRISES L.L.C.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

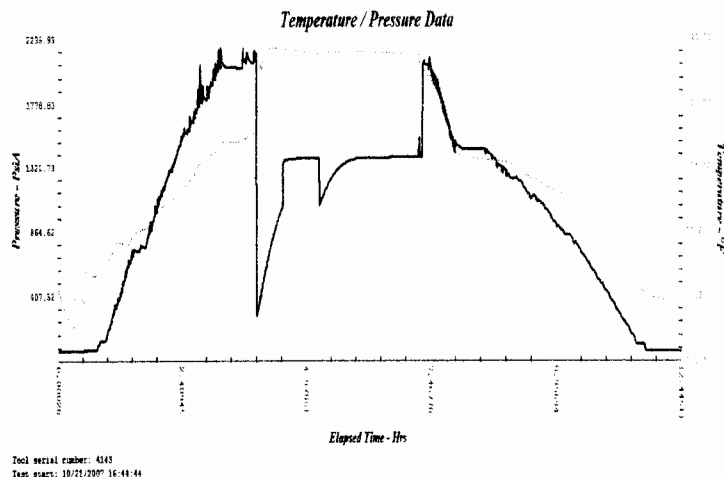

1	Initial Hydrostatic Pressure	2131
2	Initial Flow Pressure	268
3	Final Initial Flow Pressure	1034
4	Initial Shut-In Pressure	1387
5	Initial Final Flow Pressure	1046
6	Final Flow Pressure	1379
7	Final Shut-In Pressure	1395
8	Final Hydrostatic Pressure	2075

Maximum Temperature 124

GENERAL INFORMATION

COMPANY NAME HARTMAN OIL CO. INC.

TEST DATE 10/21/07

SECTION-TOWN-RANGE 18-21S-22W

STATE KANSAS

COUNTY HODGEMAN

ELEVATION GROUND LEVEL 2280

COMPANY REPRESENTATIVE JIM MUSGROVE

LEASE AND WELL NUMBER ANTRIM #6

FORMATION TESTED MISSISSIPPI

DRILL STEM TEST NUMBER 4

REPORT NUMBER 15213

ELEVATION KELLY BUSHINGS 2290

TESTING ENGINEER KEVIN WEBSTER

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4390

TEST INTERVAL (to) 4408

ANCHOR LENGTH 18

TOTAL DEPTH (ft) 4408

TOP PACKER DEPTH 4385

BOTTOM PACKER DEPTH 4390

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 6:00

TOOL OPEN (to) 6:30

DURATION (min.) 30

INITIAL SHUT-IN

TOOL CLOSED (from) 6:30

TOOL CLOSED (to) 7:15

DURATION (min.) 45

FINAL OPEN

TOOL OPEN (from) 7:15

TOOL OPEN (to) 8:00

DURATION (min.) 45

FINAL SHUT-IN

TOOL CLOSED (from) 8:00

TOOL CLOSED (to) 9:00

DURATION (min.) 60

INITIAL FLOW

STRONG BLOW BOTTOM OF BUCKET 1 MINUTE

FINAL FLOW

STRONG BLOW BOTTOM OF BUCKET 1 MINUTE

Company: HARTMAN OIL CO. INC. Lease & Well No. ANTRIM #6 Test #: 4 Date: 10/21/07 SEC. 18
TWP. 21S RGE. 22W

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	HARTMAN OIL CO. INC.	LEASE AND WELL NUMBER	ANTRIM #6
TEST DATE	10/21/07	FORMATION TESTED	MISSISSIPPI
SECTION-TOWN-RANGE	18-21S-22W	DRILL STEM TEST NUMBER	4
STATE	KANSAS	REPORT NUMBER	15213
COUNTY	HODGEMAN	ELEVATION KELLY BUSHINGS	2290
ELEVATION GROUND LEVEL	2280	TESTING ENGINEER	KEVIN WEBSTER
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	152 MILES ROUND TRIP FROM	GREAT BEND	
TOP RECORDER DEPTH	4404	BOTTOM RECORDER DEPTH	4405
RECORDER NUMBER	4023	RECORDER NUMBER	3088

WELL INFORMATION

DRILLING CONTRACTOR	H 2 #2	DRILL COLLAR LENGTH	123
DRILL PIPE LENGTH	4247	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		

COMMENTS

Temperature / Pressure Data

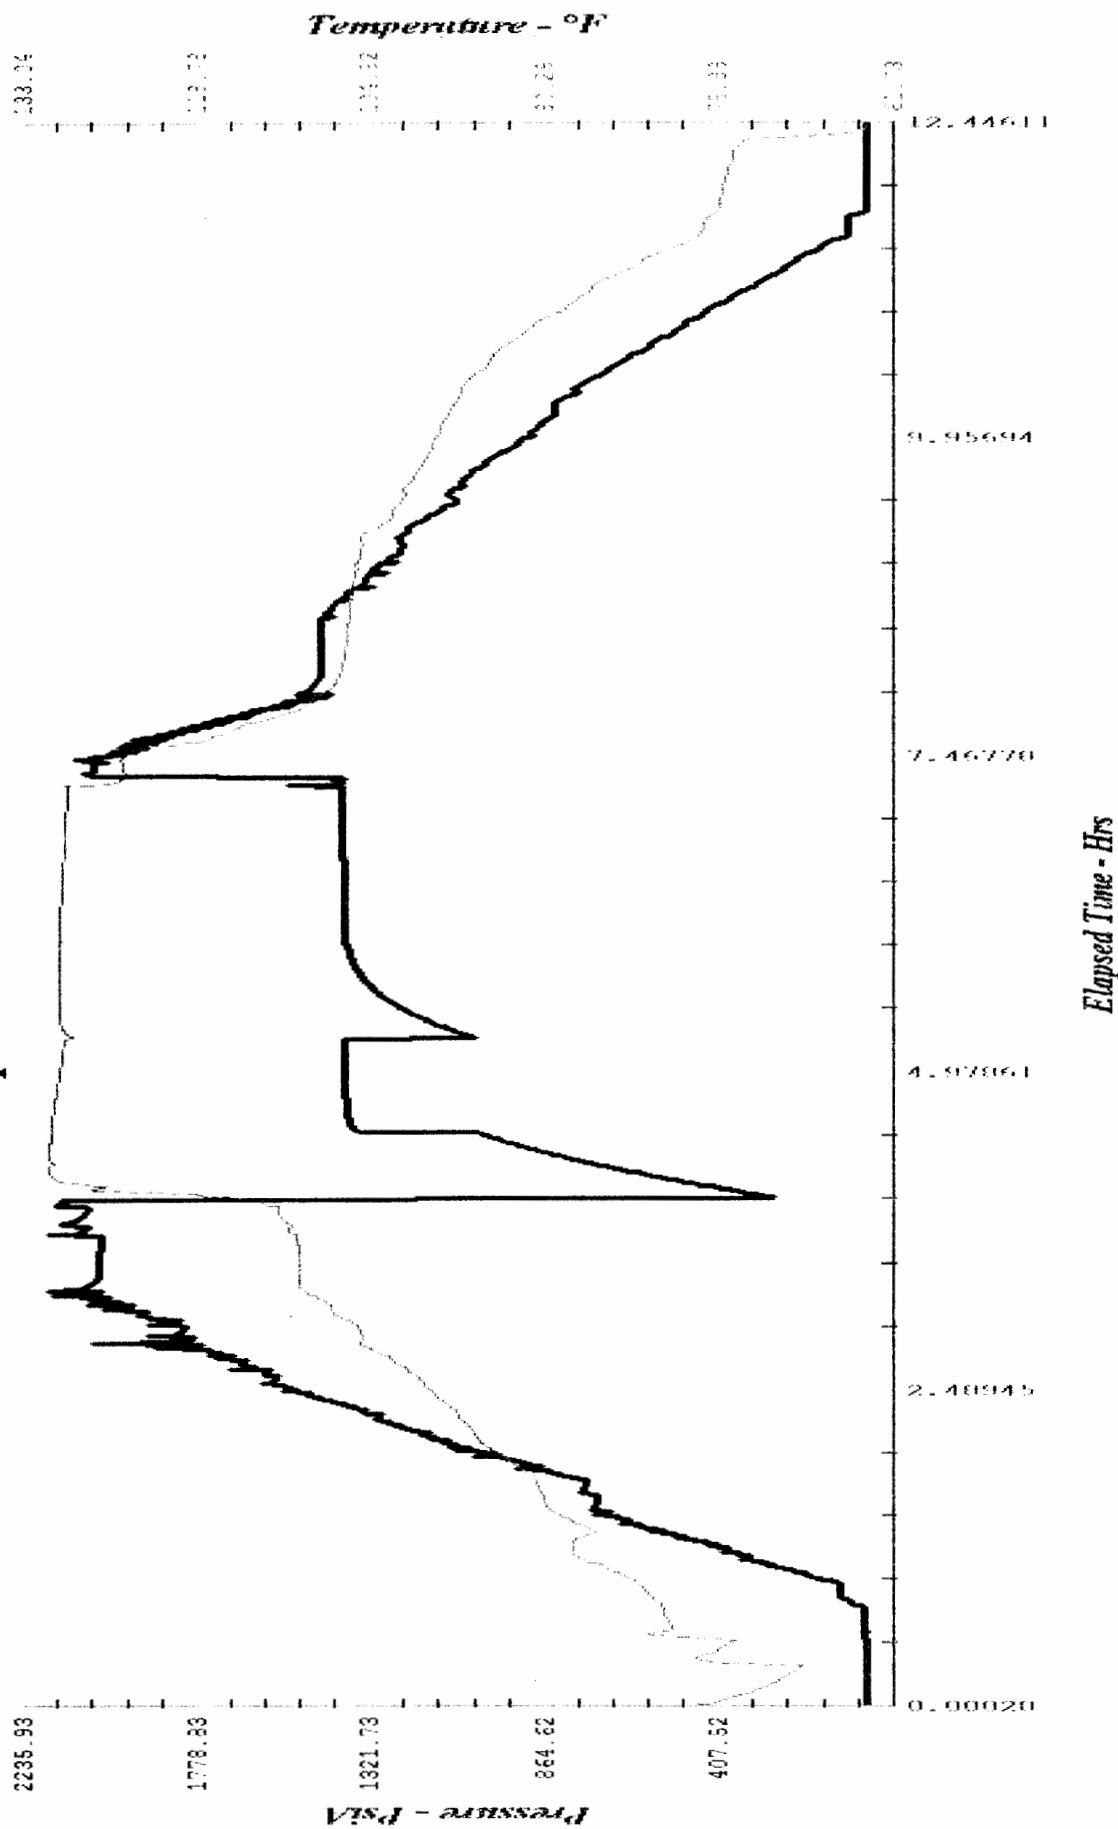

Tool serial number: 4143
 Test start: 10/21/2007 16:44:44
