


Section 27 Township 21 Range 16 W

Well No. # 4 J. B. Cossman

Company Mid-Continent Petroleum Corp.

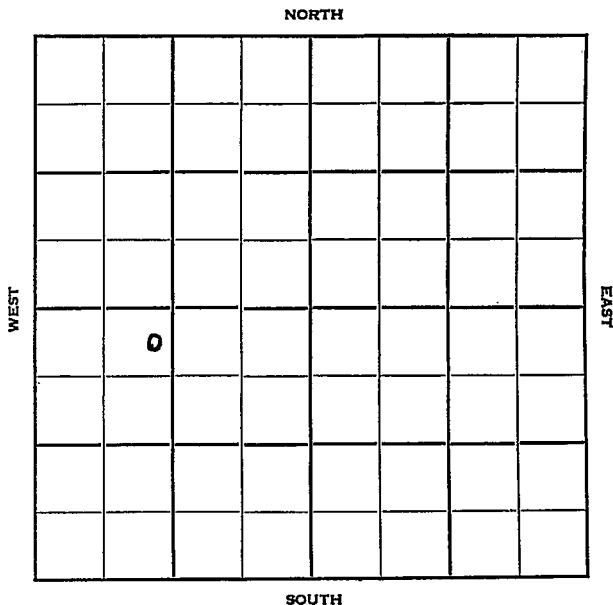

HOT FILE

Sec. 27 Twp. 21 R. 16W

Well No. #4 J.B. Cossman Farm

Mid-Continent Petroleum Corp Company

Barnett Drlg. Contractor


Larned Pool

330 Ft. from N. Line

_____ Ft. from S. Line

_____ Ft. from E. Line

1140 Ft. from W. Line

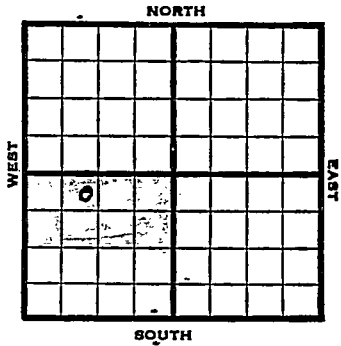

NE NW SW
MEPC 100%

1953	Elév. 1994' DF REPORT
5/26	Location Notice
5/27	Location
6/1	TD 995' Sp. 5-2953 8-5/8" @ 8995' w/450 sx (DR)
6/2	TD 1050' Drlg. "
6/3	TD 1790', shale "
6/3	Anhy 985' 8-5/8" @ 995' Drlg. 1790' (Tel)
6/4	TD 2140', drlg. (DR)
6/5	TD 2410', drlg. "
6/8	Drlg. 3170'. "
6/9	Drlg. 3315' "
6/10	Drlg. 3430' "
6/11	Heav 3389' Toro 3404' Br li 3494' Lans 3505' Drlg. 3570' (Tel)
6/12	Drlg. 3655' (DR)
6/15	Drlg. 3861' Cong. 3809' Top Arbuckle 3857' 5 1/2" @ 3858 w/125 sax. "

$$\begin{array}{r} 3857 \\ - 1863 \\ \hline 3149 \end{array}$$

$$\begin{array}{r} 3857 \\ - 3505 \\ \hline 350 \end{array}$$

OVER

1953
 6/16 TD 3861' WOC (DR)
 6/17 TD 3861' Bailing mud "
 6/18 TD 3867' Filled up 3200' w/oil "
 Testing "
 6/19 TD 3867'
 COMP. 6-19-53 300 BPD on pump "
 6/25 Completed for a maxium well of
 3000 BOPD. Productivity test of
 3850 BOPD (Ltr-McGehee)
 6/24 Spud 5-29-53 Oil well TD 3867
 Anhy 985 8" @ 995 Heeb 3389
 Tor. 3404 Br. lime 3494 Lans 3505
 Cong. 3809 Arb. 3857
 TD 3861 5" @ 3858 DD 3867
 FU 2000' oil 1½ hr. FU 3320' oil 3½
 hr. S/21 BOPH 3 hr. S/54 BOPD 3 hr.
 Comp. 3000 BOPD
 Prod. test 3850 BOPD

COMPLETED

