

TEST TICKET

BEE FORMATION TESTING CO., INC.

P. O. BOX 491

GREAT BEND, KANSAS

No 2070

DATE 7/8/57

CUSTOMER'S ORDER NO.

NAME OF COMPANY

ADDRESS TO MAIL INVOICE

ADDRESS TO MAIL PRESSURE CHARTS

LEASE Schlattermeyer

WELL NO. #2

COUNTY Stafford

STATE Kans.

TESTER J. D. Dumes

APPROVED M. J. Pryor

DRILL STEM TEST NO. 1

SUCCESSFUL NO. 1

MIS-RUN NO. -

FORMATION TESTED A.C.

SIZE HOLE 7 7/8

TOOL JT. 4 1/2 FH

RUBBER SIZE 6 3/4

TEST TOOL SIZE 4 7/8

PACKER SET AT 3282

ANCHOR SIZE 4 1/2 FH

TOTAL DEPTH WELL 3307

LENGTH ANCHOR 25'

PRESSURE RECORDER CAP. 3500-3500

DRILL PIPE RUN: DRY -

WITH FLUID -

RESULTS:

PACKER SET 4:00

M. TOOL OPEN 4:02

M. TOOL OPEN

HRS.

BLOW

Good blow 30 min - Fair blow 15 min - Weak blow 15 min.

RECOVERY

70' H-GCM

300' GAS.

SHUT IN PRESSURE TIME 20 min

MUD WT. 10

VIS. 37

WATER LOSS 18.8

BHP 0

IFP 0

FFP 0

HYDROSTATIC HEAD 1850

EXTRA EQUIPMENT none

JARS -

NO. -


SIZE -

OPERATOR TIME -

TOOL RENTAL TIME -

BEE FORMATION TESTING CO., INC.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

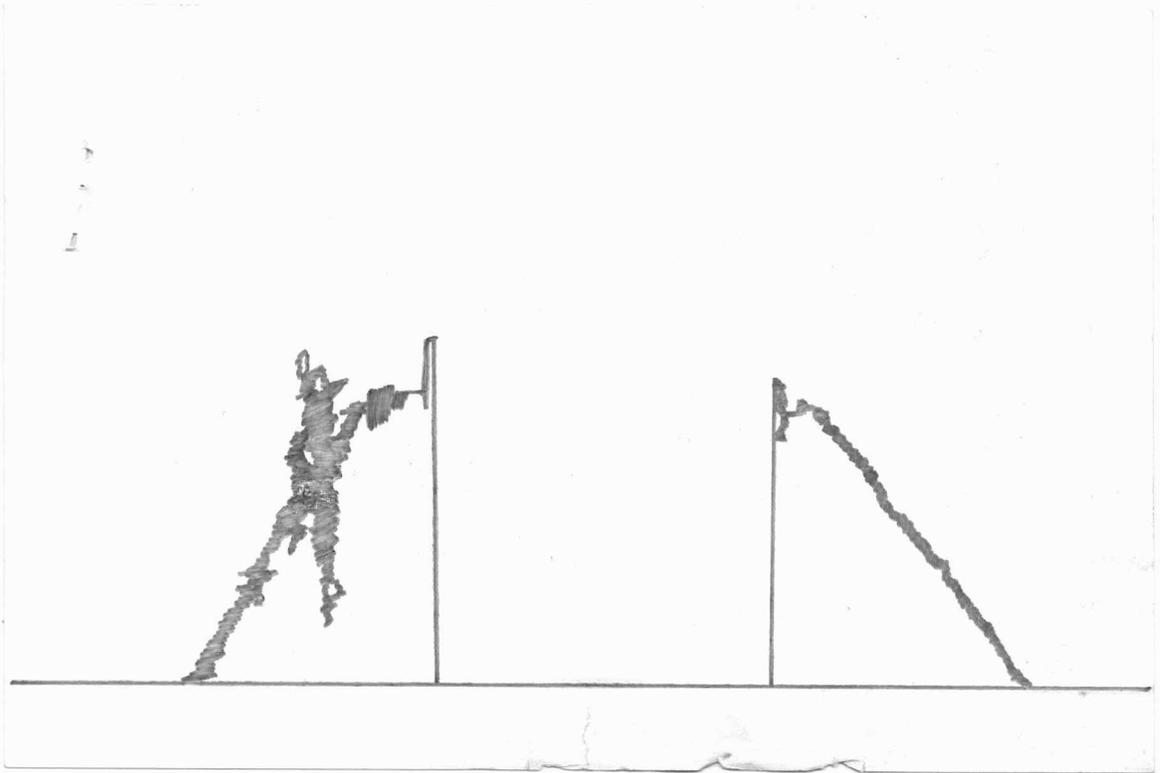

BEE FORMATION TESTING CO., INC.

P. O. BOX 491

GREAT BEND, KANSAS

No 2071

2-SS
2 Charts

DATE 7/8/57

CUSTOMER'S ORDER NO.

NAME OF COMPANY

Duke Drly. Co.

ADDRESS TO MAIL INVOICE

Great Bend, Kas

ADDRESS TO MAIL PRESSURE CHARTS

same

LEASE

Schlostermeyer

WELL NO.

2

COUNTY

Stafford

STATE

Kans.

TESTER

J. D. Turner

APPROVED

M. J. Pryor

DRILL STEM TEST NO.

2

SUCCESSFUL NO.

2

MIS-RUN NO.

-

FORMATION TESTED

alk.

SIZE HOLE

7/8

TOOL JT.

4 1/2 FH

RUBBER SIZE

6 3/4

TEST TOOL SIZE

4 5/8

PACKER SET AT

3426

ANCHOR SIZE

4 1/2 FH

TOTAL DEPTH WELL

3434

LENGTH ANCHOR

8'

PRESSURE RECORDER CAP.

3500-3500

DRILL PIPE RUN: DRY

-

WITH FLUID

-

RESULTS:

PACKER SET

9:53

M. TOOL OPEN

9:55

M. TOOL OPEN

45 min.

HRS.

BLOW

Good blow through out test

RECOVERY

540' Gas 160' oil muddy oil

SHUT IN PRESSURE TIME

20 min.

MUD WT.

10.3

VIS.

37

WATER LOSS

18.8

BHP

975

IFP

0

FFP

75

HYDROSTATIC HEAD

1850

EXTRA EQUIPMENT

none

JARS

NO.

SIZE

OPERATOR TIME

TOOL RENTAL TIME

BEE FORMATION TESTING CO., INC.

SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND TO THE PROPERTY OR PERSONNEL OF THE PARTY FOR WHOM A TEST IS MADE, OR FROM ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH OR IN THE COURSE OF THE USE OF ITS EQUIPMENT, ALL OF WHICH LOSS OR DAMAGE IS ASSUMED BY THE CUSTOMER. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT THE COST OF THE PARTY FOR WHOM TEST IS MADE.

