




OIL WELL CEMENTING INC.

Date 8-16-68

DRILL STEM TEST RECOVERY REPORT

Ticket No. 5847

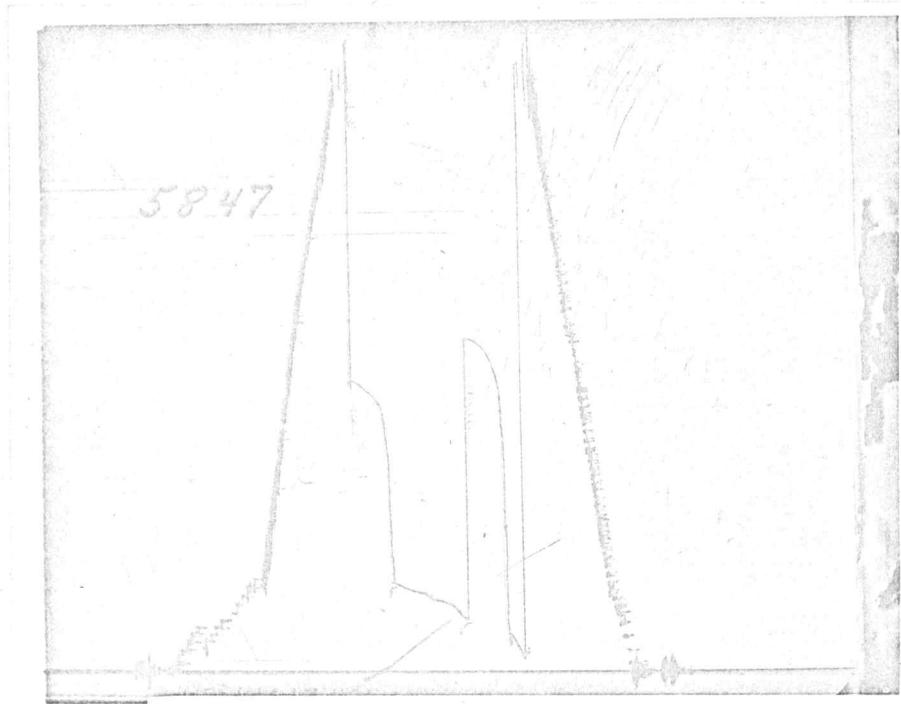

Company Sterling Drlg Co. Contractor Co-tools

Well No. 1 Lease Mooney (E) County Hodgeman Sec. 6 Twp 23 Rng 21

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4"IF

Interval Tested From 4526 To 4572 Depth of Well 4572 Size Choke 5/8

Fluid Recovered In ### Drill colhors Temp. 124 Elev. \_\_\_\_\_

Initial Hyd. 2441 P.S.I. Final Hyd. 2441 P.S.I.

First Initial Flow Pressure 87 P.S.I. Opened Tool 6:30 ### P.M.

First Final Flow Pressure 138 P.S.I. First Flow Pres. 15 Min.

Initial Closed-in Pressure 1324 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 189 P.S.I. Second Flow Pres. 60 Min.

Second Final Flow Pressure 344 P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 1137 P.S.I.

Blow Good thru-out test

Recovery 30' very slightly oil & gas cut mud 180' very hvy. oil & gas cut mud  
60' very hvy. mud cut oil 570' clean oil

Remarks \_\_\_\_\_

Approved By Shepherd Tester Lewis



5847

