

Sun Oil Well Cementing, Inc.

DRILL STEM TEST DATA

P.O. Box 169

Great Bend, Kansas 67530

Lease	Greenwalt	Well No. 1			Date	3-4-75
County	Edwards	Sec. 11	Twp. 25	Rng. 20	Elevation	
Company	L. G. Stepehson				Test No.	1
Contractor	Red Tiger Drilling #6				Zone Tested	Miss.
Charge To	L. G. Stephenson				Ticket #	6140
Approved By	Bob Hammond				Tester	W. Bowman 015

Initial Hydro Mud Press. 2482 P.S.I.

Initial Flow Press. 23 To 38 P.S.I. Initial Flow Period 30 Min.

Initial Shut-in Press. 1470 P.S.I. Initial Shut-in 45 Min.

Final Flow Press. 48 To 76 P.S.I. Final Flow Period 60 Min.

Final Shut-in Press. 1433 P.S.I. Final Shut-in 45 Min.

Final Hydro Mud Press. 2480 P.S.I. TIME TOOL OPEN

Temperature 141

Mud Weight 9.5 Viscosity 38

Fluid Loss

Interval Tested 4630 To 4657

Top Packer Depth 4625 Surface Choke Size

Bottom Packer Depth 4630 Bottom Choke Size 5/8

Total Depth 4657 Main Hole Size 7 7/8


Drill Pipe Size 4 1/2 FH Wt 4 1/2 FH Rubber Size 6 3/4

Drill Collar I.D. Ft. Run

Blow Very weak blow thru-out test

Recovery 120' muddy water few specks oil.

TOP

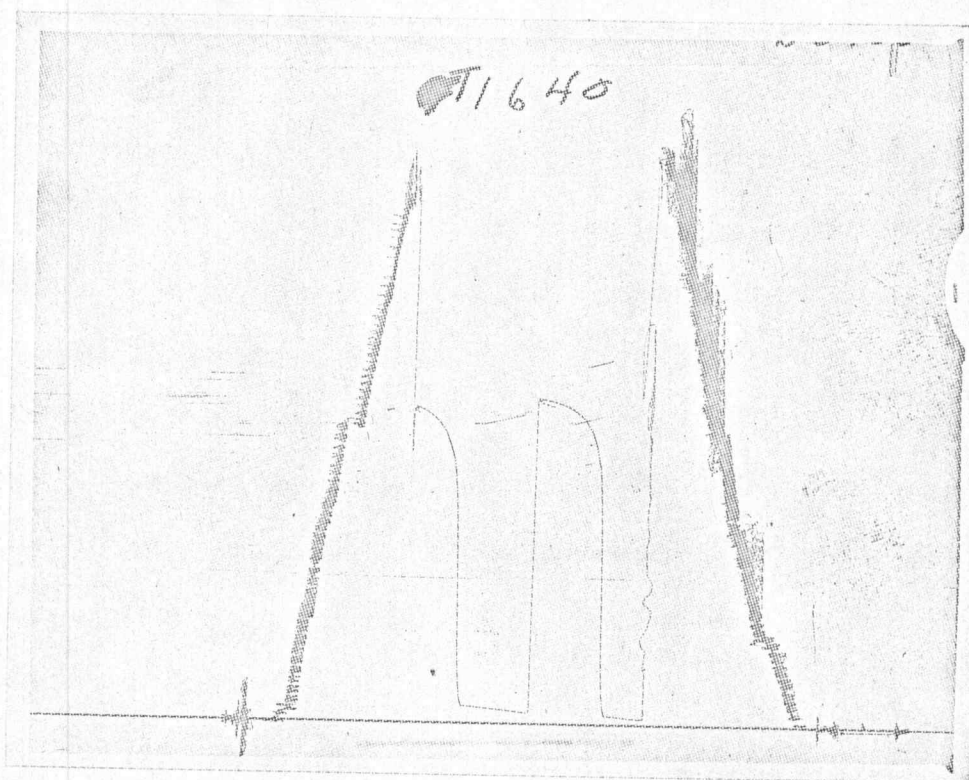

BOTTOM

